



AUTHORIZATION TO PURCHASE AND TRANSPORT OIL FROM LEASE - FORM 8

INDUSTRIAL COMMISSION OF NORTH DAKOTA
OIL AND GAS DIVISION
600 EAST BOULEVARD DEPT 405
BISMARCK, ND 58505-0840
SFSN 5698 (03-2000)

RECEIVED

JAN 28 2020

Well File No.

23359

PLEASE READ INSTRUCTIONS BEFORE FILLING OUT FORM.
PLEASE SUBMIT THE ORIGINAL.

ND OIL & GAS DIVISION

Well Name and Number Atlanta 14-6H	Qtr-Qtr NENW	Section 6	Township 153 N	Range 101 W	County Williams
Operator Continental Resources, Inc.	Telephone Number 405-234-9000		Field Baker		
Address P.O. Box 268870	City Oklahoma City		State OK	Zip Code 73126	

Name of First Purchaser Continental Resources, Inc.	Telephone Number 405-234-9000	% Purchased 100	Date Effective March 8, 2014
Principal Place of Business 20 N. Broadway	City Oklahoma City	State OK	Zip Code 73102
Field Address	City	State	Zip Code
Name of Transporter Hiland Crude	Telephone Number 580-616-2050	% Transported 100	Date Effective March 8, 2014
Address 8811 S. Yale, Ste. 200	City Tulsa	State OK	Zip Code 74137

The above named producer authorizes the above named purchaser to purchase the percentage of oil stated above which is produced from the lease designated above until further notice. The oil will be transported by the above named transporter.

Other First Purchasers Purchasing From This Lease	% Purchased	Date Effective
Other First Purchasers Purchasing From This Lease	% Purchased	Date Effective
Other Transporters Transporting From This Lease	% Transported	Date Effective
Other Transporters Transporting From This Lease	% Transported	Date Effective
Comments		

I hereby swear or affirm that all transporters of Bakken Petroleum System oil listed above implement or adhere to a tariff specification as stringent as the Commissions VPCR₄ requirement 13.7 psi VPCR₄ Tariff Specification Hiland Crude Tariff Authority


I hereby swear or affirm that the information provided is true, complete and correct as determined from all available records.		Date January 20, 2020
Signature 	Printed Name Terry L. Olson	Title Regulatory Compliance Specialist

Above Signature Witnessed By

Witness Signature 	Witness Printed Name Christi Scritchfield	Witness Title Regulatory Compliance Specialist
-----------------------	---	--

FOR STATE USE ONLY

Date Approved JAN 29 2020	NDIC CTB NO 223372
By 	
Title Regulatory Compliance Specialist	



Oil and Gas Division

Lynn D. Helms - Director

Bruce E. Hicks - Assistant Director

Department of Mineral Resources

Lynn D. Helms - Director

North Dakota Industrial Commission

www.dmr.nd.gov/oilgas/

January 29, 2018

Ms. Donna Patocka
Continental Resources, Inc.
P.O. Box 269000
Oklahoma City, OK 73126

**RE: Atlanta #14-6H
NENW Sec. 6, T.153N., R.101W.
Williams County, North Dakota
Baker Field
Well File No. 23359
STRIPPER WELL DETERMINATION**

Dear Ms. Patocka:

Continental Resources, Inc. (Continental) filed with the North Dakota Industrial Commission – Oil and Gas Division (Commission) on January 12, 2018 an application for a Stripper Well Determination for the above captioned well.

Information contained in the application indicates that the above mentioned well is a stripper well pursuant to statute and rule, and Continental has elected to designate said well as a stripper well. The well produced from a well depth greater than 10000 feet and was completed after June 30, 2013. During the qualifying period, September 1, 2016 through August 31, 2017, the well produced at a maximum efficient rate or was not capable of exceeding the production threshold. The average daily production from the well was 32.3 barrels of oil per day during this period.

It is therefore determined that the above captioned well qualifies as a “Stripper Well” pursuant to Section 57-51.1-01 of the North Dakota Century Code. This determination is applicable only to the Bakken Pool in and under said well.

The Commission shall have continuing jurisdiction, and shall have the authority to review the matter, and to amend or rescind the determination if such action is supported by additional or newly discovered information. If you have any questions, do not hesitate to contact me.

Sincerely,

David J. McCusker
Petroleum Engineer

Cc: ND Tax Department



SUNDRY NOTICES AND REPORTS ON WELLS - FORM 4

INDUSTRIAL COMMISSION OF NORTH DAKOTA
OIL AND GAS DIVISION
600 EAST BOULEVARD DEPT 405
BISMARCK, ND 58505-0840
SFN 5749 (09-2006)

Well File No.
23359



PLEASE READ INSTRUCTIONS BEFORE FILLING OUT FORM.
PLEASE SUBMIT THE ORIGINAL AND ONE COPY.

<input type="checkbox"/> Notice of Intent	Approximate Start Date	<input type="checkbox"/> Drilling Program	<input type="checkbox"/> Spill Report
<input checked="" type="checkbox"/> Report of Work Done	Date Work Completed June 4, 2014	<input type="checkbox"/> Redrilling or Repair	<input type="checkbox"/> Shooting
<input type="checkbox"/> Notice of Intent to Begin a Workover Project that may Qualify for a Tax Exemption Pursuant to NDCC Section 57-51.1-03.	Approximate Start Date	<input type="checkbox"/> Casing or Liner	<input type="checkbox"/> Acidizing
		<input type="checkbox"/> Plug Well	<input type="checkbox"/> Fracture Treatment
		<input type="checkbox"/> Supplemental History	<input checked="" type="checkbox"/> Change Production Method
		<input type="checkbox"/> Temporarily Abandon	<input type="checkbox"/> Reclamation
		<input type="checkbox"/> Other	

Well Name and Number
Atlanta 14-6H

Footages	495 F N L	1485 F W L	Qtr-Qtr	Section	Township	Range
				6	153 N	101 W
Field	Pool Bakken			County	Williams	

24-HOUR PRODUCTION RATE	
Before	After
Oil 201 Bbls	Oil 161 Bbls
Water 346 Bbls	Water 268 Bbls
Gas 151 MCF	Gas 180 MCF

Name of Contractor(s)

Address	City	State

DETAILS OF WORK

Continental Resources would like to request a change in production on the Atlanta 14-6H. The well went from flowing to pumping on 6/4/2014.

Company Continental Resources	Telephone Number (405) 234-9000
Address P.O. Box 268870	
City Oklahoma City	State OK
Zip Code 73126	
Signature 	Printed Name Zach Green
Title Regulatory Compliance Specialist	Date July 17, 2014
Email Address Zach.Green@clr.com	

FOR STATE USE ONLY

<input checked="" type="checkbox"/> Received	<input type="checkbox"/> Approved
Date 7/18/14	
By	
Title ND Oil & Gas Division	

GEOLOGICAL MARKERS

PLUG BACK INFORMATION

CORES CUT

Top (Ft)	Bottom (Ft)	Formation	Top (Ft)	Bottom (Ft)	Formation

Drill Stem Test

Well Specific Stimulation

Date Stimulated	Stimulated Formation	Top (Ft)	Bottom (Ft)	Stimulation Stages	Volume	Volume Units
1/20/2014	3 Forks	10924	19085	27	51087	Barrels
Type Treatment	Acid %	Lbs Proppant	Maximum Treatment Pressure (PSI)			Maximum Treatment Rate (BBLS/Min)
Sand Frac		3009408	8352			28.0

Details

Pumped 124649# 40/70 mesh, 2065196# 20/40 sand and 819563# 20/40 creamic.

Date Stimulated	Stimulated Formation	Top (Ft)	Bottom (Ft)	Stimulation Stages	Volume	Volume Units
Type Treatment	Acid %	Lbs Proppant	Maximum Treatment Pressure (PSI)			Maximum Treatment Rate (BBLS/Min)

Details

Date Stimulated	Stimulated Formation	Top (Ft)	Bottom (Ft)	Stimulation Stages	Volume	Volume Units
Type Treatment	Acid %	Lbs Proppant	Maximum Treatment Pressure (PSI)			Maximum Treatment Rate (BBLS/Min)

Details


Date Stimulated	Stimulated Formation	Top (Ft)	Bottom (Ft)	Stimulation Stages	Volume	Volume Units
Type Treatment	Acid %	Lbs Proppant	Maximum Treatment Pressure (PSI)			Maximum Treatment Rate (BBLS/Min)

Details

Date Stimulated	Stimulated Formation	Top (Ft)	Bottom (Ft)	Stimulation Stages	Volume	Volume Units
Type Treatment	Acid %	Lbs Proppant	Maximum Treatment Pressure (PSI)			Maximum Treatment Rate (BBLS/Min)

Details

ADDITIONAL INFORMATION AND/OR LIST OF ATTACHMENTS

I hereby swear or affirm that the information provided is true, complete and correct as determined from all available records.	Email Address Terry.Olson@clr.com	Date 4/4/2014
Signature 	Printed Name Terry L. Olson	Title Regulatory Compliance Specialist

**AUTHORIZATION TO PURCHASE AND TRANSPORT OIL FROM LEASE - FORM 8**

INDUSTRIAL COMMISSION OF NORTH DAKOTA
OIL AND GAS DIVISION
600 EAST BOULEVARD DEPT 405
BISMARCK, ND 58505-0840
SFN 5698 (03-2000)



Well File No. 23359
NDIC CTB No. <i>22335D</i>

PLEASE READ INSTRUCTIONS BEFORE FILLING OUT FORM.

PLEASE SUBMIT THE ORIGINAL AND FOUR COPIES.

Well Name and Number Atlanta 14-6H	Qtr-Qtr NENW	Section 6	Township 153 N	Range 101 W	County Williams
Operator Continental Resources, Inc.	Telephone Number 405-234-9000		Field Baker		
Address P.O. Box 268870	City Oklahoma City		State OK	Zip Code 73126	

Name of First Purchaser Continental Resources, Inc.	Telephone Number 405-234-9000	% Purchased 100	Date Effective March 8, 2014
Principal Place of Business 20 N. Broadway	City Oklahoma City	State OK	Zip Code 73102
Field Address	City	State	Zip Code
Name of Transporter Hiland Crude (West Camp Creek Pipe)	Telephone Number	% Transported	Date Effective March 8, 2014
Address P.O. Box 3886	City Enid	State OK	Zip Code 73702

The above named producer authorizes the above named purchaser to purchase the percentage of oil stated above which is produced from the lease designated above until further notice. The oil will be transported by the above named transporter.

Other First Purchasers Purchasing From This Lease	% Purchased	Date Effective
Other First Purchasers Purchasing From This Lease	% Purchased	Date Effective
Other Transporters Transporting From This Lease	% Transported	Date Effective
Other Transporters Transporting From This Lease	% Transported	Date Effective
Comments		

I hereby swear or affirm that the information provided is true, complete and correct as determined from all available records.	Date March 21, 2014
Signature <i>Terry L. Olson</i>	Printed Name Terry L. Olson
Title Regulatory Compliance Specialist	

Above Signature Witnessed By

Witness Signature <i>Christi Scritchfield</i>	Witness Printed Name Christi Scritchfield	Witness Title Regulatory Compliance Specialist
--	---	--

FOR STATE USE ONLY	
Date Approved <i>APR 14 2014</i>	
By <i>Annette Tretter</i>	
Title Oil & Gas Production Analyst	

Continental Resources Inc.

**Atlanta 14-6H – Cyclone 2
Atlanta 14 Well Eco Pad
NENW Sec 6 – NENE Sec 5
Sec 6 & 5 - T153N-R100W
Williams & McKenzie Co., North Dakota
API# 33-105-02719**

**By: Jed D Nelson & Adam Swoboda
Geo-Link Inc.**

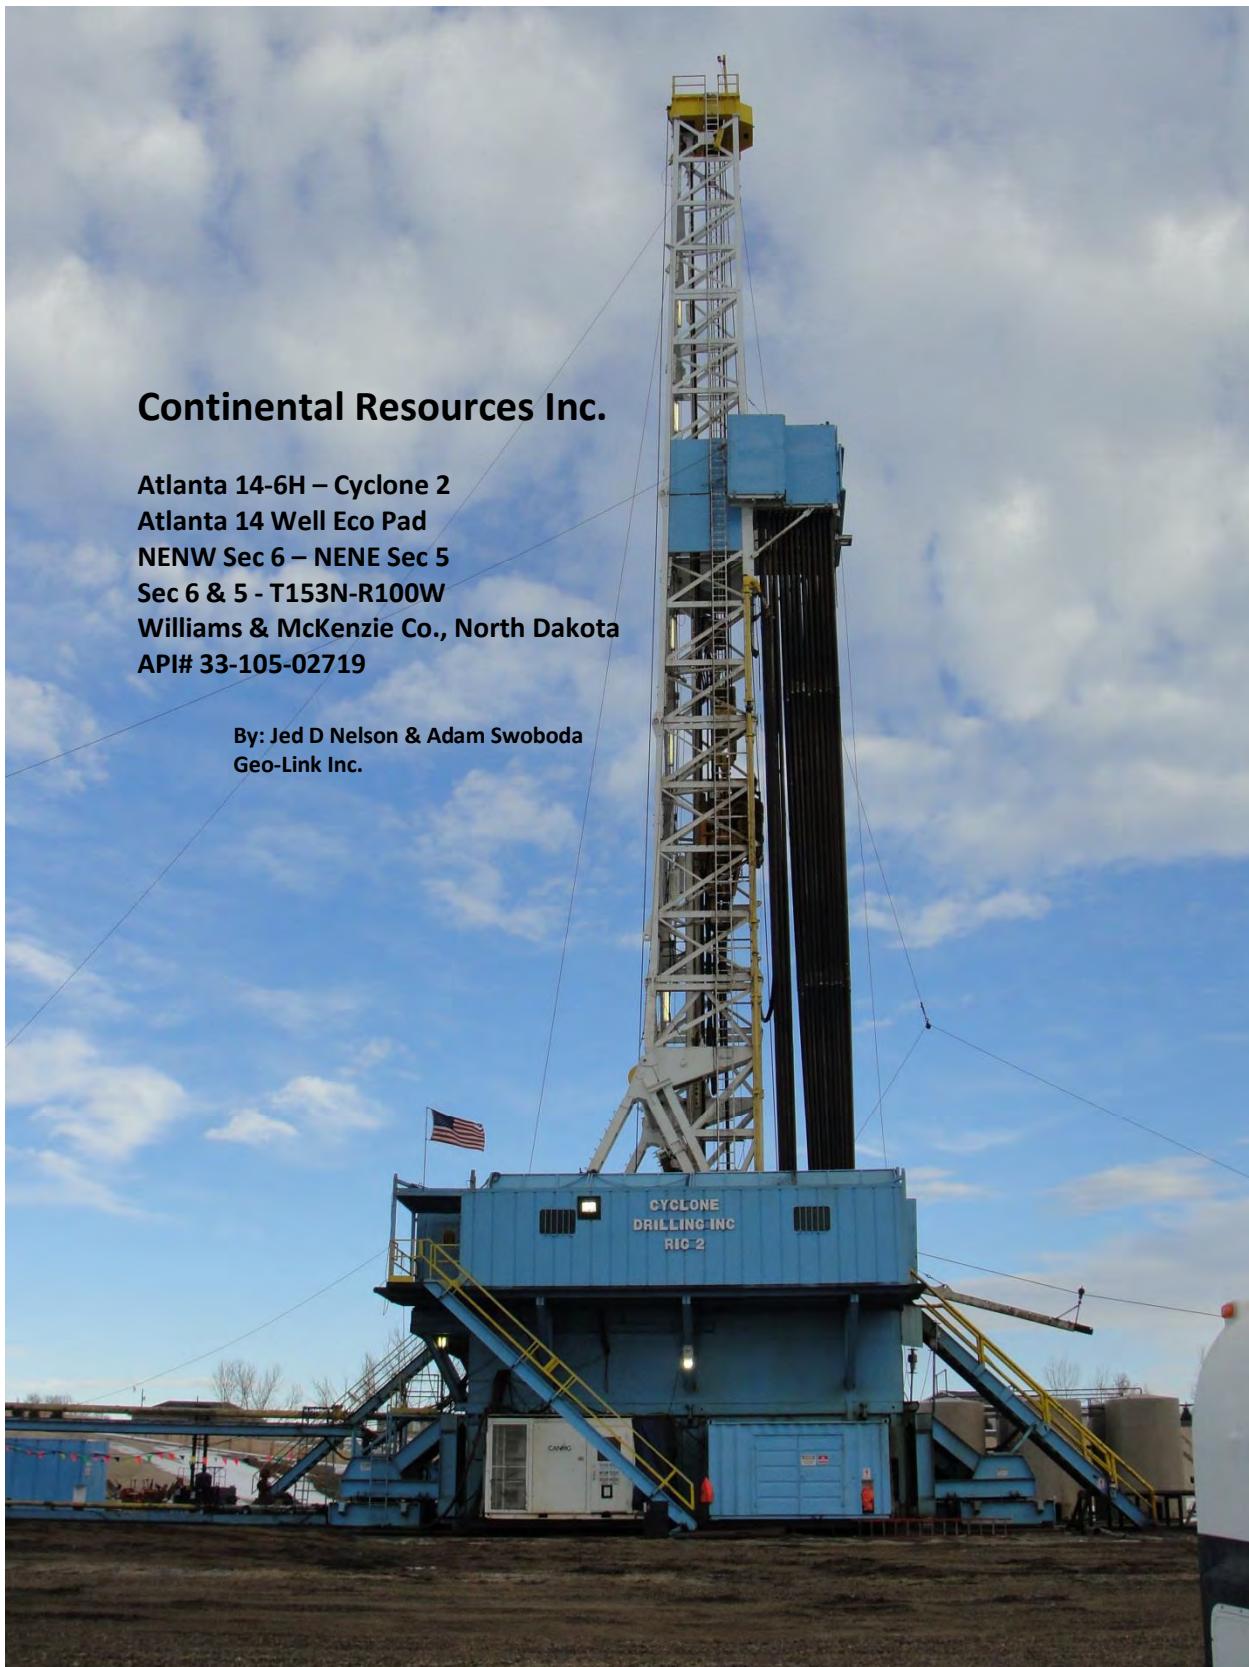




Table of Contents

Well Information

Cross Sections

Well Synopsis

Drilling Activity

Chronological Gas / Sample Show

Gamma Ray, Avg. ROP, 24 Hr Progress, Gas, Mud Weight, Oil Show Plot

Formation Tops, Critical Points, Lateral Summary

Formation Structure

Plots

MWD Surveys

Drilling / Slide Report

TVD Log



Well Information

WELL NAME:	Atlanta 14-6H Atlanta 14 Well Eco Pad
OPERATOR:	Continental Resources, Inc. P.O. Box 269000 Oklahoma City, Ok 73126
SURFACE LOCATION:	495 4FNL & 1485 4FWL NENW Section 6, T153N, R101W
CASING:	7 1/2" Intermediate casing set at 10924 4MD; 10586 4TVD 528 4FNL & 2128 4FWL NENW Section 6, T153N, R101W
BOTTOM HOLE LOCATION:	Projection to Bit: 19085 4MD; 10562 4TVD 651 4FNL & 233 4FEL NENE Section 5, T153N, R101W
FIELD/AREA:	Williston
COUNTY:	Williams & McKenzie Co.
STATE:	North Dakota
API#:	33-105-02719
ELEVATION:	GL: 1945 4 KB: 1967 4
SPUD:	March 5 th 2013
DRILLED OUT OF CASING: (LATERAL)	April 17 th 2013
TOTAL DEPTH/DATE: Total Days:	19085 4MD 4 April 23, 2013 49
BOTTOM HOLE DATA:	
Kick-off Point:	MD=10040 4TVD=10039 4
Vertical Section:	8799.35 4
Drift of Azimuth	91.07°
Average Inclination (lateral):	90.12°
Lateral footage:	8161 4
WELL STATUS:	To be completed as a Three Forks oil well
MWD REP:	MS Energy Services



Well Information

DIRECTIONAL REP: MS Energy Services

MUD LOGGING SERVICE: Geo-Link Inc.

GEOLOGICAL CONSULTANT: Jed D Nelson & Adam Swoboda
Second Hand: R.C. Whitmore & RC Whitmore

GAS EQUIPMENT: M-Logger / M-Control SN ML-197
Spare SN ML-077

SAMPLE PROGRAM:
Vertical & Build Section:
30+ Samples lagged and caught by mud loggers 8300 + 0920 +
Charles Salt, Mission Canyon, Lodgepole, Upper Bakken Shale,
Middle Bakken Member, Lower Bakken Shale, Three Forks
Dolomite

Lateral Section:
100+ Samples lagged and caught by mud loggers 11000 + 9085 +
Logging: Three Forks Dolomite
One set sent to NDGS Core Library (Grand Forks)

DISTRIBUTION LIST:

Continental Resources, Inc.
Land Department

Memo

To: Archie Taylor, Ben Ainsworth, Brian A. Moss, Cameron Thompson, David McMahan, Doug Pollitt, Gerry Allen, Gil Smith, Gina Callaway, Greg Blocker, Jack Stark, Jaclyn Jantz, Jeanette McDonald, Josh Byler, Marjorie McKenzie, Matt Liter, Neil Olesen, Paula Fast, Renee Sanders, Rob Hersom, Robert Sandbo, Sally Messenger, Shamika Morrison, Shawn Roche, Shelly Ramirez and William Parker

From: Nicole Hodges

CC: Rick Muncrief and Heath Hibbard



Well Information

Date: January 2, 2013

RE: **Atlanta 14-6H**

Sections 5, 6, 7 & 8-153N-101W

Williams & McKenzie Counties, North Dakota

Regarding the referenced well, the following parties are entitled to receive the indicated information and be contacted for elections as shown.

"Standard Information" means the following:

DURING DRILLING OPERATIONS:

E-mail the following
during drilling and completion operations:

- 1) Daily Drilling Report
- 2) Mud Log
- 3) Lateral Profile
- 4) Gamma Ray, MD & TVD Logs
- 5) Directional Surveys

POST DRILL:

Mail the following items after
drilling is completed:

- 1) Complete Electric Log
- 2) Complete Mud Log
- 3) Complete DST report
- 4) Core Analyses
- 5) Complete Directional Surveys
- 6) Complete Lateral Profile
- 7) Water, Oil & Gas Analysis
- 8) Cement Bond Log
- 9) Final complete drilling report

Owner	Information	Casing Point Election	Dry Hole Takeover Election
NDIC Oil and Gas Division Attn: Open Hole Logs 1016 East Calgary Ave. Bismarck, ND 58503-5512 Email: digitallogs@nd.gov	Open Hole Logs (1 paper copy) – (email TIFF/ LAS)	No	No
Continental Resources, Inc. Attn: Robert Sandbo P.O. Box 269000 OKC, OK 73126 Email: GeoOps@clr.com	Standard Information (2 copies of Final Geological Reports/Mud Logs) – (email PDF)	No	No
Continental Resources, Inc. Attn: Robert Sandbo P.O. Box 269000 OKC, OK 73126 Email: GeoOps@clr.com	Cased and Open Hole Logs (2 hard-copies) – (email	No	No



Well Information

	TIFF/LAS)		
Black Stone Energy Company, LLC c/o Mark Connally 1001 Fannin, Suite 2020 Houston, TX 77002 Phone: 713.658.0647 Fax: 713.658.0943 Email: kdolfi@blackstoneminerals.com , mconnally@blackstoneminerals.com (Send Well Information daily, via email)	See Attached Well Requirements	No	Yes
Boedecker Resources 151 O'Brien Ln. Moore, MT 59464 Phone: 406.374.2270 (Send Well Info weekly, via US Mail)	Standard Well Information	No	Yes
Brigham Oil & Gas, L.P. 6300 Bridge Point Parkway Building 2, Suite 500 Austin, TX 78730 Phone: 512.427.3300 Fax: 512.427.3388 Email: reports@bexp3d.com (Send Well Information daily, via email)	See Attached Well Requirements	No	Yes
Dale Lease Acquisitions 2011-B, L.P. Attn: John D. Crocker, Jr. 2100 Ross Avenue, Suite 1870 Dallas, TX 75201 Phone: 214.979.9010, Ext. 16 Fax: 214.969.9394 Email: reports@dale-energy.com , johnc@dale-energy.com (Send Well Information daily, via email)	See Attached Well Requirements	No	Yes
Golden Eye Resources, LLC 5460 South Quebec Street, Suite 335 Greenwood Village, CO 80111 Phone: 303.832.1994 Fax: 303.832.5118 Email: reports@goldeneyerесources.com	See Attached Well Requirements	No	Yes




Well Information


(Send Well Information daily, via email)			
Helm Energy, LLC c/o Joe Brinkman 5251 DTC Parkway Suite 425 Greenwood Village, CO 80111 Email: jbrinkman@helmenergy.com (Send Well Information daily, via email)	See Attached Well Requirements	No	Yes
Intervention Energy, LLC Attn: John Zimmerman P.O. Box 1028 Minot, ND 58702-1028 Email: john@interventionenergy.com (Send Well Information daily, via email)	Standard Well Information	No	Yes
John H. Holt Oil Properties, Inc. Attn: John H. Holt P.O. Box 24 Williston, ND 58802 Phone: 701.774.1200 Fax: 701.572.8499 Email: john@jhhop.com (Send Well Information daily, via email)	Standard Well Information	No	Yes
Lario Oil & Gas Company P.O. Box 29 Denver, CO 80201-0029 Fax: 303.595.4849 Email: reportsdenver@lario.net (Send Well Information daily, via email)	See Attached Well Requirements	No	Yes
Liberty Resources, LLC Attn: Reports 1200 17 th Street, Suite 2050 Denver, CO 80202 Email: reports@libertyresourcesllc.com (Send Well Information daily, via email)	See Attached Well Requirements	No	Yes
MHM Resources, LP Attn: Julie Larson P.O. Box 51570 Midland, TX 79710 Phone: 432.685.6045 Fax: 432.685.9081 Email:	See Attached Well Requirements	No	Yes



Well Information

<p>drlreports@mhmresourceslp.com, jlarson@mhmresourceslp.com (Send Well Information daily, via email)</p>			
<p>Michael Harrison Moore 2006 Trust Attn: Julie Larson P.O. Box 51570 Midland, TX 79710 Phone: 432.685.6045 Fax: 432.685.9081 Email: drlreports@mhmresourceslp.com, jlarson@mhmresourceslp.com (Send Well Information daily, via email)</p>	See Attached Well Requirements	No	Yes
<p>Steven H. Harris Family L.P. P.O. Box 2323 Bismarck, ND 58502 Phone: 701.223.4866 Fax: 701.223.2556 Email: w2harris@aol.com (Send Well Information daily, via email)</p>	Standard Well Information	No	Yes
<p>XTO Energy, Inc. Attn: Randy Hosey 810 Houston Street Fort Worth, TX 76102 Phone: 817.885.2398 Fax: 817.885.2698 Email: randy_hosey@xtoenergy.com, non-op_reports@xtoenergy.com, rose_holman@xtoenergy.com (Send Well Information daily, via email)</p>	See Attached Well Requirements	No	Yes

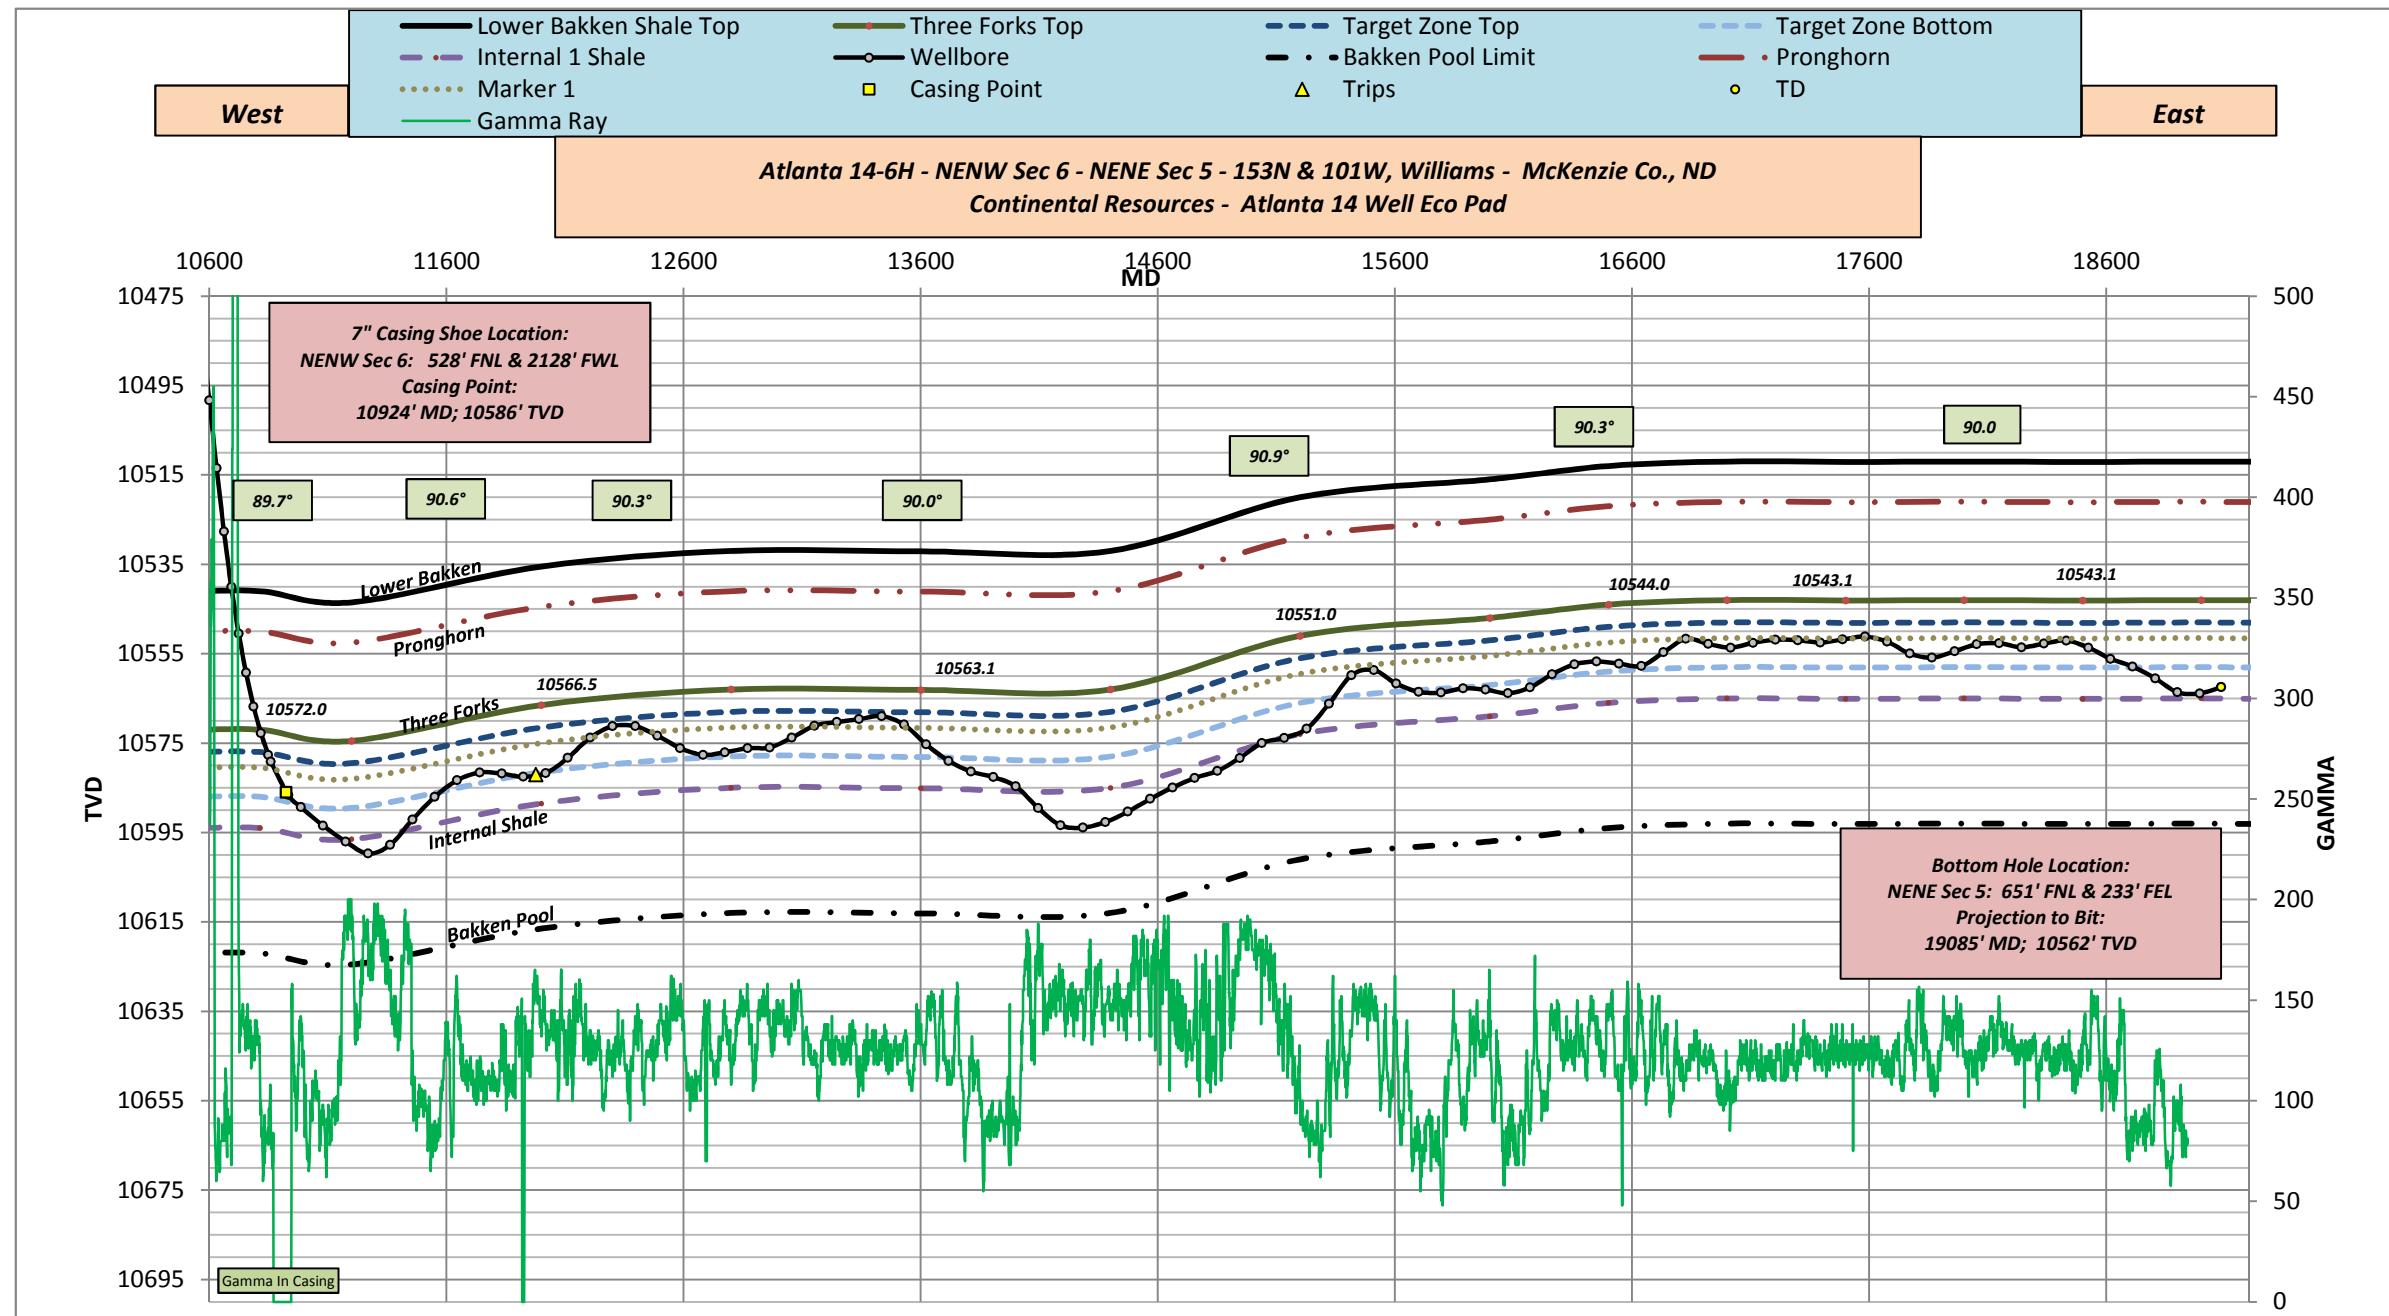

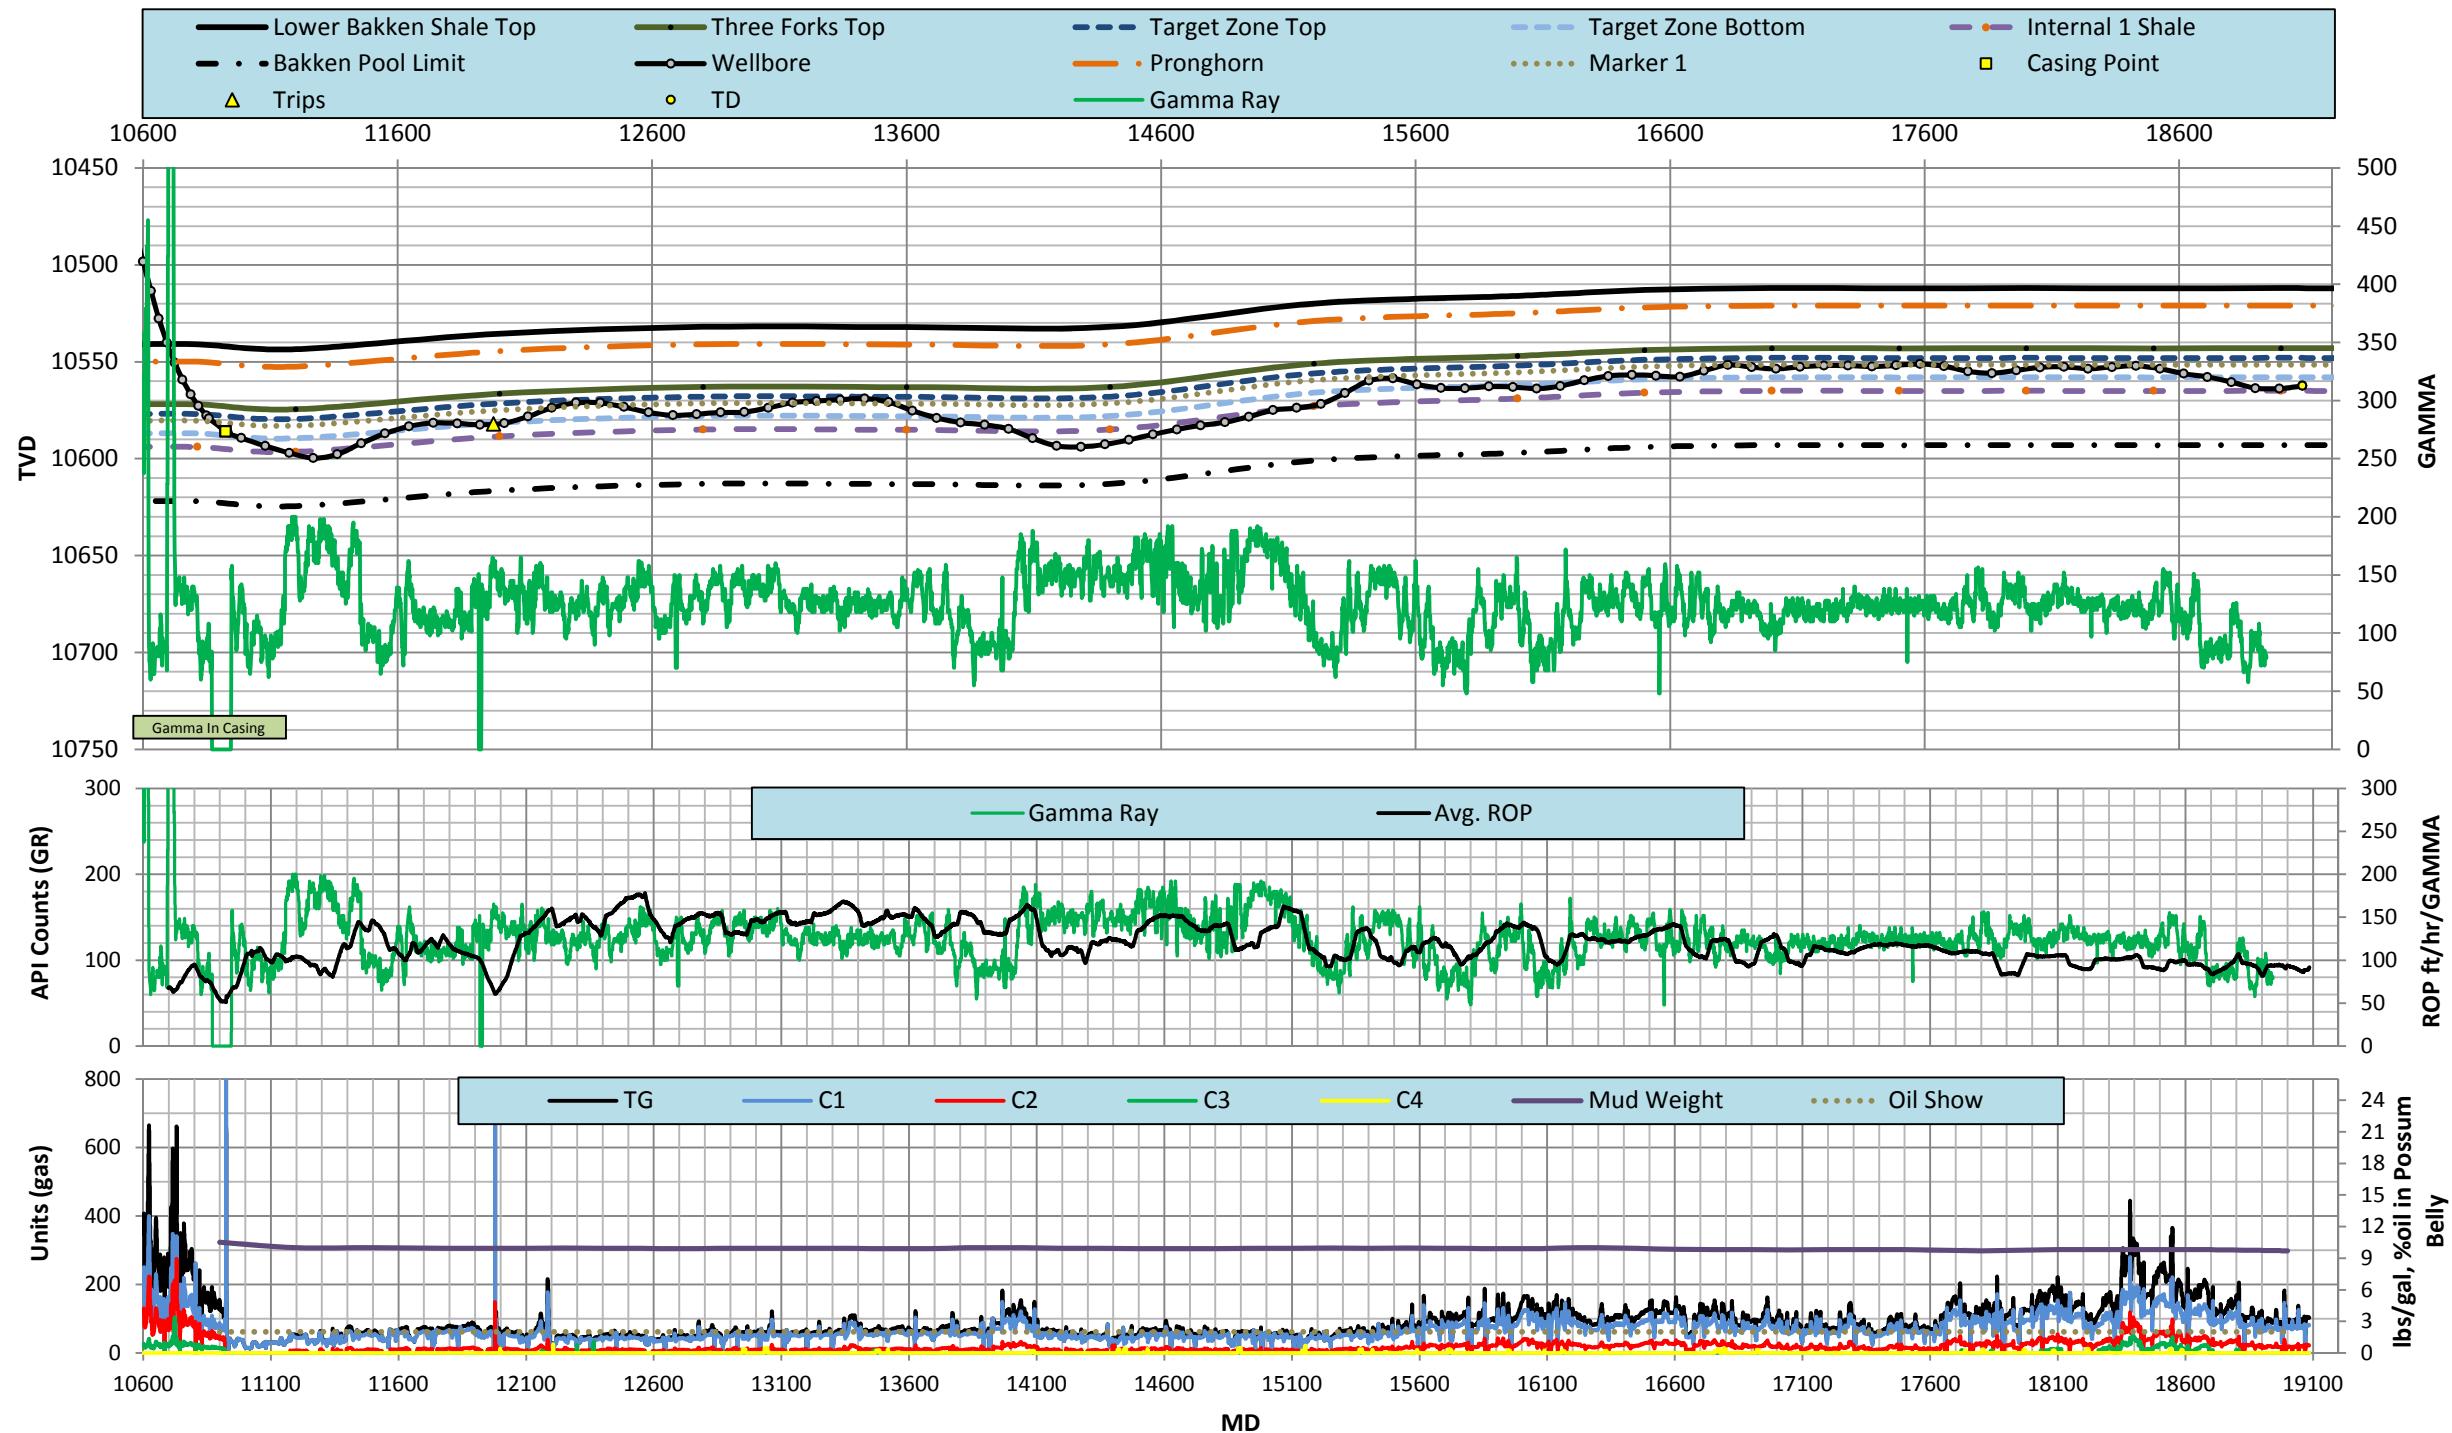



WELL SYNOPSIS

Well Plan: *The Atlanta 14-6H was spud on March 5th, 2013 with a surface location of 495' FNL and 1485' FWL, NENW Section 6 - Township 153 North and Range 101 West in Williams Co., North Dakota. This well was operated by Continental Resources Incorporated with the objective target of the late Devonian Three Forks Formation.*

The plan showed a build section with a kickoff point of 10011' MD in the Mississippian Lodgepole with a 10°/100' build rate to the landing point of 10909' MD; 10584' TVD in the clean gamma zone within the Three Forks Formation. This zone started approximately 5' below the Three Forks. The landing target was approximately 15' into the Three Forks Formation. The plan was to drill lateral for an estimated 8257' to the hardline in the NENE corner of section 5 - Township 153 North and Range 101 West following the estimated dip of 89.8°. The projected well path is to the East with a proposed azimuth of 91.09°.

The offsets provided were the Atlanta wells already drilled on the Atlanta Eco pad. These include the Atlanta 1-6H, 2-6H, 3-6H, 4-6H, 11-6H, 12-6H and 13-6H drilled by Continental Resources.

Gas logged in the vertical and lateral sections were monitored using Mud Logging Systems – Mlogger & Mcontrol. (Primary Logger: ML-197 – Backup Logger ML-077)

M-Logger CC & TC filaments calibrated with 1% and 100% test gas – Chromatograph calibrated with 1% test gas (gas-units).

Build Section: *The Build assembly was picked up at 10040' MD; 10039' TVD on April 13th, 2013. The well was kicked off at 10040' MD on April 13th, 2013 at 13:20 hrs. This assembly was able to generate sufficient builds to land the build section within the target zone. The up hole markers logged were the Top of the Charles Salt (830' TVD); Base of the Last Salt (9021' TVD); Mission Canyon (NP); and the Lodgepole (9781' TVD). The down hole markers below kick off point consisted of the False Bakken (10486' TVD); Upper Bakken Shale (10495' TVD); Middle Bakken Member (10509' TVD); Lower Bakken Shale (10541' TVD); and the Three Forks Dolomite (10572' TVD). These markers came in consistently with the Atlanta 12-6H. With these markers coming in close to the Atlanta 12-6H our landing was estimated at 10590' TVD. The Lower Bakken Shale had a thickness of 11' of actual black-brown shale, but consisted of a sticky intermediate layer (Pronghorn) below the shale that was 24' thick – our landing was targeted 15' below this intermediate layer. The landing for 7" intermediate casing was completed April 14th, 2013 at 14:45 hrs, 13' into the Three Forks Dolomite with a landing at 10585' TVD. Casing point: 10924' MD; 10585' TVD and casing location of NENW Sec 6 – 528' FNL & 2128' FWL (see Atlanta 14-6H build and TVD log for more information regarding samples & formation thicknesses)*

Gas observed in the build section which showed gas averaging 46-152 units through the Lodgepole formation with no background sample shows and oil shows. Both Upper and Lower Bakken Shales resulted in 240-660 units. The Middle Bakken Member ranged from 240-395 units, averaging 450 units. The Three Forks ranged from 70-240 units, averaging 147 units. Circulating trip gas through casing resulted in 75-815 units.



WELL SYNOPSIS

Lateral Leg: Penetration of the lateral section started on April 17th, 2013, at 10:20 hrs with a depth of 10924' MD, drilling with a 6" PDC bit and 1.5° mud motor. The plan was to drill in the Target zone and follow the 9' zone of interest between two hot gamma markers, close to the Three Forks top (Pronghorn) in the condensed Pyrite zone. The lateral section was drilled from 10924' MD to 19085' MD for a lateral length of 8161', with a bottom hole location: 651' FNL & 233' FEL – NENE Sec 5, T153N-R101W – completed on April 23rd, 2013 – 07:00 hrs. The lateral section was drilled entirely in the Three Forks Formation with one complete trip for a BHA @ 11977' MD.




Samples collected in the lateral section mostly consisted of light-medium gray, buff-tan Dolomite/Limestone consisting of varying amounts of disseminated Pyrite, and also of the blue-green shale, mainly in our target zone starting 5' below the Three Forks top. The lower zone resulted in tan/brown clean Dolomite, above the Internal 1 Shale. These two zones showed fair to good porosity, but trace amounts of oil shows and cut. Gas averaged 82 units and ranged from 82 units to 1388 units of gas and displayed about 2% - 3% oil accumulating in the possum belly – fluorescence was generally increasing the further out we got, but didn't display large amounts of hydrocarbons. Connection gasses ranged from 45 units to 635 units and trip gas ranged from 2500 units to 4200 units. (For more detailed sample descriptions – see Atlanta 14-6H Lateral Log)

The formation dip was configured using two significant hot spots in our target zone. These were illustrated by the upper and lower target markers. Both markers ranged from 120–150 (API) and consisted of erratic gamma in between these with counts ranging from 90-138 (API). Below our bottom target zone was a cool gamma zone roughly 4' above the cooler gamma zone we saw in the beginning of the lateral. Below this cool gamma was the Internal 1 Shale with ranged from 102-200 (API) seen around the start of the lateral. There was a total of 1262' drilled in the Internal 1 Shale, mostly towards the middle of the lateral. The markers in the bottom were definitely clearer cut versus the top in the target zone. The target zone displayed more Pyrite giving more erratic and hotter counts whereas, below the target zone displayed less Pyrite in the clean tan-brown Dolomite giving us lower counts 55-89 (API). Utilizing both zones we were able to calculate an accurate dip angle which was different from the prognosis of the estimated structure. The Formation climbed 29' from the start of the lateral, a 90.12° formation dip, which was at first projected to drop 22' through the lateral section. (For more detailed gamma signatures and structure please see Atlanta 14-6H cross section)

Drilling Activity															
Atlanta 14-6H															
Day	Date	Depth	Footage	WOB	RPM	Diff P	ROP	SPP	SPM	WT	VIS	ACTIVITY			
38	4/12/2013	9506	1459	38.9	64	621.3	50.4	3329	100	10.4	76	Drilling Vertical Section: Drill, Survey, Slide, Rig Service			
39	4/13/2013	10040	534	NA	NA	NA	NA	NA	NA	10.4	72	TOOH & TIH for BHA/Drilling Vertical Section: Drill, Survey, Slide, Rig Service/ TOOH for Build Assembly			
40	4/14/2013	10585	545	28.3	0	186	28.1	3027	99	10.4	65	TIH: Build Assembly/Drilling Build Section: Drill, Slide Survey, Rig Service			
41	4/15/2013	10924	339	NA	NA	NA	NA	NA	NA	NA	NA	Drilling Build Section: Slide, Survet, Drill, Rig Service/ TD'D Build Section @ 10924' MD & 10585' TVD			
42	4/16/2013	CASING OPERATIONS													
43	4/17/2013	CASING OPERATIONS													
44	4/18/2013	11977	1053	NA	NA	NA	NA	NA	NA	NA	NA	Drilling Lateral: Drill, Survey, Slide, Rig Service; TOOH/TIH: BHA			
45	4/19/2013	12930	953	11.8	62	516.2	60.7	2758	89	9.9	31	Drilling Lateral: Drill, Survey, Slide, Rig Service			
46	4/20/2013	14533	1603	12.6	62	615.7	157.3	3180	90	9.9	32	Drilling Lateral: Drill, Survey, Slide, Rig Service			
47	4/21/2013	15870	1337	14.3	57	650.7	139.3	3181	90	9	32	Drilling Lateral: Drill, Survey, Slide, Rig Service			
48	4/22/2013	17605	1735	15.9	45	828.7	113.9	3202	88	9.8	31	Drilling Lateral: Drill, Survey, Slide, Rig Service			
49	4/23/2013	18991	1386	87.3	0	189.7	26.6	2390	86	9.8	32	Drilling Lateral: Drill, Survey, Slide, Rig Service			
49	4/23/2013	19085	94	12.6	47	582.6	87.3	3195	87	9.7	32	TD Atlanta 14-6H @ 19085' MD - 4/23/13 - 07:00, Drill, Survey, Slide, Rig Service			

Chronological Gas/Sample/Oil
Atlanta 14-6H

Date	Depth 0500hrs	Max Gas(u)	Avg Gas(u)	Conn Gas(u)	Trip Gas(u)	Oil Show	<u>Sample Show</u>
4/12/2013	9506	58	16	NA	NA	0%	No Shows
4/13/2013	10040	95	39	NA	NA	0%	No Shows
4/14/2013	10585	152	46	NA	40	0%	No Shows
4/15/2013	10924	242	664	NA	NA	0%	No Shows
4/16/2013	CASING OPERATIONS						
4/17/2013	CASING OPERATIONS						
4/18/2013	11977	818	52	10--52	NA	2%	Trace
4/19/2013	12930	1390	52	19--45	1390	2%	Trace
4/20/2013	14533	182	67	34--87	NA	2%	Trace
4/21/2013	15870	167	63	29-72	NA	2%	Trace
4/22/2013	17605	174	100	84-170	NA	2%	Trace
4/23/2013	18991	441	145	154-335	NA	2%	Trace
4/23/2013	19085	137	94	NA	NA	2%	Trace

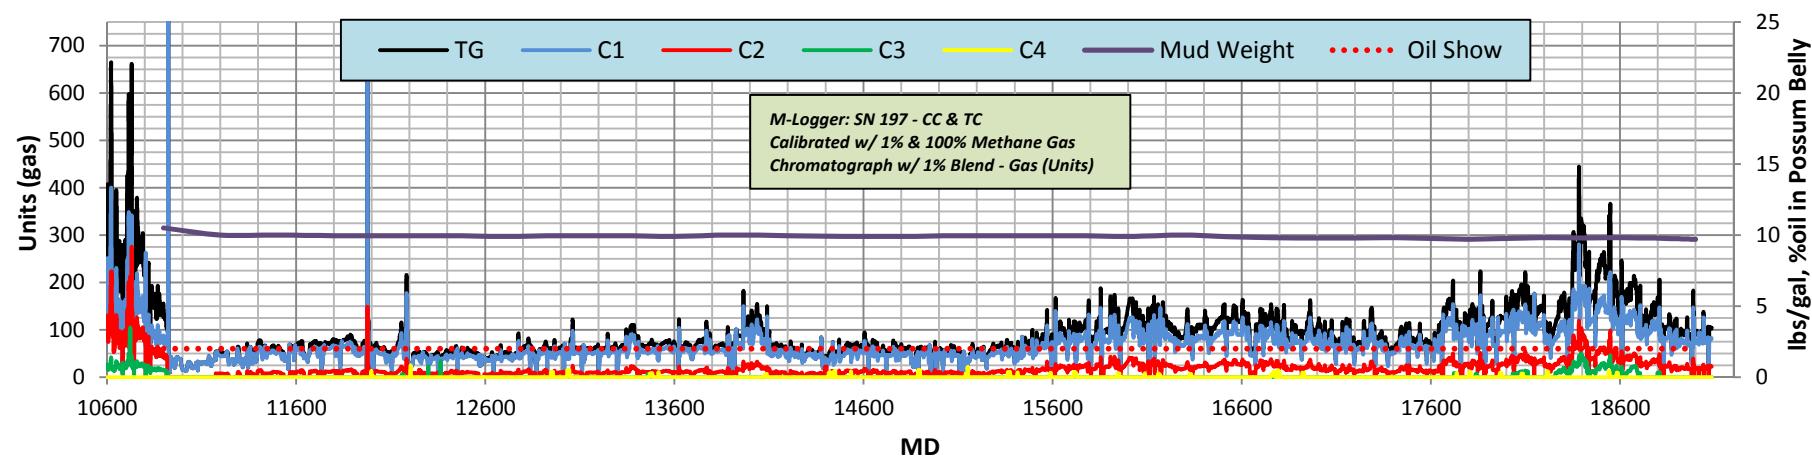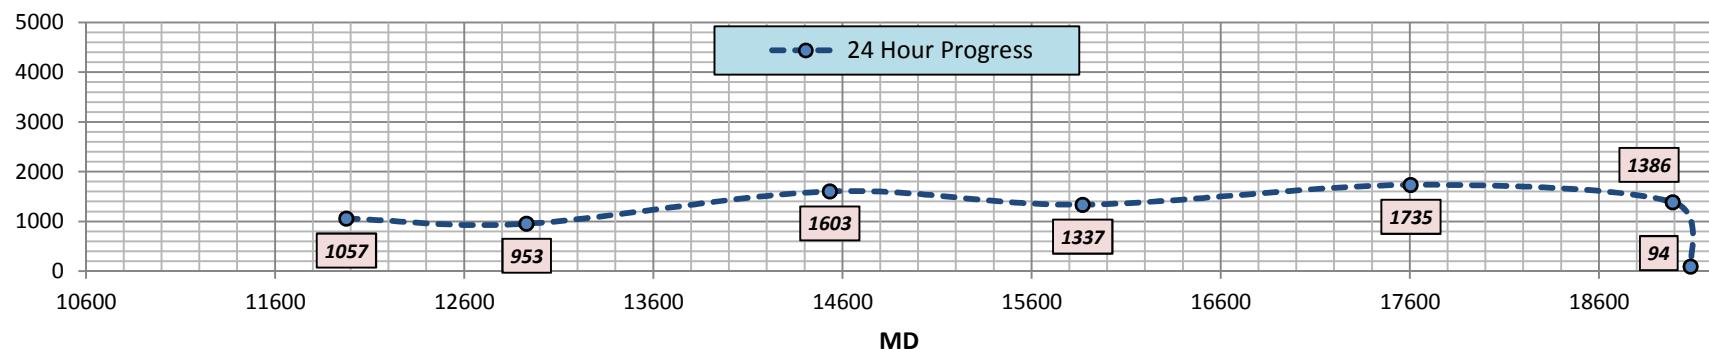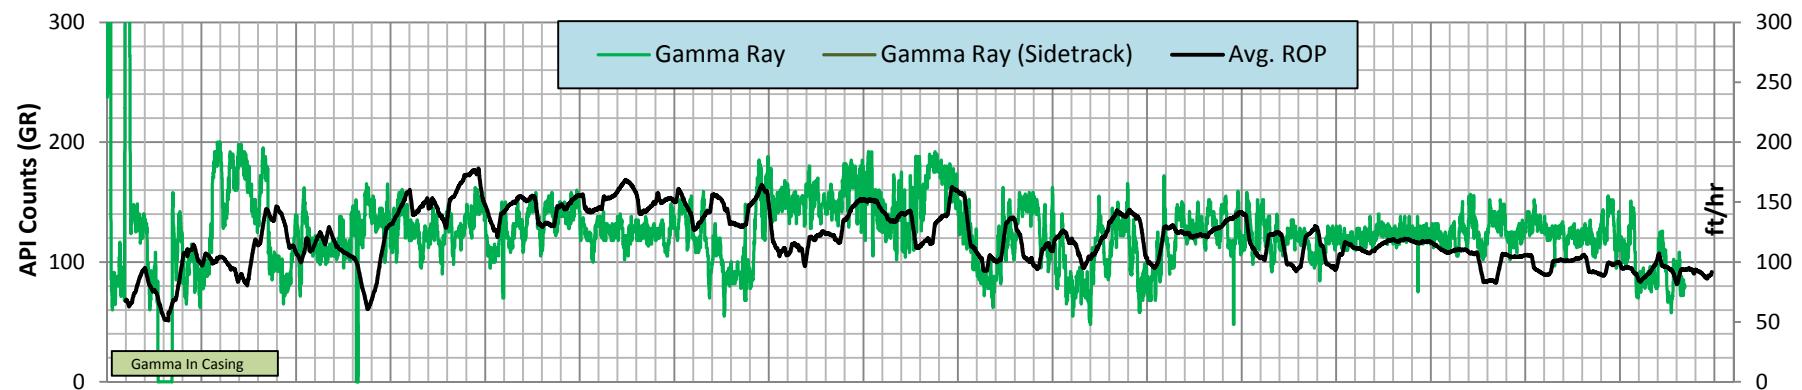

Formation Tops - Atlanta 14-6H

VERTICAL & BUILD SECTIONS

FORMATION TOPS	Ground Elevation:	1945	Kelly Bushing:	1967	Prognosed SS		
Formation	MD (ft)	TVD (ft)	VS (ft)	SS (ft)	(ft)	Difference	
Pierre Shale		1867		100	-2958		
Greenhorn		4549			-2582		
Dakota Grp. (fka Mowry)		4925			-3657		
Base of Dakota Sand		5624					
Dunham Salt Top		na			na		
Dunham Salt Base		na			na		
Pine Salt Top		7156			-5189		
Pine Salt Base		7183			-5216		
Minnekahta		7202			-5235		
Opeche Salt Top		na			na		
Opeche Salt Base		na			na		
Minnelusa Grp.		7431			-5464		
Tyler		7617			-5650		
Kibbey		8153			-6186		
Charles	8305	8304	60.14	-6337	-6333	4	
BLS	9022	9021	56.69	-7054	-7044	10	
Mission Canyon	NP	NP	NP	NP	-7267	NA	
Lodgepole	9782	9781	61.36	-7814	-7820	-6	
False Bakken	10576	10486	315.25	-8519			
Upper Bakken Shale	10592	10495	328.91	-8528	-8529	-1	
Middle Bakken	10622	10509	354.90	-8542	-8543	-1	
Lower Bakken Shale	10695	10541	420.53	-8574	-8574	0	
Three Forks	10814	10572	534.56	-8605	-8602	3	
Three Forks Target	10933	10587	652.33	-8620	-8617	3	
				Projected Tops			
				<i>Tops picked by Drilling breaks (ROP & Differential Data), Samples, and Gamma</i>			


Critical Points	MD	TVD	SUBSEA	V/S
Three Forks Formation	10814	10572	-8605	534.56
Kick off Point (KOP)	10040	10039	-8072	65.67
Surface Hole location	NENW Sec 6: 495' FNL & 1485' FWL			
Casing Point	10924	10586	-8619	643.39
Casing Location	NENW Sec 6: 528' FNL & 2128' FWL			
Total Depth (projection to Bit)	19085	10562	-8595	8799.35
Bottom Hole Location	NENE Sec 5: 651' FNL & 233' FEL			

Lateral Trips	MD	TVD	Vertical & Build Trips	MD	TVD
BHA	11977	10582	For MWD TOOL & Bit	9523	9522
			For Build Assembly	10040	10039

LATERAL SUMMARY

Total Lateral Footage	8161	%	
Three Forks	6899	84.5%	<i>Target Zone</i>
Internal Shale	1262	15.5%	<i>Out of Target Zone</i>
			100.0%

STRUCTURE (MD - TVD) - Atlanta 14-6H										
MD (ft)	Lower Bakken			Target						Dip Rate (ft/100)
	Shale Top	Three Forks Top	Target Zone Top	Zone Bottom	Internal 1 Shale	Bakken Pool Limit	Pronghorn	Marker 1	Dip (angle)	
10400.0	10541.0	10572.0	10577.0	10587.0	10594.0	10622.0	10550.0	10580.5		
10500.0	10541.1	10572.1	10577.1	10587.1	10594.1	10622.1	10550.1	10580.6	89.94	0.10
10814.0	10541.0	10572.0	10577.0	10587.0	10594.0	10622.0	10550.0	10580.5	90.02	-0.03
11200.0	10543.5	10574.5	10579.5	10589.5	10596.5	10624.5	10552.5	10583.0	89.63	0.65
12000.0	10535.5	10566.5	10571.5	10581.5	10588.5	10616.5	10544.5	10575.0	90.57	-1.00
12800.0	10532.0	10563.0	10568.0	10578.0	10585.0	10613.0	10541.0	10571.5	90.25	-0.44
13600.0	10532.1	10563.1	10568.1	10578.1	10585.1	10613.1	10541.1	10571.6	89.99	0.01
14400.0	10532.0	10563.0	10568.0	10578.0	10585.0	10613.0	10541.0	10571.5	90.01	-0.01
15200.0	10520.0	10551.0	10556.0	10566.0	10573.0	10601.0	10529.0	10559.5	90.86	-1.50
16000.0	10516.0	10547.0	10552.0	10562.0	10569.0	10597.0	10525.0	10555.5	90.29	-0.50
16500.0	10513.0	10544.0	10549.0	10559.0	10566.0	10594.0	10522.0	10552.5	90.34	-0.60
17000.0	10512.0	10543.0	10548.0	10558.0	10565.0	10593.0	10521.0	10551.5	90.11	-0.20
17500.0	10512.1	10543.1	10548.1	10558.1	10565.1	10593.1	10521.1	10551.6	89.99	0.02
18000.0	10512.0	10543.0	10548.0	10558.0	10565.0	10593.0	10521.0	10551.5	90.01	-0.02
18500.0	10512.1	10543.1	10548.1	10558.1	10565.1	10593.1	10521.1	10551.6	89.99	0.02
19000.0	10512.0	10543.0	10548.0	10558.0	10565.0	10593.0	10521.0	10551.5	90.01	-0.02
19500.0	10512.2	10543.2	10548.2	10558.2	10565.2	10593.2	10521.2	10551.7	89.98	0.04

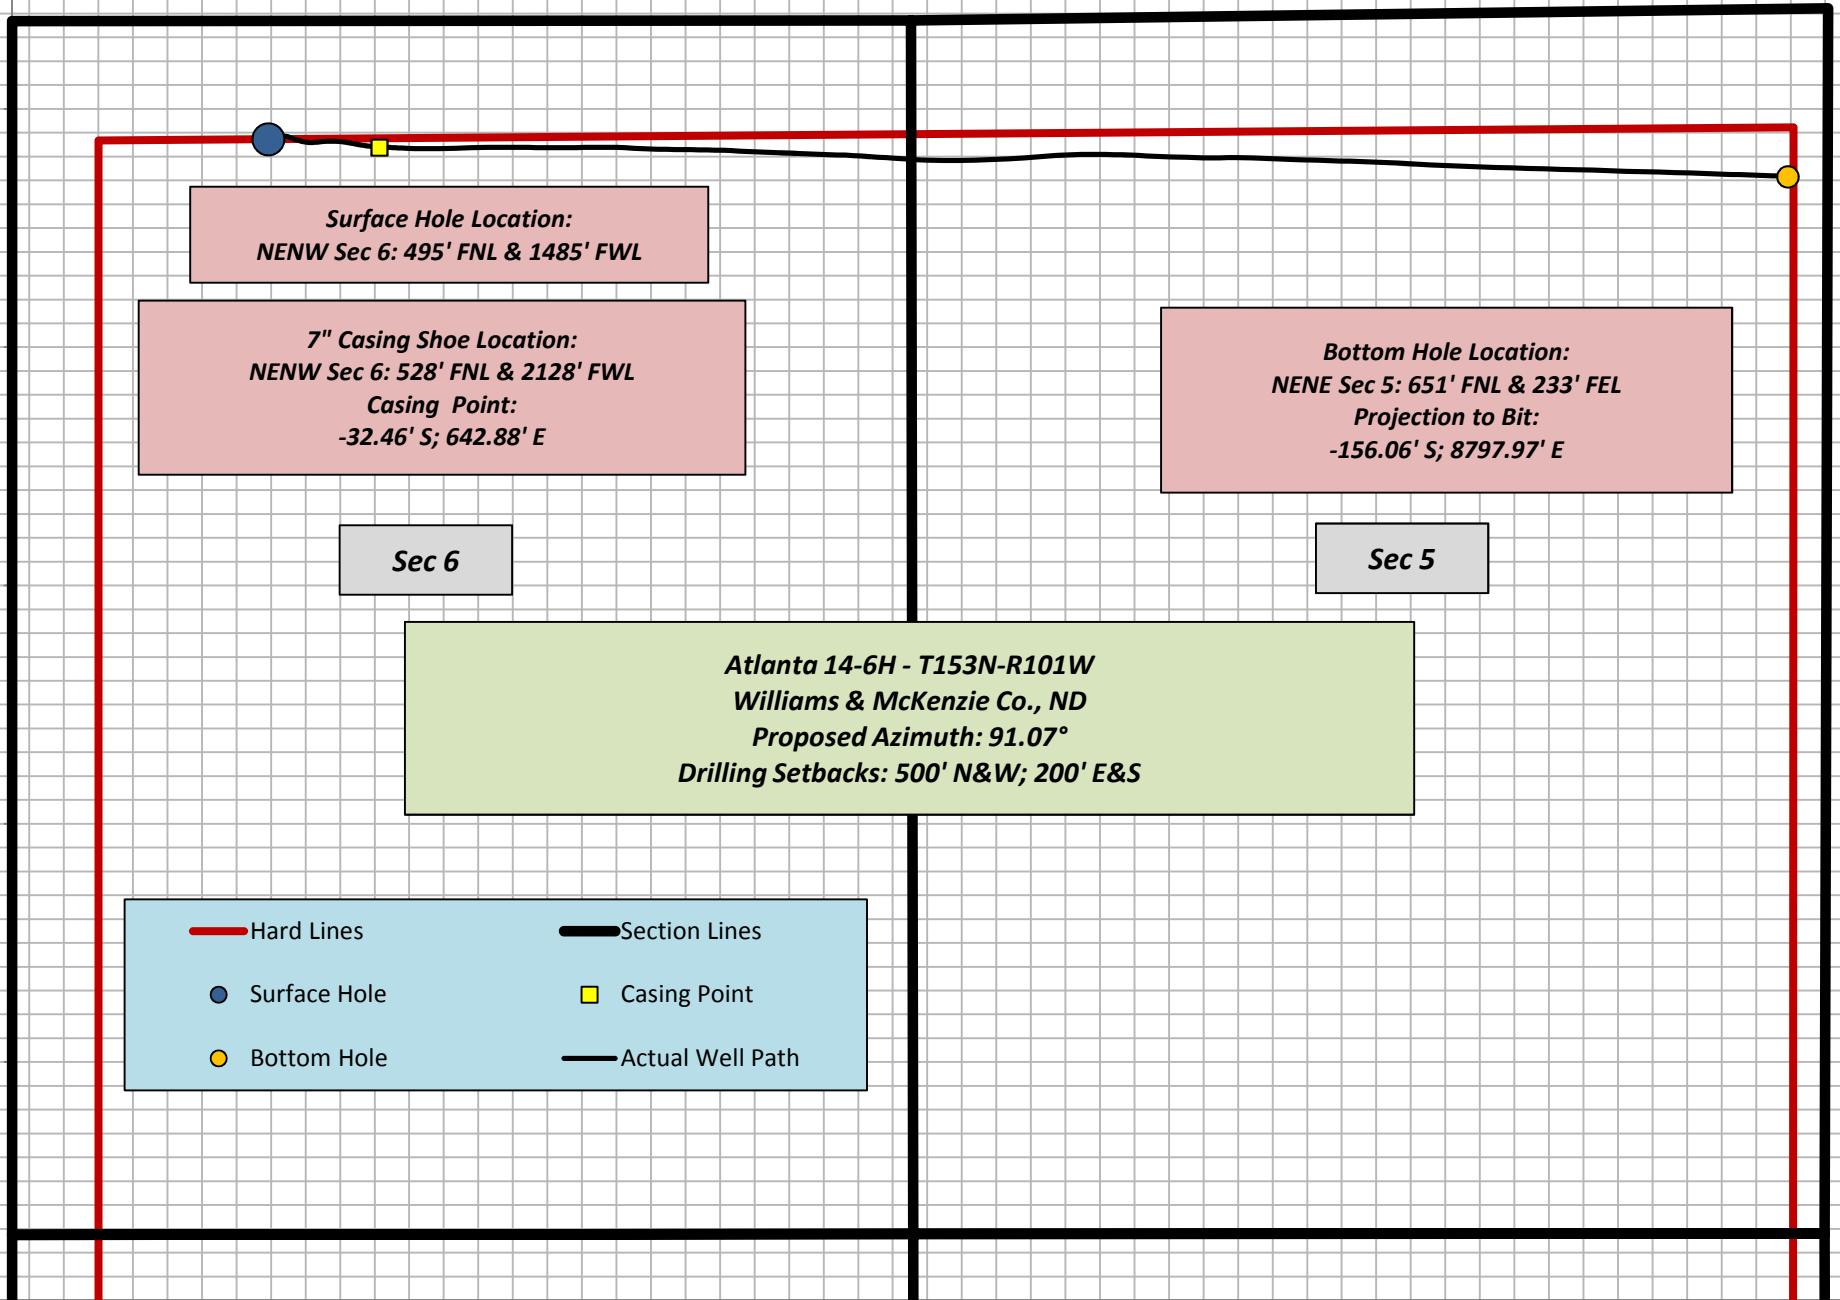

N



		SURVEY CALCULATION PROGRAM											ctrl-shift-I = Insert Survey ctrl-shift-D = Delete Survey			
		Minimum Curviture														File:
OIL & GAS CO.:		Continental Resources						Target Information				VS Referenced to Offset from Surface				
WELL:		Atlanta 14-6H						TARGET TVD:		10584.00		NORTH/SOUTH:		0.00		
COUNTY / STATE:		Williams Co, ND						TARGET INCL:		89.80		EAST/WEST:		0.00		
RIG:		Cyclone #2						TARGET AZM:		91.09		(Enter 0' N and 0' E for Surface)				
JOB NUMBER:		DDMT- 130258														
SURVEY COMPANY:			DIRECTIONAL COMPANY:			PROPOSED DIRECTION:			91.09		MAG-DEC. / TOTAL CORR.(+/-):			8.54		
MS Guidance			MSDirectional								REFERENCED TO:			True North		
MWD SPECIALIST(S):			DIRECTIONAL DRILLER(S):			COMMENTS:										
Tim Coleman Cliff Bray			Kurtis Wortley/Casey Crawford			TIE-IN INFORMATION PROVIDED BY CONTINENTAL RESOURCES. Final survey is PBHL										
														Target Calculations		
			TRUE	TEMP	Course				Surface	CLOSURE		DLS/	BUR/	TVD AT 0'	RIGHT(+)	ABOVE (+)
SVY	MD	INC	AZM	F	Length	TVD	N-S	E-W	Vert Sect	DIST	DIR	100	10 0'	V. SEC.	LEFT(-)	BELOW (-)
Tie In	1961	0.90	88.40			1960.91	-5.03	-10.00	-9.90	11.19	243.30			1960.94	5.22	8623.06
1	2065	0.50	116.70	66.9	104	2064.90	-5.21	-8.78	-8.68	10.21	239.30	0.50	-0.38	2064.93	5.38	8519.07
2	2159	1.20	85.40	81.2	94	2158.89	-5.32	-7.43	-7.33	9.14	234.42	0.87	0.74	2158.92	5.46	8425.08
3	2253	2.00	90.00	83.9	94	2252.85	-5.24	-4.81	-4.71	7.11	222.56	0.86	0.85	2252.87	5.33	8331.13
4	2346	2.20	91.20	87.5	93	2345.79	-5.27	-1.40	-1.30	5.46	194.88	0.22	0.22	2345.80	5.30	8238.20
5	2440	1.90	102.20	90.2	94	2439.73	-5.64	1.93	2.03	5.96	161.16	0.52	-0.32	2439.72	5.60	8144.28
6	2533	1.40	106.70	92.9	93	2532.69	-6.29	4.52	4.64	7.75	144.31	0.55	-0.54	2532.68	6.21	8051.32
7	2627	1.10	127.20	94.7	94	2626.67	-7.17	6.34	6.47	9.57	138.52	0.57	-0.32	2626.65	7.05	7957.35
8	2719	0.90	137.80	97.4	92	2718.66	-8.24	7.53	7.68	11.16	137.58	0.30	-0.22	2718.63	8.09	7865.37
9	2811	1.60	108.10	101.0	92	2810.64	-9.17	9.23	9.41	13.02	134.81	1.01	0.76	2810.60	9.00	7773.40
10	2904	1.50	110.10	102.8	93	2903.60	-9.99	11.61	11.80	15.32	130.72	0.12	-0.11	2903.56	9.77	7680.44
11	2998	1.50	115.40	104.6	94	2997.57	-10.95	13.88	14.08	17.67	128.26	0.15	0.00	2997.52	10.68	7586.48
12	3092	1.60	110.40	106.4	94	3091.54	-11.93	16.22	16.44	20.13	126.34	0.18	0.11	3091.48	11.62	7492.52
13	3185	1.40	113.90	108.2	93	3184.50	-12.84	18.47	18.72	22.50	124.81	0.24	-0.22	3184.44	12.49	7399.56
14	3277	1.40	115.40	110.0	92	3276.48	-13.78	20.52	20.78	24.72	123.89	0.04	0.00	3276.40	13.39	7307.60
15	3369	2.30	105.90	113.6	92	3368.43	-14.77	23.31	23.59	27.59	122.36	1.03	0.98	3368.34	14.32	7215.66
16	3462	2.20	102.90	115.4	93	3461.36	-15.68	26.84	27.14	31.09	120.29	0.17	-0.11	3461.26	15.16	7122.74
17	3556	1.80	80.70	117.2	94	3555.30	-15.84	30.06	30.35	33.98	117.79	0.92	-0.43	3555.19	15.27	7028.81
18	3649	1.50	81.10	119.0	93	3648.26	-15.42	32.70	32.99	36.16	115.24	0.32	-0.32	3648.15	14.79	6935.85
19	3743	1.40	89.90	119.9	94	3742.23	-15.23	35.07	35.35	38.23	113.47	0.26	-0.11	3742.11	14.56	6841.89
20	3837	1.30	92.70	121.6	94	3836.20	-15.27	37.28	37.56	40.29	112.28	0.13	-0.11	3836.07	14.56	6747.93
21	3929	0.90	38.10	122.5	92	3928.19	-14.75	38.77	39.04	41.48	110.84	1.16	-0.43	3928.05	14.01	6655.95
22	4023	0.60	26.30	125.2	94	4022.18	-13.73	39.44	39.70	41.76	109.20	0.36	-0.32	4022.04	12.98	6561.96

											Target Calculations					
			TRUE	TEMP	Course				Surface	CLOSURE		DLS/	BUR/	TVD AT 0'	RIGHT(+)	ABOVE (+)
SVY	MD	INC	AZM	F	Length	TVD	N-S	E-W	Vert Sect	DIST	DIR	100	10 0'	V. SEC.	LEFT(-)	BELOW (-)
23	4116	0.50	51.30	127.0	93	4115.18	-13.04	39.97	40.22	42.05	108.07	0.28	-0.11	4115.04	12.28	6468.96
24	4209	0.40	58.00	128.0	93	4208.17	-12.62	40.57	40.80	42.48	107.28	0.12	-0.11	4208.03	11.84	6375.97
25	4303	0.30	43.90	187.2	94	4302.17	-12.27	41.02	41.24	42.81	106.65	0.14	-0.11	4302.03	11.48	6281.97
26	4397	0.20	37.00	138.7	94	4396.17	-11.96	41.28	41.50	42.98	106.15	0.11	-0.11	4396.03	11.17	6187.97
27	4490	0.10	81.50	133.3	93	4489.17	-11.82	41.46	41.68	43.11	105.91	0.16	-0.11	4489.03	11.02	6094.97
28	4584	0.10	97.80	135.1	94	4583.17	-11.81	41.62	41.84	43.27	105.85	0.03	0.00	4583.03	11.02	6000.97
29	4677	0.20	102.80	135.1	93	4676.17	-11.86	41.86	42.08	43.51	105.82	0.11	0.11	4676.02	11.06	5907.98
30	4771	0.40	189.20	136.0	94	4770.17	-12.22	41.97	42.20	43.71	106.24	0.46	0.21	4770.02	11.42	5813.98
31	4865	0.60	195.60	138.7	94	4864.17	-13.02	41.79	42.03	43.77	107.31	0.22	0.21	4864.02	12.22	5719.98
32	4958	0.90	193.80	138.7	93	4957.16	-14.20	41.48	41.74	43.84	108.89	0.32	0.32	4957.01	13.41	5626.99
33	5052	0.50	184.30	137.8	94	5051.15	-15.32	41.27	41.56	44.03	110.37	0.44	-0.43	5051.01	14.54	5532.99
34	5144	0.70	106.50	138.0	92	5143.15	-15.88	41.78	42.08	44.70	110.81	0.84	0.22	5143.00	15.09	5441.00
35	5238	0.40	99.90	140.5	94	5237.14	-16.10	42.66	42.96	45.60	110.68	0.33	-0.32	5236.99	15.29	5347.01
36	5330	0.50	115.70	144.1	92	5329.14	-16.33	43.33	43.64	46.31	110.65	0.17	0.11	5328.99	15.51	5255.01
37	5424	1.10	22.40	144.1	94	5423.13	-15.68	44.05	44.34	46.75	109.59	1.31	0.64	5422.98	14.84	5161.02
38	5518	1.10	20.50	146.0	94	5517.12	-14.00	44.71	44.97	46.85	107.38	0.04	0.00	5516.96	13.14	5067.04
39	5612	1.00	30.60	148.6	94	5611.10	-12.45	45.44	45.67	47.12	105.32	0.22	-0.11	5610.94	11.58	4973.06
40	5705	0.90	28.20	149.5	93	5704.09	-11.10	46.20	46.40	47.52	103.51	0.12	-0.11	5703.93	10.22	4880.07
41	5799	0.80	58.00	151.3	94	5798.08	-10.11	47.11	47.29	48.18	102.11	0.48	-0.11	5797.91	9.21	4786.09
42	5893	0.90	99.90	152.2	94	5892.07	-9.88	48.39	48.57	49.39	101.54	0.65	0.11	5891.90	8.96	4692.10
43	5986	1.20	132.90	153.1	93	5985.05	-10.67	49.82	50.02	50.95	102.09	0.71	0.32	5984.88	9.72	4599.12
44	6080	1.20	128.60	150.4	94	6079.03	-11.96	51.31	51.53	52.69	103.12	0.10	0.00	6078.85	10.98	4505.15
45	6174	1.60	136.60	153.1	94	6173.00	-13.52	52.98	53.23	54.68	104.32	0.47	0.43	6172.82	12.51	4411.18
46	6267	1.00	155.00	155.8	93	6265.98	-15.20	54.22	54.50	56.31	105.66	0.78	-0.65	6265.79	14.17	4318.21
47	6361	1.30	152.00	158.5	94	6359.96	-16.89	55.07	55.38	57.60	107.05	0.33	0.32	6359.77	15.84	4224.23
48	6454	1.00	130.90	160.3	93	6452.94	-18.35	56.17	56.51	59.10	108.09	0.55	-0.32	6452.75	17.28	4131.25
49	6548	1.30	119.20	160.3	94	6546.92	-19.41	57.73	58.08	60.90	108.58	0.40	0.32	6546.72	18.31	4037.28
50	6641	1.00	110.40	160.3	93	6639.91	-20.21	59.41	59.78	62.75	108.78	0.37	-0.32	6639.70	19.07	3944.30
51	6735	1.00	57.80	163.0	94	6733.89	-20.05	60.87	61.24	64.09	108.24	0.94	0.00	6733.68	18.89	3850.32
52	6827	1.20	24.30	165.7	92	6825.88	-18.75	61.95	62.29	64.72	106.84	0.72	0.22	6825.66	17.57	3758.34
53	6921	1.50	2.70	163.0	94	6919.85	-16.62	62.41	62.71	64.58	104.91	0.62	0.32	6919.63	15.43	3664.37
54	7014	1.40	2.00	164.8	93	7012.82	-14.27	62.51	62.77	64.11	102.86	0.11	-0.11	7012.60	13.08	3571.40
55	7108	1.50	358.20	166.6	94	7106.79	-11.89	62.51	62.72	63.63	100.77	0.15	0.11	7106.57	10.70	3477.43
56	7201	1.50	359.20	167.5	93	7199.76	-9.46	62.45	62.62	63.16	98.61	0.03	0.00	7199.54	8.27	3384.46
57	7295	1.40	1.70	166.6	94	7293.73	-7.08	62.47	62.59	62.87	96.47	0.13	-0.11	7293.51	5.89	3290.49
58	7388	1.30	7.70	166.6	93	7386.70	-4.90	62.64	62.73	62.83	94.47	0.19	-0.11	7386.48	3.71	3197.52
59	7482	1.30	9.20	165.7	94	7480.68	-2.79	62.96	63.00	63.02	92.54	0.04	0.00	7480.46	1.59	3103.54

										Target Calculations						
			TRUE	TEMP	Course				Surface	CLOSURE		DLS/	BUR/	TVD AT 0'	RIGHT(+)	ABOVE (+)
SVY	MD	INC	AZM	F	Length	TVD	N-S	E-W	Vert Sect	DIST	DIR	100	10 0'	V. SEC.	LEFT(-)	BELOW (-)
60	7575	1.10	358.30	167.9	93	7573.66	-0.86	63.10	63.10	90.78	0.33	-0.22	7573.44	-0.34	3010.56	
61	7669	1.10	358.50	168.4	94	7667.64	0.95	63.05	63.02	63.06	89.14	0.00	0.00	7667.42	-2.14	2916.58
62	7763	1.00	356.90	169.3	94	7761.63	2.67	62.98	62.92	63.04	87.58	0.11	-0.11	7761.41	-3.86	2822.59
63	7855	1.00	4.00	149.5	92	7853.61	4.27	62.99	62.90	63.14	86.12	0.13	0.00	7853.39	-5.47	2730.61
64	7948	0.60	325.60	171.1	93	7946.60	5.48	62.77	62.66	63.01	85.01	0.70	-0.43	7946.38	-6.67	2637.62
65	8042	0.60	336.30	173.7	94	8040.60	6.34	62.30	62.17	62.62	84.19	0.12	0.00	8040.38	-7.52	2543.62
66	8136	0.60	318.00	171.9	94	8134.59	7.15	61.77	61.62	62.18	83.39	0.20	0.00	8134.38	-8.33	2449.62
67	8229	0.60	301.70	176.4	93	8227.59	7.77	61.03	60.87	61.52	82.74	0.18	0.00	8227.38	-8.93	2356.62
68	8323	0.70	303.90	178.2	94	8321.58	8.35	60.14	59.97	60.71	82.09	0.11	0.11	8321.37	-9.49	2262.63
69	8417	0.70	303.60	180.0	94	8415.58	8.99	59.18	59.00	59.86	81.36	0.00	0.00	8415.37	-10.11	2168.63
70	8510	0.60	291.60	181.8	93	8508.57	9.48	58.26	58.06	59.02	80.76	0.18	-0.11	8508.37	-10.59	2075.63
71	8603	0.40	331.90	180.0	93	8601.57	9.95	57.65	57.45	58.50	80.21	0.42	-0.22	8601.37	-11.04	1982.63
72	8695	0.40	337.10	182.4	92	8693.56	10.53	57.37	57.16	58.33	79.60	0.04	0.00	8693.36	-11.62	1890.64
73	8789	0.30	302.40	181.8	94	8787.56	10.96	57.04	56.82	58.08	79.12	0.24	-0.11	8787.36	-12.04	1796.64
74	8883	0.30	325.00	187.2	94	8881.56	11.29	56.69	56.46	57.80	78.73	0.13	0.00	8881.36	-12.37	1702.64
75	8971	0.20	52.00		88	8969.56	11.58	56.68	56.45	57.85	78.46	0.40	-0.11	8969.36	-12.65	1614.64
76	9064	0.40	77.20		93	9062.56	11.75	57.12	56.89	58.32	78.38	0.25	0.22	9062.36	-12.83	1521.64
77	9158	0.50	84.80		94	9156.56	11.86	57.85	57.61	59.05	78.42	0.12	0.11	9156.35	-12.96	1427.65
78	9252	0.50	86.50		94	9250.55	11.92	58.67	58.43	59.87	78.51	0.02	0.00	9250.35	-13.04	1333.65
79	9345	0.40	89.40		93	9343.55	11.95	59.40	59.16	60.59	78.63	0.11	-0.11	9343.34	-13.08	1240.66
80	9439	0.30	98.30		94	9437.55	11.92	59.97	59.73	61.14	78.76	0.12	-0.11	9437.34	-13.06	1146.66
81	9533	0.30	101.40	170.2	94	9531.55	11.83	60.45	60.22	61.60	78.93	0.02	0.00	9531.34	-12.98	1052.66
82	9625	0.30	78.10	177.3	92	9623.55	11.84	60.93	60.69	62.07	79.01	0.13	0.00	9623.33	-12.99	960.67
83	9719	0.20	84.80	183.6	94	9717.54	11.90	61.33	61.09	62.47	79.02	0.11	-0.11	9717.33	-13.07	866.67
84	9812	0.30	101.40	190.8	93	9810.54	11.87	61.73	61.49	62.86	79.12	0.13	0.11	9810.33	-13.04	773.67
85	9906	0.50	91.20	193.5	94	9904.54	11.81	62.38	62.15	63.49	79.28	0.23	0.21	9904.32	-12.99	679.68
86	9985	1.00	74.50	192.6	79	9983.53	11.99	63.39	63.15	64.51	79.29	0.68	0.63	9983.31	-13.19	600.69
87	10008	1.20	72.30	176.4	23	10006.53	12.11	63.81	63.57	64.95	79.25	0.89	0.87	10006.31	-13.33	577.69
88	10101	6.40	93.00	177.3	93	10099.30	12.14	69.92	69.68	70.97	80.15	5.69	5.59	10099.05	-13.47	484.95
89	10132	12.10	89.90	180.0	31	10129.88	12.05	74.90	74.66	75.86	80.86	18.45	18.39	10129.62	-13.48	454.38
90	10163	16.70	88.10	180.9	31	10159.90	12.21	82.61	82.36	83.50	81.59	14.91	14.84	10159.61	-13.78	424.39
91	10195	19.90	90.30	180.9	32	10190.28	12.33	92.65	92.40	93.47	82.42	10.23	10.00	10189.95	-14.09	394.05
92	10226	20.10	94.80	180.9	31	10219.41	11.86	103.23	102.99	103.91	83.45	5.01	0.65	10219.05	-13.82	364.95
93	10257	21.90	103.20	180.9	31	10248.36	10.09	114.17	113.96	114.62	84.95	11.30	5.81	10247.96	-12.26	336.04
94	10288	24.30	107.30	181.8	31	10276.87	6.87	125.90	125.74	126.08	86.87	9.32	7.74	10276.43	-9.27	307.57
95	10319	28.10	105.20	181.8	31	10304.68	3.06	139.04	138.95	139.07	88.74	12.62	12.26	10304.19	-5.71	279.81
96	10350	32.00	103.60	182.0	31	10331.51	-0.79	154.07	154.06	154.07	90.29	12.84	12.58	10330.97	-2.15	253.03

										Target Calculations						
			TRUE	TEMP	Course				Surface	CLOSURE		DLS/	BUR/	TVD AT 0'	RIGHT(+)	ABOVE (+)
SVY	MD	INC	AZM	F	Length	TVD	N-S	E-W	Vert Sect	DIST	DIR	100	10 0'	V. SEC.	LEFT(-)	BELOW (-)
97	10381	36.10	102.30	185.4	31	10357.19	-4.66	170.98	171.04	171.05	91.56	13.43	13.23	10356.59	1.41	227.41
98	10413	41.60	100.30	187.2	32	10382.10	-8.58	190.66	190.79	190.86	92.58	17.63	17.19	10381.44	4.95	202.56
99	10444	45.60	97.20	187.2	31	10404.55	-11.80	211.79	211.97	212.11	93.19	14.63	12.90	10403.81	7.77	180.19
100	10475	48.00	92.70	186.3	31	10425.77	-13.74	234.29	234.51	234.69	93.36	13.11	7.74	10424.96	9.28	159.04
101	10506	51.30	87.90	185.4	31	10445.85	-13.84	257.90	258.11	258.27	93.07	15.89	10.65	10444.95	8.93	139.05
102	10538	54.90	85.50	185.4	32	10465.06	-12.35	283.44	283.62	283.71	92.49	12.75	11.25	10464.07	6.96	119.93
103	10569	57.50	86.30	186.3	31	10482.30	-10.51	309.13	309.27	309.31	91.95	8.66	8.39	10481.23	4.63	102.77
104	10600	60.30	87.30	186.3	31	10498.32	-9.03	335.63	335.74	335.75	91.54	9.44	9.03	10497.14	2.65	86.86
105	10631	61.10	88.80	186.3	31	10513.49	-8.11	362.65	362.73	362.74	91.28	4.95	2.58	10512.22	1.21	71.78
106	10662	64.30	92.30	187.2	31	10527.71	-8.39	390.18	390.27	390.27	91.23	14.39	10.32	10526.34	0.97	57.66
107	10693	68.60	95.10	188.1	31	10540.09	-10.24	418.53	418.65	418.65	91.40	16.15	13.87	10538.63	2.27	45.37
108	10724	72.20	96.60	189.0	31	10550.49	-13.22	447.57	447.75	447.77	91.69	12.48	11.61	10548.93	4.70	35.07
109	10755	75.10	97.20	189.0	31	10559.22	-16.79	477.10	477.34	477.40	92.02	9.54	9.35	10557.55	7.71	26.45
110	10787	77.30	97.70	189.9	32	10566.85	-20.82	507.91	508.22	508.34	92.35	7.04	6.88	10565.07	11.15	18.93
111	10818	80.60	96.70	189.0	31	10572.79	-24.63	538.10	538.47	538.66	92.62	11.11	10.65	10570.91	14.39	13.09
112	10849	81.30	96.00	189.0	31	10577.67	-28.02	568.52	568.95	569.21	92.82	3.17	2.26	10575.68	17.20	8.32
113	10859	81.50	95.60		10	10579.16	-29.02	578.36	578.81	579.09	92.87	4.43	2.00	10577.14	18.01	6.86
114	10933	87.00	90.90	213.3	74	10586.58	-33.17	651.82	652.33	652.66	92.91	9.75	7.43	10584.30	20.77	-0.30
115	10986	87.00	92.80	210.6	53	10589.35	-34.88	704.72	705.25	705.58	92.83	3.58	0.00	10586.89	21.47	-2.89
116	11080	88.00	91.40	210.6	94	10593.45	-38.32	798.56	799.14	799.48	92.75	1.83	1.06	10590.66	23.12	-6.66
117	11175	87.70	89.80	211.5	95	10597.02	-39.32	893.48	894.07	894.35	92.52	1.71	-0.32	10593.89	22.31	-9.89
118	11269	89.00	89.80	207.9	94	10599.72	-38.99	987.44	988.01	988.21	92.26	1.38	1.38	10596.27	20.20	-12.27
119	11363	93.40	88.60	209.7	94	10597.75	-37.68	1081.39	1081.91	1082.05	92.00	4.85	4.68	10593.98	17.10	-9.98
120	11457	93.50	88.80	214.2	94	10592.10	-35.55	1175.19	1175.66	1175.73	91.73	0.24	0.11	10587.99	13.19	-3.99
121	11551	92.70	89.50	215.1	94	10587.01	-34.16	1269.05	1269.47	1269.50	91.54	1.13	-0.85	10582.58	10.01	1.42
122	11645	91.80	89.90	216.0	94	10583.32	-33.66	1362.97	1363.36	1363.39	91.41	1.05	-0.96	10578.56	7.73	5.44
123	11740	90.30	90.90	218.7	95	10581.58	-34.33	1457.95	1458.34	1458.35	91.35	1.90	-1.58	10576.49	6.59	7.51
124	11834	89.40	90.10	220.5	94	10581.83	-35.15	1551.94	1552.33	1552.34	91.30	1.28	-0.96	10576.41	5.62	7.59
125	11924	89.70	90.70	234.8	90	10582.53	-35.78	1641.94	1642.32	1642.33	91.25	0.75	0.33	10576.80	4.54	7.20
126	12019	91.30	89.20	231.2	95	10581.71	-35.69	1736.93	1737.29	1737.29	91.18	2.31	1.68	10575.64	2.65	8.36
127	12112	92.90	89.40	292.3	93	10578.30	-34.56	1829.85	1830.18	1830.18	91.08	1.73	1.72	10571.91	-0.26	12.09
128	12206	92.60	89.80	230.3	94	10573.79	-33.90	1923.74	1924.04	1924.04	91.01	0.53	-0.32	10567.07	-2.70	16.93
129	12301	90.50	91.30	230.3	95	10571.22	-34.82	2018.70	2018.99	2019.00	90.99	2.72	-2.21	10564.17	-3.59	19.83
130	12396	89.50	92.10	233.9	95	10571.22	-37.63	2113.65	2113.99	2113.99	91.02	1.35	-1.05	10563.84	-2.58	20.16
131	12490	87.90	91.70	234.8	94	10573.35	-40.75	2207.57	2207.95	2207.95	91.06	1.75	-1.70	10565.64	-1.25	18.36
132	12586	88.80	90.80	232.1	96	10576.12	-42.84	2303.51	2303.91	2303.91	91.07	1.33	0.94	10568.07	-0.98	15.93

										Target Calculations						
			TRUE	TEMP	Course				Surface	CLOSURE		DLS/	BUR/	TVD AT 0'	RIGHT(+)	ABOVE (+)
SVY	MD	INC	AZM	F	Length	TVD	N-S	E-W	Vert Sect	DIST	DIR	100	10 0'	V. SEC.	LEFT(-)	BELOW (-)
133	12682	89.40	90.30	235.7	96	10577.62	-43.76	2399.49	2399.89	2399.89	91.04	0.81	0.63	10569.25	-1.89	14.75
134	12775	91.30	90.80	237.5	93	10577.06	-44.66	2492.48	2492.88	2492.88	91.03	2.11	2.04	10568.35	-2.77	15.65
135	12870	89.80	90.80	235.7	95	10576.14	-45.98	2587.47	2587.87	2587.87	91.02	1.58	-1.58	10567.11	-3.25	16.89
136	12963	90.40	92.00	238.4	93	10575.98	-48.25	2680.44	2680.87	2680.87	91.03	1.44	0.65	10566.62	-2.74	17.38
137	13057	92.30	92.40	240.2	94	10573.77	-51.86	2774.34	2774.82	2774.82	91.07	2.07	2.02	10564.08	-0.92	19.92
138	13152	90.90	91.30	239.3	95	10571.11	-54.93	2869.25	2869.77	2869.77	91.10	1.87	-1.47	10561.10	0.34	22.90
139	13246	90.10	91.30	241.1	94	10570.29	-57.06	2963.22	2963.77	2963.77	91.10	0.85	-0.85	10559.95	0.68	24.05
140	13340	90.70	91.30	242.0	94	10569.64	-59.19	3057.19	3057.76	3057.76	91.11	0.64	0.64	10558.96	1.02	25.04
141	13435	90.10	92.10	241.1	95	10568.97	-62.01	3152.14	3152.75	3152.75	91.13	1.05	-0.63	10557.97	2.04	26.03
142	13530	87.60	91.20	242.0	95	10570.88	-64.75	3247.08	3247.72	3247.72	91.14	2.80	-2.63	10559.54	2.96	24.46
143	13623	87.00	91.70	242.9	93	10575.26	-67.10	3339.94	3340.62	3340.62	91.15	0.84	-0.65	10563.60	3.55	20.40
144	13718	88.50	92.80	242.0	95	10578.99	-70.82	3434.79	3435.52	3435.52	91.18	1.96	1.58	10567.00	5.47	17.00
145	13812	88.60	92.70	243.8	94	10581.37	-75.33	3528.65	3529.45	3529.46	91.22	0.15	0.11	10569.05	8.19	14.95
146	13907	89.90	92.70	240.7	95	10582.61	-79.81	3623.54	3624.40	3624.42	91.26	1.37	1.37	10569.96	10.86	14.04
147	14001	87.60	92.80	245.6	94	10584.66	-84.31	3717.40	3718.33	3718.36	91.30	2.45	-2.45	10571.68	13.58	12.32
148	14095	86.50	91.50	241.1	94	10589.50	-87.84	3811.21	3812.19	3812.22	91.32	1.81	-1.17	10576.19	15.32	7.81
149	14190	88.80	90.30	241.1	95	10593.40	-89.33	3906.11	3907.10	3907.13	91.31	2.73	2.42	10579.76	15.01	4.24
150	14285	90.60	89.10	242.0	95	10593.89	-88.83	4001.10	4002.07	4002.09	91.27	2.28	1.89	10579.92	12.70	4.08
151	14379	90.90	89.20	242.0	94	10592.66	-87.44	4095.08	4096.00	4096.01	91.22	0.34	0.32	10578.37	9.52	5.63
152	14474	91.90	88.50	244.7	95	10590.34	-85.53	4190.03	4190.90	4190.91	91.17	1.28	1.05	10575.71	5.81	8.29
153	14568	91.60	87.70	245.6	94	10587.47	-82.41	4283.94	4284.73	4284.73	91.10	0.91	-0.32	10572.52	0.91	11.48
154	14662	91.50	87.60	132.0	94	10584.93	-78.56	4377.82	4378.52	4378.53	91.03	0.15	-0.11	10569.65	-4.73	14.35
155	14756	91.10	86.50	248.3	94	10582.80	-73.72	4471.67	4472.27	4472.28	90.94	1.24	-0.43	10567.19	-11.35	16.81
156	14851	90.80	86.90	245.6	95	10581.22	-68.26	4566.50	4566.97	4567.01	90.86	0.53	-0.32	10565.28	-18.62	18.72
157	14945	92.70	89.00	244.7	94	10578.35	-64.90	4660.39	4660.78	4660.84	90.80	3.01	2.02	10562.08	-23.77	21.92
158	15039	91.40	90.20	248.3	94	10574.99	-64.24	4754.32	4754.68	4754.76	90.77	1.88	-1.38	10558.39	-26.21	25.61
159	15133	90.00	90.00	244.7	94	10573.84	-64.40	4848.31	4848.66	4848.74	90.76	1.50	-1.49	10556.91	-27.84	27.09
160	15228	92.50	91.00	243.8	95	10571.77	-65.23	4943.28	4943.62	4943.71	90.76	2.83	2.63	10554.51	-28.81	29.49
161	15322	94.30	92.90	247.4	94	10566.19	-68.42	5037.05	5037.44	5037.51	90.78	2.78	1.91	10548.61	-27.41	35.39
162	15417	93.40	91.90	245.6	95	10559.81	-72.39	5131.75	5132.20	5132.26	90.81	1.41	-0.95	10541.90	-25.24	42.10
163	15511	88.00	90.90	246.5	94	10558.67	-74.69	5225.68	5226.15	5226.21	90.82	5.84	-5.74	10540.42	-24.73	43.58
164	15605	88.30	91.30	248.3	94	10561.70	-76.49	5319.61	5320.10	5320.16	90.82	0.53	0.32	10543.13	-24.72	40.87
165	15700	89.50	90.90	247.4	95	10563.52	-78.31	5414.57	5415.08	5415.14	90.83	1.33	1.26	10544.62	-24.70	39.38
166	15794	90.30	88.70	247.4	94	10563.69	-77.99	5508.57	5509.05	5509.12	90.81	2.49	0.85	10544.46	-26.82	39.54
167	15888	90.80	91.00	250.1	94	10562.79	-77.74	5602.56	5603.02	5603.10	90.79	2.50	0.53	10543.23	-28.85	40.77
168	15982	88.90	90.50	251.9	94	10563.03	-78.97	5696.54	5697.01	5697.09	90.79	2.09	-2.02	10543.15	-29.41	40.85



JOB NO.: DDMT-130258
Company: Continental Resources
LOCATION: Williston, ND
RIG NAME: Cyclone 2
STATE: North Dakota
COUNTY: Country
WELL NAME: Atlanta 14-6H

FIELD: Atlanta
Township: 155N
Range: 97W

MOTOR INFORMATION	
Desc: 4 3/4 5/6 5.4; 1.125rpg	
Bent Hsg/Sub:	1.83 / 0
Bit to Bend:	6
Pad OD:	.25
NB Stab:	

Slide Report for all BHA's in Job: DDMT-130258

Note: Surveys listed are interpolated from the actual surveys

#	Date	Drill Mode	Start Time	End Time	Hours	Start MD	End MD	Depth Drilled	WOB	ROP	RPM	Surf. Torque	Flow Rate	SPP	TFO	INC	AZM	DLS	Note
1	9-Apr	Drilling	14:50	15:24	0.57	2005	2115	110	15	194.1	100	3000	590	2900		0.00	0.00	0.00	
1	9-Apr	Sliding	15:35	16:00	0.42	2115	2130	15	8	36.0	0	0	590	2900	90	0.50	116.70	0.00	
1	9-Apr	Drilling	16:00	16:12	0.20	2130	2209	79	15	395.0	100	3000	590	2900		0.00	0.00	0.00	
1	9-Apr	Sliding	16:24	16:32	0.13	2209	2222	13	8	97.5	0	590	2900	2900	90	0.00	0.00	0.00	
1	9-Apr	Drilling	16:32	16:46	0.23	2222	2303	81	15	347.1	100	3000	590	2900		0.00	0.00	0.00	
1	9-Apr	Drilling	16:51	17:02	0.18	2303	2396	93	15	507.3	100	3000	590	2900		0.00	0.00	0.00	
1	9-Apr	Drilling	17:08	17:20	0.20	2396	2490	94	15	470.0	100	3000	590	2900		0.00	0.00	0.00	
1	9-Apr	Drilling	17:26	17:45	0.32	2490	2583	93	15	293.7	100	3000	590	2900		0.00	0.00	0.00	
1	9-Apr	Drilling	18:00	18:13	0.22	2583	2769	186	15	858.5	100	3000	590	2900		0.00	0.00	0.00	
1	9-Apr	Sliding	18:20	18:35	0.25	2769	2788	19	8	76.0	100	3000	590	2900	90	0.00	0.00	0.00	
1	9-Apr	Drilling	18:35	20:00	1.42	2788	3327	539	15	380.5	100	3000	590	2900		0.00	0.00	0.00	
1	9-Apr	Sliding	20:30	20:40	0.17	3327	3345	18	8	108.0	0	0	590	2900	70	0.00	0.00	0.00	
1	9-Apr	Drilling	20:40	21:00	0.33	3345	3521	176	15	528.0	100	3000	590	2900		0.00	0.00	0.00	
1	9-Apr	Sliding	21:15	21:30	0.25	3521	3535	14	12	56.0	0	0	590	3000		0.00	0.00	0.00	
1	9-Apr	Drilling	21:30	22:15	0.75	3535	3892	357	30	476.0	100	7500	590	3500		0.00	0.00	0.00	
1	9-Apr	Sliding	22:45	23:00	0.25	3892	3908	16	12	64.0	0	0	590	3000	300	0.00	0.00	0.00	
1	9-Apr	Drilling	23:00	23:30	0.50	3908	4230	322	15	644.0	100	7500	590	3500		0.00	0.00	0.00	
1	10-Apr	Drilling	00:00	02:00	2.00	4230	5010	780	25	390.0	100	7500	590	3500		0.00	0.00	0.00	
1	10-Apr	Sliding	02:45	03:00	0.25	5010	5026	16	10	64.0	0	0	590	3000	300	0.00	0.00	0.00	
1	10-Apr	Drilling	03:00	03:30	0.50	5026	5198	172	25	344.0	100	7500	590	3500		0.00	0.00	0.00	
1	10-Apr	Sliding	03:30	03:45	0.25	5198	5216	18	10	72.0	100	7500	590	3000	300	0.00	0.00	0.00	
1	10-Apr	Drilling	03:45	04:15	0.50	5216	5385	169	25	338.0	75	7500	590	3350		0.00	0.00	0.00	
1	10-Apr	Sliding	04:45	05:00	0.25	5385	5412	27	15	108.0	0	0	590	3000	300	0.00	0.00	0.00	
1	10-Apr	Drilling	05:00	08:10	3.17	5412	6036	624	25	197.1	50	6000	590	3000		0.00	0.00	0.00	
1	10-Apr	Sliding	08:10	08:20	0.17	6036	6046	10	15	60.0	0	0	590	3000	340	0.00	0.00	0.00	
1	10-Apr	Drilling	08:20	09:16	0.93	6046	6224	178	25	190.7	50	6000	590	3000		0.00	0.00	0.00	

Slide Report for all BHA's in Job: DDMT-130258																		Note: Surveys listed are interpolated from the actual surveys			
#	Date	Drill Mode	Start Time	End Time	Hours	Start MD	End MD	Depth Drilled	WOB	ROP	RPM	Surf. Torque	Flow Rate	SPP	TFO	INC	AZM	DLS	Note		
1	10-Apr	Sliding	09:16	09:38	0.37	6224	6242	18	15	49.1	50	0	590	3000	310	0.00	0.00	0.00			
1	10-Apr	Drilling	09:38	10:10	0.53	6242	6317	75	25	140.6	50	6000	590	3000		0.00	0.00	0.00			
1	10-Apr	Sliding	10:10	10:38	0.47	6317	6337	20	15	42.9	0	0	590	3000	10	0.00	0.00	0.00			
1	10-Apr	Drilling	10:38	11:10	0.53	6337	6411	74	25	138.8	50	6000	590	3000		0.00	0.00	0.00			
1	10-Apr	Sliding	11:10	11:35	0.42	6411	6435	24	15	57.6	50	6000	590	3000	10	0.00	0.00	0.00			
1	10-Apr	Drilling	11:35	12:05	0.50	6435	6504	69	25	138.0	50	6000	590	3000		0.00	0.00	0.00			
1	10-Apr	Sliding	12:05	12:35	0.50	6504	6514	10	18	20.0	0	6000	590	3000	10	0.00	0.00	0.00			
1	10-Apr	Drilling	12:35	13:00	0.42	6514	6598	84	18	201.6	50	6000	490	3100	10	0.00	0.00	0.00			
1	10-Apr	Sliding	13:00	13:30	0.50	6598	6614	16	18	32.0	0	6000	490	2900	350	0.00	0.00	0.00			
1	10-Apr	Drilling	13:30	14:10	0.67	6614	6666	52	25	78.0	50	6000	490	3100		0.00	0.00	0.00			
1	10-Apr	Sliding	14:10	15:05	0.92	6666	6701	35	18	38.2	50	6000	490	2900	350	0.00	0.00	0.00			
1	10-Apr	Drilling	15:05	15:50	0.75	6701	6785	84	25	112.0	50	6000	490	3100		0.00	0.00	0.00			
1	10-Apr	Sliding	15:50	16:10	0.33	6785	6805	20	10	60.0	0	0	490	2900	350	0.00	0.00	0.00			
1	10-Apr	Drilling	16:10	16:35	0.42	6805	6877	72	25	172.8	50	6000	490	3100		0.00	0.00	0.00			
1	10-Apr	Drilling	17:35	23:00	5.42	6877	7595	718	25	132.6	50	6000	490	3100		0.00	0.00	0.00			
1	11-Apr	Drilling	00:00	02:00	2.00	7595	7907	312	25	156.0	50	6000	490	3200		0.00	0.00	0.00			
1	11-Apr	Sliding	02:45	03:00	0.25	7907	7925	18	17	72.0	0	0	490	3000	240	0.00	0.00	0.00			
1	11-Apr	Drilling	03:00	15:05	12.08	7925	8745	820	25	67.9	50	6000	490	3200		0.00	0.00	0.00			
1	11-Apr	Drilling	15:15	17:05	1.83	8745	8839	94	35	51.3	50	6000	490	3200		0.00	0.00	0.00			
1	11-Apr	Drilling	17:25	20:30	3.08	8839	9081	242	35	78.5	50	6000	490	3200		0.00	0.00	0.00			
1	11-Apr	Drilling	22:00	23:30	1.50	9081	9205	124	35	82.7	50	6000	490	3200		0.00	0.00	0.00			
1	12-Apr	Drilling	00:00	05:00	5.00	9205	9523	318	38	63.6	60	6000	490	3200		0.00	0.00	0.00			
2	12-Apr	Drilling	17:45	23:15	5.50	9523	9898	375	38	68.2	60	6000	490	3200		0.00	0.00	0.00			
2	13-Apr	Drilling	00:00	02:00	2.00	9898	10040	142	38	71.0	60	6000	490	3200		0.00	0.00	0.00			
3	13-Apr	Drilling	13:20	14:00	0.67	10040	10073	33	20	49.5	30	6000	490	3300		0.00	0.00	0.00			
3	13-Apr	Sliding	14:00	17:00	3.00	10073	10197	124	35	41.3	0	0	490	3400	90	0.00	0.00	0.00			
3	13-Apr	Drilling	17:00	17:35	0.58	10197	10228	31	20	53.1	30	0	490	3400		0.00	0.00	0.00			
3	13-Apr	Sliding	17:35	18:30	0.92	10228	10260	32	35	34.9	0	0	490	3400	45 R	0.00	0.00	0.00			
3	13-Apr	Sliding	18:40	19:40	1.00	10260	10291	31	35	31.0	0	0	490	3400	45 R	0.00	0.00	0.00			
3	13-Apr	Sliding	19:45	20:10	0.42	10291	10296	5	35	12.0	0	0	490	3400	30 L	0.00	0.00	0.00			
3	13-Apr	Drilling	20:10	20:15	0.08	10296	10301	5	30	60.0	30	0	490	3400		0.00	0.00	0.00			
3	13-Apr	Sliding	20:15	20:20	0.08	10301	10302	1	40	12.0	0	0	490	3400	30 L	0.00	0.00	0.00			
3	13-Apr	Sliding	20:30	23:15	2.75	10302	10352	50	40	18.2	0	0	490	3400	45 L	0.00	0.00	0.00			
3	13-Apr	Sliding	23:30	24:00	0.50	10352	10368	16	40	32.0	0	0	490	3400	30 L	0.00	0.00	0.00			

Slide Report for all BHA's in Job: DDMT-130258

Note: Surveys listed are interpolated from the actual surveys

#	Date	Drill Mode	Start Time	End Time	Hours	Start MD	End MD	Depth Drilled	WOB	ROP	RPM	Surf. Torque	Flow Rate	SPP	TFO	INC	AZM	DLS	Note
3	14-Apr	Sliding	00:00	01:10	1.17	10368	10446	78	40	66.9	0	0	490	3400	45 L	0.00	0.00	0.00	
3	14-Apr	Sliding	01:30	03:00	1.50	10446	10541	95	40	63.3	0	0	490	3400	45 L	0.00	0.00	0.00	
3	14-Apr	Drilling	03:45	04:00	0.25	10541	10560	19	30	76.0	30	0	490	3400		0.00	0.00	0.00	
3	14-Apr	Sliding	04:00	04:15	0.25	10560	10573	13	40	52.0	30	0	490	3400	45 L	0.00	0.00	0.00	
3	14-Apr	Drilling	04:30	04:45	0.25	10573	10582	9	30	36.0	30	0	490	3400		0.00	0.00	0.00	
3	14-Apr	Sliding	04:45	05:45	1.00	10582	10605	23	40	23.0	30	0	490	3400	45 R	0.00	0.00	0.00	
3	14-Apr	Drilling	05:45	06:20	0.58	10605	10634	29	30	49.7	30	0	490	3400		0.00	0.00	0.00	
3	14-Apr	Sliding	06:20	08:40	2.33	10634	10727	93	40	39.9	30	0	490	3400	45 R	0.00	0.00	0.00	
3	14-Apr	Drilling	08:40	08:55	0.25	10727	10742	15	30	60.0	30	0	490	3400		0.00	0.00	0.00	
3	14-Apr	Sliding	08:55	09:15	0.33	10742	10758	16	40	48.0	30	0	490	3400	10 R	0.00	0.00	0.00	
3	14-Apr	Drilling	09:15	09:45	0.50	10758	10789	31	30	62.0	30	0	490	3400		0.00	0.00	0.00	
3	14-Apr	Sliding	09:45	11:00	1.25	10789	10820	31	40	24.8	30	0	490	3400	40L	0.00	0.00	0.00	
3	14-Apr	Drilling	11:00	12:10	1.17	10820	10883	63	30	54.0	30	0	490	3400		0.00	0.00	0.00	
3	14-Apr	Sliding	12:10	14:35	2.42	10883	10924	41	40	17.0	0	0	490	3400	20L	0.00	0.00	0.00	
4	17-Apr	Drilling	10:20	10:45	0.42	10924	10963	39	15	93.6	75	5	285	3400		0.00	0.00	0.00	
4	17-Apr	Drilling	10:50	11:10	0.33	10963	11005	42	15	126.0	75	5	285	3400		0.00	0.00	0.00	
4	17-Apr	Sliding	11:10	11:35	0.42	11005	11020	15	20	36.0	0	5	490	3400	20L	0.00	0.00	0.00	
4	17-Apr	Drilling	11:35	12:00	0.42	11020	11058	38	15	91.2	75	5	285	3400		0.00	0.00	0.00	
4	17-Apr	Sliding	12:10	12:45	0.58	11058	11080	22	20	37.7	75	5	490	3400	70L	0.00	0.00	0.00	
4	17-Apr	Drilling	12:45	13:25	0.67	11080	11152	72	15	108.0	75	5	285	3400		0.00	0.00	0.00	
4	17-Apr	Sliding	13:35	14:00	0.42	11152	11175	23	18	55.2	0	5	285	3400	30L	0.00	0.00	0.00	
4	17-Apr	Drilling	14:00	14:45	0.75	11175	11247	72	18	96.0	75	5	285	3400		0.00	0.00	0.00	
4	17-Apr	Sliding	14:55	16:00	1.08	11247	11292	45	18	41.5	75	5	285	3400		0.00	0.00	0.00	
4	17-Apr	Drilling	16:00	16:15	0.25	11292	11312	20	18	80.0	75	5	285	3400		0.00	0.00	0.00	
4	17-Apr	Sliding	16:30	17:20	0.83	11312	11341	29	25	34.8	0	0	285	3400		0.00	0.00	0.00	
4	17-Apr	Drilling	17:30	18:00	0.50	11341	11385	44	18	88.0	75	5000	285	3350		0.00	0.00	0.00	
4	17-Apr	Sliding	18:00	18:20	0.33	11385	11395	10	25	30.0	0	0	285	2850		0.00	0.00	0.00	
4	17-Apr	Drilling	18:20	19:45	1.42	11395	11545	150	18	105.9	75	5000	285	3350		0.00	0.00	0.00	
4	17-Apr	Sliding	20:00	20:30	0.50	11545	11563	18	35	36.0	0	0	285	2850	150 R	0.00	0.00	0.00	
4	17-Apr	Drilling	20:30	21:45	1.25	11563	11653	90	18	72.0	75	5000	285	3350		0.00	0.00	0.00	
4	17-Apr	Sliding	21:45	22:15	0.50	11653	11671	18	35	36.0	0	0	285	2800	150 R	0.00	0.00	0.00	
4	17-Apr	Drilling	22:15	23:30	1.25	11671	11817	146	20	116.8	75	5000	285	3350		0.00	0.00	0.00	
4	18-Apr	Drilling	00:00	01:30	1.50	11817	11930	113	20	75.3	75	5000	285	3350		0.00	0.00	0.00	
4	18-Apr	Sliding	01:30	02:30	1.00	11930	11950	20	25	20.0	0	0	285	3350	30 R	0.00	0.00	0.00	

Slide Report for all BHA's in Job: DDMT-130258															Note: Surveys listed are interpolated from the actual surveys					
#	Date	Drill Mode	Start Time	End Time	Hours	Start MD	End MD	Depth Drilled	WOB	ROP	RPM	Surf. Torque	Flow Rate	SPP	TFO	INC	AZM	DLS	Note	
4	18-Apr	Drilling	02:30	03:30	1.00	11950	11977	27	20	27.0	75	5000	285	3350		0.00	0.00	0.00		
5	18-Apr	Drilling	15:35	15:45	0.17	11977	11983	6	15	36.0	75	5000	285	3350		0.00	0.00	0.00		
5	18-Apr	Drilling	16:20	17:20	1.00	11983	12078	95	15	95.0	60	5000	285	3350		0.00	0.00	0.00		
5	18-Apr	Drilling	17:30	18:15	0.75	12078	12171	93	15	124.0	60	5000	285	3350		0.00	0.00	0.00		
5	18-Apr	Drilling	18:45	19:15	0.50	12171	12203	32	15	64.0	60	5000	285	3350		0.00	0.00	0.00		
5	18-Apr	Sliding	19:15	19:45	0.50	12203	12218	15	20	30.0	0	0	285	2800	150 R	0.00	0.00	0.00		
5	18-Apr	Drilling	19:45	20:45	1.00	12218	12297	79	15	79.0	60	5000	285	3350		0.00	0.00	0.00		
5	18-Apr	Sliding	20:45	21:15	0.50	12297	12312	15	20	30.0	0	0	285	2800	120 R	0.00	0.00	0.00		
5	18-Apr	Drilling	21:15	22:15	1.00	12312	12455	143	15	143.0	60	5000	285	3350		0.00	0.00	0.00		
5	18-Apr	Drilling	22:30	23:30	1.00	12455	12567	112	15	112.0	60	5000	285	3350		0.00	0.00	0.00		
5	18-Apr	Sliding	23:45	24:00	0.25	12567	12570	3	25	12.0	0	0	285	2800	0 G	0.00	0.00	0.00		
5	19-Apr	Sliding	00:20	00:50	0.50	12570	12582	12	25	24.0	0	0	285	2350	0 G	0.00	0.00	0.00		
5	19-Apr	Drilling	00:50	03:30	2.67	12582	12867	285	15	106.9	60	6300	285	2850		0.00	0.00	0.00		
5	19-Apr	Sliding	04:00	04:20	0.33	12867	12882	15	25	45.0	0	0	285	2350	170 R	0.00	0.00	0.00		
5	19-Apr	Drilling	04:20	06:30	2.17	12882	13116	234	15	108.0	60	6300	275	2850		0.00	0.00	0.00		
5	19-Apr	Sliding	06:35	07:10	0.58	13116	13125	9	25	15.4	0	0	285	2850	160L	0.00	0.00	0.00		
5	19-Apr	Drilling	07:10	08:00	0.83	13125	13211	86	15	103.2	60	6300	275	2850		0.00	0.00	0.00		
5	19-Apr	Drilling	08:10	08:45	0.58	13211	13305	94	15	161.1	60	6300	275	2850		0.00	0.00	0.00		
5	19-Apr	Drilling	08:50	09:30	0.67	13305	13399	94	15	141.0	60	6300	275	2850		0.00	0.00	0.00		
5	19-Apr	Drilling	09:40	09:45	0.08	13399	13405	6	15	72.0	60	6300	275	2850		0.00	0.00	0.00		
5	19-Apr	Sliding	09:45	10:10	0.42	13405	13415	10	25	24.0	60	6300	285	2850	150R	0.00	0.00	0.00		
5	19-Apr	Drilling	10:10	10:45	0.58	13415	13494	79	25	135.4	60	6300	285	2850	150R	0.00	0.00	0.00		
5	19-Apr	Drilling	10:55	11:10	0.25	13494	13510	16	20	64.0	60	6300	285	2850		0.00	0.00	0.00		
5	19-Apr	Sliding	11:10	11:30	0.33	13510	13518	8	25	24.0	0	6300	285	2850	170R	0.00	0.00	0.00		
5	19-Apr	Drilling	11:30	12:00	0.50	13518	13589	71	20	142.0	60	7300	285	2850		0.00	0.00	0.00		
5	19-Apr	Drilling	12:10	12:55	0.75	13589	13682	93	20	124.0	60	7300	285	2850		0.00	0.00	0.00		
5	19-Apr	Drilling	13:00	13:10	0.17	13682	13690	8	20	48.0	60	7300	285	2850		0.00	0.00	0.00		
5	19-Apr	Sliding	13:10	13:55	0.75	13690	13705	15	25	20.0	60	7300	285	2850	30R	0.00	0.00	0.00		
5	19-Apr	Drilling	13:55	14:30	0.58	13705	13777	72	25	123.4	60	7300	285	2850	30R	0.00	0.00	0.00		
5	19-Apr	Drilling	14:40	15:30	0.83	13777	13871	94	25	112.8	60	7300	285	2850		0.00	0.00	0.00		
5	19-Apr	Drilling	15:40	15:45	0.08	13871	13880	9	25	108.0	60	7300	285	2850		0.00	0.00	0.00		
5	19-Apr	Sliding	15:45	16:20	0.58	13880	13892	12	50	20.6	0	0	285	2850	30L	0.00	0.00	0.00		
5	19-Apr	Drilling	16:20	17:00	0.67	13892	13966	74	15	111.0	60	7300	285	2850		0.00	0.00	0.00		
5	19-Apr	Drilling	17:30	19:00	1.50	13966	14093	127	15	84.7	60	7300	265	3000		0.00	0.00	0.00		

Slide Report for all BHA's in Job: DDMT-130258

Note: Surveys listed are interpolated from the actual surveys

#	Date	Drill Mode	Start Time	End Time	Hours	Start MD	End MD	Depth Drilled	WOB	ROP	RPM	Surf. Torque	Flow Rate	SPP	TFO	INC	AZM	DLS	Note
5	19-Apr	Sliding	19:15	19:45	0.50	14093	14105	12	50	24.0	0	0	265	2400	30L	0.00	0.00	0.00	
5	19-Apr	Sliding	20:00	20:20	0.33	14105	14112	7	50	21.0	0	0	265	2400	30L	0.00	0.00	0.00	
5	19-Apr	Sliding	20:35	21:00	0.42	14112	14122	10	50	24.0	0	0	255	2300	30L	0.00	0.00	0.00	
5	19-Apr	Drilling	21:00	21:50	0.83	14122	14189	67	15	80.4	60	7300	265	2850		0.00	0.00	0.00	
5	19-Apr	Sliding	22:05	23:30	1.42	14189	14216	27	45	19.1	0	0	255	2350	0 G	0.00	0.00	0.00	
5	19-Apr	Drilling	23:30	24:00	0.50	14216	14249	33	15	66.0	60	7500	265	2350		0.00	0.00	0.00	
5	20-Apr	Drilling	00:00	00:20	0.33	14249	14275	26	15	78.0	62	6000	262	3000		0.00	0.00	0.00	
5	20-Apr	Sliding	00:40	01:30	0.83	14275	14290	15	35	18.0	0	0	250	2300	25R	0.00	0.00	0.00	
5	20-Apr	Drilling	01:30	02:30	1.00	14290	14375	85	15	85.0	62	6100	262	3000		0.00	0.00	0.00	
5	20-Apr	Sliding	02:30	03:15	0.75	14375	14390	15	38	20.0	0	0	250	2330	15R	0.00	0.00	0.00	
5	20-Apr	Drilling	03:15	03:45	0.50	14390	14438	48	15	96.0	62	6100	262	3000		90.90	89.20	0.34	
5	20-Apr	Drilling	04:15	05:00	0.75	14438	14533	95	13	126.7	62	6100	262	3130		91.90	88.50	1.28	
5	20-Apr	Drilling	05:30	07:30	2.00	14533	14852	319	13	159.5	62	6100	262	3120		0.00	0.00	0.00	
5	20-Apr	Sliding	08:00	09:00	1.00	14852	14878	26	38	26.0	0	0	250	2300	70 R	0.00	0.00	0.00	
5	20-Apr	Drilling	09:00	10:00	1.00	14878	14948	70	13	70.0	62	6100	262	3100		0.00	0.00	0.00	
5	20-Apr	Sliding	10:20	11:15	0.92	14948	14965	17	38	18.5	0	0	250	2300	80 R	0.00	0.00	0.00	
5	20-Apr	Drilling	11:15	12:45	1.50	14965	15137	172	15	114.7	62	6100	262	3100		0.00	0.00	0.00	
5	20-Apr	Sliding	13:00	14:30	1.50	15137	15167	30	38	20.0	0	0	250	2300	20 R	0.00	0.00	0.00	
5	20-Apr	Drilling	14:30	15:15	0.75	15167	15228	61	15	81.3	62	6100	262	3100		0.00	0.00	0.00	
5	20-Apr	Sliding	15:15	16:30	1.25	15228	15253	25	38	20.0	0	0	250	2350	60 R	0.00	0.00	0.00	
5	20-Apr	Drilling	16:30	17:00	0.50	15253	15286	33	15	66.0	62	6100	262	3100		0.00	0.00	0.00	
5	20-Apr	Drilling	17:30	18:30	1.00	15286	15396	110	17	110.0	62	7800	262	3175		0.00	0.00	0.00	
5	20-Apr	Sliding	18:30	19:15	0.75	15396	15411	15	60	20.0	0	0	250	2420	150L	0.00	0.00	0.00	
5	20-Apr	Drilling	19:15	19:40	0.42	15411	15430	19	18	45.6	62	7800	262	3175		0.00	0.00	0.00	
5	20-Apr	Sliding	19:40	20:35	0.92	15430	15445	15	40	16.4	0	0	250	2320	150L	0.00	0.00	0.00	
5	20-Apr	Drilling	20:35	21:15	0.67	15445	15491	46	18	69.0	62	7600	262	3180		0.00	0.00	0.00	
5	20-Apr	Sliding	21:15	22:05	0.83	15491	15511	20	38	24.0	0	0	262	2670	180	0.00	0.00	0.00	
5	20-Apr	Drilling	22:05	22:45	0.67	15511	15570	59	18	88.5	62	7600	262	3180		0.00	0.00	0.00	
5	20-Apr	Drilling	23:20	23:30	0.17	15570	15588	18	18	108.0	62	7600	262	3180		0.00	0.00	0.00	
5	20-Apr	Sliding	23:30	23:45	0.25	15588	15598	10	40	40.0	0	0	250	2400	10R	0.00	0.00	0.00	
5	20-Apr	Drilling	23:45	24:00	0.25	15598	15632	34	18	136.0	62	7000	262	3175		0.00	0.00	0.00	
5	21-Apr	Drilling	00:00	00:30	0.50	15632	15680	48	16	96.0	62	7000	262	3175		0.00	0.00	0.00	
5	21-Apr	Sliding	00:30	01:15	0.75	15680	15692	12	40	16.0	0	0	250	2370	10L	0.00	0.00	0.00	
5	21-Apr	Drilling	01:15	01:20	0.08	15692	15695	3	14	36.0	62	7000	262	3300		0.00	0.00	0.00	

Slide Report for all BHA's in Job: DDMT-130258

Note: Surveys listed are interpolated from the actual surveys

#	Date	Drill Mode	Start Time	End Time	Hours	Start MD	End MD	Depth Drilled	WOB	ROP	RPM	Surf. Torque	Flow Rate	SPP	TFO	INC	AZM	DLS	Note
5	21-Apr	Drilling	01:50	03:05	1.25	15695	15790	95	14	76.0	62	7000	262	3200		0.00	0.00	0.00	
5	21-Apr	Sliding	03:05	03:45	0.67	15790	15802	12	65	18.0	0	0	250	2300	10R	0.00	0.00	0.00	
5	21-Apr	Drilling	03:45	04:30	0.75	15802	15853	51	14	68.0	55	820	262	3220		0.00	0.00	0.00	
5	21-Apr	Drilling	05:00	06:30	1.50	15853	16065	212	14	141.3	55	8200	262	3200		0.00	0.00	0.00	
5	21-Apr	Sliding	07:00	07:30	0.50	16065	16077	12	65	24.0	0	0	250	2400	45 R	0.00	0.00	0.00	
5	21-Apr	Sliding	07:50	08:30	0.67	16077	16090	13	45	19.5	0	0	250	2400	45 R	0.00	0.00	0.00	
5	21-Apr	Drilling	08:30	09:00	0.50	16090	16136	46	14	92.0	55	8200	262	3200		0.00	0.00	0.00	
5	21-Apr	Drilling	09:15	13:15	4.00	16136	16627	491	14	122.8	55	8200	262	3200		0.00	0.00	0.00	
5	21-Apr	Sliding	14:15	15:15	1.00	16627	16642	15	57	15.0	0	0	250	2375	30 R	0.00	0.00	0.00	
5	21-Apr	Drilling	15:15	15:45	0.50	16642	16698	56	14	112.0	55	8200	262	3200		0.00	0.00	0.00	
5	21-Apr	Drilling	16:15	17:30	1.25	16698	16813	115	18	92.0	55	8200	262	3200		0.00	0.00	0.00	
5	21-Apr	Sliding	17:45	18:25	0.67	16813	16838	25	62	37.5	0	0	250	2220	170R	0.00	0.00	0.00	
5	21-Apr	Drilling	18:25	20:30	2.08	16838	17000	162	17	77.8	45	6200	262	3040		0.00	0.00	0.00	
5	21-Apr	Sliding	20:30	21:15	0.75	17000	17012	12	75	16.0	0	0	250	2300	5R	0.00	0.00	0.00	
5	21-Apr	Drilling	21:15	21:30	0.25	17012	17030	18	15	72.0	45	6200	262	3000		0.00	0.00	0.00	
5	21-Apr	Sliding	21:30	22:05	0.58	17030	17040	10	75	17.1	0	0	250	2320	10L	0.00	0.00	0.00	
5	21-Apr	Drilling	22:05	24:00	1.92	17040	17199	159	15	83.0	47	5400	250	3130		0.00	0.00	0.00	
5	22-Apr	Drilling	00:00	00:40	0.67	17199	17264	65	15	97.5	47	5400	262	3130		0.00	0.00	0.00	
5	22-Apr	Drilling	01:00	04:00	3.00	17264	17547	283	15	94.3	47	5400	262	3130		0.00	0.00	0.00	
5	22-Apr	Drilling	04:20	07:30	3.17	17547	17848	301	15	95.1	47	5400	262	3130		0.00	0.00	0.00	
5	22-Apr	Sliding	08:00	08:35	0.58	17848	17868	20	53	34.3	0	0	250	2350	20 R	0.00	0.00	0.00	
5	22-Apr	Sliding	08:45	09:00	0.25	17868	17878	10	53	40.0	0	0	250	2350	30 R	0.00	0.00	0.00	
5	22-Apr	Drilling	09:00	12:15	3.25	17878	18133	255	15	78.5	47	8500	262	3130		0.00	0.00	0.00	
5	22-Apr	Sliding	12:45	13:30	0.75	18133	18145	12	60	16.0	0	0	250	2350	150 R	0.00	0.00	0.00	
5	22-Apr	Drilling	13:30	16:30	3.00	18145	18422	277	15	92.3	47	8500	262	3130		0.00	0.00	0.00	
5	22-Apr	Sliding	17:00	17:45	0.75	18422	18436	14	75	18.7	0	0	250	2350	160 R	0.00	0.00	0.00	
5	22-Apr	Drilling	17:45	20:00	2.25	18436	18600	164	18	72.9	46	7000	262	3200		0.00	0.00	0.00	
5	22-Apr	Sliding	20:00	20:25	0.42	18600	18608	8	35	19.2	0	0	250	2400	25L	0.00	0.00	0.00	
5	22-Apr	Drilling	20:25	21:30	1.08	18608	18677	69	18	63.7	46	7000	262	3200		0.00	0.00	0.00	
5	22-Apr	Drilling	21:50	22:00	0.17	18677	18690	13	18	78.0	46	7000	262	3200		0.00	0.00	0.00	
5	22-Apr	Sliding	22:00	22:30	0.50	18690	18705	15	75	30.0	0	0	250	2380	10L	0.00	0.00	0.00	
5	22-Apr	Drilling	22:30	24:00	1.50	18705	18802	97	15	64.7	46	6700	262	3285		0.00	0.00	0.00	
5	23-Apr	Sliding	00:00	01:00	1.00	18802	18820	18	40	18.0	0	0	250	2525		0.00	0.00	0.00	
5	23-Apr	Drilling	01:00	01:25	0.42	18820	18865	45	15	108.0	46	7000	262	3220		0.00	0.00	0.00	

Slide Report for all BHA's in Job: DDMT-130258

Note: Surveys listed are interpolated from the actual surveys

#	Date	Drill Mode	Start Time	End Time	Hours	Start MD	End MD	Depth Drilled	WOB	ROP	RPM	Surf. Torque	Flow Rate	SPP	TFO	INC	AZM	DLS	Note
5	23-Apr	Drilling	01:55	02:00	0.08	18865	18880	15	17	180.0	47	6900	262	3250		0.00	0.00	0.00	
5	23-Apr	Sliding	02:00	02:45	0.75	18880	18895	15	75	20.0	0	0	250	2530	20R	0.00	0.00	0.00	
5	23-Apr	Drilling	02:45	03:45	1.00	18895	18959	64	18	64.0	45	7000	262	3250		0.00	0.00	0.00	
5	23-Apr	Drilling	04:05	04:15	0.17	18959	18975	16	16	96.0	45	10000	262	3200		0.00	0.00	0.00	
5	23-Apr	Sliding	04:15	04:55	0.67	18975	18985	10	85	15.0	0	0	250	2340		0.00	0.00	0.00	
5	23-Apr	Drilling	04:55	07:00	2.08	18985	19085	100	16	48.0	45	0	262	2340		0.00	0.00	0.00	
Total Drilled:				17080	Avg. Total ROP:				87.16	DEPTH% - TIME %									
Total Rotary Drilled:				15313	Avg. Rotary ROP:				111.30	Percent Rotary: 89.65 - 70.21									
Total Drilled Sliding:				1767	Avg. Slide ROP:				30.27	Percent Slide: 10.35 - 29.79									



Scale 1:240 (5"=100') Imperial
Measured Depth Log

Well Name: Atlanta 14-6H (Atlanta 14 Well Eco Pad)
Location: NENW Sec 6 - T153N - R101W - Williams Co., ND
License Number: 33-105-02719 Region: Williston
Spud Date: 03/05/13 Drilling Completed: 04/14/13
Surface Coordinates: NENW Sec 6 - T153N - R101W - Williams Co., ND
495' FNL & 1485' FWL
Bottom Hole NENW Sec 6 - T153N - R101W - Williams Co., ND
Coordinates: Casing Point: 10924' MD; 10586' TVD, 528' FNL & 2128' FWL
Ground Elevation (ft): 1945' K.B. Elevation (ft): 1967'
Logged Interval (ft): 9700' To: 10586' Total Depth (ft): 886'
Formation: MCyn, Lodgp, UBkkn SH, MBkkn, LBkkn SH, ThrFks
Type of Drilling Fluid: Invert

Printed by MUD.LOG from WellSight Systems 1-800-447-1534 www.WellSight.com

CORE

Contractor:
Core #:
Formation:
Core Interval: From: Cut:
To: Recovered:
Bit type:
Size:
Coring Time:

OPERATOR

Company: Continental Resources, Inc.
Address: 20 N. Broadway
P.O. Box 269000
Oklahoma City, Ok 73126

GEOLOGIST

Name: Jed D Nelson
Company: Geo-Link Inc
Address: PO Box 1764
Red Lodge, MT 59068

Directional:

ROCK TYPES


	Anhy		Clyst		Gyp		Mrslst		Shgy
	Bent		Coal		Igne		Salt		Sltst
	Brec		Congl		Lmst		Shale		Ss
	Cht		Dol		Meta		Shcol		Till


ACCESSORIES


MINERAL	Gyp	FOSSIL	Ostra	TEXTURE

OTHER SYMBOLS


POROSITY TYPE	Vuggy	ROUNDING	Spotted	EVENTS
SORTING	Well	Subrnd	Ques	
Moderate	Moderate	Subang	Dead	
Poor	Poor	Angular		
OIL SHOWS	Even			

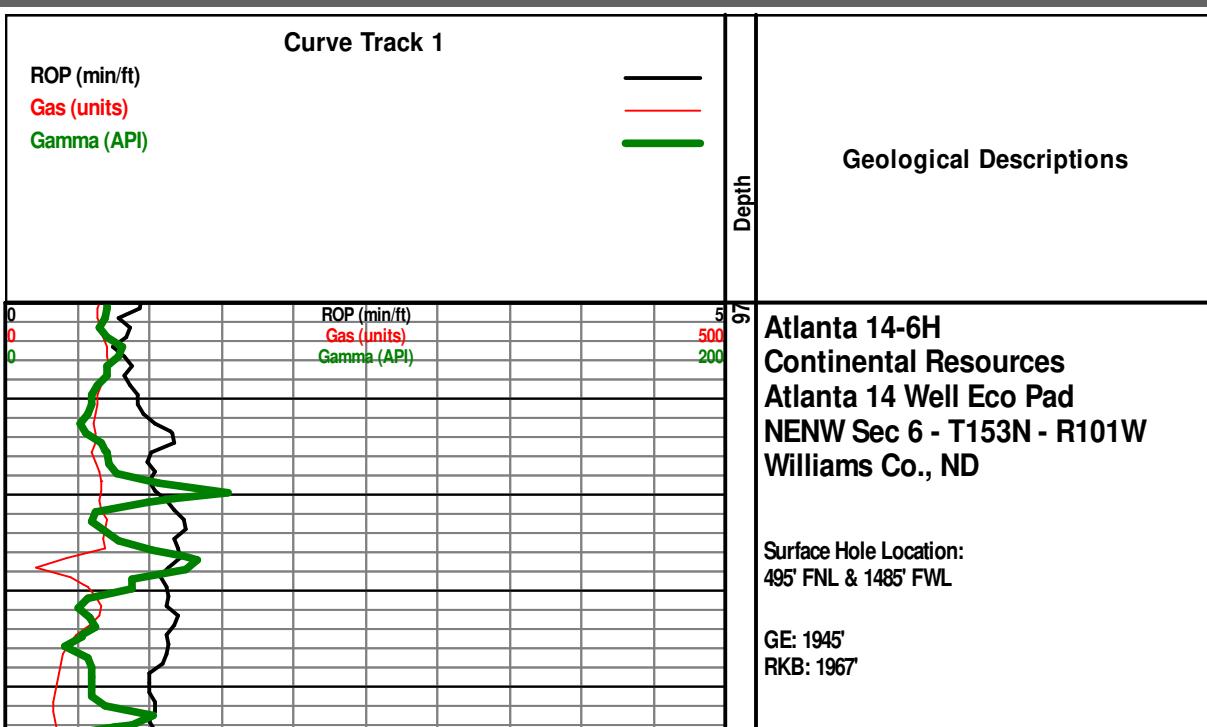


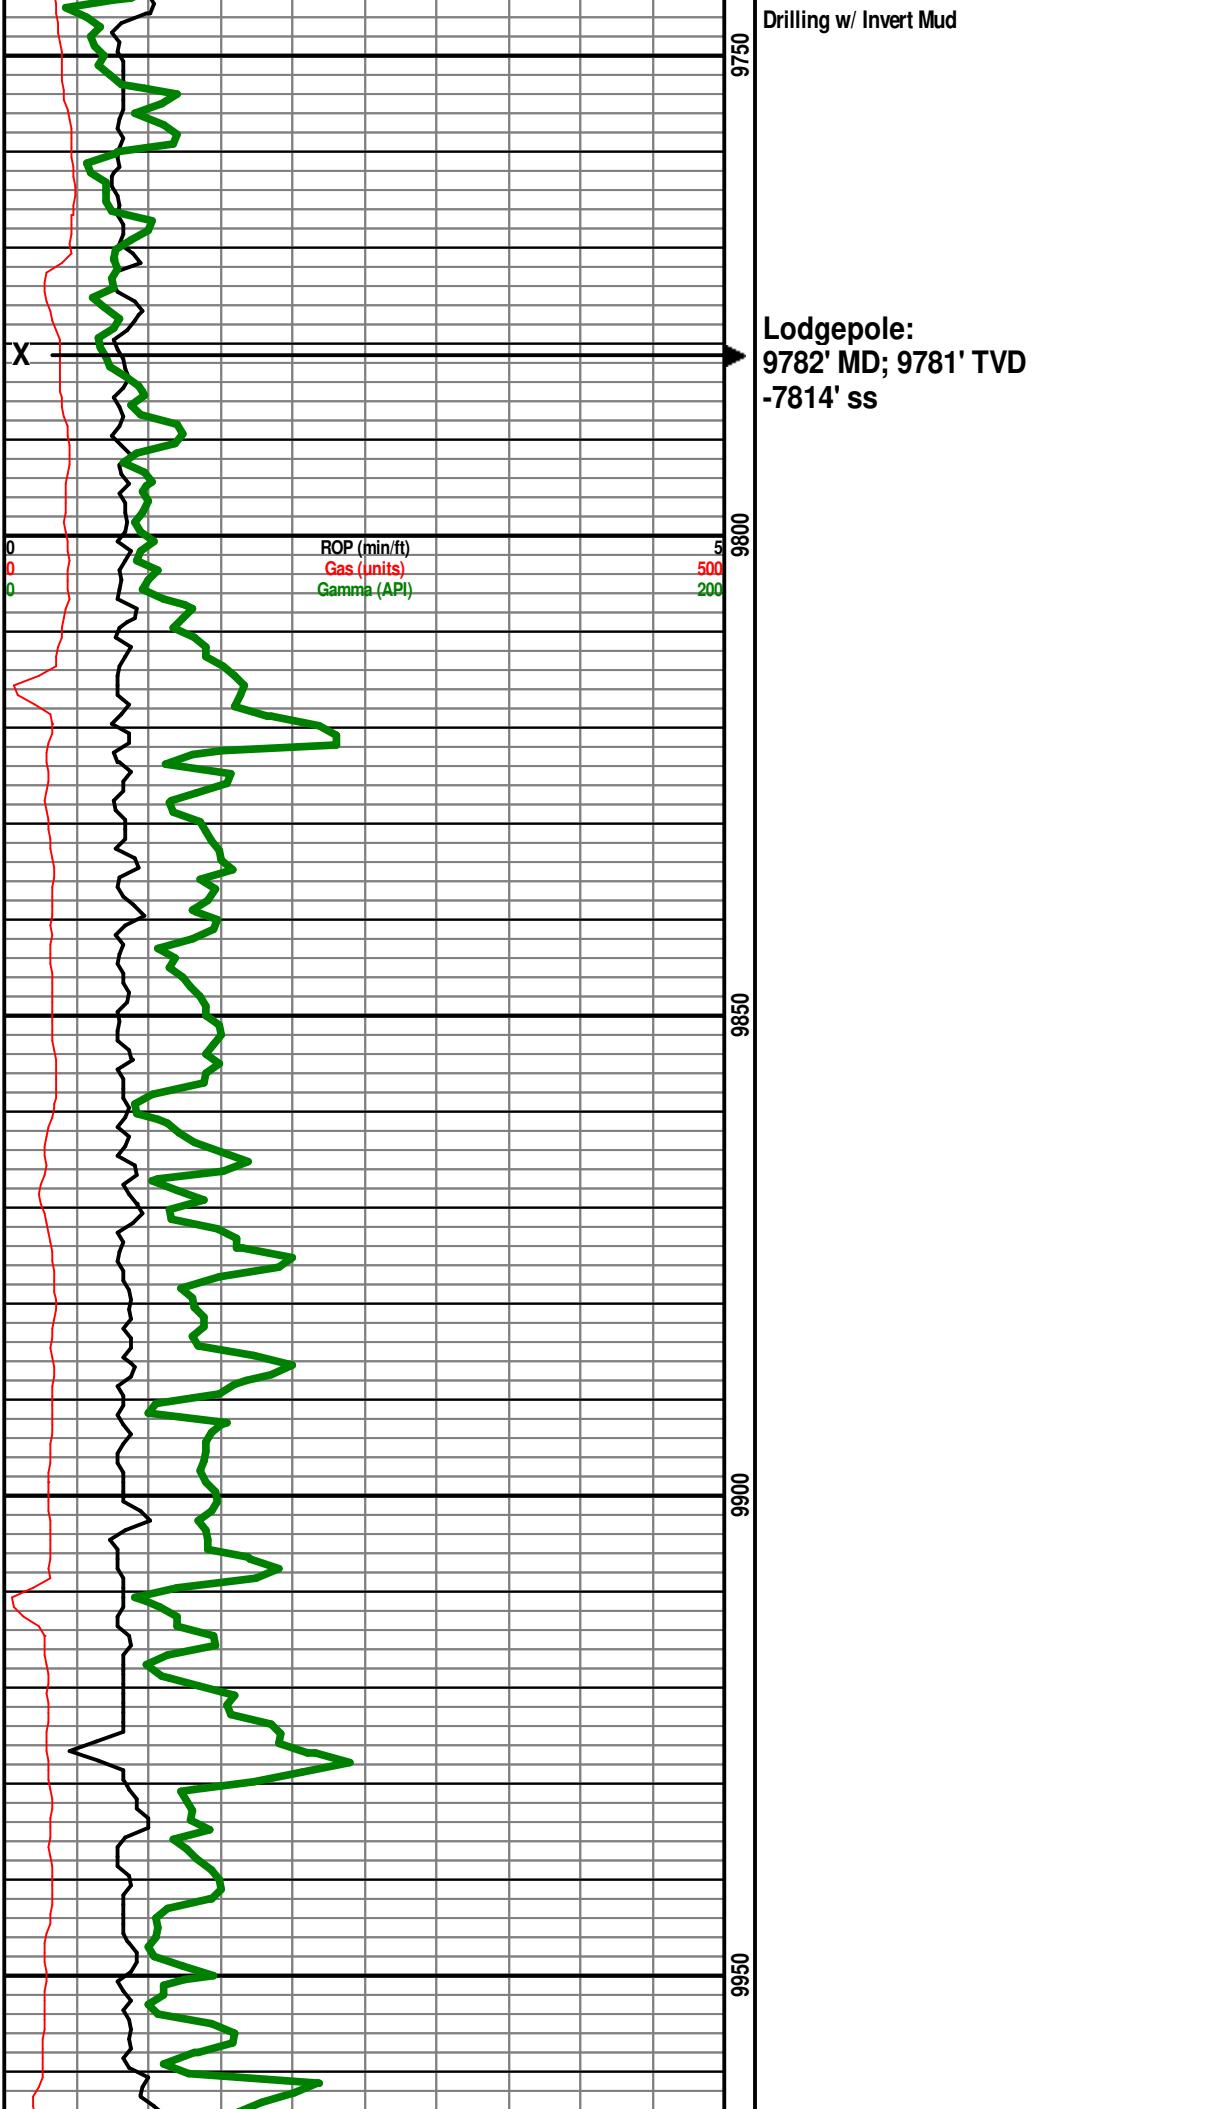

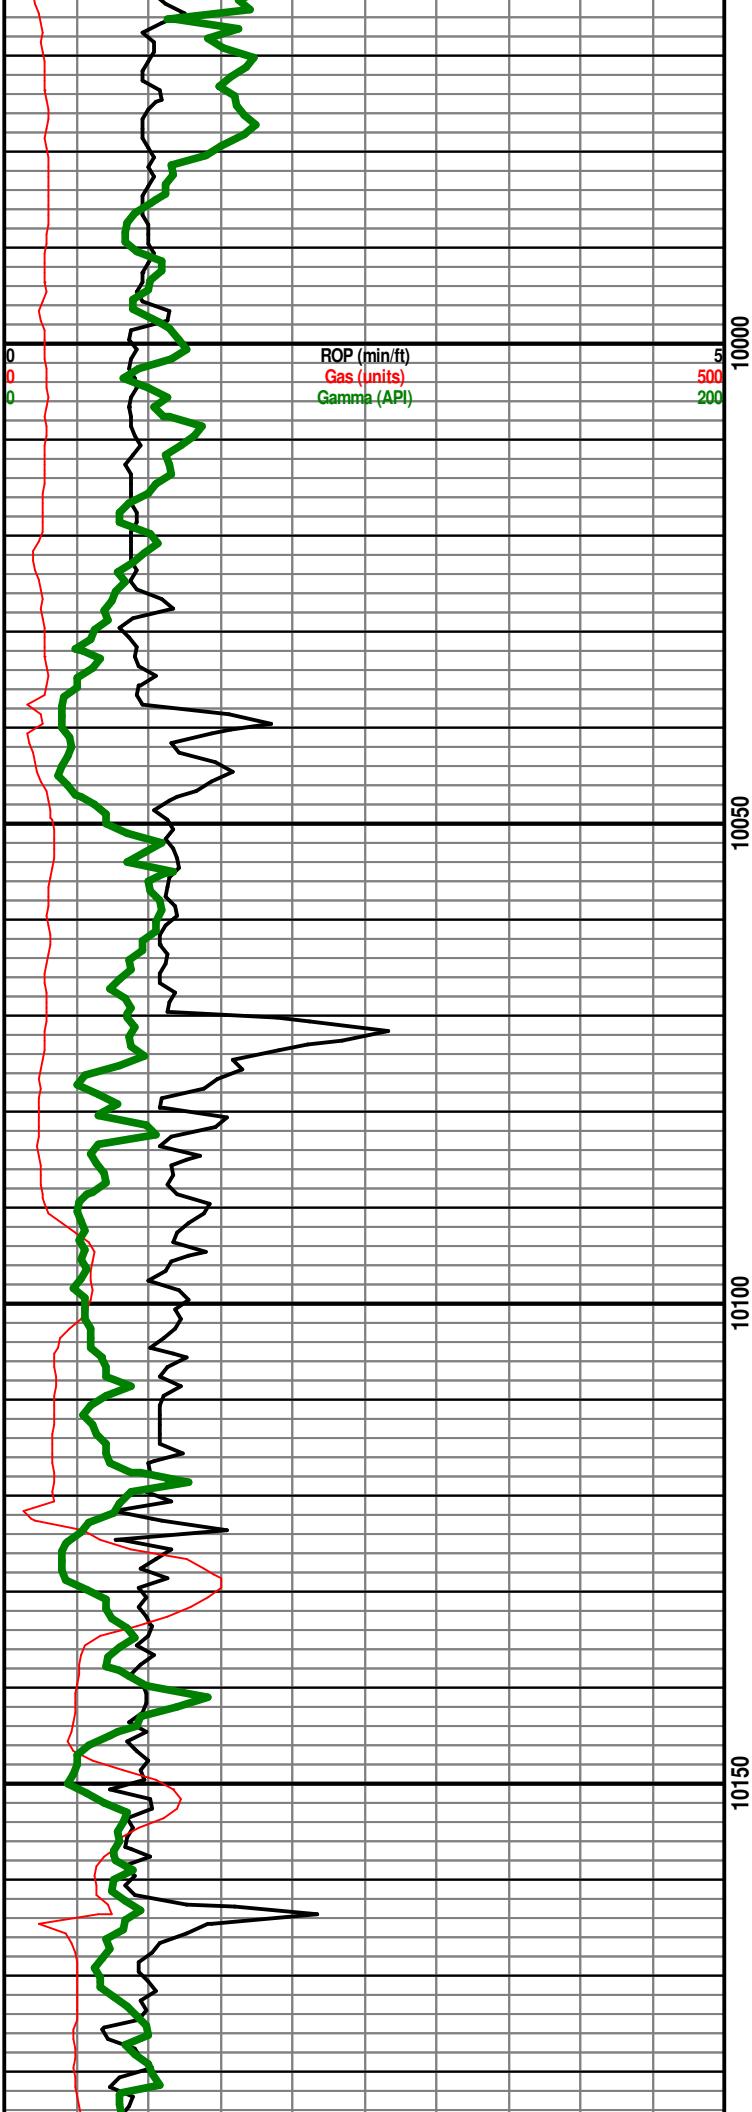

TOOH: Pick up Build Assembly @ 10040' MD;
10039' TVD - 4/13/13 - 02:20
Resume Drilling 4/13/13 - 13:20

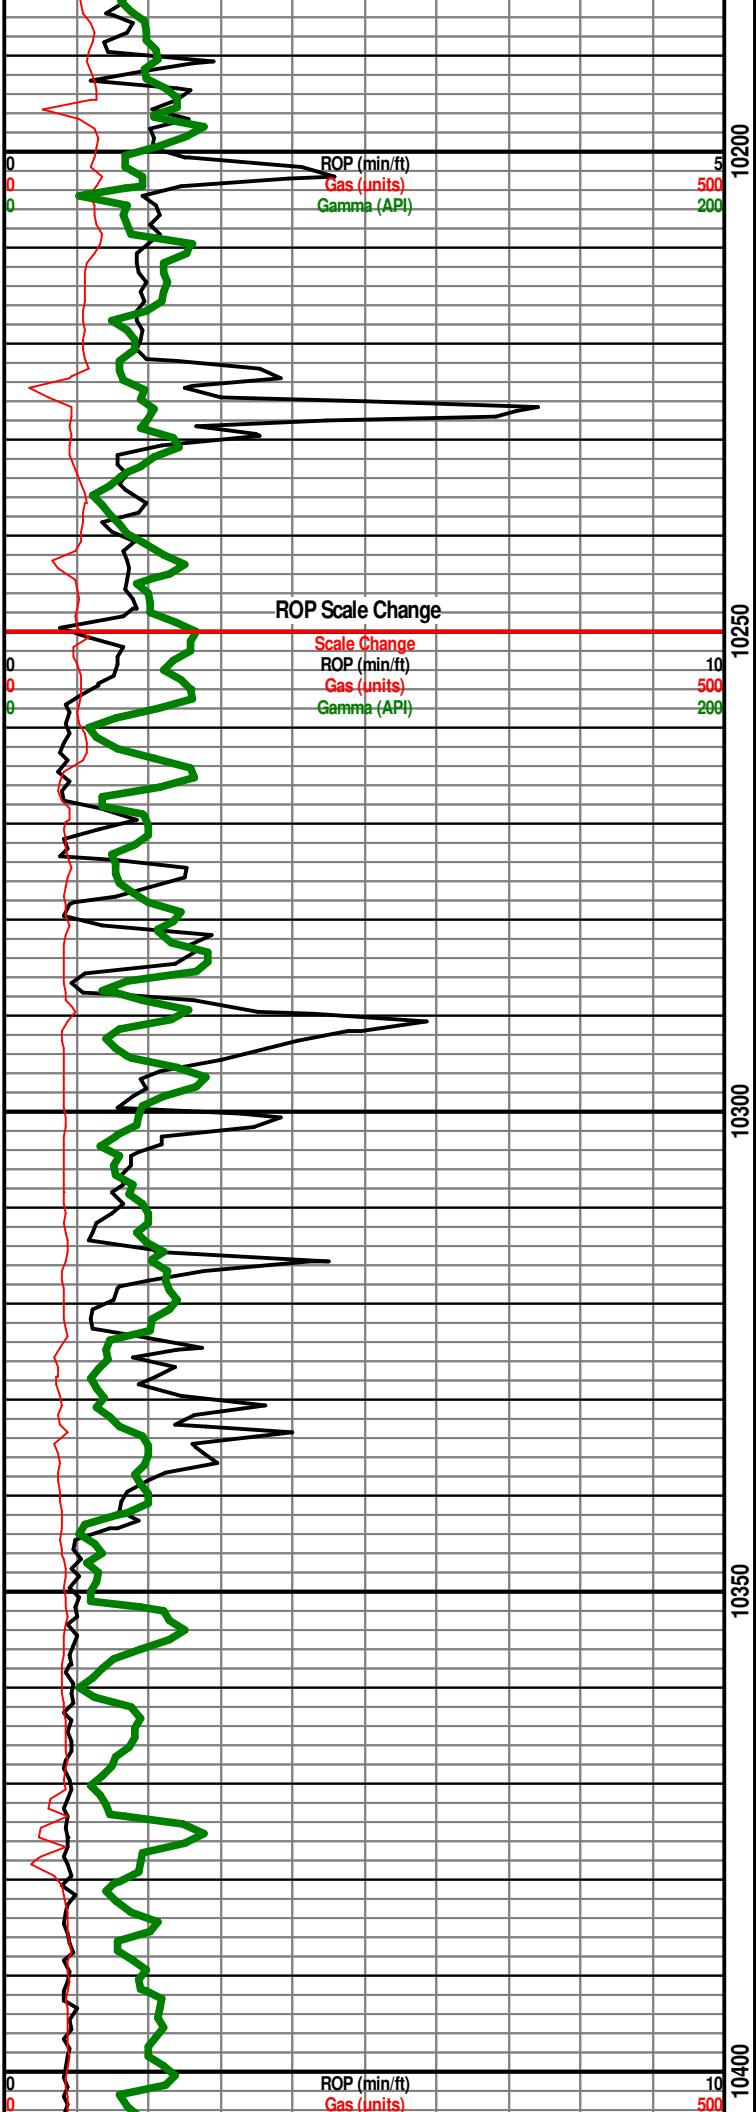

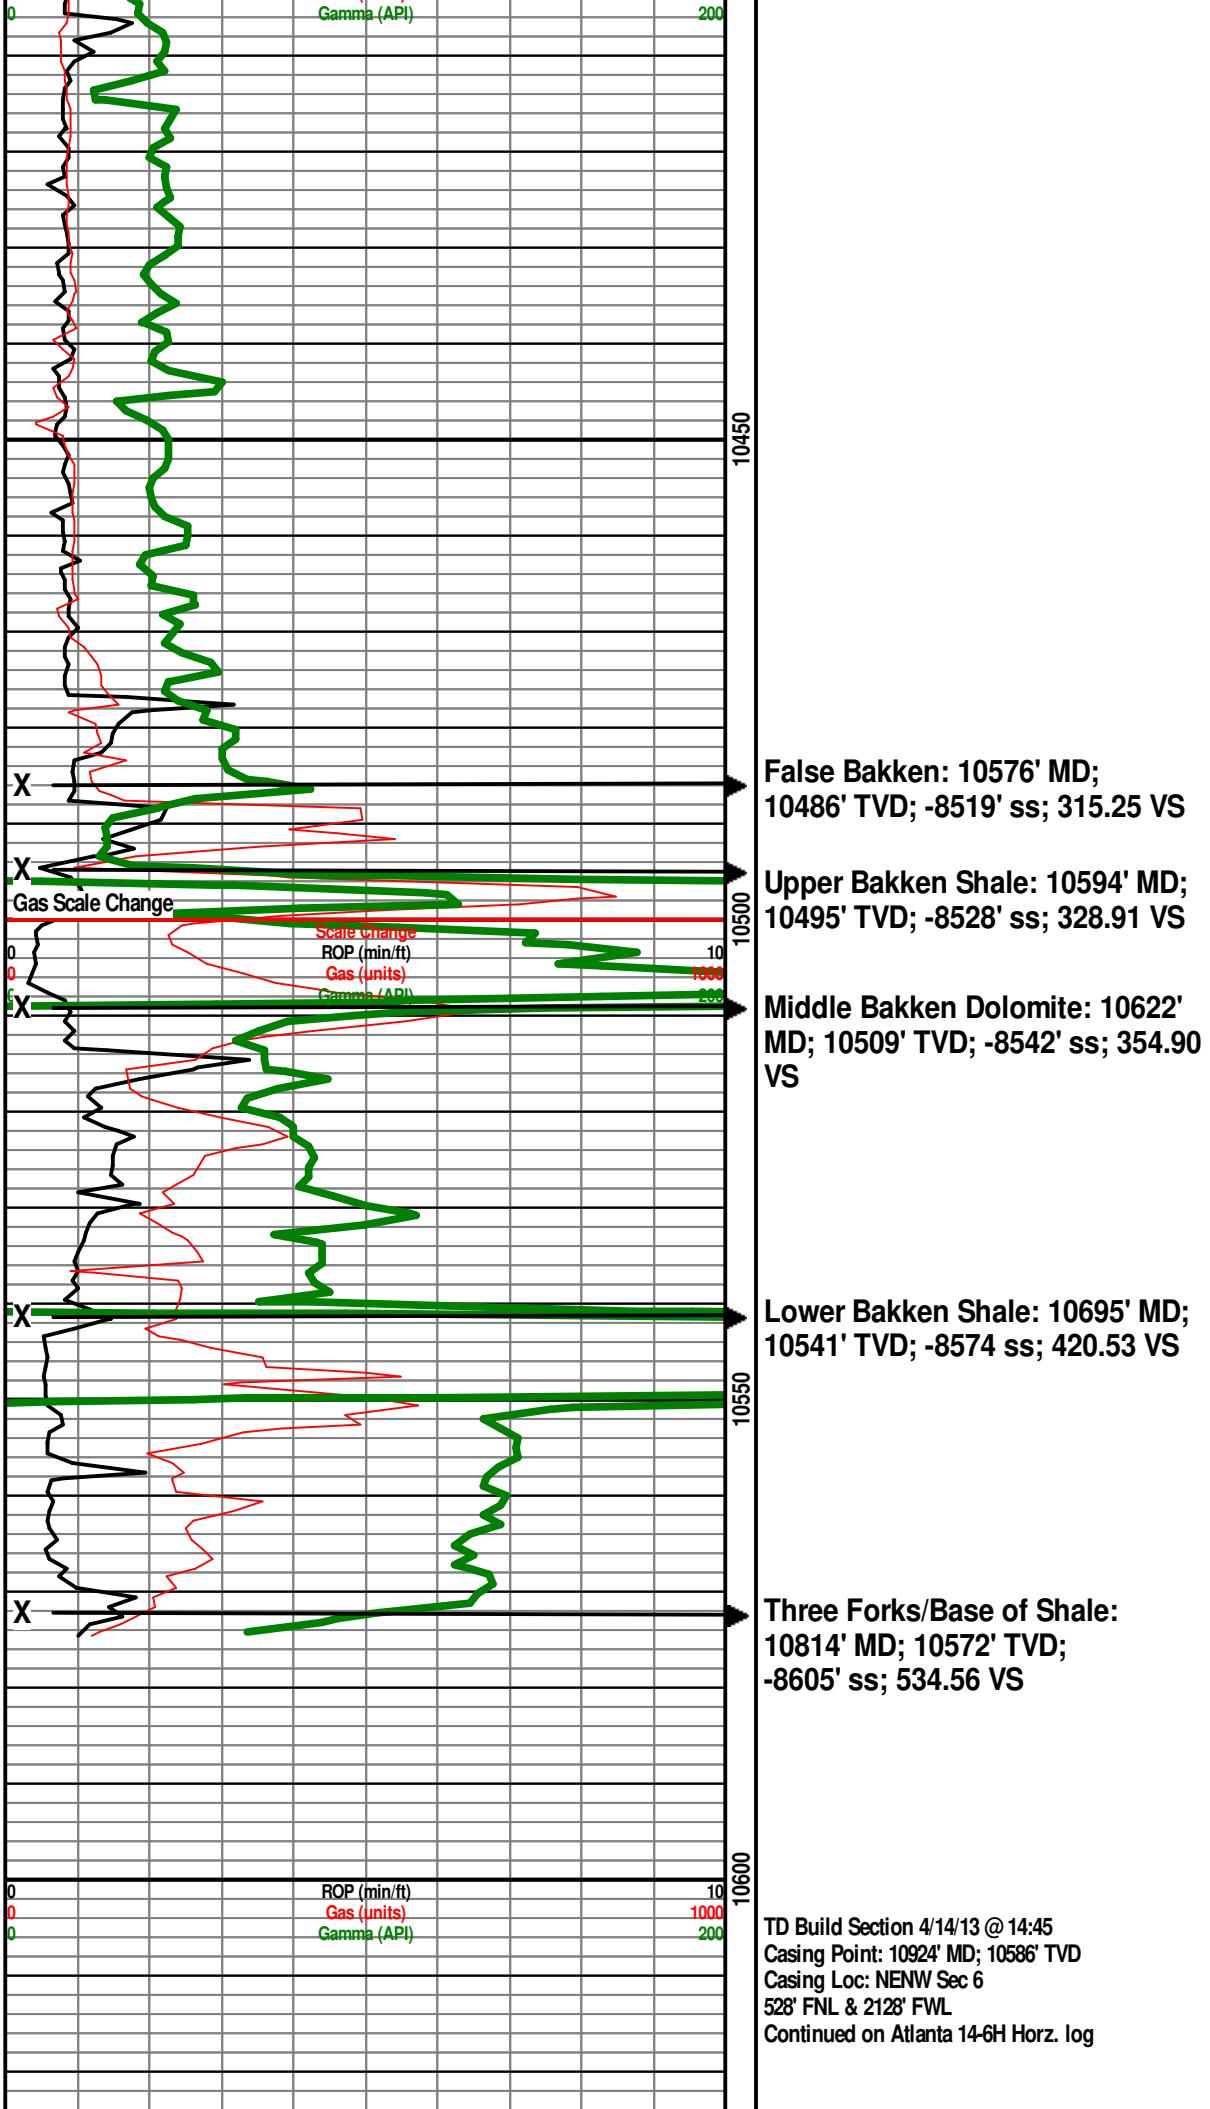

Field Geologist: Jed D Nelson
Second Hand: R.C. Whitmore

Thank You For Using Geo-Link Inc.

NEWSCO

International Energy Services Inc.

Continental Resources
Company

33144
Job Number

3/11/2013
Date

Cyclone 2
Rig

Atlanta 14-6H
Well Name

Williams Co., ND
County & State

Surveyed from depth of: Surface to 1961'

GL to KB: 22'


Type of Survey: Nvader

True North

Directional Supervisor/Surveyor: David Hopper

The data and calculations for this survey have been checked by me and conform to the standards and procedures set forth by Newsco International Energy Services Inc. This report represents a true and correct directional survey of this well based on the original data obtained at the well site. Wellbore

Certified by:



Joshua Mahoney

NEWSCO

Directional Services U.S.A.

CLIENT: Continental Resources
DATE: 3-11-2013
STATE: North Dakota
FIELD: Williams Co.

NEWSCO JOB #33144

WELL NAME: Atlanta 14-6H

RIG: 2

CONTRACTOR: Cyclone

TIE-ON DATA

C/L (10,30,100):	100.00	Feet
MEASURED DEPTH:	0.00	Feet
TVD:	0.00	Feet
INCLINATION:	0.00	Deg.
AZIMUTH:	0.00	Deg.
N(+) S(-):	0.00	Feet
E(+) W(-):	0.00	Feet
VISECTION PLANE:	0.00	Deg.
VISECTION :	0.00	Feet

TARGET DATA

SENSOR TO BIT:	54.00
KB TO GL :	22.00
Total:	54.00
TVD:	0.00
INC:	0.00
VS:	0.00

0.00



7821 Will Rogers Blvd.
Fort Worth, Texas 76140

817.568.1038 (office)
817.568.1499 (fax)
www.msenergyservices.com

May 2, 2013

North Dakota Mineral Resources
Survey Certification Sheet

Company: Continental Resources, Inc.

Lease: Atlanta 14

Well Number: 6H

Location: Williams County, ND

Job Number: DDMT-130258

Well API# 33-105-02719

Attached please find the original surveys performed on the above referenced well by MS Energy Services. The data is true, correct, complete and within the limitations of the tool as set forth by MS Energy Services. I am authorized and qualified to make this report and it conforms to the principles and procedures as set forth by MS Energy Services. The surveys were performed as listed below.

<u>Name of Surveyor</u>	<u>Drain hole No.</u>	<u>Surveyed Depths</u>	<u>Dates Performed</u>	<u>Survey</u>
Tim Coleman	Original Wellbore	2,065' – 18,994' MD	04/08/2013 to 04/24/2013	MWD

If any other information is required, please contact the undersigned at the letterhead address and telephone number.

Sincerely,

Amber Greer

MWD Operations Office Administrator

Attachments



V09.04.02

SURVEY CALCULATION PROGRAM

5/2/13 10:54

Company:	Continental Resources, Inc.									
Well Name:	Atlanta 14-6H									
Location:	Williams County, ND									
Rig:	Cyclone #2									
Job Number:	DDMT-130258									
API #:	33-105-02719									
Vertical Section Azimuth:	91.09		Proposed Direction: 91.09							
Survey Calculation Method:	Minimum Curvature									
PTB:	MD	INC	AZM	TVD	N/S	E/W	VS			
	19,085	90.9	91.5	10562.44	-156.06	8797.97	8799.34			
#	Depth Feet	Inc Degrees	Azm Degrees	TVD Feet	N/S Feet	E/W Feet	Surface Vert Sec	Closure Distance	DLS/ 100	BUR/ 100'
TIE IN	1,961	0.90	88.40	1960.91	-5.03	-10.00	-9.90	11.19	243.30	
1	2,065	0.50	116.70	2064.90	-5.21	-8.78	-8.68	10.21	239.30	0.50
2	2,159	1.20	85.40	2158.89	-5.32	-7.43	-7.33	9.14	234.42	0.87
3	2,253	2.00	90.00	2252.85	-5.24	-4.81	-4.71	7.11	222.56	0.86
4	2,346	2.20	91.20	2345.79	-5.27	-1.40	-1.30	5.46	194.88	0.22
5	2,440	1.90	102.20	2439.73	-5.64	1.93	2.03	5.96	161.16	0.52
6	2,533	1.40	106.70	2532.69	-6.29	4.52	4.64	7.75	144.31	0.55
7	2,627	1.10	127.20	2626.67	-7.17	6.34	6.47	9.57	138.52	0.57
8	2,719	0.90	137.80	2718.66	-8.24	7.53	7.68	11.16	137.58	0.30
9	2,811	1.60	108.10	2810.64	-9.17	9.23	9.41	13.02	134.81	1.01
10	2,904	1.50	110.10	2903.60	-9.99	11.61	11.80	15.32	130.72	0.12
11	2,998	1.50	115.40	2997.57	-10.95	13.88	14.08	17.67	128.26	0.15
12	3,092	1.60	110.40	3091.54	-11.93	16.22	16.44	20.13	126.34	0.18
13	3,185	1.40	113.90	3184.50	-12.84	18.47	18.72	22.50	124.81	0.24
14	3,277	1.40	115.40	3276.48	-13.78	20.52	20.78	24.72	123.89	0.04
15	3,369	2.30	105.90	3368.43	-14.77	23.31	23.59	27.59	122.36	1.03
16	3,462	2.20	102.90	3461.36	-15.68	26.84	27.14	31.09	120.29	0.17
17	3,556	1.80	80.70	3555.30	-15.84	30.06	30.35	33.98	117.79	0.92
18	3,649	1.50	81.10	3648.26	-15.42	32.70	32.99	36.16	115.24	0.32
19	3,743	1.40	89.90	3742.23	-15.23	35.07	35.35	38.23	113.47	0.26
20	3,837	1.30	92.70	3836.20	-15.27	37.28	37.56	40.29	112.28	0.13
21	3,929	0.90	38.10	3928.19	-14.75	38.77	39.04	41.48	110.84	1.16
22	4,023	0.60	26.30	4022.18	-13.73	39.44	39.70	41.76	109.20	0.36
23	4,116	0.50	51.30	4115.18	-13.04	39.97	40.22	42.05	108.07	0.28
24	4,209	0.40	58.00	4208.17	-12.62	40.57	40.80	42.48	107.28	0.12
25	4,303	0.30	43.90	4302.17	-12.27	41.02	41.24	42.81	106.65	0.14
26	4,397	0.20	37.00	4396.17	-11.96	41.28	41.50	42.98	106.15	0.11
27	4,490	0.10	81.50	4489.17	-11.82	41.46	41.68	43.11	105.91	0.16
28	4,584	0.10	97.80	4583.17	-11.81	41.62	41.84	43.27	105.85	0.03
29	4,677	0.20	102.80	4676.17	-11.86	41.86	42.08	43.51	105.82	0.11
30	4,771	0.40	189.20	4770.17	-12.22	41.97	42.20	43.71	106.24	0.46
31	4,865	0.60	195.60	4864.17	-13.02	41.79	42.03	43.77	107.31	0.22



V09.04.02

SURVEY CALCULATION PROGRAM

5/2/13 10:54

Company:	Continental Resources, Inc.
Well Name:	Atlanta 14-6H
Location:	Williams County, ND
Rig:	Cyclone #2
Job Number:	DDMT-130258
API #:	33-105-02719

Magnetic Declination: 8.54 REFERENCED TO TRUE NORTH ▼

Vertical Section Azimuth:	91.09	Proposed Direction:	91.09
---------------------------	-------	---------------------	-------

Survey Calculation Method:	Minimum Curvature
----------------------------	-------------------

PTB:	MD	INC	AZM	TVD	N/S	E/W	Closure		DLS/	BUR/	
	19,085	90.9	91.5	10562.44	-156.06	8797.97	Distance	Azm	100	100'	
#	Depth Feet	Inc Degrees	Azm Degrees	TVD Feet	N/S Feet	E/W Feet	Surface Vert Sec				
32	4,958	0.90	193.80	4957.16	-14.20	41.48	41.74	43.84	108.89	0.32	0.32
33	5,052	0.50	184.30	5051.15	-15.32	41.27	41.56	44.03	110.37	0.44	-0.43
34	5,144	0.70	106.50	5143.15	-15.88	41.78	42.08	44.70	110.81	0.84	0.22
35	5,238	0.40	99.90	5237.14	-16.10	42.66	42.96	45.60	110.68	0.33	-0.32
36	5,330	0.50	115.70	5329.14	-16.33	43.33	43.64	46.31	110.65	0.17	0.11
37	5,424	1.10	22.40	5423.13	-15.68	44.05	44.34	46.75	109.59	1.31	0.64
38	5,518	1.10	20.50	5517.12	-14.00	44.71	44.97	46.85	107.38	0.04	0.00
39	5,612	1.00	30.60	5611.10	-12.45	45.44	45.67	47.12	105.32	0.22	-0.11
40	5,705	0.90	28.20	5704.09	-11.10	46.20	46.40	47.52	103.51	0.12	-0.11
41	5,799	0.80	58.00	5798.08	-10.11	47.11	47.29	48.18	102.11	0.48	-0.11
42	5,893	0.90	99.90	5892.07	-9.88	48.39	48.57	49.39	101.54	0.65	0.11
43	5,986	1.20	132.90	5985.05	-10.67	49.82	50.02	50.95	102.09	0.71	0.32
44	6,080	1.20	128.60	6079.03	-11.96	51.31	51.53	52.69	103.12	0.10	0.00
45	6,174	1.60	136.60	6173.00	-13.52	52.98	53.23	54.68	104.32	0.47	0.43
46	6,267	1.00	155.00	6265.98	-15.20	54.22	54.50	56.31	105.66	0.78	-0.65
47	6,361	1.30	152.00	6359.96	-16.89	55.07	55.38	57.60	107.05	0.33	0.32
48	6,454	1.00	130.90	6452.94	-18.35	56.17	56.51	59.10	108.09	0.55	-0.32
49	6,548	1.30	119.20	6546.92	-19.41	57.73	58.08	60.90	108.58	0.40	0.32
50	6,641	1.00	110.40	6639.91	-20.21	59.41	59.78	62.75	108.78	0.37	-0.32
51	6,735	1.00	57.80	6733.89	-20.05	60.87	61.24	64.09	108.24	0.94	0.00
52	6,827	1.20	24.30	6825.88	-18.75	61.95	62.29	64.72	106.84	0.72	0.22
53	6,921	1.50	2.70	6919.85	-16.62	62.41	62.71	64.58	104.91	0.62	0.32
54	7,014	1.40	2.00	7012.82	-14.27	62.51	62.77	64.11	102.86	0.11	-0.11
55	7,108	1.50	358.20	7106.79	-11.89	62.51	62.72	63.63	100.77	0.15	0.11
56	7,201	1.50	359.20	7199.76	-9.46	62.45	62.62	63.16	98.61	0.03	0.00
57	7,295	1.40	1.70	7293.73	-7.08	62.47	62.59	62.87	96.47	0.13	-0.11
58	7,388	1.30	7.70	7386.70	-4.90	62.64	62.73	62.83	94.47	0.19	-0.11
59	7,482	1.30	9.20	7480.68	-2.79	62.96	63.00	63.02	92.54	0.04	0.00
60	7,575	1.10	358.30	7573.66	-0.86	63.10	63.10	63.10	90.78	0.33	-0.22
61	7,669	1.10	358.50	7667.64	0.95	63.05	63.02	63.06	89.14	0.00	0.00
62	7,763	1.00	356.90	7761.63	2.67	62.98	62.92	63.04	87.58	0.11	-0.11
63	7,855	1.00	4.00	7853.61	4.27	62.99	62.90	63.14	86.12	0.13	0.00
64	7,948	0.60	325.60	7946.60	5.48	62.77	62.66	63.01	85.01	0.70	-0.43



V09.04.02

SURVEY CALCULATION PROGRAM

5/2/13 10:54

Company:	Continental Resources, Inc.
Well Name:	Atlanta 14-6H
Location:	Williams County, ND
Rig:	Cyclone #2
Job Number:	DDMT-130258
API #:	33-105-02719

Magnetic Declination: 8.54 REFERENCED TO TRUE NORTH ▼

Vertical Section Azimuth:	91.09	Proposed Direction:	91.09
---------------------------	-------	---------------------	-------

Survey Calculation Method:	Minimum Curvature
----------------------------	-------------------

PTB:	MD		INC		AZM		TVD	N/S	E/W		VS	
	19,085		90.9		91.5		10562.44	-156.06	8797.97		8799.34	
#	Depth Feet	Inc Degrees	Azm Degrees	TVD Feet	N/S Feet	E/W Feet	Surface Vert Sec	Closure		DLS/ 100	BUR/ 100'	
65	8,042	0.60	336.30	8040.60	6.34	62.30	62.17	62.62	84.19	0.12	0.00	
66	8,136	0.60	318.00	8134.59	7.15	61.77	61.62	62.18	83.39	0.20	0.00	
67	8,229	0.60	301.70	8227.59	7.77	61.03	60.87	61.52	82.74	0.18	0.00	
68	8,323	0.70	303.90	8321.58	8.35	60.14	59.97	60.71	82.09	0.11	0.11	
69	8,417	0.70	303.60	8415.58	8.99	59.18	59.00	59.86	81.36	0.00	0.00	
70	8,510	0.60	291.60	8508.57	9.48	58.26	58.06	59.02	80.76	0.18	-0.11	
71	8,603	0.40	331.90	8601.57	9.95	57.65	57.45	58.50	80.21	0.42	-0.22	
72	8,695	0.40	337.10	8693.56	10.53	57.37	57.16	58.33	79.60	0.04	0.00	
73	8,789	0.30	302.40	8787.56	10.96	57.04	56.82	58.08	79.12	0.24	-0.11	
74	8,883	0.30	325.00	8881.56	11.29	56.69	56.46	57.80	78.73	0.13	0.00	
75	8,971	0.20	52.00	8969.56	11.58	56.68	56.45	57.85	78.46	0.40	-0.11	
76	9,064	0.40	77.20	9062.56	11.75	57.12	56.89	58.32	78.38	0.25	0.22	
77	9,158	0.50	84.80	9156.56	11.86	57.85	57.61	59.05	78.42	0.12	0.11	
78	9,252	0.50	86.50	9250.55	11.92	58.67	58.43	59.87	78.51	0.02	0.00	
79	9,345	0.40	89.40	9343.55	11.95	59.40	59.16	60.59	78.63	0.11	-0.11	
80	9,439	0.30	98.30	9437.55	11.92	59.97	59.73	61.14	78.76	0.12	-0.11	
81	9,533	0.30	101.40	9531.55	11.83	60.45	60.22	61.60	78.93	0.02	0.00	
82	9,625	0.30	78.10	9623.55	11.84	60.93	60.69	62.07	79.01	0.13	0.00	
83	9,719	0.20	84.80	9717.54	11.90	61.33	61.09	62.47	79.02	0.11	-0.11	
84	9,812	0.30	101.40	9810.54	11.87	61.73	61.49	62.86	79.12	0.13	0.11	
85	9,906	0.50	91.20	9904.54	11.81	62.38	62.15	63.49	79.28	0.23	0.21	
86	9,985	1.00	74.50	9983.53	11.99	63.39	63.15	64.51	79.29	0.68	0.63	
87	10,008	1.20	72.30	10006.53	12.11	63.81	63.57	64.95	79.25	0.89	0.87	
88	10,101	6.40	93.00	10099.30	12.14	69.92	69.68	70.97	80.15	5.69	5.59	
89	10,132	12.10	89.90	10129.88	12.05	74.90	74.66	75.86	80.86	18.45	18.39	
90	10,163	16.70	88.10	10159.90	12.21	82.61	82.36	83.50	81.59	14.91	14.84	
91	10,195	19.90	90.30	10190.28	12.33	92.65	92.40	93.47	82.42	10.23	10.00	
92	10,226	20.10	94.80	10219.41	11.86	103.23	102.99	103.91	83.45	5.01	0.65	
93	10,257	21.90	103.20	10248.36	10.09	114.17	113.96	114.62	84.95	11.30	5.81	
94	10,288	24.30	107.30	10276.87	6.87	125.90	125.74	126.08	86.87	9.32	7.74	
95	10,319	28.10	105.20	10304.68	3.06	139.04	138.95	139.07	88.74	12.62	12.26	
96	10,350	32.00	103.60	10331.51	-0.79	154.07	154.06	154.07	90.29	12.84	12.58	



V09.04.02

SURVEY CALCULATION PROGRAM

5/2/13 10:54

Company:	Continental Resources, Inc.										
Well Name:	Atlanta 14-6H										
Location:	Williams County, ND										
Rig:	Cyclone #2										
Job Number:	DDMT-130258										
API #:	33-105-02719										
Vertical Section Azimuth:	91.09		Proposed Direction: 91.09								
Survey Calculation Method:	Minimum Curvature										
PTB:	MD	INC	AZM	TVD	N/S	E/W	VS				
	19,085	90.9	91.5	10562.44	-156.06	8797.97	8799.34				
#	Depth Feet	Inc Degrees	Azm Degrees	TVD Feet	N/S Feet	E/W Feet	Surface Vert Sec	Closure Distance	DLS/ 100	BUR/ 100'	
97	10,381	36.10	102.30	10357.19	-4.66	170.98	171.04	171.05	91.56	13.43	13.23
98	10,413	41.60	100.30	10382.10	-8.58	190.66	190.79	190.86	92.58	17.63	17.19
99	10,444	45.60	97.20	10404.55	-11.80	211.79	211.97	212.11	93.19	14.63	12.90
100	10,475	48.00	92.70	10425.77	-13.74	234.29	234.51	234.69	93.36	13.11	7.74
101	10,506	51.30	87.90	10445.85	-13.84	257.90	258.11	258.27	93.07	15.89	10.65
102	10,538	54.90	85.50	10465.06	-12.35	283.44	283.62	283.71	92.49	12.75	11.25
103	10,569	57.50	86.30	10482.30	-10.51	309.13	309.27	309.31	91.95	8.66	8.39
104	10,600	60.30	87.30	10498.32	-9.03	335.63	335.74	335.75	91.54	9.44	9.03
105	10,631	61.10	88.80	10513.49	-8.11	362.65	362.73	362.74	91.28	4.95	2.58
106	10,662	64.30	92.30	10527.71	-8.39	390.18	390.27	390.27	91.23	14.39	10.32
107	10,693	68.60	95.10	10540.09	-10.24	418.53	418.65	418.65	91.40	16.15	13.87
108	10,724	72.20	96.60	10550.49	-13.22	447.57	447.75	447.77	91.69	12.48	11.61
109	10,755	75.10	97.20	10559.22	-16.79	477.10	477.34	477.40	92.02	9.54	9.35
110	10,787	77.30	97.70	10566.85	-20.82	507.91	508.22	508.34	92.35	7.04	6.88
111	10,818	80.60	96.70	10572.79	-24.63	538.10	538.47	538.66	92.62	11.11	10.65
112	10,849	81.30	96.00	10577.67	-28.02	568.52	568.95	569.21	92.82	3.17	2.26
113	10,859	81.50	95.60	10579.16	-29.02	578.36	578.81	579.09	92.87	4.43	2.00
114	10,933	87.00	90.90	10586.58	-33.17	651.82	652.33	652.66	92.91	9.75	7.43
115	10,986	87.00	92.80	10589.35	-34.88	704.72	705.25	705.58	92.83	3.58	0.00
116	11,080	88.00	91.40	10593.45	-38.32	798.56	799.14	799.48	92.75	1.83	1.06
117	11,175	87.70	89.80	10597.02	-39.32	893.48	894.07	894.35	92.52	1.71	-0.32
118	11,269	89.00	89.80	10599.72	-38.99	987.44	988.01	988.21	92.26	1.38	1.38
119	11,363	93.40	88.60	10597.75	-37.68	1081.39	1081.91	1082.05	92.00	4.85	4.68
120	11,457	93.50	88.80	10592.10	-35.55	1175.19	1175.66	1175.73	91.73	0.24	0.11
121	11,551	92.70	89.50	10587.01	-34.16	1269.05	1269.47	1269.50	91.54	1.13	-0.85
122	11,645	91.80	89.90	10583.32	-33.66	1362.97	1363.36	1363.39	91.41	1.05	-0.96
123	11,740	90.30	90.90	10581.58	-34.33	1457.95	1458.34	1458.35	91.35	1.90	-1.58
124	11,834	89.40	90.10	10581.83	-35.15	1551.94	1552.33	1552.34	91.30	1.28	-0.96
125	11,924	89.70	90.70	10582.53	-35.78	1641.94	1642.32	1642.33	91.25	0.75	0.33
126	12,019	91.30	89.20	10581.71	-35.69	1736.93	1737.29	1737.29	91.18	2.31	1.68
127	12,112	92.90	89.40	10578.30	-34.56	1829.85	1830.18	1830.18	91.08	1.73	1.72
128	12,206	92.60	89.80	10573.79	-33.90	1923.74	1924.04	1924.04	91.01	0.53	-0.32



V09.04.02

SURVEY CALCULATION PROGRAM

5/2/13 10:54

Company:	Continental Resources, Inc.
Well Name:	Atlanta 14-6H
Location:	Williams County, ND
Rig:	Cyclone #2
Job Number:	DDMT-130258
API #:	33-105-02719

Magnetic Declination: 8.54 REFERENCED TO TRUE NORTH ▼

Vertical Section Azimuth: 91.09 Proposed Direction: 91.09

Survey Calculation Method: Minimum Curvature

PTB:	MD	INC	AZM	TVD	N/S	E/W	VS
	19,085	90.9	91.5	10562.44	-156.06	8797.97	8799.34

#	Depth Feet	Inc Degrees	Azm Degrees	TVD Feet	N/S Feet	E/W Feet	Surface Vert Sec	Closure Distance	DLS/ 100	BUR/ 100'	
129	12,301	90.50	91.30	10571.22	-34.82	2018.70	2018.99	2019.00	90.99	2.72	-2.21
130	12,396	89.50	92.10	10571.22	-37.63	2113.65	2113.99	2113.99	91.02	1.35	-1.05
131	12,490	87.90	91.70	10573.35	-40.75	2207.57	2207.95	2207.95	91.06	1.75	-1.70
132	12,586	88.80	90.80	10576.12	-42.84	2303.51	2303.91	2303.91	91.07	1.33	0.94
133	12,682	89.40	90.30	10577.62	-43.76	2399.49	2399.89	2399.89	91.04	0.81	0.63
134	12,775	91.30	90.80	10577.06	-44.66	2492.48	2492.88	2492.88	91.03	2.11	2.04
135	12,870	89.80	90.80	10576.14	-45.98	2587.47	2587.87	2587.87	91.02	1.58	-1.58
136	12,963	90.40	92.00	10575.98	-48.25	2680.44	2680.87	2680.87	91.03	1.44	0.65
137	13,057	92.30	92.40	10573.77	-51.86	2774.34	2774.82	2774.82	91.07	2.07	2.02
138	13,152	90.90	91.30	10571.11	-54.93	2869.25	2869.77	2869.77	91.10	1.87	-1.47
139	13,246	90.10	91.30	10570.29	-57.06	2963.22	2963.77	2963.77	91.10	0.85	-0.85
140	13,340	90.70	91.30	10569.64	-59.19	3057.19	3057.76	3057.76	91.11	0.64	0.64
141	13,435	90.10	92.10	10568.97	-62.01	3152.14	3152.75	3152.75	91.13	1.05	-0.63
142	13,530	87.60	91.20	10570.88	-64.75	3247.08	3247.72	3247.72	91.14	2.80	-2.63
143	13,623	87.00	91.70	10575.26	-67.10	3339.94	3340.62	3340.62	91.15	0.84	-0.65
144	13,718	88.50	92.80	10578.99	-70.82	3434.79	3435.52	3435.52	91.18	1.96	1.58
145	13,812	88.60	92.70	10581.37	-75.33	3528.65	3529.45	3529.46	91.22	0.15	0.11
146	13,907	89.90	92.70	10582.61	-79.81	3623.54	3624.40	3624.42	91.26	1.37	1.37
147	14,001	87.60	92.80	10584.66	-84.31	3717.40	3718.33	3718.36	91.30	2.45	-2.45
148	14,095	86.50	91.50	10589.50	-87.84	3811.21	3812.19	3812.22	91.32	1.81	-1.17
149	14,190	88.80	90.30	10593.40	-89.33	3906.11	3907.10	3907.13	91.31	2.73	2.42
150	14,285	90.60	89.10	10593.89	-88.83	4001.10	4002.07	4002.09	91.27	2.28	1.89
151	14,379	90.90	89.20	10592.66	-87.44	4095.08	4096.00	4096.01	91.22	0.34	0.32
152	14,474	91.90	88.50	10590.34	-85.53	4190.03	4190.90	4190.91	91.17	1.28	1.05
153	14,568	91.60	87.70	10587.47	-82.41	4283.94	4284.73	4284.73	91.10	0.91	-0.32
154	14,662	91.50	87.60	10584.93	-78.56	4377.82	4378.52	4378.53	91.03	0.15	-0.11
155	14,756	91.10	86.50	10582.80	-73.72	4471.67	4472.27	4472.28	90.94	1.24	-0.43
156	14,851	90.80	86.90	10581.22	-68.26	4566.50	4566.97	4567.01	90.86	0.53	-0.32
157	14,945	92.70	89.00	10578.35	-64.90	4660.39	4660.78	4660.84	90.80	3.01	2.02
158	15,039	91.40	90.20	10574.99	-64.24	4754.32	4754.68	4754.76	90.77	1.88	-1.38
159	15,133	90.00	90.00	10573.84	-64.40	4848.31	4848.66	4848.74	90.76	1.50	-1.49
160	15,228	92.50	91.00	10571.77	-65.23	4943.28	4943.62	4943.71	90.76	2.83	2.63



V09.04.02

SURVEY CALCULATION PROGRAM

5/2/13 10:54

Company:	Continental Resources, Inc.
Well Name:	Atlanta 14-6H
Location:	Williams County, ND
Rig:	Cyclone #2
Job Number:	DDMT-130258
API #:	33-105-02719

Magnetic Declination: 8.54 REFERENCED TO TRUE NORTH ▼

Vertical Section Azimuth: 91.09 Proposed Direction: 91.09

Survey Calculation Method: Minimum Curvature

PTB:	MD	INC	AZM	TVD	N/S	E/W	VS
	19,085	90.9	91.5	10562.44	-156.06	8797.97	8799.34

#	Depth Feet	Inc Degrees	Azm Degrees	TVD Feet	N/S Feet	E/W Feet	Surface Vert Sec	Closure Distance	DLS/ 100	BUR/ 100'	
161	15,322	94.30	92.90	10566.19	-68.42	5037.05	5037.44	5037.51	90.78	2.78	1.91
162	15,417	93.40	91.90	10559.81	-72.39	5131.75	5132.20	5132.26	90.81	1.41	-0.95
163	15,511	88.00	90.90	10558.67	-74.69	5225.68	5226.15	5226.21	90.82	5.84	-5.74
164	15,605	88.30	91.30	10561.70	-76.49	5319.61	5320.10	5320.16	90.82	0.53	0.32
165	15,700	89.50	90.90	10563.52	-78.31	5414.57	5415.08	5415.14	90.83	1.33	1.26
166	15,794	90.30	88.70	10563.69	-77.99	5508.57	5509.05	5509.12	90.81	2.49	0.85
167	15,888	90.80	91.00	10562.79	-77.74	5602.56	5603.02	5603.10	90.79	2.50	0.53
168	15,982	88.90	90.50	10563.03	-78.97	5696.54	5697.01	5697.09	90.79	2.09	-2.02
169	16,076	90.10	91.90	10563.85	-80.94	5790.52	5791.01	5791.08	90.80	1.96	1.28
170	16,169	91.50	91.70	10562.55	-83.86	5883.46	5883.99	5884.06	90.82	1.52	1.51
171	16,263	92.10	91.40	10559.60	-86.40	5977.38	5977.94	5978.00	90.83	0.71	0.64
172	16,357	90.60	91.20	10557.39	-88.53	6071.32	6071.91	6071.97	90.84	1.61	-1.60
173	16,450	90.20	91.30	10556.74	-90.56	6164.30	6164.91	6164.96	90.84	0.44	-0.43
174	16,545	89.20	91.20	10557.23	-92.63	6259.27	6259.90	6259.96	90.85	1.06	-1.05
175	16,639	90.20	91.90	10557.73	-95.18	6353.24	6353.90	6353.95	90.86	1.30	1.06
176	16,733	93.50	91.30	10554.69	-97.80	6447.14	6447.83	6447.88	90.87	3.57	3.51
177	16,827	90.20	92.10	10551.66	-100.59	6541.03	6541.76	6541.81	90.88	3.61	-3.51
178	16,921	88.40	91.70	10552.81	-103.70	6634.97	6635.74	6635.78	90.90	1.96	-1.91
179	17,016	90.60	93.00	10553.64	-107.60	6729.88	6730.71	6730.74	90.92	2.69	2.32
180	17,110	90.70	91.50	10552.57	-111.29	6823.80	6824.68	6824.71	90.93	1.60	0.11
181	17,205	90.10	91.40	10551.91	-113.69	6918.76	6919.68	6919.70	90.94	0.64	-0.63
182	17,299	89.80	91.50	10551.99	-116.07	7012.73	7013.67	7013.69	90.95	0.34	-0.32
183	17,394	89.60	91.40	10552.49	-118.48	7107.70	7108.67	7108.69	90.95	0.24	-0.21
184	17,488	91.20	91.30	10551.83	-120.69	7201.67	7202.66	7202.68	90.96	1.71	1.70
185	17,582	89.60	90.90	10551.17	-122.49	7295.65	7296.66	7296.68	90.96	1.75	-1.70
186	17,676	89.00	91.60	10552.32	-124.54	7389.62	7390.65	7390.67	90.97	0.98	-0.64
187	17,771	87.80	90.80	10554.97	-126.53	7484.56	7485.61	7485.63	90.97	1.52	-1.26
188	17,865	91.10	91.20	10555.88	-128.17	7578.53	7579.59	7579.61	90.97	3.54	3.51
189	17,960	90.60	90.90	10554.47	-129.91	7673.50	7674.58	7674.60	90.97	0.61	-0.53
190	18,054	91.30	91.70	10552.91	-132.05	7767.46	7768.57	7768.58	90.97	1.13	0.74
191	18,148	89.00	91.20	10552.66	-134.43	7861.42	7862.56	7862.57	90.98	2.50	-2.45
192	18,242	89.90	91.00	10553.56	-136.23	7955.40	7956.55	7956.57	90.98	0.98	0.96



V09.04.02

SURVEY CALCULATION PROGRAM

5/2/13 10:54

Company:	Continental Resources, Inc.
Well Name:	Atlanta 14-6H
Location:	Williams County, ND

Rig:	Cyclone #2
Job Number:	DDMT-130258
API #:	33-105-02719

Vertical Section Azimuth:	91.09
Survey Calculation Method:	Minimum Curvature

PTB:	MD	INC	AZM	TVD	N/S	E/W	VS
	19,085	90.9	91.5	10562.44	-156.06	8797.97	8799.34

#	Depth	Inc	Azm	TVD	N/S	E/W	Surface	Closure		DLS/	BUR/
	Feet	Degrees	Degrees	Feet	Feet	Feet	Vert Sec	Distance	Azm	100	100'
193	18,337	91.10	91.20	10552.74	-138.05	8050.38	8051.55	8051.56	90.98	1.28	1.26
194	18,431	89.70	90.80	10552.08	-139.69	8144.36	8145.54	8145.56	90.98	1.55	-1.49
195	18,525	88.40	91.90	10553.64	-141.91	8238.32	8239.52	8239.54	90.99	1.81	-1.38
196	18,618	88.50	91.90	10556.15	-144.99	8331.23	8332.48	8332.49	91.00	0.11	0.11
197	18,711	89.40	90.80	10557.86	-147.18	8424.19	8425.46	8425.47	91.00	1.53	0.97
198	18,806	87.40	91.20	10560.51	-148.84	8519.13	8520.42	8520.43	91.00	2.15	-2.11
199	18,900	88.80	91.60	10563.63	-151.13	8613.05	8614.36	8614.37	91.01	1.55	1.49
200	18,994	90.90	91.50	10563.87	-153.68	8707.01	8708.36	8708.36	91.01	2.24	2.23



SUNDRY NOTICES AND REPORTS ON WELLS - FORM 4

INDUSTRIAL COMMISSION OF NORTH DAKOTA
OIL AND GAS DIVISION
600 EAST BOULEVARD DEPT 405
BISMARCK, ND 58505-0840
SFN 5749 (03-2004)

AA



Well File No.

23359

PLEASE READ INSTRUCTIONS BEFORE FILLING OUT FORM.
PLEASE SUBMIT THE ORIGINAL AND ONE COPY.

<input checked="" type="checkbox"/> Notice of Intent	Approximate Start Date January 29, 2013	<input type="checkbox"/> Drilling Prognosis	<input type="checkbox"/> Spill Report
<input type="checkbox"/> Report of Work Done	Date Work Completed	<input type="checkbox"/> Redrilling or Repair	<input type="checkbox"/> Shooting
<input type="checkbox"/> Notice of Intent to Begin a Workover Project that may Qualify for a Tax Exemption Pursuant to NDCC Section 57-51.1-03.		<input type="checkbox"/> Casing or Liner	<input type="checkbox"/> Acidizing
Approximate Start Date		<input type="checkbox"/> Plug Well	<input type="checkbox"/> Fracture Treatment
		<input type="checkbox"/> Supplemental History	<input type="checkbox"/> Change Production Method
		<input type="checkbox"/> Temporarily Abandon	<input type="checkbox"/> Reclamation
		<input checked="" type="checkbox"/> Other	Flow back exemption

Well Name and Number

Atlanta 14-6H

Footages	495 F N L	1485 F W L	Qtr-Qtr	Section	Township	Range
			NENW	6	153 N	101 W
Field	Baker		Pool	County		Williams

24-HOUR PRODUCTION RATE

Before		After	
Oil	Bbls	Oil	Bbls
Water	Bbls	Water	Bbls
Gas	MCF	Gas	MCF

Name of Contractor(s)

Address	City	State	Zip Code
---------	------	-------	----------

DETAILS OF WORK

Continental Resources, Inc. requests a waiver from the tubing/pkr requirement included in NDIC 43-02-03-21: Casing, Tubing, and Cementing Requirements during the completion period immediately following the upcoming fracture stimulation. The following assurances apply:

- 1) The well is equipped with 26#/ft P-110 7" casing at surface with an API burst rating of 9960 psig for the 26 #/ft casing.
- 2) The frac design will use a safety factor of 0.85 * API burst rating to determine the max pressure.
- 3) Damage to the casing during the frac would be detected immediately by monitoring equipment.
- 4) The casing is exposed to significantly lower rates and pressures during flow back than during the frac job.
- 5) The frac fluid and formation fluids have very low corrosion and erosion rates
- 6) Production equipment will be installed as soon as possible after the well ceases flowing.
- 7) A 300# gauge will be installed on surface casing during flowback period.

Company Continental Resources, Inc.	Telephone Number 405-234-9000	
Address P.O. Box 269000		
City Oklahoma City	State OK	Zip Code 73126
Signature 	Printed Name Jim Landrigan	
Title Completion Engineer	Date December 3, 2012	

FOR STATE USE ONLY

<input type="checkbox"/> Received	<input checked="" type="checkbox"/> Approved
Date <i>December 14, 2012</i>	
By <i>J. Landrigan</i>	
Title PETROLEUM ENGINEER	

**AMERICAN
TECHNICAL
SERVICES, INC.**

8105 Black Hawk Rd • PQ Box 558 • Black Hawk, SD 57718-0558 • Phone (605) 787-9303 • FAX (605) 787-9515
140 Pine Needle Drive • Spearfish, SD 57783 • Phone (605) 642-2742 • Mobile 390-3768

CONTINENTAL RESOURCES, INC.

C/O Brosz Engineering
P.O. Box 357
Bowman, North Dakota 58623

June 12, 2012

Attn: Jade Hedge

Subj: Report of Geotechnical Engineering Analysis
Atlanta Drill Pad
Continental Resources
Near Williston, North Dakota

ATS No. 12-12165

We have completed the geotechnical engineering analysis of the soils at the proposed Atlanta Drill Pad site located approximately 5 miles southwest of Williston, North Dakota. This analysis was authorized by Jade Hedge of Brosz Engineering on behalf of Continental Resources. Our soil design and construction recommendations are attached.

Geologic Profile:

Based on our analysis, we have determined the soil profile at the proposed Atlanta Drill Pad site consists of variable depths of sand and clay glacial deposits overlying fat clay glacial till and Pierre Shale. The sand and clay glacial deposits have variable amounts of clay, sand, gravel and traces of coal. The sands are of low plasticity and the fat clay glacial till is highly plastic and expansive.

Global Slope Stability:

The Owner elected not to conduct a slope stability analysis at this site. Thus, our recommendations are given with no acceptance or assumption of the global stability of the slopes at this site. Global stability issues may be present and may create land shifting or sliding in the future.

Geotechnical Summary:

The Atlanta Drill Pad will be constructed on a site with ridge and swale topography on the breaks of the Missouri River near Williston. We understand the Atlanta Drill pad will be created with massive cut and fill earthwork techniques. Cut depths on the order of 20 to 25 feet and fill depths up to 50 feet are planned for the construction of the drill pad.

We are providing drill pad construction earthwork recommendations given the soil profile and knowing the earthwork required to create the drill pad. We offer the following:

Cut Sections:

We recommend that any structure, drill rig, or other more permanent elements which are intolerant to differential movement be placed on the cut areas of the site.

Based on our drill program, we know that variable depths of sand mixtures overlie fat clay glacial till in the cut areas of the site. We recommend the fill pad finished elevation be established at the fat clay till contact or the sands be totally removed to the glacial till contact and then replaced with compacted clays. It is desired to not have layers of sand over clays as instability can result with moisture accumulation below sands and atop clays.

Fill Sections:

We recommend that no structure, drill rig, or other more permanent elements which are intolerant to differential movement be placed over fill areas. If it is desired or necessary to occupy fill areas, we recommend placement of such elements not be conducted until the fill sections have been allowed to consolidate for a minimum of one (1) year. We recommend the fill sections be monitored for vertical and horizontal movement upon completion in order to determine the stability of the sections.

We recommend the swales (valleys) which will be filled have underdrains installed prior to placing fill. We recommend pairs (set of 2 pipes) of 6" flexible PVC drain tile materials be installed along the toes of the existing swales prior to placing fill. The underdrain pipes should be sloped to daylight and must be kept unobstructed.

Fill placed on the existing toes of slopes must be keyed in a minimum depth of five (5) feet prior to placing fill. Fill must also be horizontally benched into existing slopes as fill is placed. We recommend benches be a minimum of 8 feet wide and be installed every two (2) feet vertically.

Drainage Considerations:

We recommend an intercepting drainage trench be excavated atop the cut to divert surface runoff away from the site. We also recommend the final drill pad be sloped to drain at a minimum rate of 5%.

We recommend the drill pad finished surface consist of compacted clays (either exposed native soils or placed clay soils) to minimize subsurface infiltration. Service gravel with separation fabric should be used in traffic areas to allow for access over clay surfaces.

Earthwork Considerations:

All fill soils must be moisture conditioned to +/-3% of optimum moisture content and be compacted to a minimum of 95% of ASTM D 698 standard proctor value.

Loose lifts of fill must not exceed 8" and may be increased to 12" if proper compaction equipment is used and density is verified. Cut/fill earthwork operations in freezing weather must be monitored for frost intrusion and frost lensing. Cut/fill earthwork in winter months is not recommended for this site due to the depths of fill planned.

**CONTINENTAL RESOURCES, INC.
Report of Geotechnical Engineering Analysis
Atlanta Drill Pad**

**June 12, 2012
ATS No. 12-12165
Near Williston, ND**

Closure:

Critical specific recommendations are presented in the report. Reference the site plan in the Appendix for boring locations.

We are available to give further design or consultation if necessary. We should be retained to observe, test, and approve the soils at the time of construction.

We look forward to working with you on future projects.

Sincerely,
American Technical Services, Inc.



Dave G. Bressler, P.E.
Director of Engineering

Copies to: Addressee (4)

INTRODUCTION

This report presents the results of our geotechnical engineering analysis of the soils at the proposed Atlanta Drill Pad site located approximately 5 miles southwest of Williston, North Dakota. This analysis was authorized by Jade Hedge of Brosz Engineering on behalf of Continental Resources.

Our services included laboratory testing of provided samples, performing engineering analysis, providing recommendations for use in drill pad design and construction. Results of the laboratory tests are presented in the report.

Our professional services were performed using the degree of care and skill ordinarily exercised, under similar circumstances, by geotechnical engineers practicing in this or similar localities. No other warranty, express or implied, is made. This report is not a bidding document. Any contractor reviewing this report must draw his own conclusions regarding site conditions and specific construction techniques to be used on this project.

PROJECT INFORMATION

Project information supplied by Brosz Engineering indicates Continental Resources intends to construct a drill pad near Williston, North Dakota. It is our understanding the site will be leveled by massive cut/fill construction. Based on our review of the provided site plans, some fill sections will be upwards of 50 feet in depth. Based on the request for proposal from Brosz Engineering, we are to provide a geotechnical evaluation of the site, provide recommendations for benching and side slopes, and provide slope construction guidelines.

We previously submitted (March, 2012) a proposal for the work at this site which included a slope stability analysis. We understand the Owner elected not to conduct the slope stability analysis.

SUBSURFACE EXPLORATION & TESTING PROGRAMS

We conducted ten (10) explorations to depths of 21 to 61 feet below existing site grades at the Atlanta Drill pad site. The explorations were at the approximate location shown on the attached site plan.

The Unified Soil Classification System was used to classify the soils encountered. Laboratory analyses were performed on representative soil samples to aid in material classification and to estimate pertinent engineering properties of the on-site soils. Testing was performed in accordance with applicable ASTM specifications.

The scope of our services did not include any environmental assessment or investigation for the presence or absence of hazardous or toxic materials in the soil, surface water, groundwater or air, on or below this site. All conditions noted or observed are strictly for the information of our client. If environmental information is required, we recommend an environmental assessment be conducted which addresses environmental concerns.

SITE CONDITIONS

Surface:

The Atlanta Drill Pad site is located approximately 5 miles southwest of Williston, North Dakota. The site lies on the breaks of the Missouri River. The surface at the pad site consists of ridge and swale topography with well defined drainage swales present. The surface is primarily grass and weed covered with overall drainage trending to the south.

Subsurface:

Detailed soil profiles are presented in the boring logs in the Appendix. Based on our analysis, we have determined the soil profile at the proposed Atlanta Drill Pad site consists of variable depths of sand and clay glacial deposits overlying fat clay glacial till and Pierre Shale. The sand and clay glacial deposits have variable amounts of clay, sand, gravel and traces of coal. The sands are of low plasticity and the fat clay glacial till is highly plastic and expansive.

Groundwater Conditions:

Groundwater was encountered at our Boring 1 (57' below existing site grades) location, and at approximately 15 to 18 feet below existing site grades at our boring 8, 9, and 10 locations (lower area of site). Fluctuations in the groundwater table may occur for various reasons, i.e., variations in precipitation, evaporation, surface runoff, groundwater withdrawal and recharge. A more accurate evaluation of the water table would require installing and monitoring piezometers over an extended time period.

Laboratory Analyses:

In-situ moisture contents and dry densities of representative samples from the borings are presented on the boring logs in the Appendix.

CONCLUSIONS AND RECOMMENDATIONS

GENERAL

Our recommendations are based on the assumption that the soil conditions are similar to those disclosed by the provided samples. If variations are noted during construction or if changes are made in the site plan, structural loading, or foundation type, we should be notified so we can supplement our recommendations, as applicable. This report does not encompass the effects, if any, of underlying geologic hazards or regional groundwater withdrawal and expresses no opinion regarding their effects on surface movement.

Global Slope Stability:

The Owner elected not to conduct a slope stability analysis at this site. Thus, our recommendations are given with no acceptance or assumption of the global stability of the slopes at this site. Global stability issues may be present and may create land shifting or sliding in the future.

Geotechnical Summary:

The Atlanta Drill Pad will be constructed on a site with ridge and swale topography on the breaks of the Missouri River near Williston. We understand the Atlanta Drill pad will be created with massive cut and fill earthwork techniques. Cut depths on the order of 20 to 25 feet and fill depths up to 50 feet are planned for the construction of the drill pad.

We recommend an intercepting drainage trench be excavated atop the cut to divert surface runoff away from the site. We also recommend the final drill pad be sloped to drain at a minimum rate of 5%.

We recommend the drill pad finished surface consist of compacted clays (either exposed native soils or placed clay soils) to minimize subsurface infiltration. Service gravel with separation fabric should be used in traffic areas to allow for access over clay surfaces.

We are providing drill pad construction earthwork recommendations given the soil profile and knowing the earthwork required to create the drill pad.

DRILL PAD CUT SECTIONS:

We recommend that any structure, drill rig, or other more permanent elements which are intolerant to differential movement be placed on the cut areas of the site.

Based on our drill program, we know that variable depths of sand mixtures overlie fat clay glacial till in the cut areas of the site. We recommend the fill pad finished elevation be established at the fat clay till contact or the sands be totally removed to the glacial till contact and then replaced with compacted clays. It is desired to not have layers of sand over clays as instability can result with moisture accumulation below sands and atop clays.

For grading cut slope design purposes and due to the presence of sandy soils, we recommend cut slopes be designed to slope at a rate of no steeper than 3:1 (horizontal to vertical). Said slopes will allow for maintenance and repair as necessary and will minimize erosion after vegetation is established. We offer the following grading guidelines for construction of surfacing or elements (excluding permanent structures) over cut sections:

- 1) We recommend a minimum of 8 inches of the on-site surficial soils and topsoil be removed, as applicable.
- 2) We recommend the soils exposed in the cut area be scarified a minimum of 8 inches, and be moisture conditioned to +/-3% of optimum moisture content.
- 3) We recommend the soils be compacted to a minimum of 95% of ASTM 698 standard proctor value. Compaction equipment must be sufficient to gain the desired results and will depend on the soils placed. The geotechnical engineer should observe, classify, and test the soils during the fill placement to assure proper techniques are employed.

- 4) After subgrade preparation and compaction, we recommend gravel base course or desired surfacing be placed. We recommend stabilization/separation fabric such as Mirafi HP370 be placed between the soil subgrade and surfacing material. Oversized rock may be required high traffic or soft soil areas.

DRILL PAD FILL SECTIONS:

We recommend that no structure, drill rig, or other more permanent elements which are intolerant to differential movement be placed over fill areas.

If it is desired or necessary to occupy fill areas, we recommend placement of such elements not be conducted until the fill sections have been allowed to consolidate for a minimum of one (1) year. We recommend the fill sections be monitored for vertical and horizontal movement upon completion in order to determine the stability of the sections.

We recommend the final slopes be no steeper than 3:1 (horizontal to vertical).

Underdrains:

We recommend the swales (valleys) which will be filled have underdrains installed prior to placing fill. We recommend pairs (set of 2 pipes) be installed along the toes of the existing swales prior to placing fill. We recommend the underdrains consist of 6" diameter fabric wrapped flexible perforated drain pipe. We recommend the drain pipe be bedded with a minimum of 12 inches of 1" clean rock bedding for the entire pipe length at the specified locations. The underdrain pipes should be sloped to daylight and must be kept unobstructed.

Keyways:

At the toes of the existing slopes, we recommend the native soils have a keyway cut to aid in supporting slope fill retention. We recommend the slope keyway consist of a five (5) foot minimum vertical cut in the native approved soils along the east side toe. Keyway areas over daylight pipe areas may be modified depending on depth. We recommend the keyway be a minimum of 10 feet in width. Additional underdrains may be required for the system if water is encountered within keyways.

Fill Construction:

We understand the fill for the pad will come from on-site as the grading is conducted. With the aforementioned grading plan in mind and our analysis of the soils present, we offer the following grading recommendations:

- 1) We recommend the fill areas be stripped to receive new fill. Stripping should clear all vegetation, topsoil and debris. The depth of such materials and horizontal extent of the fill/cut slopes will vary along the proposed toe slopes.
- 2) We recommend a minimum of 8 inches of the soils at the base of fill sections be removed (includes topsoil).

- 3) We recommend the soils present at the bottom of the aforementioned stripping depth be proofrolled in the presence of the geotechnical engineer. Soft or debris laden soil areas may require removal or stabilization with oversized rock prior to placing fill.
- 4) It is critical that newly placed embankment fill be benched into the existing side slopes as the fill is raised. We recommend a minimum bench width of eight (8) feet or one (1) scraper width per every two (2) feet of fill placed.
- 5) The soils placed must be placed in an engineered manner. The soils should be moisture conditioned to within 3% of optimum moisture content and be compacted to a minimum of 95% of ASTM D 698 standard proctor value. Compaction equipment must be sufficient to gain the desired results and will depend on the soils placed. The geotechnical engineer should observe, classify, and test the soils during the fill placement to assure proper techniques are employed.
- 6) Loose lifts of fill must not exceed 8" and may be increased to 12" if proper compaction equipment is used and density is verified. Cut/fill earthwork operations in freezing weather must be monitored for frost intrusion and frost lensing. Cut/fill earthwork in winter months is not recommended for this site due to the depths of fill planned.
- 7) We recommend that all finished fill slopes for the roadways be covered with topsoil and/or be hydro-seeded as soon as possible after the slopes have been finished to avoid excessive moisture intrusion and erosion. Seeding and erosion control measures should then follow as dictated by progress.
- 8) Erosion control measures must be implemented during and after construction to avoid loss of soil structure and sedimentation due to surface water infiltration and erosion. Erosion control techniques and materials should be upgraded or repaired as necessary during the course of construction. We recommend final slopes be no steeper than 3:1 (horizontal to vertical) to reduce erosion and facilitate mowing, etc. Steeper slopes can be used, however, maintenance during and after construction must be provided.
- 9) We estimate a shrinkage of soil from cut to fill of 25%.

Buried Debris, Large Cobbles, Boulders & Lignite Coal Lenses:

Buried debris may be present at any location at this site. Traces of lignite coal was encountered during our drilling and sampling program at this site. Cobbles were also encountered in the mixed glacial deposit areas.

We recommend buried debris pockets and lignite coal lenses, if exposed, be observed by the geotechnical engineer to determine the affects of the soils with respect to the drill pad. Removal and replacement of said materials may be required.

Large cobbles or boulders encountered may be placed at the bottom of fill areas as long as large particles are not allowed to "nest". Such particles should be isolated and surrounded by compacted fill.

Frost Depth Considerations

A minimum frost depth of 5 feet (60 inches) should be used for pertinent element design.

DRAINAGE AND MOISTURE PROTECTION

It is extremely important that the site soils not be allowed to become saturated during or after construction. Sump pumps should be present during construction to facilitate water removal after inclement weather.

Surface drainage is critical to assure long tank pad life. Grades should be such that drainage is away from all structures. Utility line excavations should be properly backfilled to avoid possible sources for subsurface saturation. The finished exterior grades of the pad must be sloped a minimum of 5% to promote positive drainage. Respective structure or well pads should be elevated relative to the surrounding finished grades to aid in promoting positive drainage.

We recommend the surface across the pad consist of native or placed compacted clay. We recommend any clay cap material be moisture conditioned to +/-3% of optimum moisture content and be compacted to a minimum of 95% of ASTM D 698 standard proctor value.

OSHA SLOPE STABILITY

GENERAL

The owner and contractor should make themselves aware of and become familiar with applicable local, state, and federal safety regulations, including the current OSHA Excavation and Trench Safety Standards. Construction site safety generally is the sole responsibility of the Contractor, who shall also be solely responsible for the means, methods, and sequencing of construction operations. We are providing this information solely as a service to our client. Under no circumstances should the information provided below be interpreted to mean that American Technical Services, Inc., is assuming responsibility for construction site safety or the Contractor's activities; such responsibility is not being implied and should not be inferred.

EXCAVATIONS AND SLOPES

The Contractor should be aware that slope height, slope inclination, or excavation depths (including utility trench excavations) should in no case exceed those specified in local, state, or federal safety regulations, e.g., OSHA Health and Safety Standards for Excavations, 29 CFR Part 1926, or successor regulations, such regulations are strictly enforced and, if they are not followed, the Owner, Contractor, and/or earthwork and utility subcontractors could be liable for substantial penalties.

For this site, the overburden soil encountered in our exploratory investigation is primarily a sand. This is considered to be a type B soil when applying the OSHA regulations. OSHA recommends a maximum slope inclination of 1:1 - (horizontal/vertical) for type B soils. As a safety measure, it is recommended that all vehicles and soil piles be kept a minimum lateral distance from the crest of the slope equal to no less than the slope height. Also, the exposed slope face should be protected against the elements.

We recommend that you retain us to monitor the soils exposed in all excavations and provide engineering services for such slopes. This will provide an opportunity to monitor the soil types encountered and to modify the excavation slope as necessary. It also offers an opportunity to verify the soil type and bearing capacity of the exposed soils.

EARTHWORK

GENERAL

1. The conclusions in this report are contingent upon compliance with recommendations in this section.
2. Due to the possible presence of buried debris, lignite coal, and groundwater impacted soils, we recommend the geotechnical engineer or his representative observe the soils exposed at bottom of slope keyway elevations and along underdrain areas prior to placing fill. Additional overexcavation and replacement may be required.

SITE CLEARING

Strip and remove existing debris, soft or loose soil and any other deleterious materials from the building and parking areas and at least 5 feet beyond. All exposed surfaces should be free of mounds and depressions which could prevent uniform compaction.

EXCAVATION

1. Standard excavation equipment should be sufficient for excavations at this site. Buried debris or large cobble to boulder sized materials may be encountered which are difficult to handle.
2. On-site soils may pump if allowed to become saturated. Scarification and drying, replacement with granular materials, use of special equipment or stabilization may be required to minimize subgrade pumping.

CONSTRUCTION OVER CUT OR FILL AREAS

1. Drain, prepare and construct cut or fill areas as presented in the respective sections of this report. Fill section consolidation period with monitoring is recommended prior to construction of elements.
2. Drainage of cut and fill slope surfaces is critical to prevent erosion and slope movement. Drill pad surface cross-slopes must be maintained at a minimum of 5% to promote surface drainage.

3. Respective subgrade preparation area to be accomplished in a manner which will result in uniform water contents and densities after compaction.
4. Soft, wet or debris laden soil lenses may require additional removal and replacement with oversized rock to stabilize.

MATERIALS

1. Granular engineered fill for structures should consist of on-site or imported sand or gravel. Structure placement recommendations is beyond the scope of this report.
2. Frozen soils should not be used as fill or backfill.
3. Gravel surfacing materials should conform to the following:
 - o Gradation (ASTM C136):

Sieve Size	Percent Finer By Weight
3"	100
No. 4 Sieve	40-100
No. 200 Sieve	15 (max)
Liquid Limit	25 (max)
 - o Maximum expansive potential(%) *0.2

*Measured on a sample compacted to approximately 95 percent of the ASTM D698 maximum dry density at about 3 percent below optimum water content. The sample is confined under a 100 psf surcharge and submerged.

4. Acceptance of use of on-site materials shall be at the direction of the geotechnical engineer. The on-site soils shall be placed in an engineered manner. Moisture and density conditioning of the soil is critical.

PLACEMENT AND COMPACTION

1. Place and compact fill in horizontal lifts using equipment and procedures that will produce recommended water contents and densities throughout the lift.
2. No fill should be placed over frozen ground.
3. Materials should be compacted to the following:

Soil Placement	Minimum Percent Compaction (ASTM D698)
----------------	--

Miscellaneous fill ----- 95

4. On -site and imported soils should be compacted at or near optimum moisture conditions.

COMPLIANCE

Structure foundation and slab support is beyond the scope of this report. Structures supported on cut surfaces or compacted fills are dependent upon compliance to respective cut and fill construction recommendations. To assess compliance with these recommendations, observation and testing should be performed under the direction of a geotechnical engineer.

CLOSURE

Our conclusions and recommendations are predicated on observation and testing of the earthwork preparations directed by a geotechnical engineer. Responsibility for any design or construction work or for our conclusions, recommendations, opinions or interpretations, either oral or written, cannot be accepted unless we perform the plan and specification review and construction monitoring to determine whether or not the work performed is in substantial compliance with our conclusions, recommendations, opinions or interpretations, and whether changed soil conditions have occurred.

Deviations from our recommendations by the plans, written specifications, or field applications shall relieve us of responsibility unless our written concurrence with such deviations has been obtained.

APPENDIX

PROJECT LOCATION MAP


SITE PLAN WITH BORING LOCATIONS


BORING LOGS

BORING LOG GENERAL NOTES

CLASSIFICATION OF SOILS FOR ENGINEERING PURPOSES

MOISTURE-DENSITY CURVES

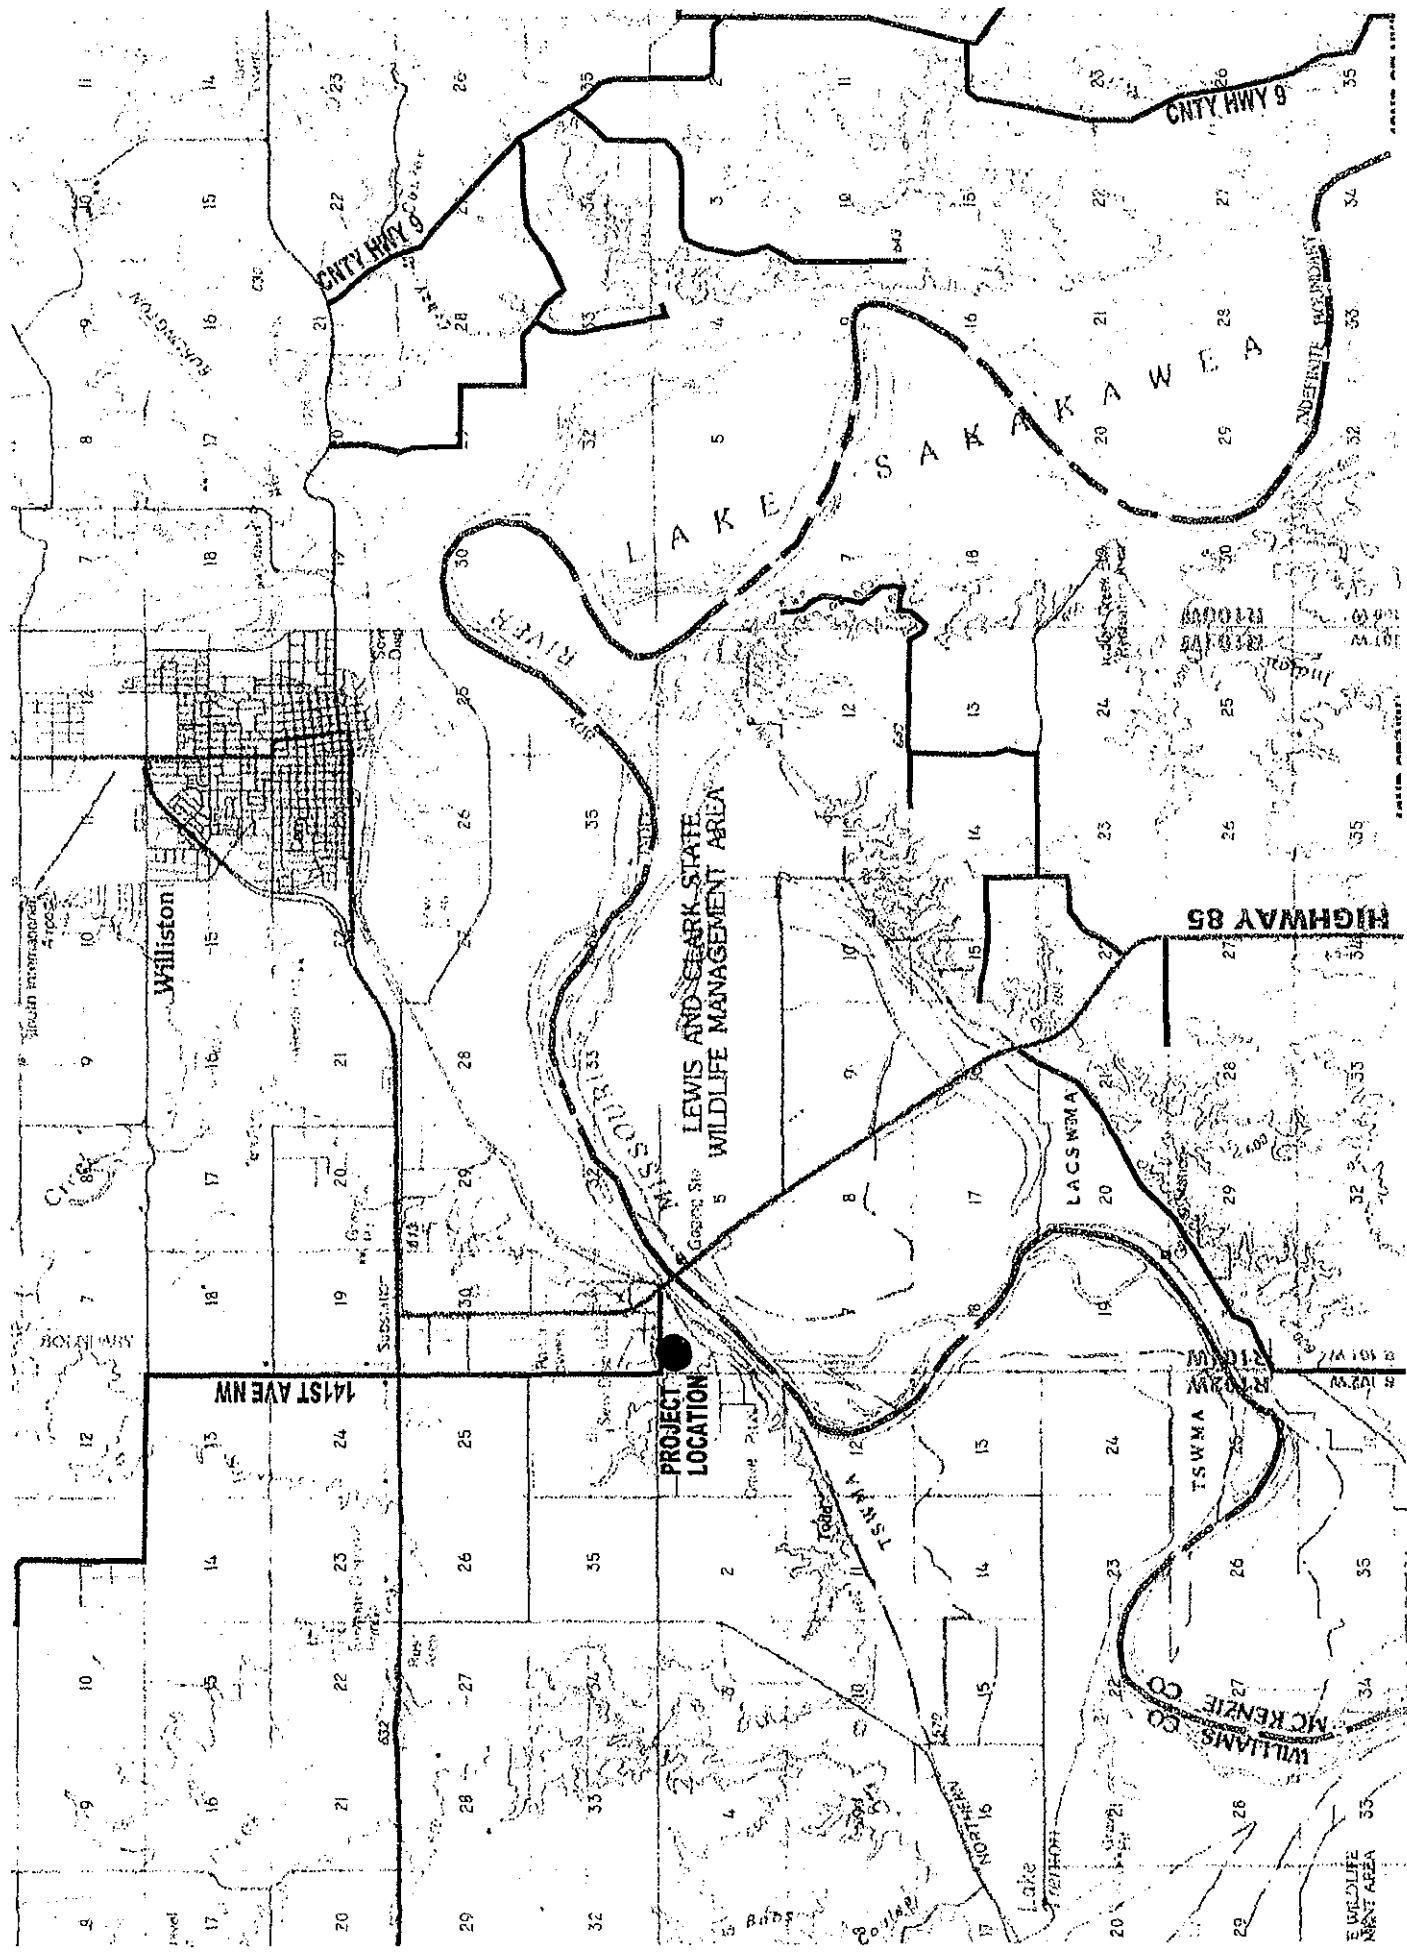

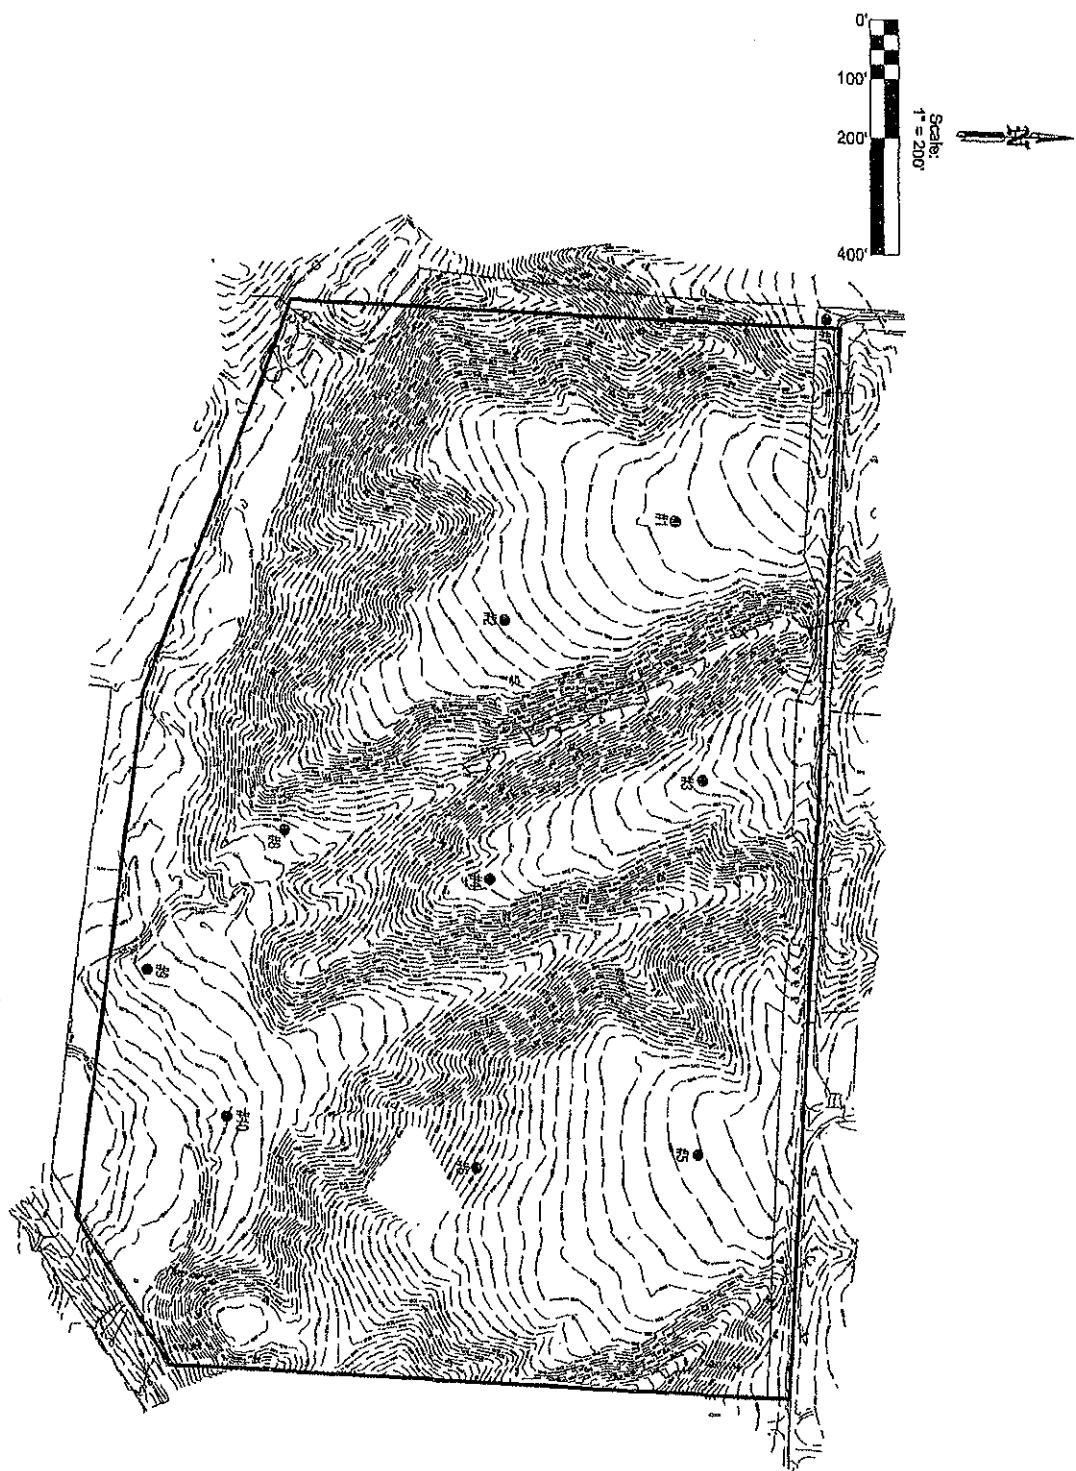

SHEET DESCRIPTION: Site Layout		REVISION	DATE	DESIGNED BY:	O OF
BROSZ	ARCHITECTURE ENGINEERING SURVEYING	1	xx/xx/xx	DRAWN BY: JBE	
109 E. Main, Box 317 Somerset, KY 42503 (606) 253-3340	PROJECT NAME: Atlanta Site	2			
	PROJECT NO.: N12B10	3			
		4			
				DATE PRINTED: 9/8/12	

TEST BORING LOG

PROJECT TITLE: Continental Atlanta Drill Pad, Near Williston, ND

PROJECT NUMBER: 12-12165

BORING NO: 1

DEPTH IN FEET	Approximate Surface Elevation = 1969.2' Description of Materials	GEOLOGIC ORIGIN	SAMPLE DATA				LABORATORY TESTS			
			WL	N	NO	TYPE	W	D	LL PL	QU
0.0'	Grass/weed cover									
2.5'	Sand w/clay: Brown, dry, loose (SC)	Alluvium								
5.0'	Sand: Brown, sl. moist, loose, m. grained, poorly graded, gravel present (SP)	Glacial Deposit		7	1	SB	4	FR	NP	
9.0'										
10.0'										
12.0'	Sandy Clay w/gravel: Brown, sl. Moist v. stiff, cobble present, variable gravel and sand content (CL w/sand and gravel)			15	2	SB	9	118		
15.0'	cobble absent, less gravel				12	3	SB	17	110	
17.5'										
20.0'	Fat Clay w/sand: Brown, moist, stiff, gravel present (CH w/sand) traces of gravel, variable sand content	Glacial Till		14	4	SB	16	108		
24.0'										
25.0'				14	5	SB				
30.0'					12	6	SB	18	108	
35.0'							NSR			
36.0'										
40.0'							13	7	SB	111
45.0'							NSR			
48.0'										
50.0'	Dk gray				14	8	SB			
55.0'										
57.0'										
58.0'							V			
60.0'	Shale: Dk. Gray, wet, m. stiff (CH)	Pierre Shale			9	9	SB	30	95	
61.0'	End of Boring									
DATE:	WATER TABLE MEASUREMENTS		DATE: 6/5/12							
6/5/12	Encountered at 57'		METHOD OF DRILLING: 2.25" HSA							
	Borehole caved to 40'		CREW CHIEF: MS							

AMERICAN TECHNICAL SERVICES, INC. (605) 787-9303

TEST BORING LOG

PROJECT TITLE: Continental Atlanta Drill Pad, Near Williston, ND

PROJECT NUMBER: 12-12165

BORING NO: 2

DEPTH IN FEET	Approximate Surface Elevation = 1955.0' Description of Materials	GEOLOGIC ORIGIN	SAMPLE DATA				LABORATORY TESTS			
			WL	N	NO	TYPE	W	D	LL	QU
										PL
0.0'	Grass/weed cover	Glacial Deposit								
2.5'	Sand w/clay: Brown, dry, loose variable clay content (SC)									
5.0'	Clayey Sand: Brown, sl. Moist, m. dense, variable sand content, trace of gravel (SC)			16	1	SB	8	117		
8.0'		Glacial Till								
10.0'	Fat Clay w/sand: Brown, moist, v. stiff, traces of gravel, variable sand content (CH)			16	2	SB	16	105	64	28
15.0'	stiff			13	3	SB	17	111		
16.0'										
20.0'	v. stiff			21	4	SB	18	102		
24.0'										
25.0'				21	5	SB	19	107		
30.0'						NSR				
32.0'										
35.0'				15	6	SB				
40.0'										
41.0'	End of Boring			14	7	SB				
DATE:	WATER TABLE MEASUREMENTS	DATE: 6/5/12								
6/5/12	Not Encountered	METHOD OF DRILLING: 2.25" HSA								
	Borehole caved to 25'	CREW CHIEF: MS								

AMERICAN TECHNICAL SERVICES, INC. (605) 787-9303

TEST BORING LOG

PROJECT TITLE: Continental Atlanta Drill Pad, Near Williston, ND
 PROJECT NUMBER: 12-12165

BORING NO: 3

DEPTH IN FEET	Approximate Surface Elevation = 1958.9' Description of Materials	GEOLOGIC ORIGIN	SAMPLE DATA				LABORATORY TESTS			
			WL	N	NO	TYPE	W	D	LL	QU
							PL			
0.0'	Grass/weed cover									
1.5'	Sand w/clay: Brown, dry, loose (SC)	Glacial Deposit								
	Sand w/clay: Brown, dry, m. dense m. grained, poorly graded (SP) variable clay content									
5.0'				18	1	SB	4	FR	NP	
8.0'										
10.0'				11	2	SB				
13.0'	Sandy Clay: Brown, moist, stiff, gravel present, variable sand content (CL)									
15.0'	Fat Clay w/sand: Brown, moist, stiff, traces of gravel variable sand content (CH)	Glacial Till		11	3	SB	17	110		
16.0'										
20.0'				12	4	SB				
24.0'										
25.0'						NSR				
30.0'	dk. Gray			13	5	SB	15	107		
32.0'										
35.0'						NSR				
40.0'	less stiff									
41.0'	End of Boring									
DATE: 6/5/12	WATER TABLE MEASUREMENTS Not Encountered Borehole caved to 25'	DATE: 6/5/12	METHOD OF DRILLING: 2.25" HSA CREW CHIEF: MS							

AMERICAN TECHNICAL SERVICES, INC. (605) 787-9303

TEST BORING LOG

PROJECT TITLE: Continental Atlanta Drill Pad, Near Williston, ND

PROJECT NUMBER: 12-12165

BORING NO: 4

DEPTH IN FEET	Approximate Surface Elevation = 1941.2' Description of Materials	GEOLOGIC ORIGIN	SAMPLE DATA				LABORATORY TESTS			
			WL	N	NO	TYPE	W	D	LL	QU
							PL			
0.0'	Grass/weed cover									
1.5'	Sand w/clay: Brown, dry, loose, gravel and cobble present (SC)	Glacial Deposit								
3.0'										
4.5'	Sand: Tan, dry, loose (SP)									
5.0'	Sandy Clay: Brown, moist, stiff, trace of gravel, variable sand content (CL)									
8.0'										
9.0'										
10.0'	Fat Clay w/sand: Brown, moist stiff, traces of gravel, variable sand content (CH)	Glacial Till	14	2	SB	11	FR	36		
15.0'			14	3	SB					
16.0'										
20.0'			14	4	SB					
24.0'										
25.0'						NSR				
30.0'										
31.0'										
32.0'	End of Boring		9	5	SB					
40.0'										
DATE: 6/6/12	WATER TABLE MEASUREMENTS Not Encountered Borehole caved to 24'	DATE: 6/6/12	METHOD OF DRILLING: 2.25" HSA				CREW CHIEF: MS			

AMERICAN TECHNICAL SERVICES, INC. (605) 787-9303

TEST BORING LOG

PROJECT TITLE: Continental Atlanta Drill Pad, Near Williston, ND

PROJECT NUMBER: 12-12165

BORING NO: 5

DEPTH IN FEET	Approximate Surface Elevation = 1963.6' Description of Materials	GEOLOGIC ORIGIN	SAMPLE DATA				LABORATORY TESTS			
			WL	N	NO	TYPE	W	D	LL PL	QU
0.0'	Grass/weed cover									
1.0'	Sand w/clay: Brown, dry, loose (SC)	Alluvium								
5.0'	Sand w/clay: Brown, sl. moist, m. dense, m. grained, poorly graded, gravel present (SP)	Glacial Deposit		13	1	SB	5	FR		
10.0'										
12.0'	Fat Clay w/sand: Brown, moist, stiff, gravel present, (CH w/sand)	Glacial Till		11	2	SB	15	112		
15.0'				11	3	SB	20	97	62	26
20.0'				10	4	SB	19	107		
24.0'										
25.0'										
30.0'										
35.0'										
36.0'										
40.0'	dk. Gray			12	6	SB	15	115		
45.0'										
48.0'										
50.0'	v. stiff			15	7	SB	15	FR		
51.0'	End of Boring									
60.0'										
DATE: 6/6/12	WATER TABLE MEASUREMENTS Not Encountered Borehole caved to 32'	DATE: 6/6/12	METHOD OF DRILLING: 2.25" HSA CREW CHIEF: MS							

AMERICAN TECHNICAL SERVICES, INC. (605) 787-9303

TEST BORING LOG

PROJECT TITLE: Continental Atlanta Drill Pad, Near Williston, ND

PROJECT NUMBER: 12-12165

BORING NO: 6

DEPTH IN FEET	Approximate Surface Elevation = 1921.5' Description of Materials	GEOLOGIC ORIGIN	SAMPLE DATA				LABORATORY TESTS			
			WL	N	NO	TYPE	W	D	LL	QU
0.0'	Grass/weed cover									
	Clayey Sand/Sandy Clay: Brown, dry, stiff/m. dense, variable clay & sand content (SC-CL)	Glacial Deposit								
4.5'										
5.0'	Fat Clay w/sand: Brown, moist, v. stiff, traces of gravel, variable sand content (CH)	Glacial Till		19	1	SB	11	114		
10.0'	less stiff				8	2	SB	11	118	
15.0'					11	3	SB	15	116	
17.0'										
	Shale: Gray & brown, moist, stiff, sand present (CH)	Pierre Shale								
20.0'					10	4	SB	34	88	
25.0'										
26.0'	End of Boring				11	5	SB			
DATE:	WATER TABLE MEASUREMENTS	DATE: 6/6/12								
6/6/12	Not Encountered	METHOD OF DRILLING: 2.25" HSA								
	Borehole caved to 24'	CREW CHIEF: MS								

AMERICAN TECHNICAL SERVICES, INC. (605) 787-9303

TEST BORING LOG

PROJECT TITLE: Continental Atlanta Drill Pad, Near Williston, ND

PROJECT NUMBER: 12-12165

BORING NO: 7

DEPTH IN FEET	Approximate Surface Elevation = 1977.1' Description of Materials	GEOLOGIC ORIGIN	SAMPLE DATA				LABORATORY TESTS			
			WL	N	NO	TYPE	W	O	LL	QU
										PL
0.0'	Grass/weed cover									
2.0'	Sand w/clay: Brown, dry, loose (SC)	Alluvium								
5.0'	Sand: Brown, sl. moist, loose, m. grained, poorly graded, gravel present (SP)	Glacial Deposit		9	1	SB	6	FR		
10.0'	Fat Clay w/sand: Brown, moist, stiff, gravel present, (CH w/sand) variable sand content	Glacial Till		10	2	SB	16	109		
12.0'										
15.0'				8	3	SB				
20.0'				9	4	SB	16	111		
24.0'										
25.0'				10	5	SB				
30.0'						NSR				
35.0'				9	6	SB				
36.0'										
40.0'						NSR				
45.0'	Dk. Gray			10	7	SB				
48.0'										
50.0'						NSR				
55.0'				9	8	SB				
60.0'										
61.0'	End of Boring			8	9	SB				
DATE: 6/6/12	WATER TABLE MEASUREMENTS Not Encountered	DATE: 6/6/12	METHOD OF DRILLING: 2.25" HSA							
	Borehole caved to 43'	CREW CHIEF: MS								

AMERICAN TECHNICAL SERVICES, INC. (605) 787-9303

TEST BORING LOG

PROJECT TITLE: Continental Atlanta Drill Pad, Near Williston, ND

PROJECT NUMBER: 12-12165

BORING NO: 8

DEPTH IN FEET	Approximate Surface Elevation = 1892.3' Description of Materials	GEOLOGIC ORIGIN	SAMPLE DATA				LABORATORY TESTS			
			WL	N	NO	TYPE	W	D	LL	QU
0.0'	Grass/weed cover	Alluvium								
	Clay w/sand: Gray, moist, stiff, sand present (CL)									
5.0'				8	1	SB	21	97		
10.0'				10	2	SB	19	107		
15.0'	Fat Clay w/sand: Brown, moist, stiff, variable sand content (CH)	Pierre Shale		9	3	SB	22	97		
18.0'			V							
20.0'				10	4	SB	33	91		
21.0'										
25.0'	End of Boring									
DATE: 6/7/12	WATER TABLE MEASUREMENTS Encountered at 18' Borehole caved to 14'	DATE: 6/7/12	METHOD OF DRILLING: 2.25" HSA							
			CREW CHIEF: MS							

AMERICAN TECHNICAL SERVICES, INC. (605) 787-9303

TEST BORING LOG

PROJECT TITLE: Continental Atlanta Drill Pad, Near Williston, ND

PROJECT NUMBER: 12-12165

BORING NO: 9

DEPTH IN FEET	Approximate Surface Elevation = 1878.6' Description of Materials	GEOLOGIC ORIGIN	SAMPLE DATA				LABORATORY TESTS			
			WL	N	NO	TYPE	W	D	LL	QU
							PL			
0.0'	Grass/weed cover									
	Sand w/clay: Brown, moist, loose, variable clay content (SC), traces of gravel present	Alluvium								
5.0'										
10.0'	Gravelly Sand: Brown, moist, dense, variable sand content (SW)									
15.0'	obstructed sampler									
18.0'	less dense, wet, less gravel									
20.0'										
21.0'	End of Boring									
25.0'										
DATE:	WATER TABLE MEASUREMENTS	DATE: 6/7/12								
6/7/12	Encountered at 18'	METHOD OF DRILLING: 2.25" HSA								
	Borehole caved to 13'	CREW CHIEF: MS								

AMERICAN TECHNICAL SERVICES, INC. (605) 787-9303

TEST BORING LOG

PROJECT TITLE: Continental Atlanta Drill Pad, Near Williston, ND

PROJECT NUMBER: 12-12165

BORING NO: 10

DEPTH IN FEET	Approximate Surface Elevation = 1874.4' Description of Materials	GEOLOGIC ORIGIN	SAMPLE DATA				LABORATORY TESTS			
			WL	N	NO	TYPE	W	D	LL	QU
							PL			
0.0'	Grass/weed cover									
	Sandy Clay/Clayey Sand: Brown, moist, m. stiff/loose, variable sand & clay content (CL-SC)	Alluvium								
5.0'	traces of gravel present			6	1	SB	11	111		
10.0'	soft/v. loose			4	2	SB	19	105		
15.0'	wet, softer/looser		V	2	3	SB	25	FR		
19.0'										
20.0'	Sand: Brown, poorly graded wet, v. loose (SP)						NSR			
22.0'	Gravel & cobble present									
25.0'							NSR			
26.0'	End of Boring									
DATE:	WATER TABLE MEASUREMENTS		DATE: 6/7/12							
6/7/12	Encountered at 15'		METHOD OF DRILLING: 2.25" HSA							
	Borehole caved to 13'		CREW CHIEF: MS							

AMERICAN TECHNICAL SERVICES, INC. (605) 787-9303

GENERAL NOTES

DESCRIPTIVE TERMINOLOGY		RELATIVE SIZES	
Density Term	"N" Value	Boulder	> 12"
Very Loose	0 - 4	Cobble	3" - 12"
Loose	4 - 10	Gravel	3/4" - 3"
Medium Dense	10 - 16	Coarse	#4 - 3/4"
Dense	16 - 30	Fine	#4 - #10
Very Dense	> 30	Sand	#10 - #40
		Coarse	#40 - #200
		Medium	#200 (PI)
		Fine	<#200 (PI)
		Silt & Clay	
Consistency Term	"N" Value	Term	Range
Very Soft	0 - 2	Trace	0 - 5%
Soft	2 - 4	A Little	5 - 15%
Medium stiff	4 - 8	Some	15 - 30%
Stiff	8 - 15	With	30 - 50%
Very stiff	15 - 30		
Hard	< 30		
BORING AND SAMPLING SYMBOLS			
SYMBOL	DEFINITION		
HSA	Hollow Stem Auger - 3 1/4" ID & 4 1/4" ID		
FA	Flight Auger - 4" OD		
HA	Hand Auger - 1 1/2" OD		
DC	Drive Casing		
PD	Pipe Drill or Clean Out Tube		
CS	Continuous Split Barrel Sampling		
DM	Drilling Mud		
JW	Jetting Water		
SB	Split Barrel Sampler		
TW	Thin Wall Tube Sampler		
LS	Split Barrel Liner Sample		
W	Wash Sample		
B	Bag Sample		
NSR	No Sample Retrieved		
NMR	No Water Level Measurement Recorded		
WL	Water Level		
N	Standard Penetration Value		
	Water Level Symbol		
LABORATORY TEST SYMBOLS			
SYMBOL	DEFINITION		
W	Moisture Content-Percent of Dry Weight ASTM D2216		
D	Dry Density-Pound Per Cubic Foot		
LL & PL	Liquid Limit and Plastic Limit ASTM D4318		
Qu	Unconfined Compressive Strength Pounds Per Square Foot ASTM D2166		

CLASSIFICATION OF SOILS FOR ENGINEERING PURPOSES

ASTM Designation: D 2487 — 69 AND D 2488 — 69

(Unified Soil Classification System)

Major divisions		Group symbols	Typical Names		Classification Criteria				
Coarse-grained soils More than 50% retained on No. 200 sieve*	Gravels More than 50% of coarse fraction retained on No. 4 sieve	GW	Well-graded gravels and gravel-sand mixtures, little or no fines	Clean gravels	$C_u = \frac{D_{50}}{D_{10}}$ greater than 4; $C_z = \frac{(D_{50})^2}{D_{10} \times D_{50}}$ between 1 and 3	Not meeting both criteria for GW			
		GP	Poorly graded gravels and gravel-sand mixtures, little or no fines	Clean gravels		Not meeting both criteria for GW			
		GM	Silty gravels, gravel-sand-silt mixtures	Clean sands	Atterberg limits below "A" line or PI. less than 4	Atterberg limits plotting in hatched area are borderline classifications requiring use of dual symbols			
		GC	Clayey gravels, gravel-sand-clay mixtures	Clean sands	Atterberg limits above "A" line with PI. greater than 7	Atterberg limits plotting in hatched area are borderline classifications requiring use of dual symbols			
		SW	Well-graded sands and gravelly sands, little or no fines	Clean sands	Classification on basis of percentage of fines Less than 5% pass No. 200 sieve GW, GP, SW, SP More than 12% pass No. 200 sieve GM, GC, SM, SC 5 to 12% pass No. 200 sieve Borderline classifications requiring use of dual symbols	Not meeting both criteria for SW			
		SP	Poorly graded sands and gravelly sands, little or no fines	Sands with fines		Atterberg limits below "A" line or PI. less than 4			
		SM	Silty sands, sand-silt mixtures	Sands with fines		Atterberg limits above "A" line with PI. greater than 7			
		SC	Clayey sands, sand-clay mixtures	Sands with fines		Atterberg limits plotting in hatched area are borderline classifications requiring use of dual symbols			
		ML	Inorganic silts, very fine sands, rock flour; silty or clayey fine sands	Silts and clays Liquid limit 50% or less		Atterberg limits plotting in hatched area are borderline classifications requiring use of dual symbols			
Fine-grained soils 50% or more passes No. 200 sieve*	Sils and clays Liquid limit greater than 50%	CL	Inorganic clays of low to medium plasticity, gravelly clays, sandy clays, silty clays, lean clays	Plasticity Chart	For classification of fine-grained soils and fine fraction of coarse-grained soils.				
		OL	Organic silts and organic silty clays of low plasticity		Atterberg Limits plotting in hatched area are borderline classifications requiring use of dual symbols.				
		MH	Inorganic silts, micaceous or diatomaceous fine sands or silts, elastic silts		Equation of A-line: $PI = 0.73 (LL - 20)$				
		CH	Inorganic clays of high plasticity, fat clays		CH				
		OH	Organic clays of medium to high plasticity		OH and MH				
	Highly organic soils	PI	Peat, muck and other highly organic soils		Based on the material passing the 3 in. (75 mm) sieve.				



AMERICAN
TECHNICAL
SERVICES, INC.

8105 Black Hawk Rd • PO Box 558 • Black Hawk, SD 57718-0558 • Phone (605) 787-9303 • FAX (605) 787-9515
140 Pine Needle Drive • Spearfish, SD 57783 • Phone (605) 642-2742 • Mobile 390-3768

PROCTOR TEST

MOISTURE DENSITY RELATION

BROSZ ENGINEERING

Proctor#: 1 Date:06/11/12

ASTM: 698 Method:A

Attn: Jade

Soil Classification: (SC-CL) Clayey
Sand/Sandy Clay


Project: Continental Atlanta Pad, Near
Williston, North Dakota

Project Number: 12-12165

MAXIMUM DENSITY: 126.5 pdf

OPTIMUM MOISTURE CONTENT: 9.7%

DRY DENSITY, pdf
130
128
126
124
122

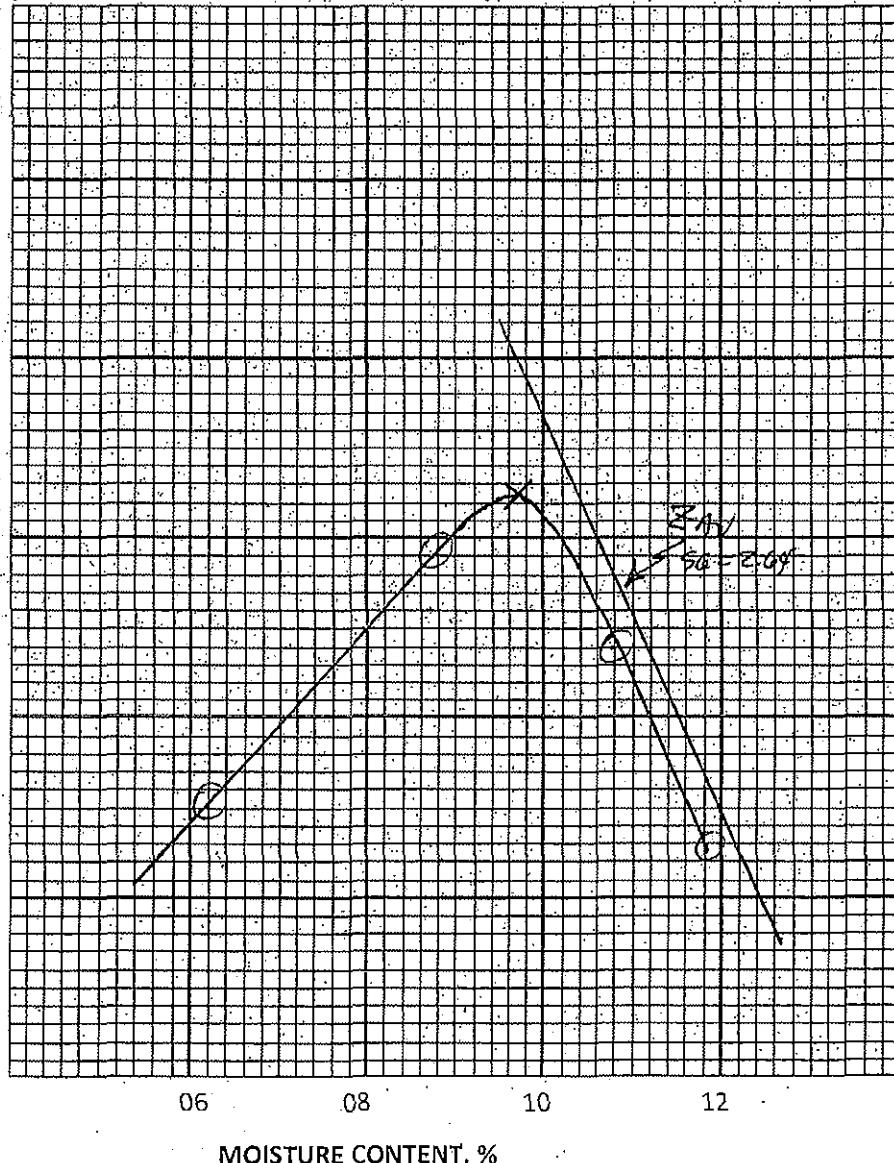

MOISTURE CONTENT, %

Cc:

SIOUX FALLS • BLACK HAWK • SPEARFISH

**AMERICAN
TECHNICAL
SERVICES, INC.**

8105 Black Hawk Rd • PO Box 558 • Black Hawk, SD 57718-0558 • Phone (605) 787-9303 • FAX (605) 787-9515
140 Pine Needle Drive • Spearfish, SD 57783 • Phone (605) 642-2742 • Mobile 390-3768

PROCTOR TEST

MOISTURE DENSITY RELATION

BROSZ ENGINEERING

Proctor#: 2 Date: 06/11/12

ASTM: 698 Method: A

Attn: Jade

Soil Classification: (SP) Sand w/ Gravel,
B15-0'-10'


Project: Continental Atlanta Pad, Near
Williston, North Dakota

Project Number: 12-12165

MAXIMUM DENSITY: 123.2 pcf

OPTIMUM MOISTURE CONTENT: 8.3%

DRY DENSITY, pcf

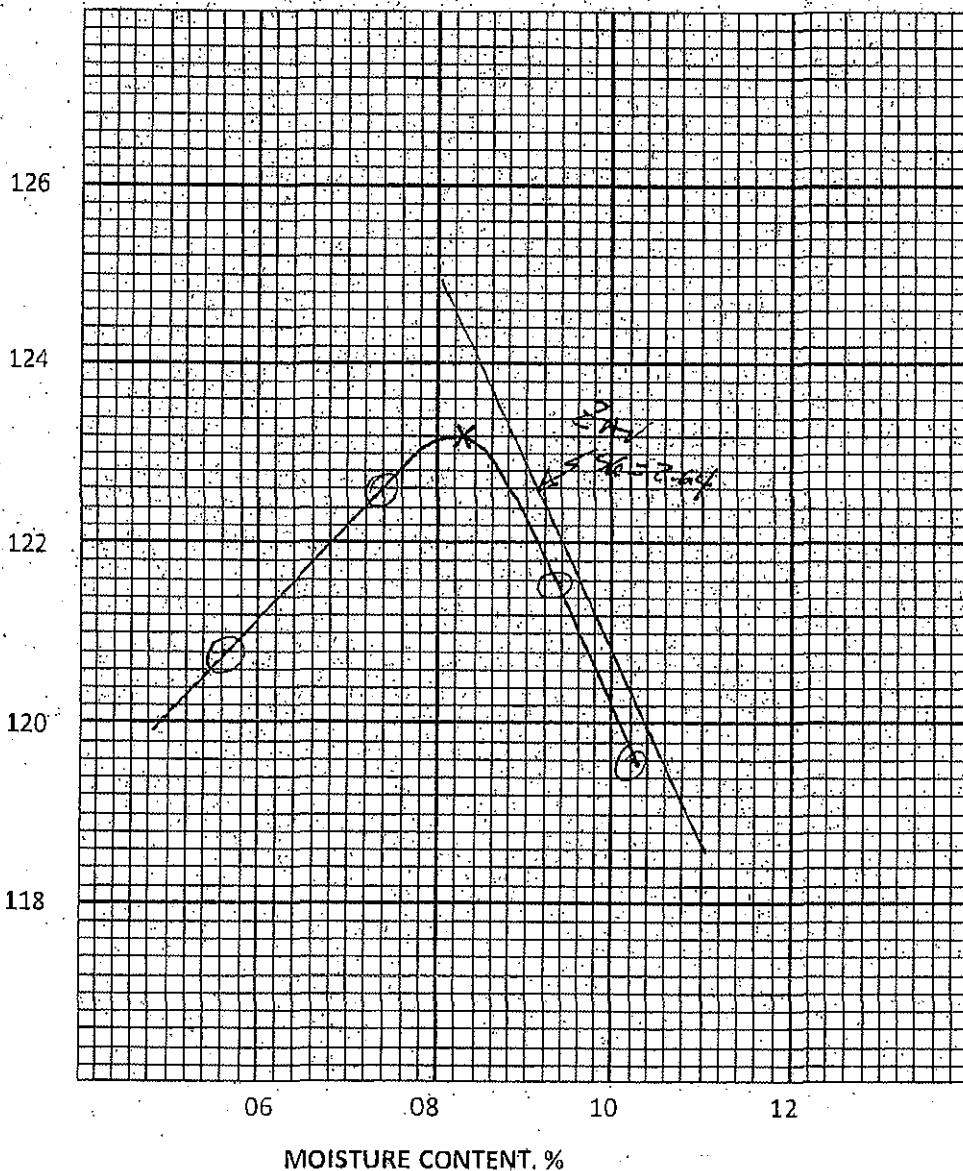

Cc:

SIOUX FALLS • BLACK HAWK • SPEARFISH

PERMEABILITY TEST REPORT

TEST DATA:

Specimen Height (cm): 7.50
 Specimen Diameter (cm): 7.07
 Dry Unit Weight (pcf): 110.8
 Moisture Before Test (%): 13.8
 Moisture After Test (%): 0.0
 Run Number: 1 • 2 ▲
 Cell Pressure (psi): 65.0
 Test Pressure(psi): 60.0
 Back Pressure(psi): 57.9
 Diff. Head (psi): 2.1
 Flow Rate (cc/sec): 6.93×10^{-3}
 Perm. (cm/sec): 9.08×10^{-6}


SAMPLE DATA:

Sample Identification: Fill No.3

Visual Description:

Remarks:

Maximum Dry Density (pcf): 116.6
 Optimum Moisture Content (%): 13.8
 ASTM(D698)
 Percent Compaction: 95.0%
 Permeameter type: Flexwett
 Sample type: Remolded

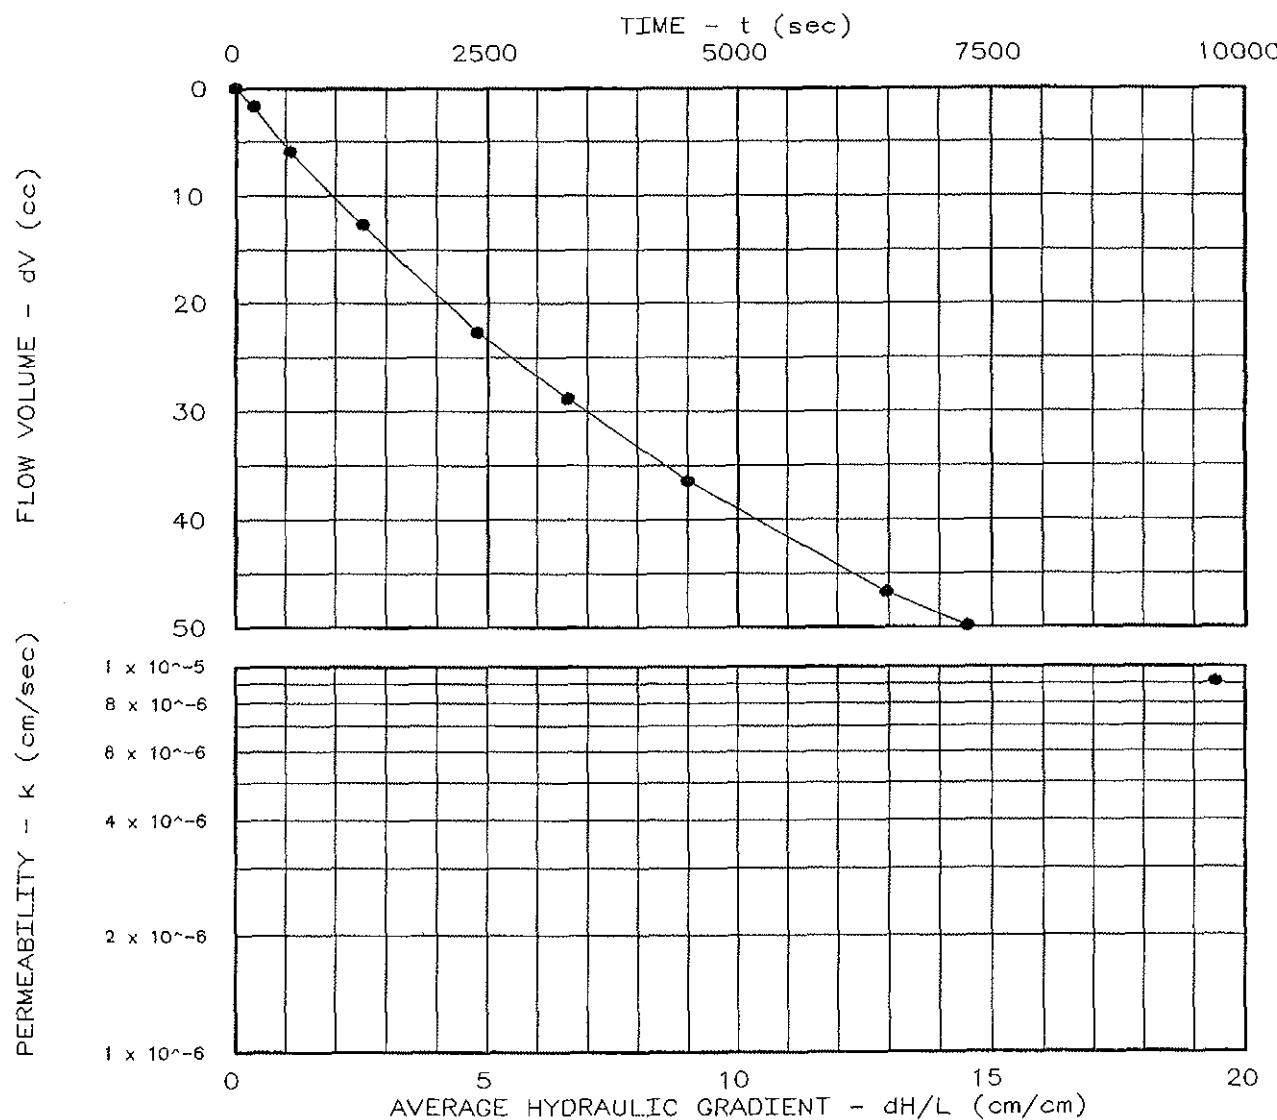

Project: Atlanta Site

Location:

Date: 9/10/2012

Project No.: 114-551057

File No.: 258

Lab No.:

Tested by:


Checked by:

Test: CH - Constant head

PERMEABILITY TEST REPORT

TETRA TECH

Moisture Density Relationship

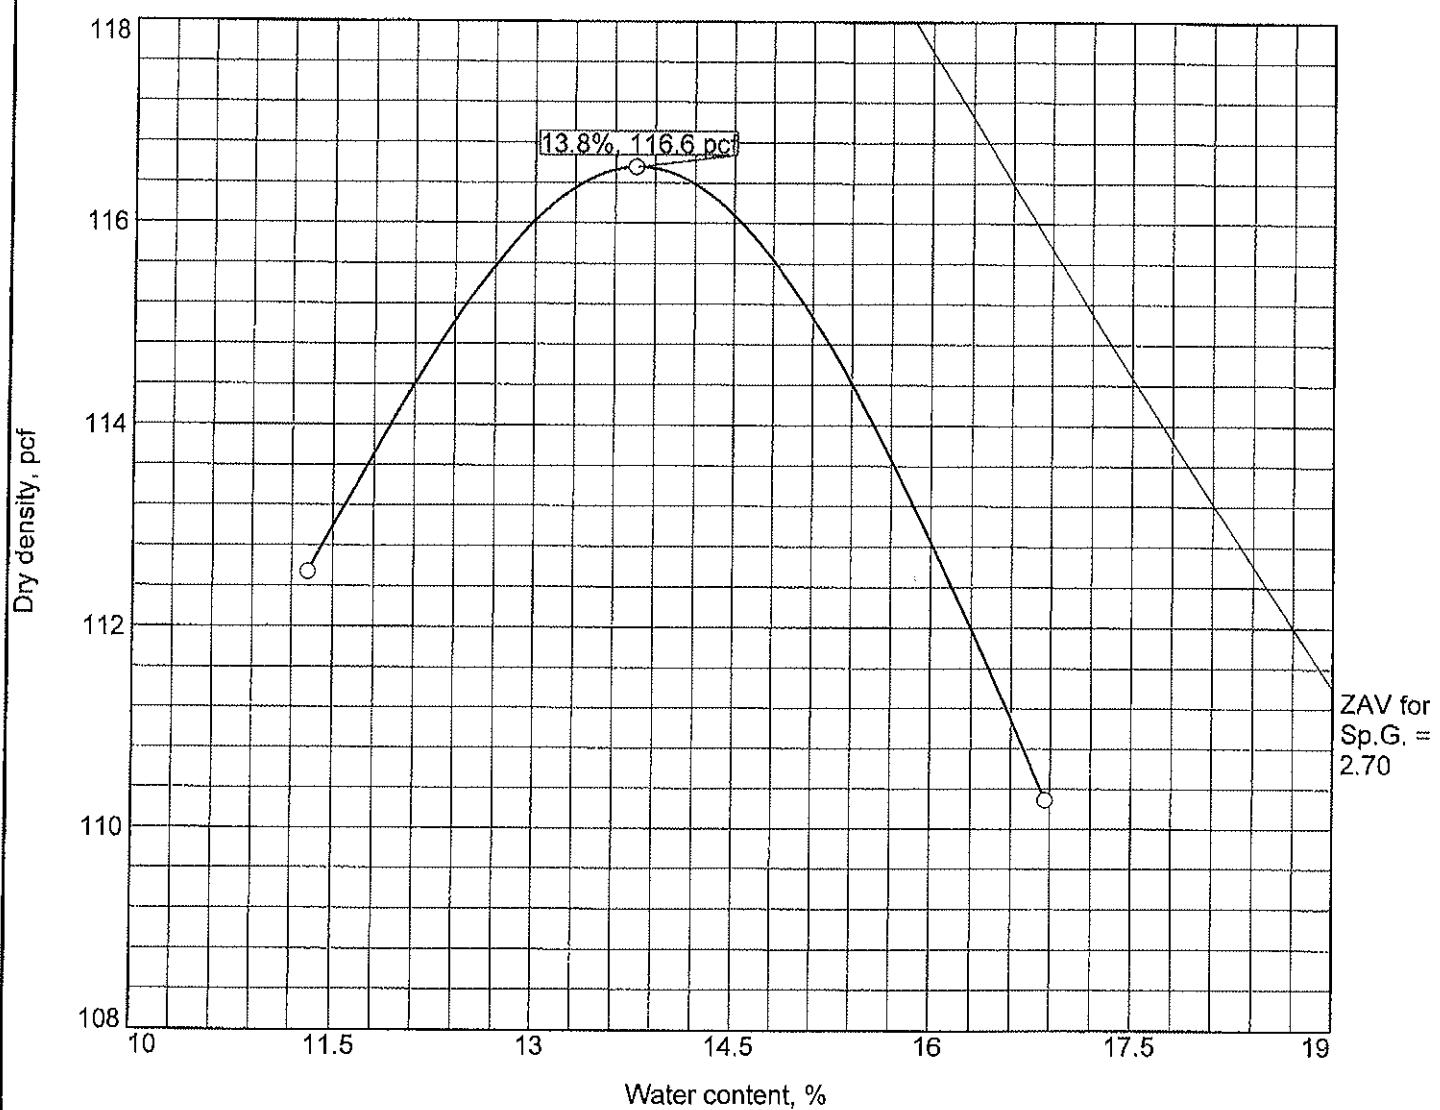

Test specification: ASTM D 698-00a Method A Standard

Elev/ Depth	Classification		Nat. Moist.	Sp.G.	LL	PI	% > #4	% < No.200
	USCS	AASHTO						
				2.70				

TEST RESULTS		MATERIAL DESCRIPTION
Maximum dry density = 116.6 pcf		
Optimum moisture = 13.8 %		
Project No. 114-551057 Client: Continental Resources Project: Atlanta Site		Remarks:
Source of Sample: Fill No. 3		
Tetra Tech, Inc.		
Billings, MT		Figure

PERMEABILITY TEST REPORT

TEST DATA:

Specimen Height (cm): 7.50
 Specimen Diameter (cm): 7.07
 Dry Unit Weight (pcf): 112.3
 Moisture Before Test (%): 13.1
 Moisture After Test (%): 0.0
 Run Number: 1 • 2 ▲
 Cell Pressure (psi): 65.0
 Test Pressure(psi): 60.0
 Back Pressure(psi): 57.9
 Diff. Head (psi): 2.1
 Flow Rate (cc/sec): 1.90×10^{-2}
 Perm. (cm/sec): 2.49×10^{-5}


SAMPLE DATA:

Sample Identification: Fill No.1

Visual Description:

Remarks:

Maximum Dry Density (pcf): 118.2
 Optimum Moisture Content (%): 12.1
 ASTM(D698)
 Percent Compaction: 95.0%
 Permeameter type: Flexwall
 Sample type: Remolded

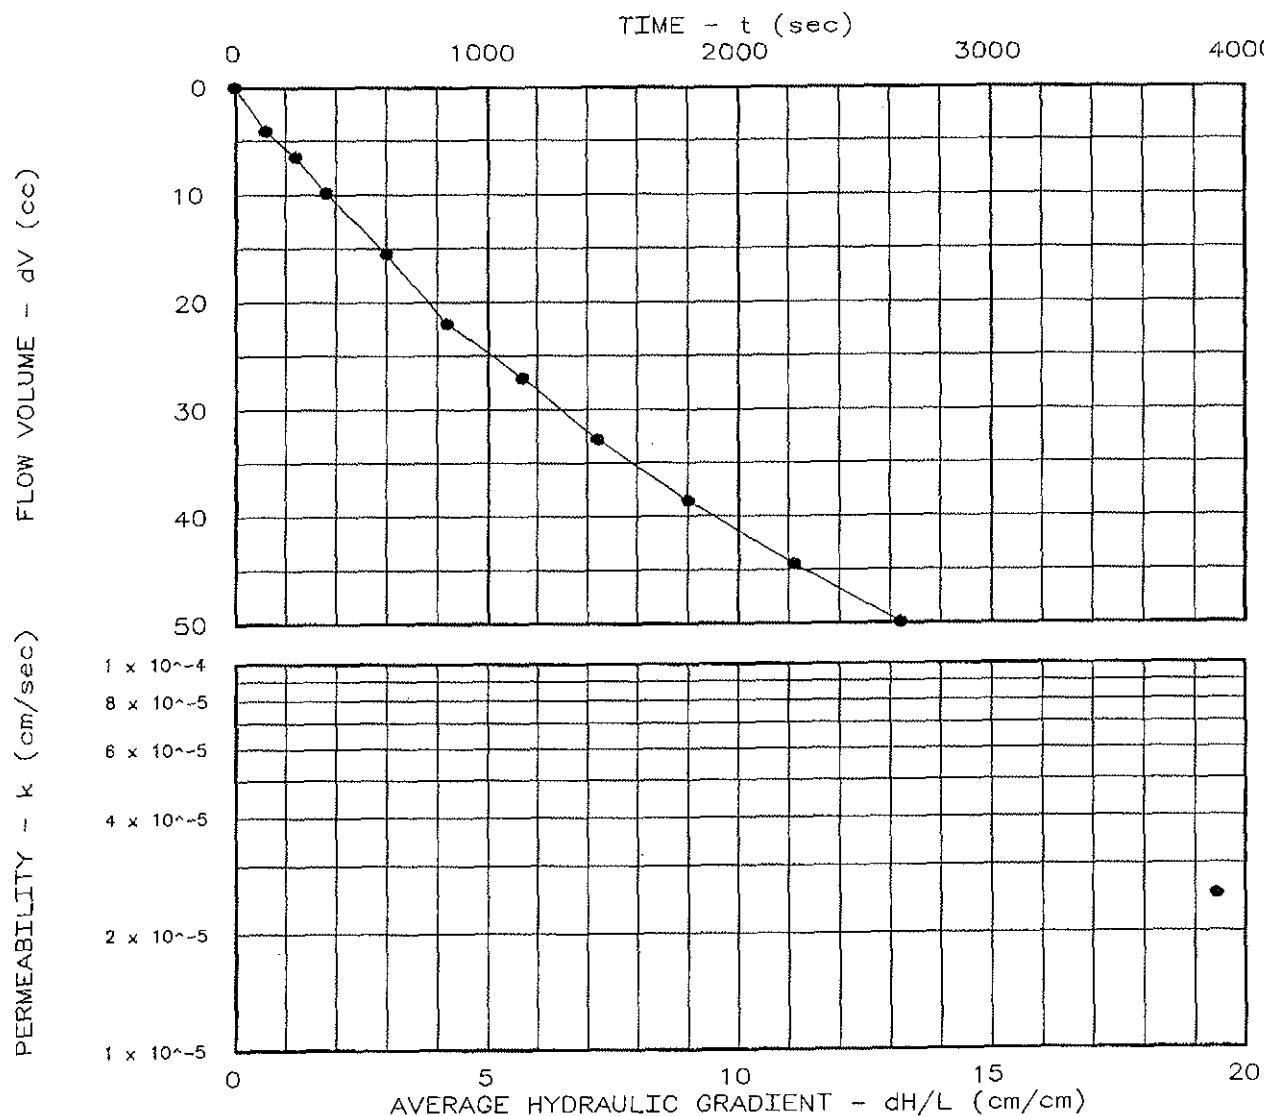

Project: Atlanta Site

Location:

Date: 9/10/2012

Project No.: 114-551057

File No.: 259

Lab No.:

Tested by:


Checked by:

Test: CH - Constant head

PERMEABILITY TEST REPORT

TETRA TECH

Moisture Density Relationship

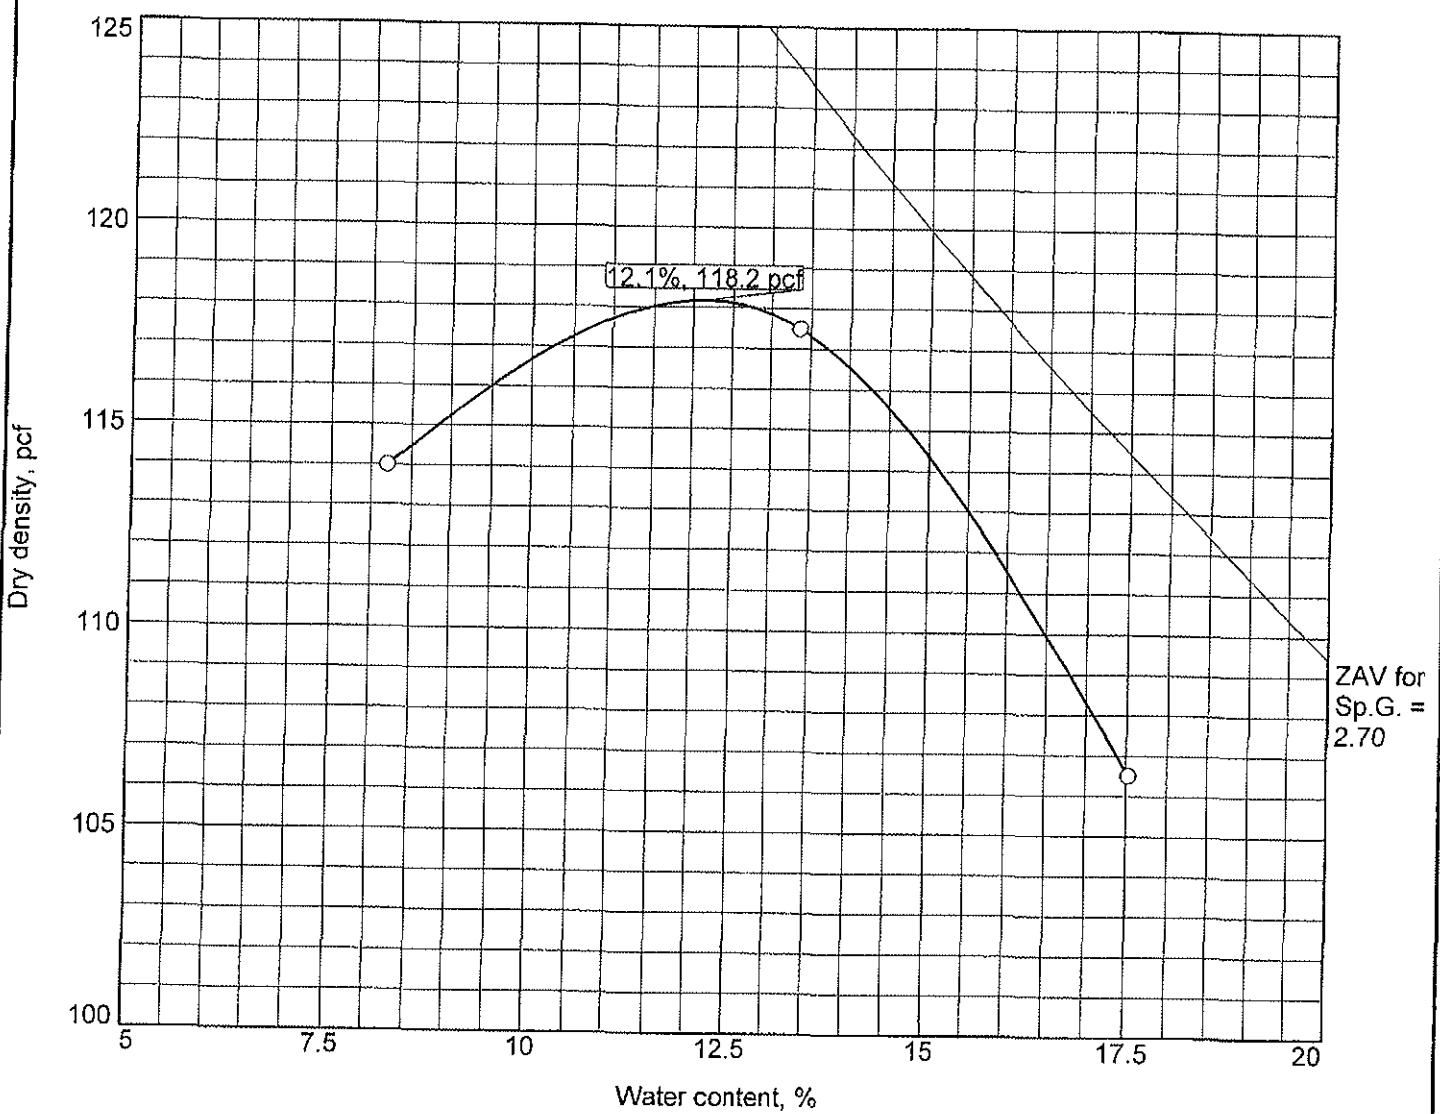

Test specification: ASTM D 698-00a Method A Standard

Elev/ Depth	Classification		Nat. Moist.	Sp.G.	LL	PI	% > #4	% < No.200
	USCS	AASHTO						
				2.70				

TEST RESULTS

Maximum dry density = 118.2 pcf

Optimum moisture = 12.1 %

MATERIAL DESCRIPTION

Project No. 114-551057 Client: Continental Resources
Project: Atlanta Site

Remarks:

Source of Sample: Fill No.1

Tetra Tech, Inc.

Billings, MT

Figure

PERMEABILITY TEST REPORT

TEST DATA:

Specimen Height (cm): 7.50
 Specimen Diameter (cm): 7.07
 Dry Unit Weight (pcf): 112.1
 Moisture Before Test (%): 12.6
 Moisture After Test (%): 0.0
 Run Number: 1 • 2 ▲
 Cell Pressure (psi): 65.0
 Test Pressure(psi): 60.0
 Back Pressure(psi): 57.9
 Diff. Head (psi): 2.1
 Flow Rate (cc/sec): 2.63×10^{-2}
 Perm. (cm/sec): 1.97×10^{-5}


SAMPLE DATA:

Sample Identification: Fill No.2

Visual Description:

Remarks:

Maximum Dry Density (pcf): 118.0
 Optimum Moisture Content (%): 12.6
 ASTM(D698)
 Percent Compaction: 95.0%
 Permeameter type: Flexwall
 Sample type: Remolded

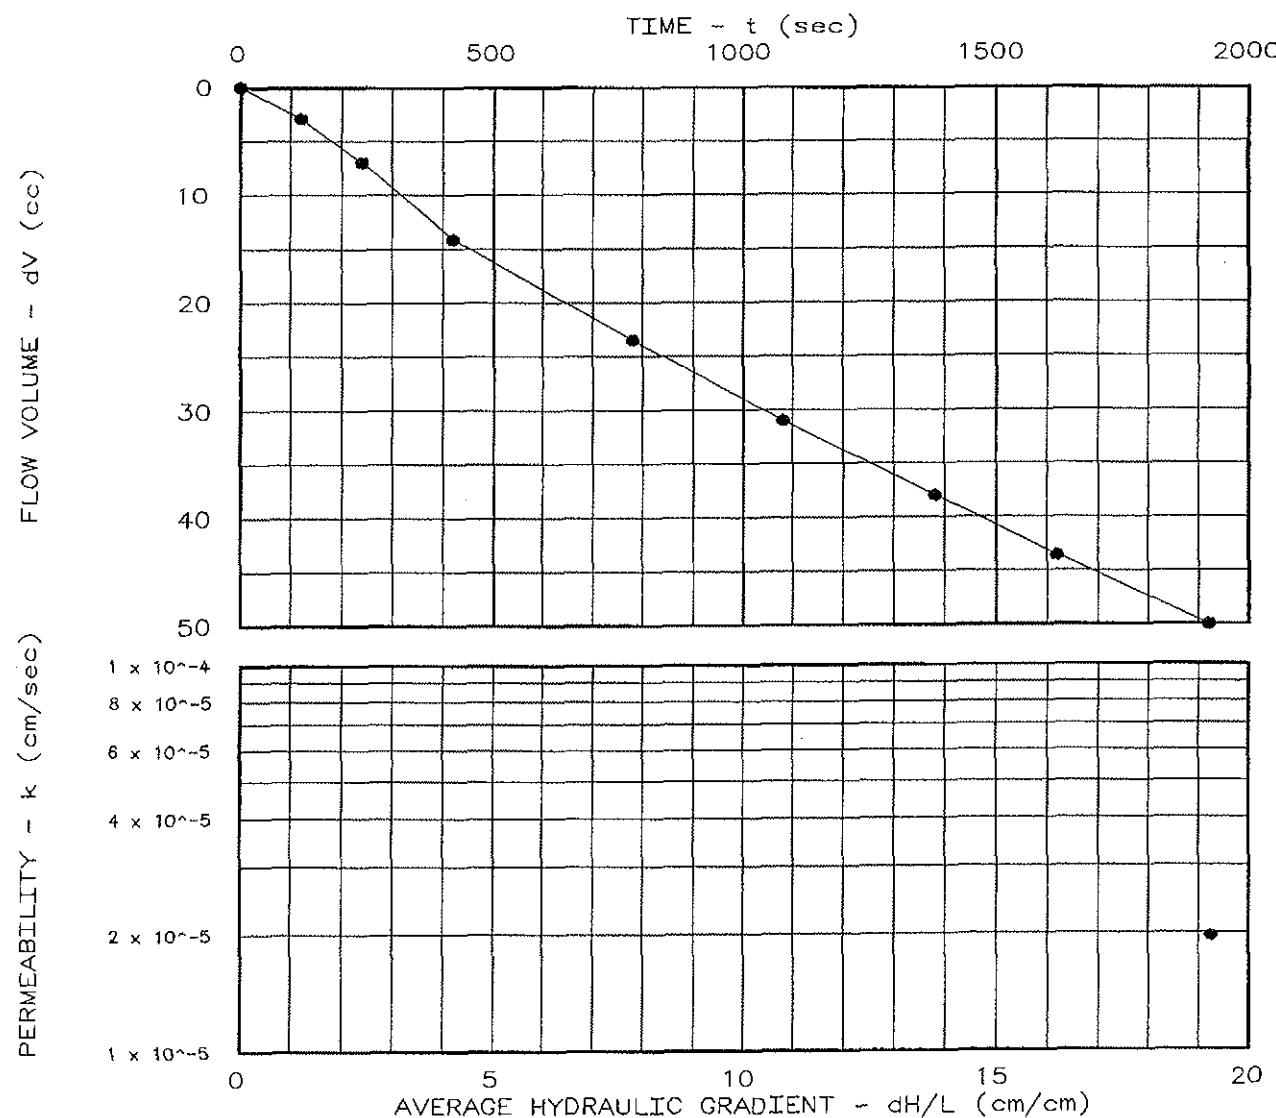

Project: Atlanta Site

Location:

Date: 9/10/2012

Project No.: 114-551057

File No.: 260

Lab No.:

Tested by:


Checked by:

Test: CH - Constant head

PERMEABILITY TEST REPORT

TETRA TECH

Moisture Density Relationship

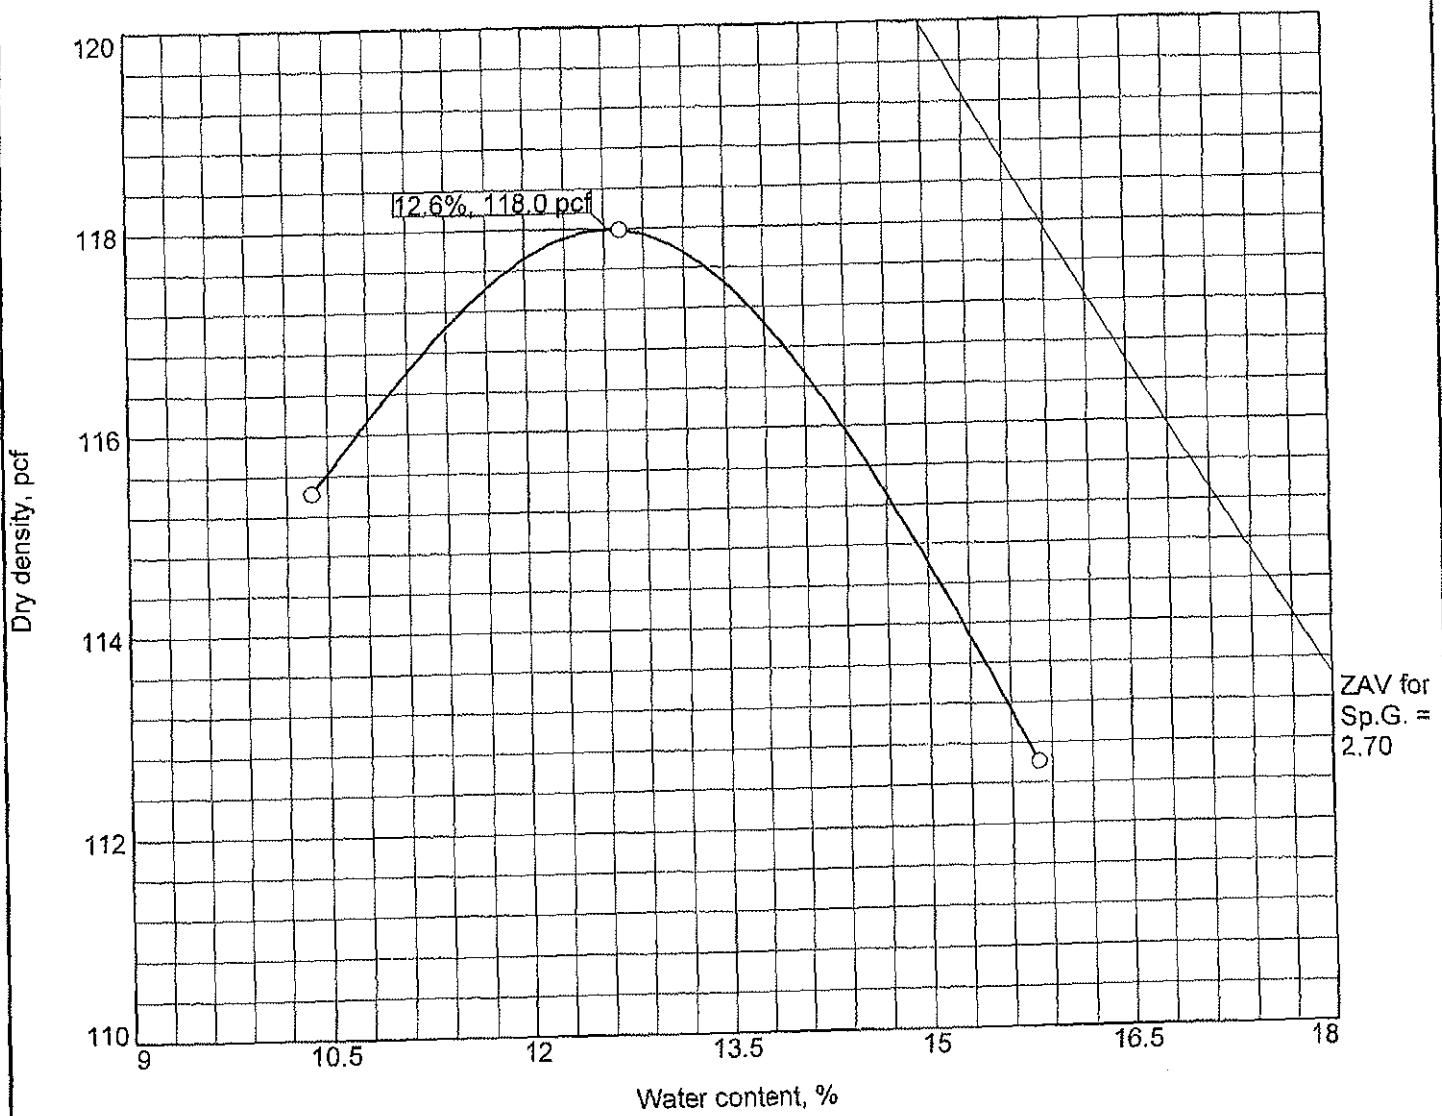

Test specification: ASTM D 698-00a Method A Standard

Elev/ Depth	Classification		Nat. Moist.	Sp.G.	LL	PI	% > #4	% < No.200
	USCS	AASHTO						
				2.70				

TEST RESULTS		MATERIAL DESCRIPTION
Maximum dry density = 118.0 pcf		
Optimum moisture = 12.6 %		
Project No. 114-551057	Client: Continental Resources	Remarks:
Project: Atlanta Site		
<input checked="" type="checkbox"/> Source of Sample: Fill No. 2		
Tetra Tech, Inc.		
Billings, MT		Figure


PERMEABILITY TEST REPORT

TEST DATA:

Specimen Height (cm): 7.50
 Specimen Diameter (cm): 7.07
 Dry Unit Weight (pcf): 98.6
 Moisture Before Test (%): 19.0
 Moisture After Test (%): 0.0
 Run Number: 1 • 2 A
 Cell Pressure (psi): 65.0
 Test Pressure(psi): 60.0
 Back Pressure(psi): 57.9
 Diff. Head (psi): 2.1
 Flow Rate (cc/sec): 1.25×10^{-3}
 Perm. (cm/sec): 1.61×10^{-6}

SAMPLE DATA:

Sample Identification: Cement No.1
 Visual Description:
 Remarks:
 Maximum Dry Density (pcf): 103.7
 Optimum Moisture Content (%): 18.9
 ASTM(D698)
 Percent Compaction: 95.0%
 Permeameter type: Flexwall
 Sample type: Remolded

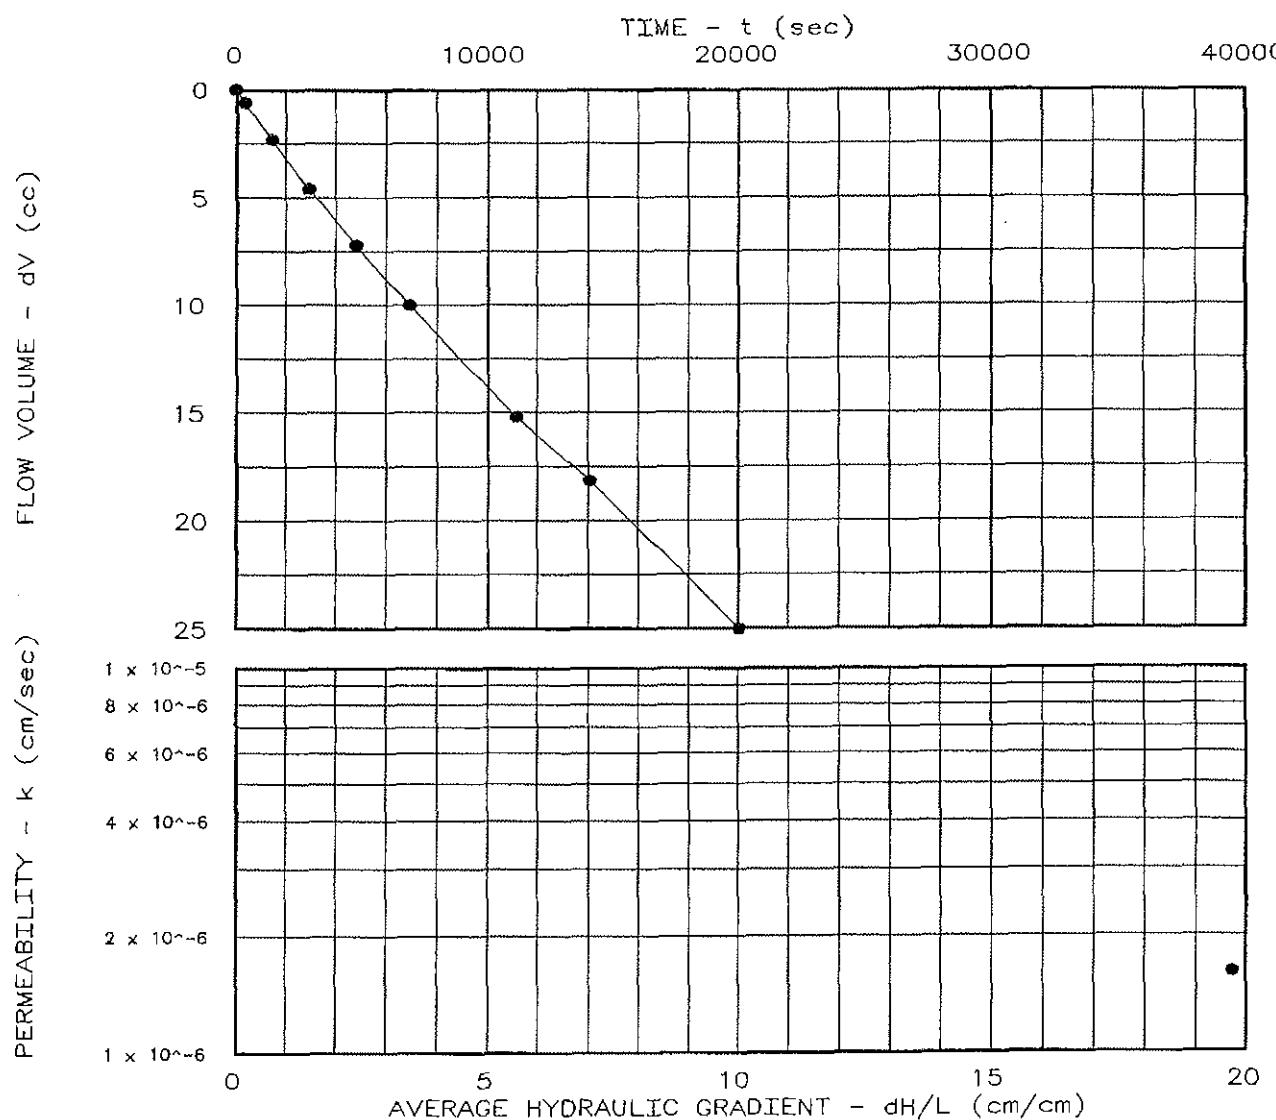

Project: Atlanta Site

Location:

Date: 9/12/2012

Project No.: 114-551057

File No.: 261

Lab No.:

Tested by:


Checked by:

Test: CH - Constant head

PERMEABILITY TEST REPORT

TETRA TECH

Moisture Density Relationship

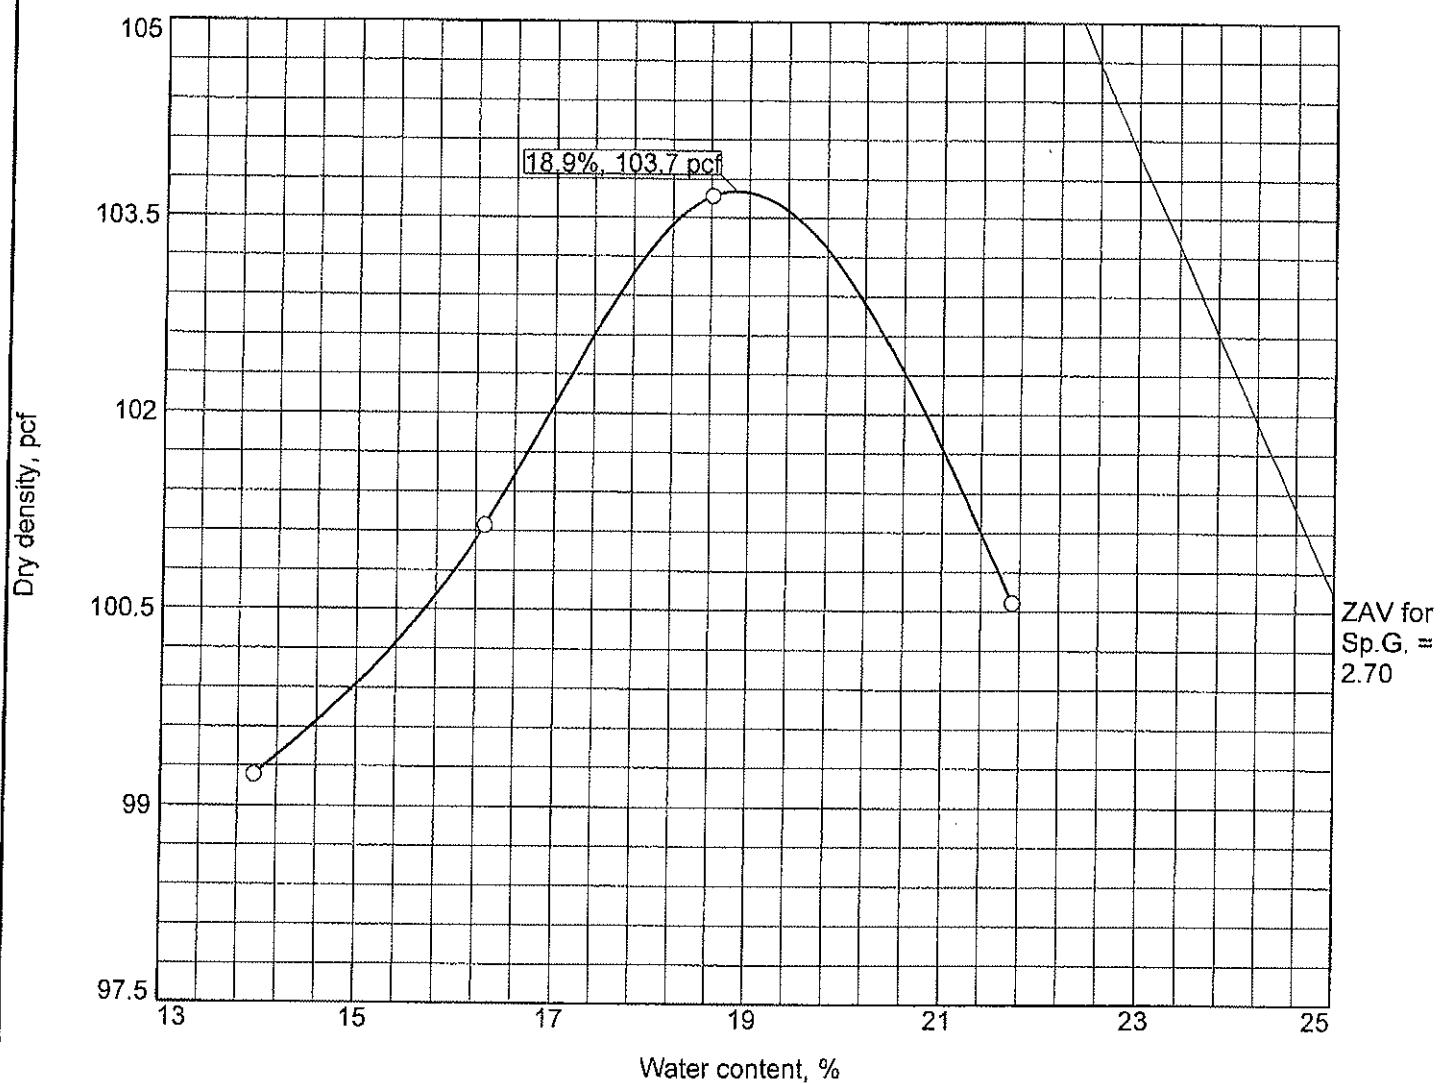

Test specification: ASTM D 698-00a Method A Standard

Elev/ Depth	Classification		Nat. Moist.	Sp.G.	LL	PI	% > #4	% < No.200
	USCS	AASHTO						
				2.70				

TEST RESULTS

MATERIAL DESCRIPTION

Maximum dry density = 103.7 pcf

Optimum moisture = 18.9 %

Project No. 114-551057 Client: Continental Resources
Project: Atlanta Site

Remarks:

○ Source of Sample: Cement No.1

Tetra Tech, Inc.

Billings, MT

Figure


PERMEABILITY TEST REPORT

TEST DATA:

Specimen Height (cm): 7.50
 Specimen Diameter (cm): 7.07
 Dry Unit Weight (pcf): 97.9
 Moisture Before Test (%): 19.0
 Moisture After Test (%): 0.0
 Run Number: 1 2
 Cell Pressure (psi): 65.0
 Test Pressure(psi): 60.0
 Back Pressure(psi): 58.0
 Diff. Head (psi): 2.0
 Flow Rate (cc/sec): 4.84×10^{-2}
 Perm. (cm/sec): 6.51×10^{-5}

SAMPLE DATA:

Sample Identification: Cement No.3
 Visual Description:
 Remarks:
 Maximum Dry Density (pcf): 103.0
 Optimum Moisture Content (%): 19.0
 ASTM(D698)
 Percent Compaction: 95.0%
 Permeameter type: Flexwall
 Sample type: Remolded

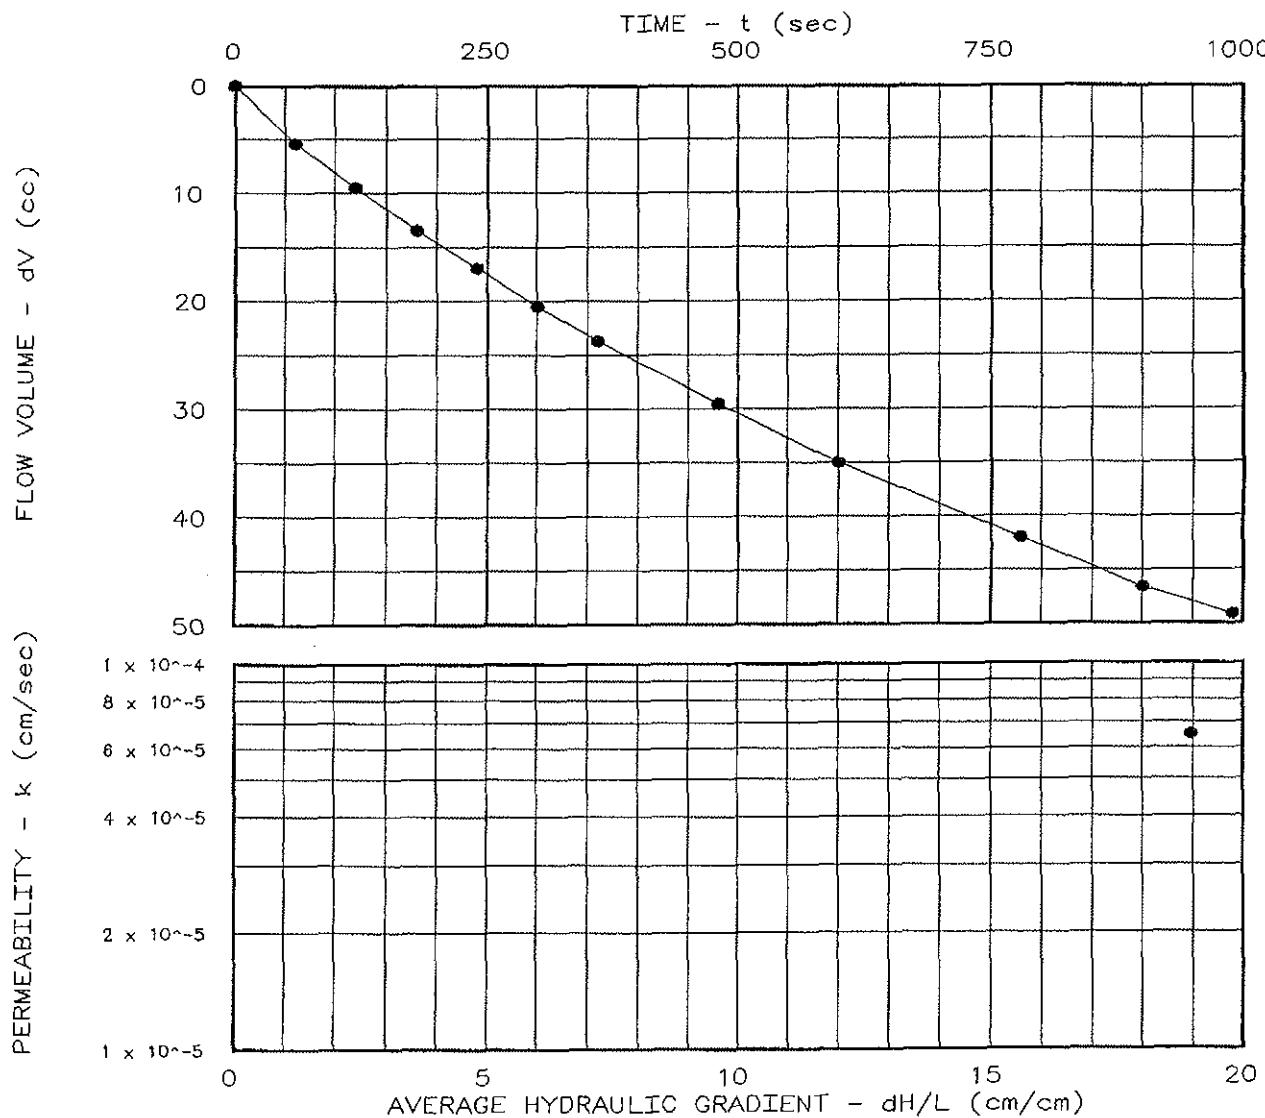

Project: Atlanta Site

Location:

Date: 9/12/12

Project No.: 114-551057

File No.: 262

Lab No.:

Tested by:


Checked by:

Test: CH - Constant head

PERMEABILITY TEST REPORT

TETRA TECH

Moisture Density Relationship

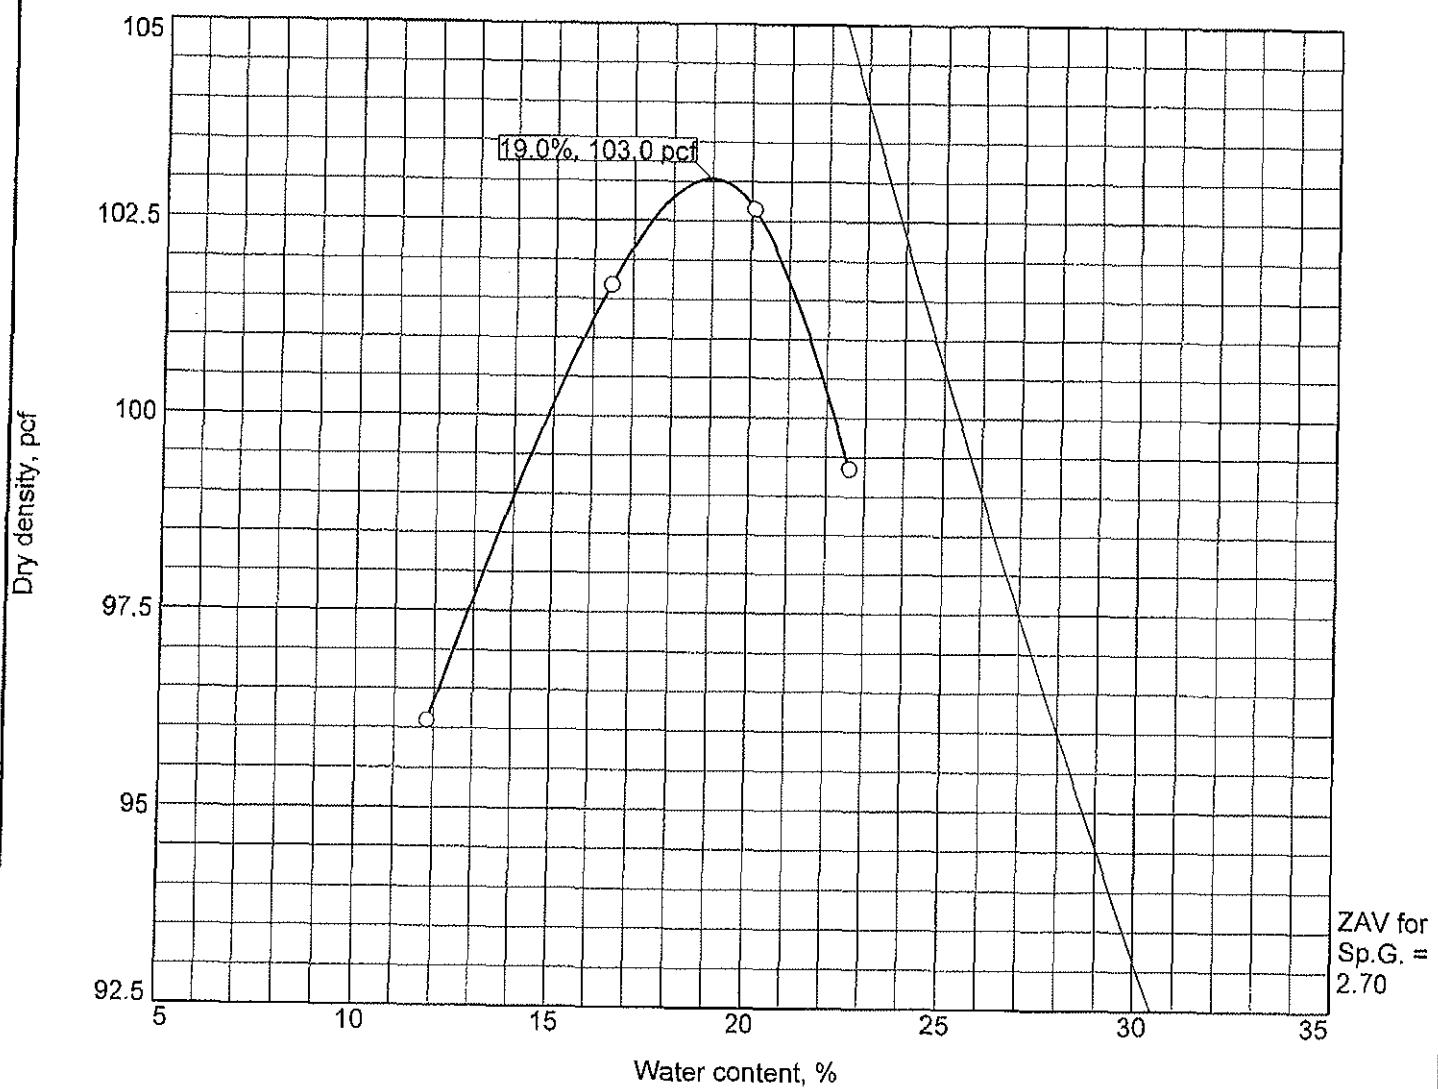

Test specification: ASTM D 698-00a Method A Standard

Elev/ Depth	Classification		Nat. Moist.	Sp.G.	LL	PI	% > #4	% < No.200
	USCS	AASHTO						
				2.70				

TEST RESULTS

Maximum dry density = 103.0 pcf

Optimum moisture = 19.0 %

MATERIAL DESCRIPTION

Project No. 114-551057 Client: Continental Resources
Project: Atlanta Site

Remarks:

Source of Sample: Cement No. 3

Tetra Tech, Inc.

Billings, MT

Figure


PERMEABILITY TEST REPORT

TEST DATA:

Specimen Height (cm): 7.50
 Specimen Diameter (cm): 7.07
 Dry Unit Weight (pcf): 102.4
 Moisture Before Test (%): 16.7
 Moisture After Test (%): 0.0
 Run Number: 1 • 2 A
 Cell Pressure (psi): 65.0
 Test Pressure (psi): 60.0
 Back Pressure (psi): 58.1
 Diff. Head (psi): 1.9
 Flow Rate (cc/sec): 3.50×10^{-2}
 Perm. (cm/sec): 4.90×10^{-5}

SAMPLE DATA:

Sample Identification: Cement No.2
 Visual Description:
 Remarks:
 Maximum Dry Density (pcf): 107.7
 Optimum Moisture Content (%): 16.7
 ASTM(D698)
 Percent Compaction: 95.0%
 Permeometer type: Flexwall
 Sample type: Remolded

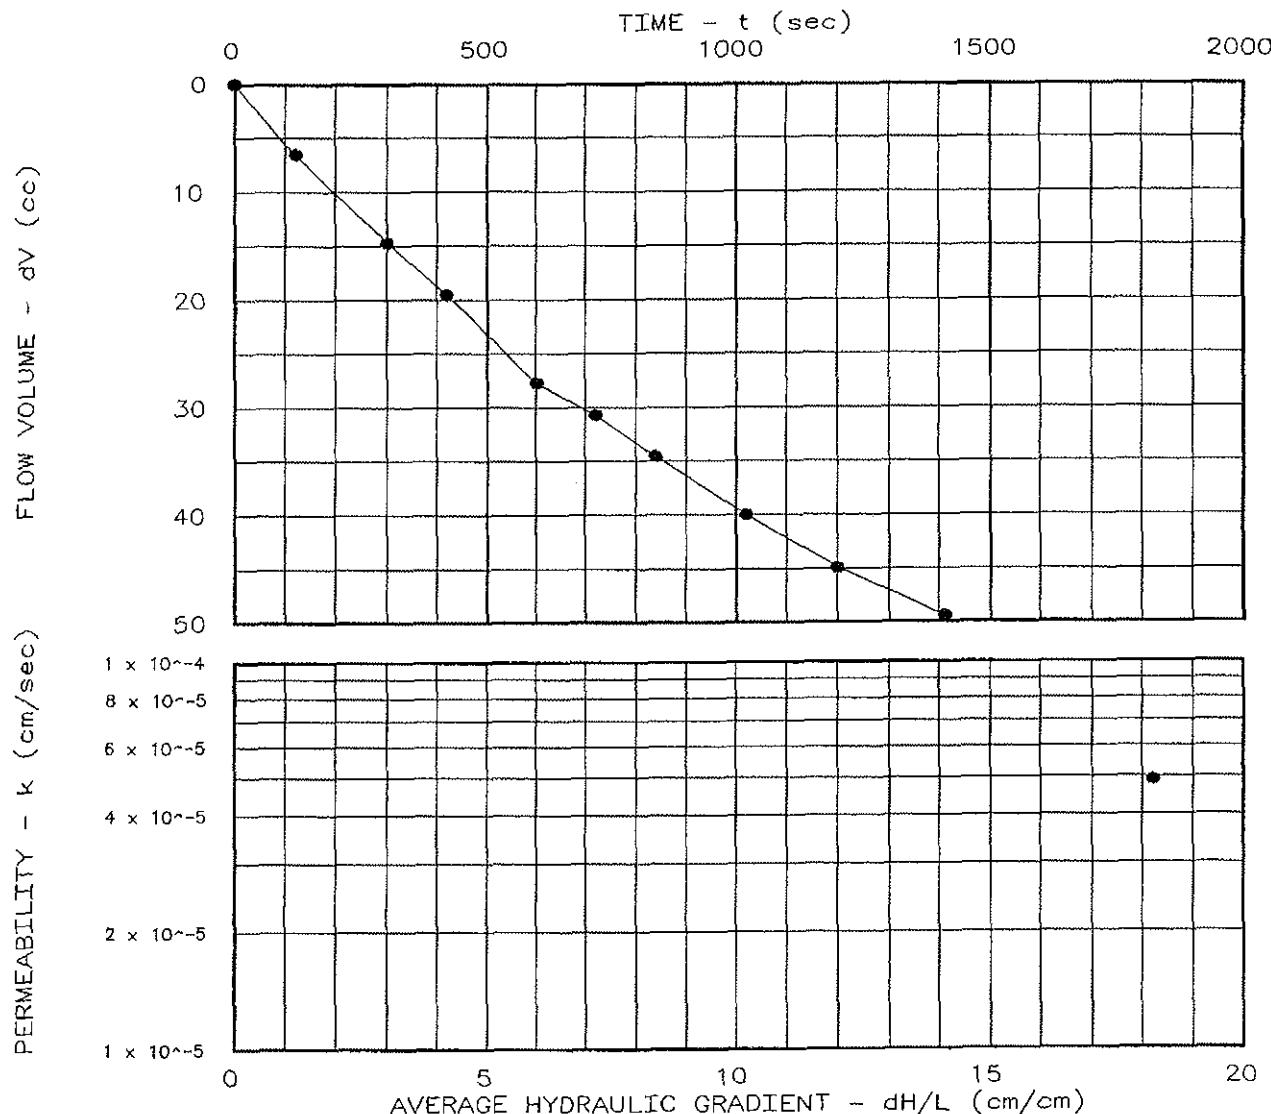

Project: Atlanta Site

Location:

Date: 9/12/12

Project No.: 114-551057

File No.: 263

Lab No.:

Tested by:


Checked by:

Test: CH - Constant head

PERMEABILITY TEST REPORT

TETRA TECH

Moisture Density Relationship

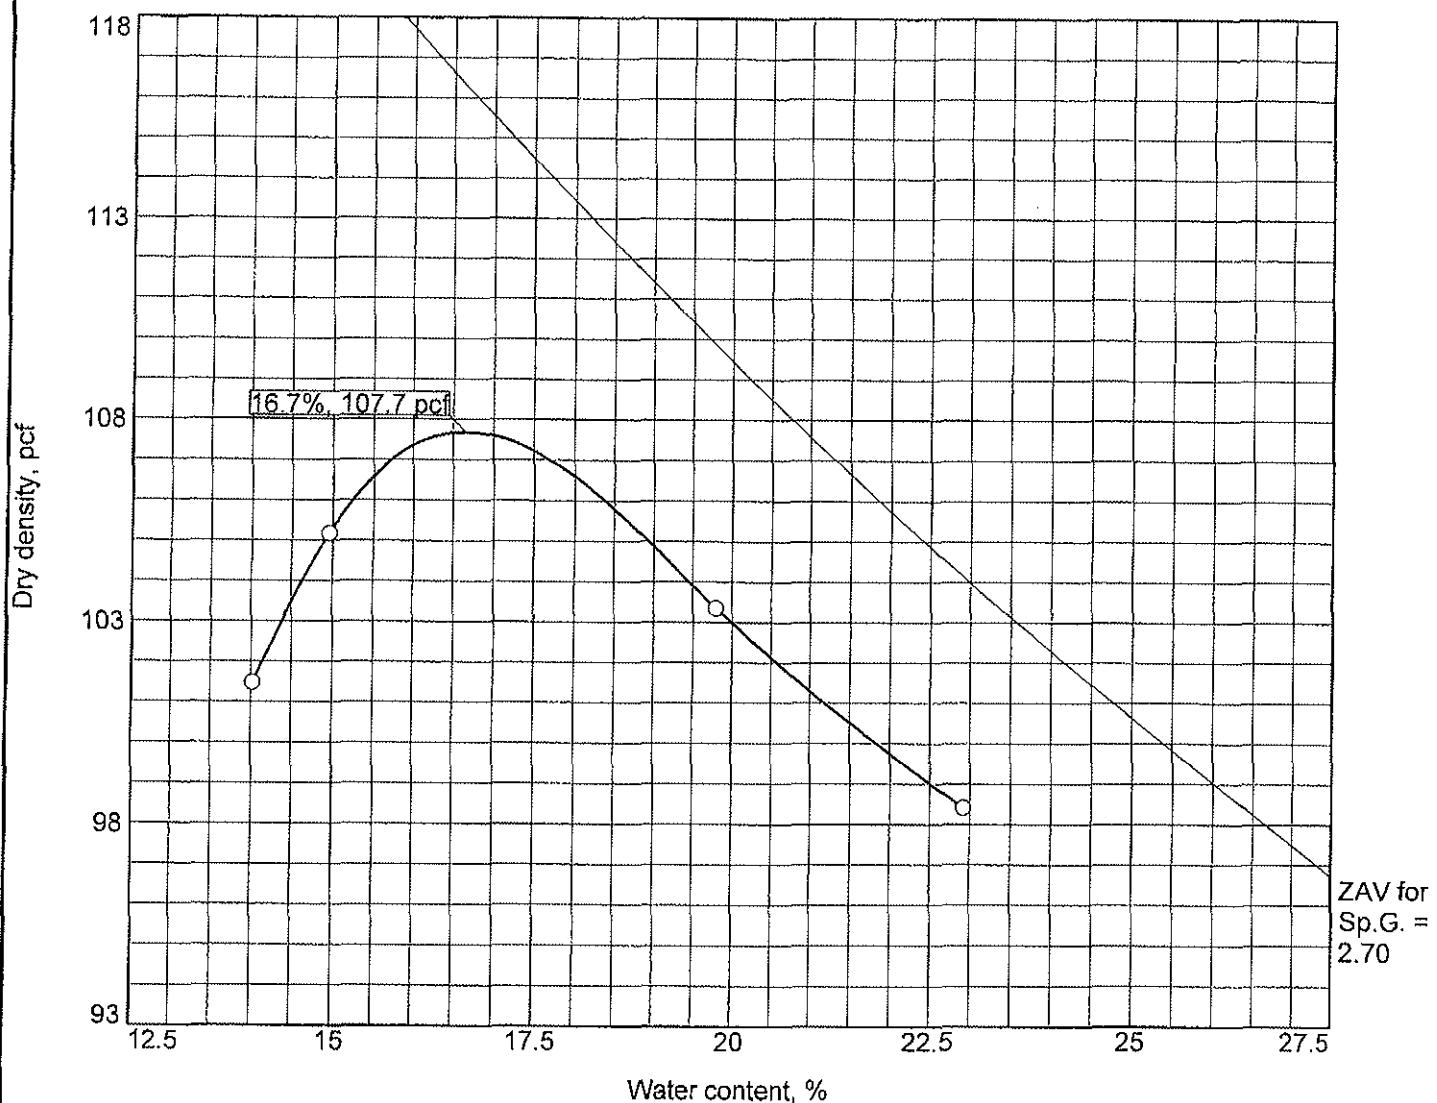

Test specification: ASTM D 698-00a Method A Standard

Elev/ Depth	Classification		Nat. Moist.	Sp.G.	LL	PI	% > #4	% < No.200
	USCS	AASHTO						
				2.70				

TEST RESULTS		MATERIAL DESCRIPTION
Maximum dry density = 107.7 pcf		
Optimum moisture = 16.7 %		
Project No. 114-551057 Client: Continental Resources Project: Atlanta Site		Remarks:
<input type="checkbox"/> Source of Sample: Cement No. 2 Tetra Tech, Inc.		Billings, MT
		Figure


PERMEABILITY TEST REPORT

TEST DATA:

Specimen Height (cm): 7.50
 Specimen Diameter (cm): 7.07
 Dry Unit Weight (pcf): 103.7
 Moisture Before Test (%): 17.2
 Moisture After Test (%): 0.0
 Run Number: 1 • 2 ▲
 Cell Pressure (psi): 65.0
 Test Pressure(psi): 60.0
 Back Pressure(psi): 57.9
 Diff. Head (psi): 2.1
 Flow Rate (cc/sec): 4.99×10^{-5}
 Perm. (cm/sec): 6.35×10^{-8}

SAMPLE DATA:


Sample Identification: Fill No. 4
 Visual Description:
 Remarks:
 Maximum Dry Density (pcf): 109.1
 Optimum Moisture Content (%): 17.2
 ASTM(D698)
 Percent Compaction: 95.0%
 Permeameter type: Flexwall
 Sample type: Remolded

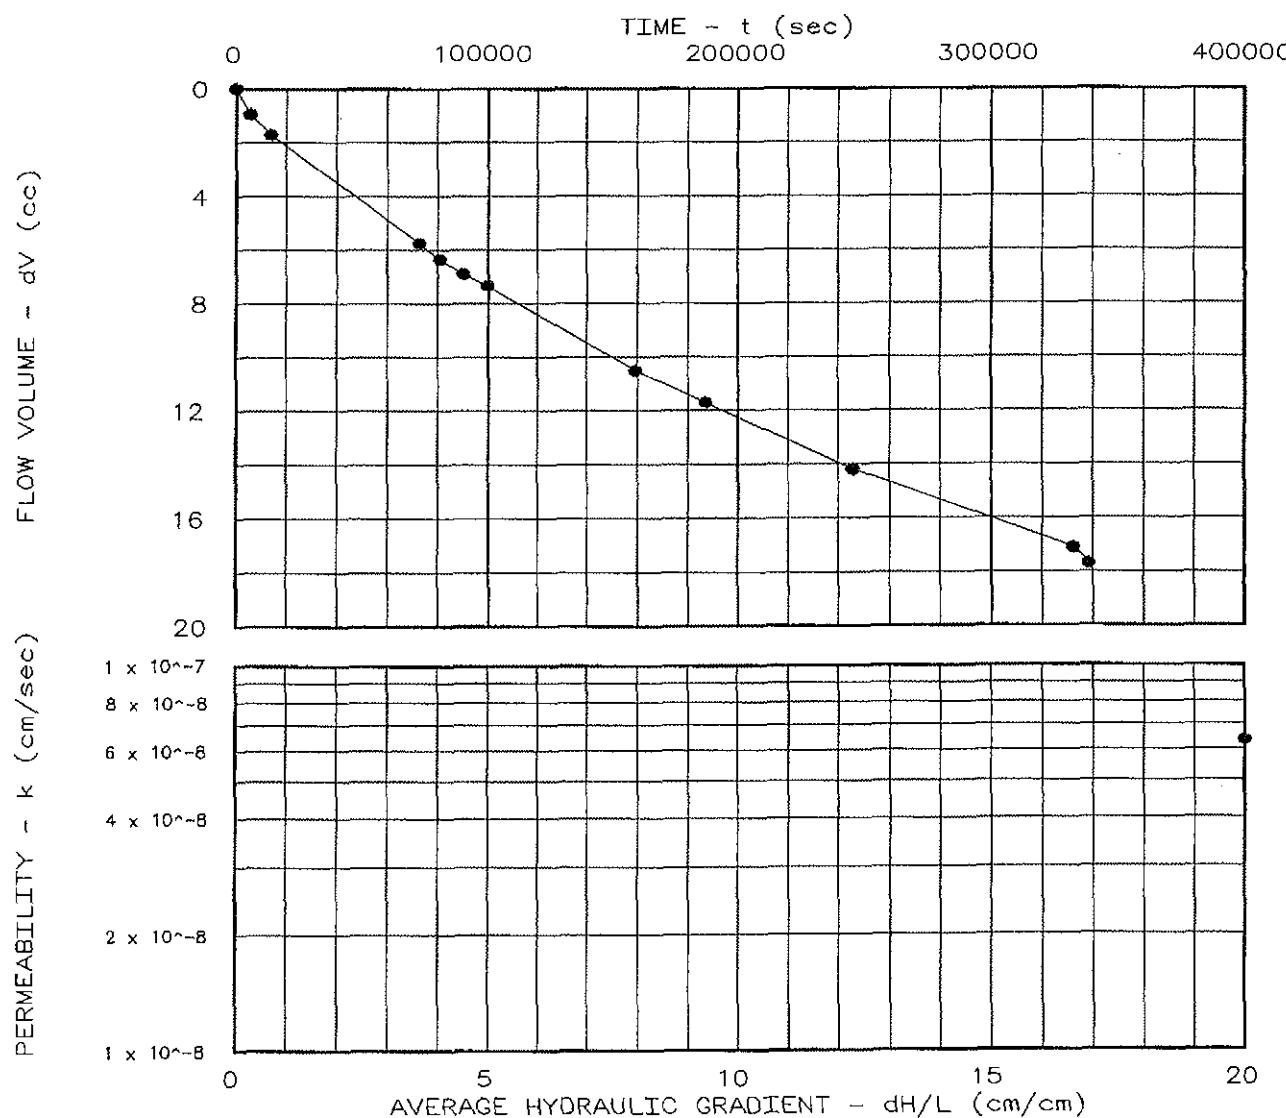

Project: Atlanta Site
 Location:
 Date: 9/14/2012

Project No.: 114-551057
 File No.: 264
 Lab No.:
 Tested by:
 Checked by:
 Test: CH - Constant head

Moisture Density Relationship

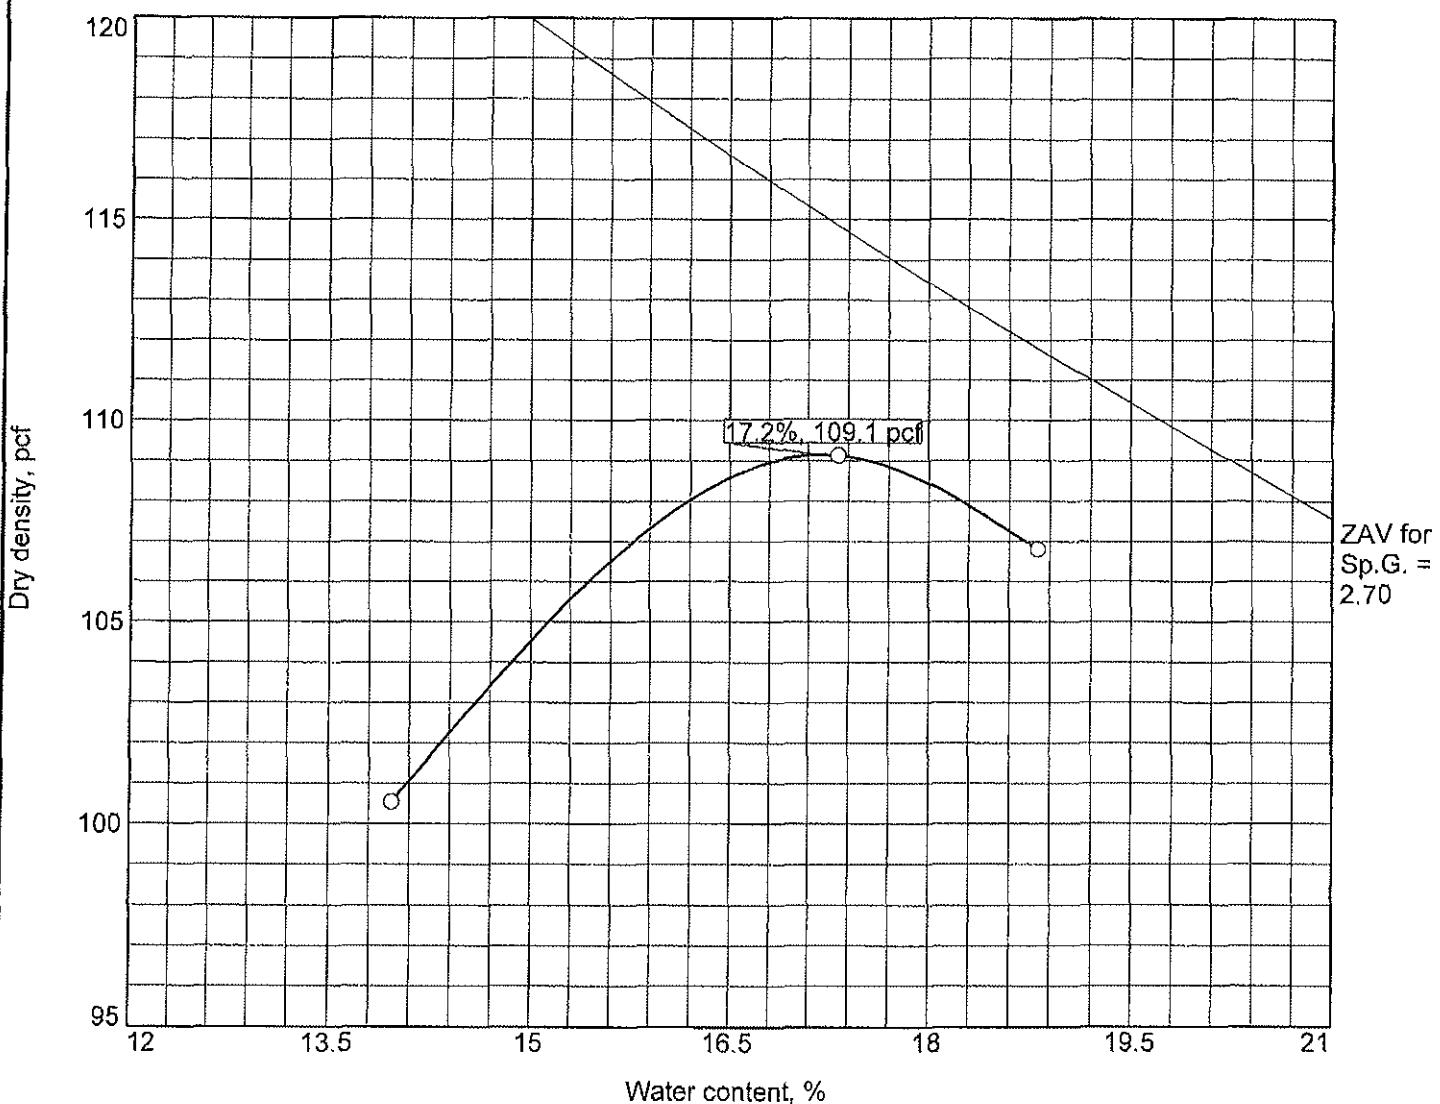

Test specification: ASTM D 698-00a Method A Standard

Elev/ Depth	Classification		Nat. Moist.	Sp.G.	LL	PI	% > #4	% < No.200
	USCS	AASHTO						
				2.70				

TEST RESULTS		MATERIAL DESCRIPTION
Maximum dry density = 109.1 pcf		
Optimum moisture = 17.2 %		
Project No. 114-551057 Client: Continental Resources Project: Atlanta Site		Remarks:
<input type="radio"/> Source of Sample: Fill No. 4 Tetra Tech, Inc.		Figure
Billings, MT		



www.energylab.com
Analytical Excellence Since 1892

Helena, MT 877-472-0711 • Billings, MT 800-735-4489 • Casper, WY 800-235-0516
Gillette, WY 800-606-7175 • Rapid City, SD 800-672-1229 • College Station, TX 800-690-2218

ANALYTICAL SUMMARY REPORT

September 06, 2012

Continental Resources
PO Box 268870
Oklahoma City, OK 73126-8870

Workorder No.: B12082786

Project Name: Atlanta Site

Energy Laboratories Inc Billings MT received the following 4 samples for Continental Resources on 8/30/2012 for analysis.

Sample ID	Client Sample ID	Collect Date	Receive Date	Matrix	Test
B12082786-001	Original Material, From Cut 08/29/12 19:00	08/30/12		Soil	Cation Exchange Capacity Cations, Saturated Paste Conductivity pH, Saturated Paste NH4AC Soil Extraction for CEC Saturated Paste Extraction Sodium Adsorption Ratio
B12082786-002	Fill #1	08/29/12 19:00	08/30/12	Soil	Same As Above
B12082786-003	Fill #2	08/29/12 19:00	08/30/12	Soil	Same As Above
B12082786-004	Fill #3	08/29/12 19:00	08/30/12	Soil	Same As Above

The analyses presented in this report were performed by Energy Laboratories, Inc., 1120 S 27th St., Billings, MT 59101, unless otherwise noted. Any exceptions or problems with the analyses are noted in the Laboratory Analytical Report, the QA/QC Summary Report, or the Case Narrative.

The results as reported relate only to the item(s) submitted for testing.

If you have any questions regarding these test results, please call.

Report Approved By:

Sonye Mallott



LABORATORY ANALYTICAL REPORT

Prepared by Billings, MT Branch

Client: Continental Resources

Project: Atlanta Site

Client Sample ID: Original Material, From Cut

Location: E-1180177.20, N-421287.75, Elv. 1940.40

Lab ID: B12082786-001

Report Date: 09/06/12

Collection Date: 08/29/12 19:00

Date Received: 08/30/12

Sampled By: Spencer Ingalls

Analyses

Result Units Qualifier Method Analysis Date / By

SATURATED PASTE

pH, sat. paste	7.8 s.u.	ASAM10-3.	09/06/12 16:30 / srm
Conductivity, sat. paste	4.8 mmhos/cm	ASA10-3	09/06/12 16:30 / srm
Calcium, sat. paste	24.4 meq/l.	SW6010B	09/05/12 13:07 / rh
Magnesium, sat. paste	29.5 meq/L	SW6010B	09/05/12 13:07 / rh
Sodium, sat. paste	18.7 meq/L	D	SW6010B 09/05/12 13:07 / rh
Sodium Adsorption Ratio (SAR)	3.60 unitless		Calculation 09/06/12 16:30 / srm

CHEMICAL CHARACTERISTICS

Cation Exchange Capacity	19.8 meq/100g	D	SW6010B	09/06/12 15:11 / rh
--------------------------	---------------	---	---------	---------------------

Report Definitions: RL - Analyte reporting limit.
QCL - Quality control limit.
D - RL increased due to sample matrix.

MCL - Maximum contaminant level.
ND - Not detected at the reporting limit.



LABORATORY ANALYTICAL REPORT

Prepared by Billings, MT Branch

Client: Continental Resources
Project: Atlanta Site
Client Sample ID: Fill #1
Location: E-1179926.05, N-421267.60, Elv. 1937.65
Lab ID: B12082786-002

Report Date: 09/06/12
Collection Date: 09/29/12 19:00
Date Received: 08/30/12
Sampled By: Spencer Ingalls

Analytes	Result	Units	Qualifier	Method	Analysis Date / By
SATURATED PASTE					
pH, sat. paste	7.7	s.u.		ASAM10-3	09/06/12 16:30 / sm
Conductivity, sat. paste	2.8	mmhos/cm		ASA10-3	09/06/12 16:30 / sm
Calcium, sat. paste	14.2	meq/L		SW6010B	09/05/12 13:14 / rh
Magnesium, sat. paste	20.1	meq/L		SW6010B	09/05/12 13:14 / rh
Sodium, sat. paste	5.61	meq/L	D	SW6010B	09/05/12 13:14 / rh
Sodium Adsorption Ratio (SAR)	1.35	unitless		Calculation	09/06/12 16:30 / sm
CHEMICAL CHARACTERISTICS					
Cation Exchange Capacity	15.1	meq/100g	D	SW6010B	09/06/12 15:15 / rh

Report Definitions: RL - Analyte reporting limit.
QCL - Quality control limit.
D - RL increased due to sample matrix.

MCL - Maximum contaminant level.
ND - Not detected at the reporting limit.



LABORATORY ANALYTICAL REPORT

Prepared by Billings, MT Branch

Client: Continental Resources
Project: Atlanta Site
Client Sample ID: Fill #2
Location: E-1179924.40, N-421196.70, Elv. 1937.95
Lab ID: B12002786-003

Report Date: 09/06/12
Collection Date: 08/29/12 19:00
Date Received: 08/30/12
Sampled By: Spencer Ingalls

Analyses	Result	Units	Qualifier	Method	Analysis Date / By
SATURATED PASTE					
pH, sat. paste	8.1	s.u.		ASAm10-3,	09/06/12 16:30 / srm
Conductivity, sat. paste	1.2	mmhos/cm		ASA10-3	09/06/12 16:30 / srm
Calcium, sat. paste	2.59	meq/L		SW6010B	09/05/12 13:28 / rh
Magnesium, sat. paste	8.07	meq/L		SW6010B	09/05/12 13:28 / rh
Sodium, sat. paste	3.40	meq/L		SW6010B	09/05/12 13:28 / rh
Sodium Adsorption Ratio (SAR)	1.47	unitless		Calculation	09/06/12 16:30 / srm
CHEMICAL CHARACTERISTICS					
Cation Exchange Capacity	12.3	meq/100g	D	SW6010B	09/06/12 15:22 / rh

Report: RL - Analyte reporting limit.
Definitions: QCL - Quality control limit.
D - RL increased due to sample matrix.

MCL - Maximum contaminant level.
ND - Not detected at the reporting limit.



LABORATORY ANALYTICAL REPORT

Prepared by Billings, MT Branch

Client: Continental Resources

Project: Atlanta Site

Client Sample ID: Fill #3

Location: E-1179963.65, N-421120.95, Elv. 1937.90

Lab ID: B120827B6-004

Report Date: 09/06/12

Collection Date: 08/29/12 19:00

Date Received: 08/30/12

Sampled By: Spencer Ingalls

Analytes

Result Units Qualifier Method Analysis Date / By

SATURATED PASTE

pH, sat. paste	7.9 s.u.	ASAM10-3	09/06/12 16:30 / srn
Conductivity, sat. paste	4.5 mmhos/cm	ASA10-3	09/06/12 16:30 / srn
Calcium, sat. paste	25.1 meq/L	SW6010B	09/05/12 13:32 / rh
Magnesium, sat. paste	36.7 meq/L	SW6010B	09/05/12 13:32 / rh
Sodium, sat. paste	11.5 meq/L	D	SW6010B 09/05/12 13:32 / rh
Sodium Adsorption Ratio (SAR)	2.07 unitless		Calculation 09/06/12 16:30 / srn

CHEMICAL CHARACTERISTICS

Cation Exchange Capacity	16.4 meq/100g	D	SW6010B	09/06/12 15:29 / rh
--------------------------	---------------	---	---------	---------------------

Report: RL - Analyte reporting limit.
Definitions: QCL - Quality control limit.
D - RL increased due to sample matrix.

MCL - Maximum contaminant level.
ND - Not detected at the reporting limit.



QA/QC Summary Report

Prepared by Billings, MT Branch

Client: Continental Resources

Report Date: 09/06/12

Project: Atlanta Site

Work Order: B12082786

Analyte	Result	Units	RL	%REC	Low Limit	High Limit	RPD	RPDLimit	Qual
Method: ASA10-3									Batch: R191314
Sample ID: B12082786-001A DUP	Sample Duplicate								09/06/12 16:30
Conductivity, sat. paste	4.86	mmhos/cm	0.10				1.2		30
Sample ID: LCS-1209061630	Laboratory Control Sample								09/06/12 16:30
Conductivity, sat. paste	7.54	mmhos/cm	0.10	97	50	150			

Qualifiers:

RL - Analyte reporting limit.

ND - Not detected at the reporting limit.



QA/QC Summary Report

Prepared by Billings, MT Branch

Client: Continental Resources

Report Date: 09/06/12

Project: Atlanta Site

Work Order: B12082786

Analyte	Result	Units	RL	%REC	Low Limit	High Limit	RPD	RPDLimit	Qual
Method: ASAM10-9.2									
Sample ID: B12082786-001A DUP pH, sat. paste	Sample Duplicate 7.60	s.u.	0.10		Run: MISC-SOIL_120906B		2.6	10	09/06/12 16:30
Sample ID: LCS-1209061630 pH, sat. paste	Laboratory Control Sample 7.00	s.u.	0.10	99	90	110			09/06/12 16:30

Qualifiers:

RL - Analyte reporting limit.

ND - Not detected at the reporting limit.



QA/QC Summary Report

Prepared by Billings, MT Branch

Client: Continental Resources

Report Date: 09/06/12

Project: Atlanta Site

Work Order: B12082786

Analyte	Result	Units	RL	%REC	Low Limit	High Limit	RPD	RPDLimit	Qual
Method: Calculation	Batch: R191314								
Sample ID: B12082786-001A DUP	Sample Duplicate				Run: MISC-SOIL_120906B				09/06/12 16:30
Sodium Adsorption Ratio (SAR)	3.86	unitless	0.010				6.7		30
Sample ID: LCS-1209061630	Laboratory Control Sample				Run: MISC-SOIL_120906B				09/06/12 16:30
Sodium Adsorption Ratio (SAR)	5.11	unitless	0.010	83	50	150			

Qualifiers:

RL - Analyte reporting limit.

ND - Not detected at the reporting limit.



QA/QC Summary Report

Prepared by Billings, MT Branch

Client: Continental Resources

Report Date: 09/06/12

Project: Atlanta Site

Work Order: B12082786

Analyte	Result	Units	RL	%REC	Low Limit	High Limit	RPD	RPDLimit	Qual
Method: SW6010B									Batch: 65170
Sample ID: LCS-65170	Laboratory Control Sample				Run: ICP201-B_120905A				09/05/12 13:03
Calcium, sat. paste	46.4	meq/L	0.050	88	50	150			
Magnesium, sat. paste	29.0	meq/L	0.082	86	50	150			
Sodium, sat. paste	32.0	meq/L	0.16	77	50	150			
Sample ID: B12082786-001A DUP	Sample Duplicate				Run: ICP201-B_120905A				09/05/12 13:10
Calcium, sat. paste	25.2	meq/L	0.050				3.1		30
Magnesium, sat. paste	31.0	meq/L	0.082				4.8		30
Sodium, sat. paste	20.4	meq/L	0.081				8.7		30
Sample ID: B12082786-002AMS2	Sample Matrix Spike				Run: ICP201-B_120905A				09/05/12 13:25
Calcium, sat. paste	26.8	meq/L	0.050	101	50	150			
Magnesium, sat. paste	39.5	meq/L	0.082	94	50	150			
Sodium, sat. paste	16.1	meq/L	0.084	96	50	150			
Method: SW6010B									Batch: 65201
Sample ID: LCS-65201	Laboratory Control Sample				Run: ICP201-B_120905B				09/06/12 15:08
Cation Exchange Capacity	22.4	meq/100g	0.16	90	60	140			
Sample ID: B12082786-002A DUP	Sample Duplicate				Run: ICP201-B_120905B				09/06/12 15:18
Cation Exchange Capacity	13.8	meq/100g	0.16				8.8		50
Sample ID: B12082786-003AMS2	Sample Matrix Spike				Run: ICP201-B_120905B				09/06/12 15:25
Cation Exchange Capacity	33.6	meq/100g	0.17	98	50	150			

Qualifiers:

RL - Analyte reporting limit.

ND - Not detected at the reporting limit.



Standard Reporting Procedures

Lab measurement of analytes considered field parameters that require analysis within 15 minutes of sampling such as pH, Dissolved Oxygen and Residual Chlorine, are qualified as being analyzed outside of recommended holding time.

Solid/soil samples are reported on a wet weight basis (as received) unless specifically indicated. If moisture corrected, data units are typically noted as -dry. For agricultural and mining soil parameters/characteristics, all samples are dried and ground prior to sample analysis.

Workorder Receipt Checklist

Continental Resources

B12082786

Login completed by: Randa Nees

Date Received: 8/30/2012

Reviewed by: BL2000\kmcdonald

Received by: jrz

Reviewed Date: 8/30/2012

Carrier Hand Del
name:

Shipping container/cooler in good condition?	Yes <input checked="" type="checkbox"/>	No <input type="checkbox"/>	Not Present <input type="checkbox"/>
Custody seals intact on shipping container/cooler?	Yes <input type="checkbox"/>	No <input type="checkbox"/>	Not Present <input checked="" type="checkbox"/>
Custody seals intact on sample bottles?	Yes <input type="checkbox"/>	No <input type="checkbox"/>	Not Present <input checked="" type="checkbox"/>
Chain of custody present?	Yes <input checked="" type="checkbox"/>	No <input type="checkbox"/>	
Chain of custody signed when relinquished and received?	Yes <input checked="" type="checkbox"/>	No <input type="checkbox"/>	
Chain of custody agrees with sample labels?	Yes <input checked="" type="checkbox"/>	No <input type="checkbox"/>	
Samples in proper container/bottle?	Yes <input checked="" type="checkbox"/>	No <input type="checkbox"/>	
Sample containers intact?	Yes <input checked="" type="checkbox"/>	No <input type="checkbox"/>	
Sufficient sample volume for indicated test?	Yes <input checked="" type="checkbox"/>	No <input type="checkbox"/>	
All samples received within holding time? (Exclude analyses that are considered field parameters such as pH, DO, Res Cl, Sulfite, Ferrous Iron, etc.)	Yes <input checked="" type="checkbox"/>	No <input type="checkbox"/>	
Temp Blank received?	Yes <input type="checkbox"/>	No <input checked="" type="checkbox"/>	Not Applicable <input type="checkbox"/>
Container/Temp Blank temperature:	24.6°C No Ice		
Water + VOA vials have zero headspace?	Yes <input type="checkbox"/>	No <input type="checkbox"/>	No VOA vials submitted <input checked="" type="checkbox"/>
Water + pH acceptable upon receipt?	Yes <input type="checkbox"/>	No <input type="checkbox"/>	Not Applicable <input checked="" type="checkbox"/>

Contact and Corrective Action Comments:

Perc analysis not done at Energy Laboratories. These samples were taken to another laboratory by Mick Albright of Continental Resources.



Chain of Custody and Analytical Request Record

PLEASE PRINT- Provide as much information as possible.

Page 1 of 1

Company Name: Continental Resources		Project Name, PWS, Permit, Etc. Atlanta Site		Sample Origin State: ND	EPA/State Compliance: Yes <input checked="" type="checkbox"/> No <input type="checkbox"/>		
Report Mail Address: PO Box 268870 73126 Oklahoma City, OK		Contact Name: Chad Newby Phone/Fax: 405-574-2172 Email: chad.newby@clr.com		Purchase Order: Spencer Ingalls	Sampler, (Please Print) Chad Newby		
Invoice Address: PO Box 268870 73126 Oklahoma City, OK		Invoice Contact & Phone: Chad Newby 405-574-2172		Quote/Bottle Order: Unknown	Shipment Hand Cedar (R40):		
Special Report/Formats - ELI must be notified prior to sample submittal for the following:		ANALYSIS REQUESTED		Comments: E-1180177.20 N-421287.75 ELU 1940.40	Receipt Temp 24.6 °C		
<input type="checkbox"/> DW <input type="checkbox"/> GSA <input type="checkbox"/> POTW/MMWTP <input type="checkbox"/> Format: _____ <input type="checkbox"/> State: _____ <input type="checkbox"/> Other: _____		<input type="checkbox"/> A2LA <input type="checkbox"/> EDD/EDT(Electronic Data) <input type="checkbox"/> LEVEL IV <input type="checkbox"/> NELAC		Number of Containers Sample Type: A/W/S/V/R/D Soil/Solids Air/Water/Bioassay Other	Normal Turnaround (TAT) 24 hrs		
SAMPLE IDENTIFICATION (Name, Location, Interval, etc.)		Collection Date 8-29-12	Collection Time 7:00pm	MATRIX I-S	SEE ATTACHED X		
Original Material (<input checked="" type="checkbox"/>) 2 3 4 5 6 7 8 9 10 11 12							
Custody Record MUST be Signed		Received by (print): Mick Albright	Date/Time: 8-30-12 9:00 AM	Signature: MM/111	Received by (print): 	Date/Time: 	Signature:
		Received by (print): Mick Albright	Date/Time: 8-30-12 3:05 PM	Signature: MM/111	Received by (print): 	Date/Time: 	Signature:
Sample Disposal: Return to Client		Lab Disposal: K	Received by Laboratory: SOLOMONS Date/Time: 8/30/12 3:05 PM Signature: J. D. J.				

In certain circumstances, samples submitted to Energy Laboratories, Inc. may be subcontracted to other certified laboratories in order to complete the analysis requested.

This serves as notice of this possibility. All sub-contract data will be clearly noted on your analytical report.
Visit our web site at www.enerylab.com for additional information, downloadable fee schedule, forms, and links.



Chain of Custody and Analytical Request Record

PLEASE PRINT- Provide as much information as possible.

Page 1 of 1

Company Name: Continental Resources		Project Name, PWS, Permit, Etc. Atlanta Site		Sample Origin State: ND	EPA/State Compliance: Yes <input checked="" type="checkbox"/> No <input type="checkbox"/>	
Report Mail Address: Oklahoma City, OK PO Box 268870 73126		Contact Name: Chad Newby Phone/Fax: 405-574-2172 Email: chad.newby@cir.com		Sampler: (Please Print) Spencer Ingalls		
Invoice Address: Oklahoma City, OK PO Box 268870 73126		Invoice Contact & Phone: Chad Newby 405-574-2172		Purchase Order: Chad Newby	Quote/Bottle Order: Unknown	
Special Report/Formats - ELI must be notified prior to sample submittal for the following:		Number of Containers Sample Type: A/W/S/V/B/O Air/Water/Solids/Solvent Vegetation/Other	ANALYSIS REQUESTED		Shipped by: Chad Carrier ID(s):	
<input type="checkbox"/> DW <input type="checkbox"/> GSA <input type="checkbox"/> POTW/WWTP <input type="checkbox"/> State: _____ <input type="checkbox"/> Other: _____		<input type="checkbox"/> A2LA <input type="checkbox"/> EDD/EDT(Electronic Data) Format: _____ <input type="checkbox"/> LEVEL IV <input type="checkbox"/> NELAC	E C S A R C E C P H P e s s	SEE ATTACHED Normal Turnaround (TAT)	R U S H Contact ELI prior to RUSH sample submittal for charges and scheduling - See Instruction Page Comments: E-1179926.05 W-421267.60 E.U. 1937.65 Receipt Temp: 24.50 C On Ice: Yes <input checked="" type="checkbox"/> No <input type="checkbox"/> Custody Seal: Y <input type="checkbox"/> Intact: Y <input type="checkbox"/> Signature: Y <input type="checkbox"/> Match: Y <input type="checkbox"/> 8/20/2012-002	
SAMPLE IDENTIFICATION (Name, Location, Interval, etc.)		Collection Date 8-29-12	Collection Time 7:00PM	MATRIX	LABORATORY USE ONLY	
1 Fill #1					X	
2						
3						
4						
5						
6						
7						
8						
9						
10						
Custody Record MUST be Signed	Relinquished by (print): Mark Albright	Date/Time: 8-30-12 9:00AM	Signature: Mark Albright	Received by (print):	Date/Time:	Signature:
	Relinquished by (print): Mark Albright	Date/Time: 8-30-12 3:05	Signature: Mark Albright	Received by (print):	Date/Time:	Signature:
Sample Deposit:	Return to Client:	Lab Disposal:	Received by Laboratory:	Date/Time:	Signature:	
In certain circumstances, samples submitted to Energy Laboratories, Inc. may be subcontracted to other certified laboratories in order to complete the analysis requested. This serves as notice of this possibility. All sub-contract data will be clearly noted on your analytical report. Visit our web site at www.energylab.com for additional information, downloadable fee schedule, forms, and links.						



Chain of Custody and Analytical Request Record

PLEASE PRINT. Provide as much information as possible.

Page 1 of 1

Company Name: Continental Resources		Project Name, PWS, Permit, Etc. Atlanta Site			Sample Origin State: ND	EPA/State Compliance: Yes <input checked="" type="checkbox"/> No <input type="checkbox"/>																																																																										
Report Mail Address: PO Box 268870 73126		Contact Name: Chad Newby Phone/Fax: 405-574-2172 Email: chad.newby@okc.com			Purchase Order: Spencer Ingalls	Sampler: (Please Print)																																																																										
Invoice Address: PO Box 268870 73126		Invoice Contact & Phone: Chad Newby 405-574-2172			Quote/Bottle Order: Chad Newby Unknown																																																																											
Special Report/Formats – ELI must be notified prior to sample submittal for the following:		<table border="1" style="margin-left: auto; margin-right: auto;"> <thead> <tr> <th colspan="4">ANALYSIS REQUESTED</th> </tr> <tr> <th>Number of Containers</th> <th>Sample Type: A/W/S/V/B/O</th> <th>Air/Water/Solids/Solids</th> <th>Vegetation/Holassay/Other</th> </tr> </thead> <tbody> <tr> <td><input type="checkbox"/> DW</td> <td><input type="checkbox"/> A2LA</td> <td><input type="checkbox"/> S/A/R</td> <td><input type="checkbox"/> Per.</td> </tr> <tr> <td><input type="checkbox"/> GSA</td> <td><input type="checkbox"/> EDD/EDT (Electronic Data)</td> <td><input type="checkbox"/> C/E/C</td> <td><input type="checkbox"/> H</td> </tr> <tr> <td><input type="checkbox"/> POTWWWWTP</td> <td>Format: <input type="checkbox"/> LEVEL IV</td> <td><input type="checkbox"/> PH</td> <td><input type="checkbox"/> S</td> </tr> <tr> <td><input type="checkbox"/> State: _____</td> <td><input type="checkbox"/> NELAC</td> <td><input type="checkbox"/> E/C</td> <td><input type="checkbox"/> U</td> </tr> <tr> <td><input type="checkbox"/> Other: _____</td> <td></td> <td><input type="checkbox"/> T</td> <td><input type="checkbox"/> R</td> </tr> </tbody> </table>			ANALYSIS REQUESTED				Number of Containers	Sample Type: A/W/S/V/B/O	Air/Water/Solids/Solids	Vegetation/Holassay/Other	<input type="checkbox"/> DW	<input type="checkbox"/> A2LA	<input type="checkbox"/> S/A/R	<input type="checkbox"/> Per.	<input type="checkbox"/> GSA	<input type="checkbox"/> EDD/EDT (Electronic Data)	<input type="checkbox"/> C/E/C	<input type="checkbox"/> H	<input type="checkbox"/> POTWWWWTP	Format: <input type="checkbox"/> LEVEL IV	<input type="checkbox"/> PH	<input type="checkbox"/> S	<input type="checkbox"/> State: _____	<input type="checkbox"/> NELAC	<input type="checkbox"/> E/C	<input type="checkbox"/> U	<input type="checkbox"/> Other: _____		<input type="checkbox"/> T	<input type="checkbox"/> R	Contact ELI prior to RUSH sample submittal for charges and scheduling - See Instruction Page	Shipped by: TNT Carrier Date:																																														
ANALYSIS REQUESTED																																																																																
Number of Containers	Sample Type: A/W/S/V/B/O	Air/Water/Solids/Solids	Vegetation/Holassay/Other																																																																													
<input type="checkbox"/> DW	<input type="checkbox"/> A2LA	<input type="checkbox"/> S/A/R	<input type="checkbox"/> Per.																																																																													
<input type="checkbox"/> GSA	<input type="checkbox"/> EDD/EDT (Electronic Data)	<input type="checkbox"/> C/E/C	<input type="checkbox"/> H																																																																													
<input type="checkbox"/> POTWWWWTP	Format: <input type="checkbox"/> LEVEL IV	<input type="checkbox"/> PH	<input type="checkbox"/> S																																																																													
<input type="checkbox"/> State: _____	<input type="checkbox"/> NELAC	<input type="checkbox"/> E/C	<input type="checkbox"/> U																																																																													
<input type="checkbox"/> Other: _____		<input type="checkbox"/> T	<input type="checkbox"/> R																																																																													
<table border="1" style="width: 100%; border-collapse: collapse;"> <tr> <td>SAMPLE IDENTIFICATION (Name, Location, Interval, etc.)</td> <td>Collection Date</td> <td>Collection Time</td> <td>MATRIX</td> <td>SEE ATTACHED</td> <td>Normal Turnaround (TRT)</td> <td>Comments:</td> </tr> <tr> <td>FILL # 2</td> <td>8/29/12</td> <td>7:00pm</td> <td>I-S</td> <td>X</td> <td>10</td> <td>E-1179924-VC N. 421196.70 Etu. 1937.95</td> </tr> <tr> <td>2</td> <td></td> <td></td> <td></td> <td></td> <td></td> <td>24.6°C</td> </tr> <tr> <td>3</td> <td></td> <td></td> <td></td> <td></td> <td></td> <td>Yes <input checked="" type="checkbox"/></td> </tr> <tr> <td>4</td> <td></td> <td></td> <td></td> <td></td> <td></td> <td>Custody Seal <input type="checkbox"/> Y <input checked="" type="checkbox"/> N</td> </tr> <tr> <td>5</td> <td></td> <td></td> <td></td> <td></td> <td></td> <td>Initial <input type="checkbox"/> Y <input checked="" type="checkbox"/> N</td> </tr> <tr> <td>6</td> <td></td> <td></td> <td></td> <td></td> <td></td> <td>Signature Match <input type="checkbox"/> Y <input checked="" type="checkbox"/> N</td> </tr> <tr> <td>7</td> <td></td> <td></td> <td></td> <td></td> <td></td> <td>2009/8/29</td> </tr> <tr> <td>8</td> <td></td> <td></td> <td></td> <td></td> <td></td> <td></td> </tr> <tr> <td>9</td> <td></td> <td></td> <td></td> <td></td> <td></td> <td></td> </tr> <tr> <td>10</td> <td></td> <td></td> <td></td> <td></td> <td></td> <td></td> </tr> </table>		SAMPLE IDENTIFICATION (Name, Location, Interval, etc.)	Collection Date	Collection Time	MATRIX	SEE ATTACHED	Normal Turnaround (TRT)	Comments:	FILL # 2	8/29/12	7:00pm	I-S	X	10	E-1179924-VC N. 421196.70 Etu. 1937.95	2						24.6°C	3						Yes <input checked="" type="checkbox"/>	4						Custody Seal <input type="checkbox"/> Y <input checked="" type="checkbox"/> N	5						Initial <input type="checkbox"/> Y <input checked="" type="checkbox"/> N	6						Signature Match <input type="checkbox"/> Y <input checked="" type="checkbox"/> N	7						2009/8/29	8							9							10							Receipt Temp: 24.6°C	Comments: 24.6°C
SAMPLE IDENTIFICATION (Name, Location, Interval, etc.)	Collection Date	Collection Time	MATRIX	SEE ATTACHED	Normal Turnaround (TRT)	Comments:																																																																										
FILL # 2	8/29/12	7:00pm	I-S	X	10	E-1179924-VC N. 421196.70 Etu. 1937.95																																																																										
2						24.6°C																																																																										
3						Yes <input checked="" type="checkbox"/>																																																																										
4						Custody Seal <input type="checkbox"/> Y <input checked="" type="checkbox"/> N																																																																										
5						Initial <input type="checkbox"/> Y <input checked="" type="checkbox"/> N																																																																										
6						Signature Match <input type="checkbox"/> Y <input checked="" type="checkbox"/> N																																																																										
7						2009/8/29																																																																										
8																																																																																
9																																																																																
10																																																																																
LABORATORY USE ONLY																																																																																
Custody Record MUST be Signed	Released by (print): Mark Albright	Date/Time: 8/30/12 9:00 AM	Signature: Mark Albright	Received by (print):	Date/Time:	Signature:																																																																										
	Released by (print): Mark Albright	Date/Time: 8/30/12 3:05 PM	Signature: Mark Albright	Received by (print):	Date/Time:	Signature:																																																																										
Sample Disposal: Return to Client:	Lab Disposal:	Received by Laboratory: Energy Lab			Date/Time: 8/30/12 3:05 PM	Signature: Mark Albright																																																																										

In certain circumstances, samples submitted to Energy Laboratories, Inc. may be subcontracted to other certified laboratories in order to complete the analysis requested. This serves as notice of this possibility. All sub-contract data will be clearly noted on your analytical report. Visit our web site at www.energylab.com for additional information, downloadable fee schedule, terms, and links.



Chain of Custody and Analytical Request Record

Page 1 of 1

PLEASE PRINT - Provide as much information as possible.			
Company Name: Continental Resources		Project Name, PMS, Permit, Etc. Atlanta Site	
Report Mail Address: PO Box 2168870 73126 Oklahoma City, OK		Sample Origin Stat: ND	
Invoice Address: PO Box 2168870 73126 Oklahoma City, OK		EPA/State Compliance: Yes <input checked="" type="checkbox"/> No <input type="checkbox"/>	
Special Report/Formats - ELI must be notified prior to sample submittal for the following:		Sampler: (Please Print) Spencer Ingalls	
<input type="checkbox"/> DW <input type="checkbox"/> GSA <input type="checkbox"/> PCTWAWWTP <input type="checkbox"/> State: _____ <input type="checkbox"/> Other: _____		<input type="checkbox"/> A2LA <input type="checkbox"/> EDD/EDT (Electronic Data) Format: _____ <input type="checkbox"/> LEVEL IV <input type="checkbox"/> NELAC	
SAMPLE IDENTIFICATION (Name, Location, Interval, etc.)		Collection Date	Collection Time
Fill #3		8-29-12	7:00pm
		1-3	d d d d d
		MATRIX	SEE ATTACHED
		CC SAR CEC P/H Perch	Normal Turnaround (TAT)
		R	Contact ELI prior to RUSH sample submittal for charges and scheduling - See Instruction Page
		U	Comments: E-1179963.65 N-421120.95 EL-1937.90
		G	Received Temp: 24.5 °C On Time: Yes No
		H	Custody Seal: Y N Initial: M Signature: Mick Albright
LABORATORY USE ONLY 600817B-004			
Custody Record MUST be Signed	Received by (print): Mick Albright Date/Time: 8-30-12 9:00AM Signature: Mick Albright		
	Received by (print): Mick Albright Date/Time: 8-30-12 3:05 PM Signature: Mick Albright		
	Received by Laboratory: Spencer Ingalls Date/Time: 8-30-12 3:05 PM Signature: Spencer Ingalls		
In certain circumstances, samples submitted to Energy Laboratories, Inc. may be subcontracted to other certified laboratories in order to complete the analysis requested. This serves as notice of this possibility. All sub-contract data will be clearly noted on your analytical report. Visit our web site at www.energylab.com for additional information, downloadable fee schedule, forms, and links.			

**AMERICAN
TECHNICAL
SERVICES, INC.**

8105 Black Hawk Rd • PO Box 558 • Black Hawk, SD 57718-0558 • Phone (605) 787-9303 • FAX (605) 787-9515
140 Pine Needle Drive • Spearfish, SD 57783 • Phone (605) 642-2742 • Mobile 390-3768

PROCTOR TEST

MOISTURE DENSITY RELATION

CONTINENTAL RESOURCES, INC.
PO Box 268836
Oklahoma City, OK 73126
Attn: Project Manager


Proctor#: Date: 08/21/12
ASTM: 698 Method: C
Soil Classification: Brown Gravelly
Sand

Project: Atlanta Drill Pad, Williston,
North Dakota

Project Number: 12-12165

MAXIMUM DENSITY: 131.4 pcf

OPTIMUM MOISTURE CONTENT: 7.2%

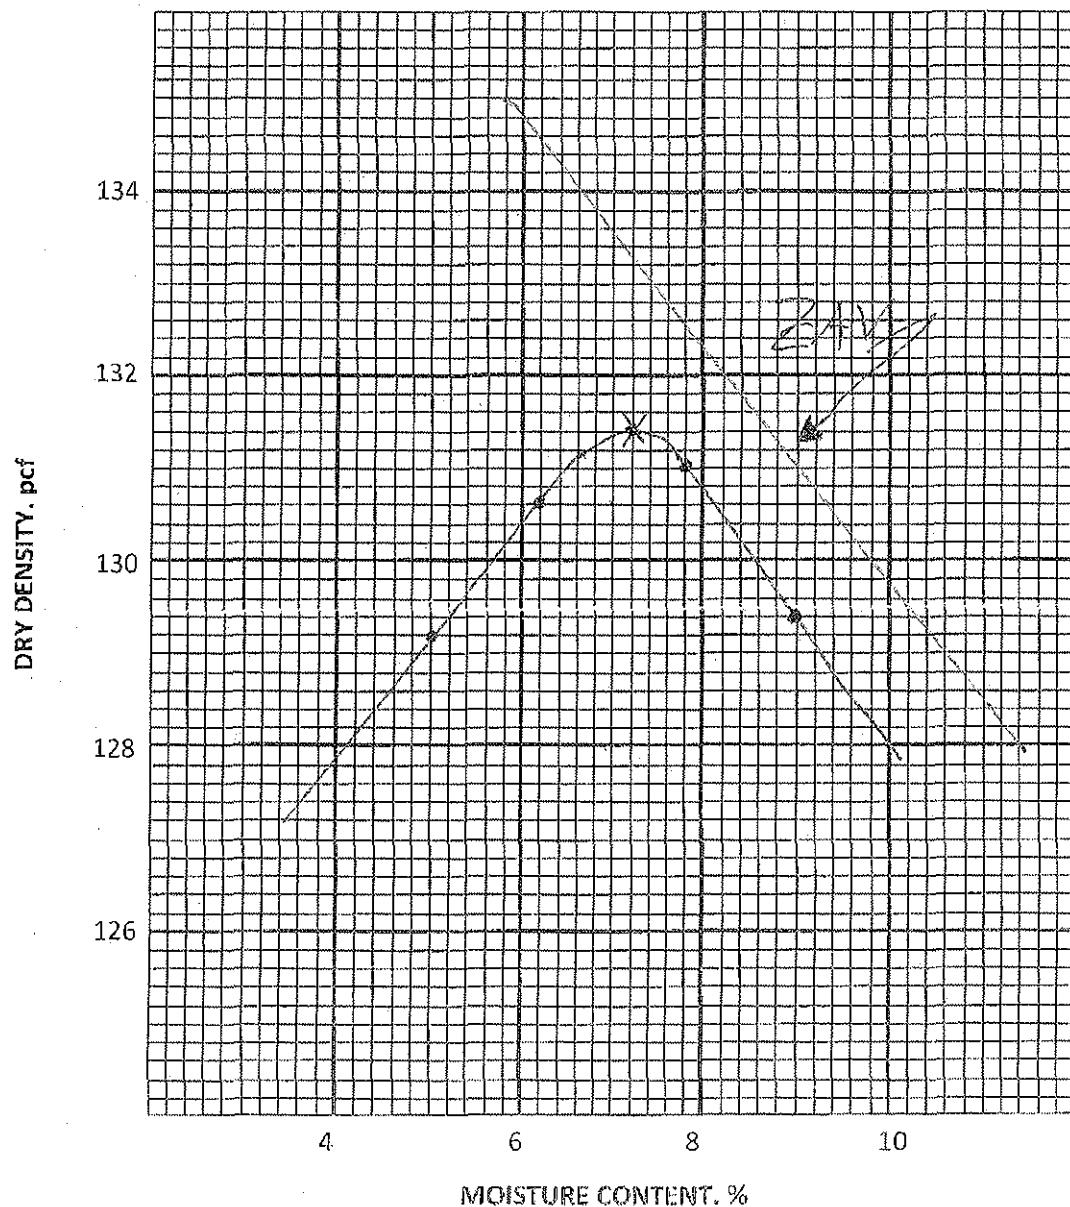

Cc:

SIOUX FALLS • BLACK HAWK • SPEARFISH

**AMERICAN
TECHNICAL
SERVICES, INC.**

8105 Black Hawk Rd • PO Box 558 • Black Hawk, SD 57718-0558 • Phone (605) 787-9303 • FAX (605) 787-9815
140 Pine Needle Drive • Spearfish, SD 57783 • Phone (605) 642-2742 • Mobile 390-3788

PROCTOR TEST

MOISTURE DENSITY RELATION

CONTINENTAL RESOURCES, INC.
PO Box 268836
Oklahoma City, OK 73126
Attn: Project Manager


Proctor#: Date: 07/31/12
ASTM: 698 Method:
Soil Classification: CL

Project: Atlanta Drill Pad, Williston,
North Dakota

Project Number: 12-12165

MAXIMUM DENSITY: 114.2pcf

OPTIMUM MOISTURE CONTENT: 15.3%

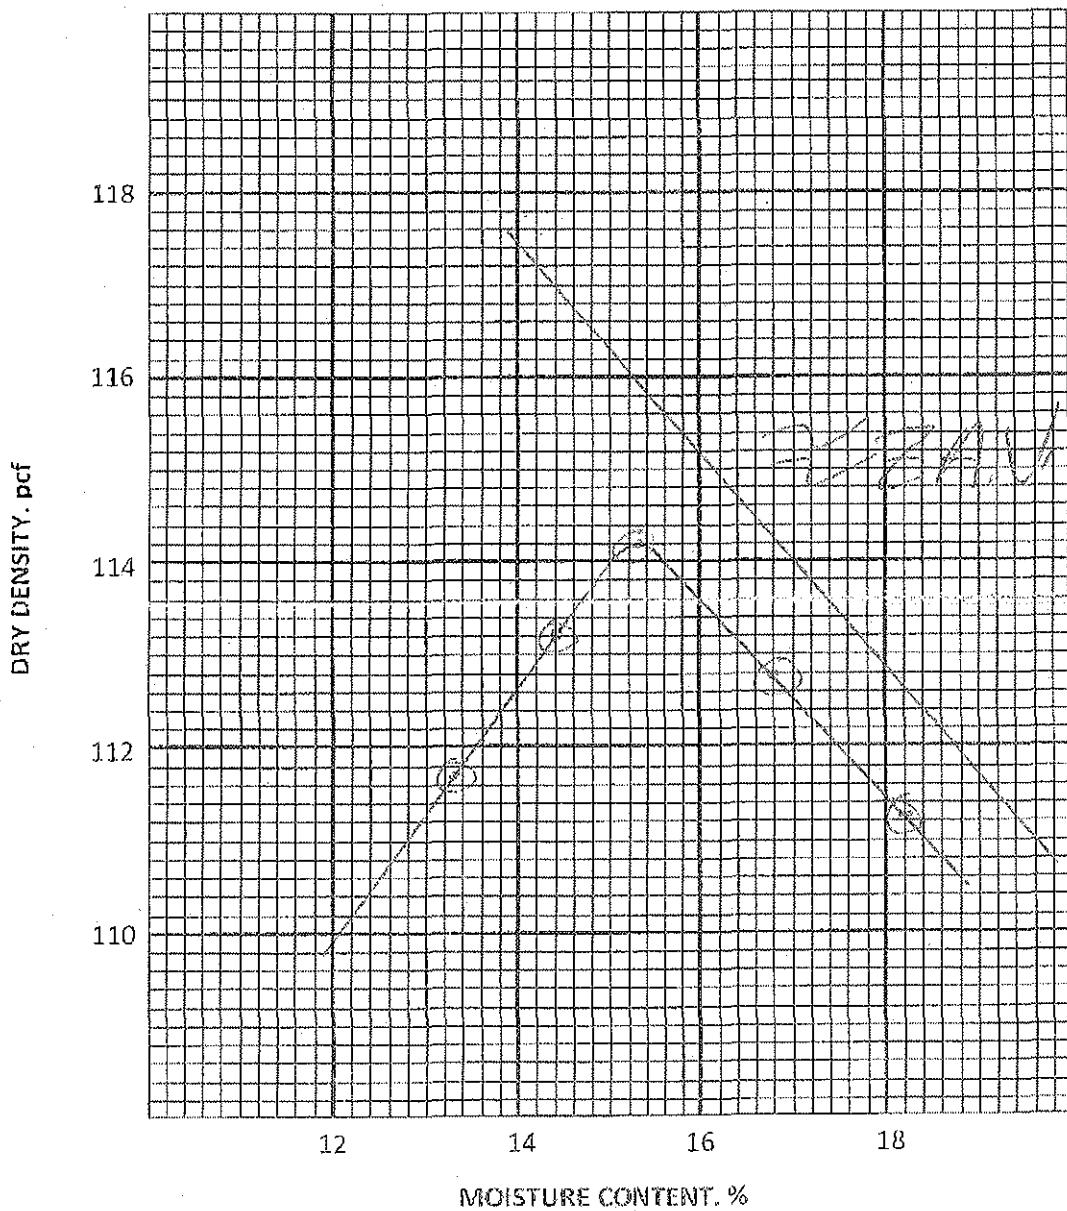

Cc:

SIOUX FALLS • BLACK HAWK • SPEARFISH

**A
MERICAN
T
ECHNICAL
S
ERVICES, INC.**

8106 Black Hawk Rd • PO Box 558 • Black Hawk, SD 57718-0558 • Phone (605) 787-9303 • FAX (605) 787-9515
140 Pine Needle Drive • Spearfish, SD 57783 • Phone (605) 642-2742 • Mobile 390-3768

REPORT OF EXCAVATION OBSERVATIONS

CONTINENTAL RESOURCES
P.O. Box 268836
Oklahoma City, OK 73126

September 7, 2012

Attn: Project Manager

Subj: Report of Excavation Observations
Drill Pad Spillage Line Construction
Atlanta Drill Pad
Williston, North Dakota

ATS No. 12-12165

INTRODUCTION

Our presence on the above referenced project was requested by Continental Resources of Oklahoma City, Oklahoma.

We were to observe and test the overexcavation and fill placement over the spillage liner placed below the Atlanta Drill Pad being constructed in Williston, North Dakota.

EXCAVATION OBSERVATIONS

Pad Spillage Liner Excavation & Subgrade Preparation:

We observed the overexcavation of the spillage liner on August 12, 2012. We observed that the bottom of the overexcavation was taken to 5 feet below finished grades in the spillage liner site. The bottom of the overexcavation was recompacted and smoothed prior to synthetic liner installation.

The synthetic liner material was delivered in rolls and placed over the prepared subgrade soils. We observed that the liner laps were welded as the liner materials were pulled into place.

Liner Area Backfill:

On August 14, 2012, we observed on-site soil placement over the synthetic liner. A cushion layer was compacted in place then material was placed via scrapers. Water was added and dozers mixed the soils prior to compaction in lifts. All compaction tests taken indicate the backfill material was placed in an engineered manner.


CONCLUSIONS AND RECOMMENDATIONS

Based on our observations and tests, it is our opinion that the liner subgrade was prepared and the backfill placed in an engineered manner.

CLOSURE

If you have questions or comments about this report, please contact us and we will be glad to respond.

Sincerely,
AMERICAN TECHNICAL SERVICES, INC.



Dave G. Bressler, P.E.
Geotechnical Consultant

cc: File

REPORT OF SOIL DENSITY TESTING - NUCLEAR METHOD

ASTM D6938

CLIENT: CONTINENTAL RESOURCES, INC.
PO Box 268836
Oklahoma City, OK 73126

ATTENTION: Project Manager

PROJECT: Atlanta Drill Site

ATS #: 12-12165
DATE: 07/30/12
ATS TECH: Russell Harwood
GAGE #: 2
BENCHMARK:

TEST #	DATE	PROCTOR # / CLASSIFICATION	LABORATORY		FIELD		SPECIFICATIONS			PASS
			% MOIST	DRY DENSITY	% MOISTURE	DRY DENSITY	% COMPACTION	SPEC MOISTURE %	SPEC COMPACTION	
1	07/25/12	#1	9.7	126.5	7.7	128.2	101	+/-2%	95	PASS
2	07/25/12	#1	9.7	126.5	8.7	120.2	95	+/-2%	95	PASS
3	07/25/12	#1	9.7	126.5	8.8	125.8	99	+/-2%	95	PASS
4	07/25/12	#1	9.7	126.5	9.9	126.8	100	+/-2%	95	PASS
5	07/25/12	#1	9.7	126.5	9.1	120.4	95	+/-2%	95	PASS
6	07/25/12	#1	9.7	126.5	7.8	121.0	96	+/-2%	95	PASS
7							#DIV/0!			
8							#DIV/0!			
9							#DIV/0!			
10							#DIV/0!			

TEST #	LOCATION	ELEVATION
1	North 421071.00, East 117953.00	1913.95
2	North 421274.95, East 1179466.60	1924.65
3	North 421032.65, East 1179535.15	1911.2
4	North 421208.75, East 1179464.72	1922.6
5	North 421225.55, East 1179501.00	1923.1
6	North 420954.70, East 1179641.10	1905.35
7		
8		
9		
10		

NOTES: All Test in West Valley Fill

RESPECTFULLY SUBMITTED

AMERICAN TECHNICAL SERVICES, INC.

AMERICAN
TECHNICAL
SERVICES, INC.

ENGINEERING • ENVIRONMENTAL • DRILLING • MATERIALS
8105 Black Hawk Rd. • PO Box 558
Black Hawk, SD 57718-0558

REPORT OF SOIL DENSITY TESTING - NUCLEAR METHOD

ASTM D6938

CLIENT CONTINENTAL RESOURCES, INC.
PO Box 268836
Oklahoma City, OK 73126

ATTENTION: Project Manager
PROJECT: Atlanta Drill Site

ATS # 12-12165
DATE 07/30/12
ATS TECH Russell Harwood
GAGE # 2
BENCHMARK

TEST #	DATE	PROCTOR # / CLASSIFICATION	LABORATORY		FIELD		SPECIFICATIONS			
			% MOIST	DRY DENSITY	% MOISTURE	DRY DENSITY	% COMPACTION	SPEC MOISTURE %	SPEC COMPACTION	PASS
7	07/26/12	#1	9.7	126.5	8.1	126.2	100	+/-2%	95	PASS
8	07/26/12	#1	9.7	126.5	7.8	128.4	102	+/-2%	95	PASS
9	07/26/12	#1	9.7	126.5	7.9	126.1	100	+/-2%	95	PASS
10	07/26/12	#1	9.7	126.5	7.7	120.2	95	+/-2%	95	PASS
11	07/26/12	#1	9.7	126.5	8.0	124.7	99	+/-2%	95	PASS
12	07/26/12	#1	9.7	126.5	8.1	123.7	98	+/-2%	95	PASS
13							#DIV/0!			
14							#DIV/0!			
15							#DIV/0!			
16							#DIV/0!			

TEST #	LOCATION	ELEVATION
7	North 420733.85, East 1179715.80	1889.35
8	North 421024.65, East 1179590.75	1911.8
9	North 4211162.20, East 1179535.00	1920.75
10	North 420989.90, East 1179617.40	1910.3
11	North 421163.80, East 1179533.60	1921.65
12	North 420730.65, East 1179774.25	1887.9
13		
14		
15		
16		

NOTES:

 CC:

RESPECTFULLY SUBMITTED

AMERICAN TECHNICAL SERVICES, INC.

**A
MERICAN
T
ECHNICAL
S
ERVICES, INC.**

ENGINEERING • ENVIRONMENTAL • DRILLING • MATERIALS
8105 Black Hawk Rd • PO Box 558
Black Hawk, SD 57718-0558

REPORT OF SOIL DENSITY TESTING - NUCLEAR METHOD

ASTM D6938

CLIENT: **CONTINENTAL RESOURCES, INC.**
PO Box 268836
Oklahoma City, OK 73126

ATTENTION: Project Manager
PROJECT: Atlanta Drill Site

ATS #: 12-12165
DATE: 07/30/12
ATS TECH: Russell Harwood
GAGE #: 2
BENCHMARK:

TEST #	DATE	PROCTOR # / CLASSIFICATION	LABORATORY		FIELD		SPECIFICATIONS			PASS
			% MOIST	DRY DENSITY	% MOISTURE	DRY DENSITY	% COMPACTION	SPEC MOISTURE %	SPEC COMPACTION	
13	07/27/12	#1	9.7	126.5	8.2	128.8	102	+/-2%	95	PASS
14	07/27/12	#1	9.7	126.5	7.8	125.7	99	+/-2%	95	PASS
15	07/27/12	#1	9.7	126.5	8.0	126.2	100	+/-2%	95	PASS
16	07/27/12	#1	9.7	126.5	7.9	126.7	100	+/-2%	95	PASS
17	07/27/12	#1	9.7	126.5	8.3	121.5	96	+/-2%	95	PASS
18	07/27/12	#1	9.7	126.5	8.0	120.7	95	+/-2%	95	PASS
19	07/27/12	#1	9.7	126.5	10.4	124.3	98	+/-2%	95	PASS
20	07/27/12	#1	9.7	126.5	8.3	121.5	96	+/-2%	95	PASS
21	07/27/12	#1	9.7	126.5	8.7	123.2	97	+/-2%	95	PASS
22	07/27/12	#1	9.7	126.5	10.1	121.2	96	+/-2%	95	PASS

TEST #	LOCATION	ELEVATION
13	North 420922.45, East 1179615.55	1907.5
14	North 421133.55, East 1179531.25	1920.75
15	North 421328.60, East 1179449.60	1930
16	North 420734.90, East 1179720.10	1891.95
17	North 421331.0, East 1179468.55	1930.25
18	North 421115.0, East 1179565.80	1920.35
19	North 421129.55, East 1179544.70	1921.55
20	North 420997.45, East 1179569.10	1913.85
21	North 421218.20, East 1179468.55	1927.65
22	North 421036.70, East 1179556.20	1916.5

NOTES

RESPECTFULLY SUBMITTED

AMERICAN TECHNICAL SERVICES, INC.

CC:

**A
MERICAN
T
ECHNICAL
S
ERVICES, INC.**

ENGINEERING • ENVIRONMENTAL • DRILLING • MATERIALS
8105 Black Hawk Rd. • PO Box 558
Black Hawk, SD 57718-0558

REPORT OF SOIL DENSITY TESTING - NUCLEAR METHOD

ASTM D6938

CLIENT: **CONTINENTAL RESOURCES, INC.**
PO Box 268836
Oklahoma City, OK 73126
ATTENTION: Project Manager
PROJECT: Atlanta Drill Site

ATS #: 12-12165
DATE: 07/30/12
ATS TECH: Russell Harwood
GAGE #: 2
BENCHMARK:

TEST #	DATE	PROCTOR # / CLASSIFICATION	LABORATORY		FIELD		SPECIFICATIONS			
			% MOIST	DRY DENSITY	% MOISTURE	DRY DENSITY	% COMPACTION	SPEC MOISTURE %	SPEC COMPACTION	PASS
23	07/28/12	#1	9.7	126.5	7.7	121.3	96	+/-2%	95	PASS
24	07/28/12	#1	9.7	126.5	8.6	122.3	97	+/-2%	95	PASS
25	07/28/12	#1	9.7	126.5	9.8	121.4	96	+/-2%	95	PASS
26	07/28/12	#1	9.7	126.5	10.3	120.4	95	+/-2%	95	PASS
27	07/28/12	#1	9.7	126.5	8.8	123.1	97	+/-2%	95	PASS
28	07/28/12	#1	9.7	126.5	10.2	121.1	96	+/-2%	95	PASS
29	07/28/12	#1	9.7	126.5	9.5	121.7	96	+/-2%	95	PASS
30	07/28/12	#1	9.7	126.5	8.9	121.6	96	+/-2%	95	PASS
31							#DIV/0!			
32							#DIV/0!			

TEST #	LOCATION	ELEVATION
23	North 421030.00, East 1179567.90	1917.25
24	North 421168.40, East 1179502.30	1925.8
25	North 420941.60, East 1179621.90	1910.9
26	North 420775.75, East 1179540.35	1915
27	North 420747.80, East 1179641.35	1901.75
28	North 421160.85, East 1179530.85	1925
29	North 421021.90, East 117618.15	1915.65
30	North 420886.85, East 1179717.40	1904.9
31		
32		

NOTES:

RESPECTFULLY SUBMITTED



CC:

AMERICAN TECHNICAL SERVICES, INC.

**A
M
E
R
I
C
A
N
T
E
C
H
N
I
C
A
L
S
E
R
V
I
C
E
S
, I
N
C**

REPORT OF SOIL DENSITY TESTING - NUCLEAR METHOD

ASTM D6938

ENGINEERING • ENVIRONMENTAL • DRILLING • MATERIALS
8105 Black Hawk Rd. • PO Box 558
Black Hawk SD 57718-0558

CLIENT:	<u>CONTINENTAL RESOURCES, INC.</u>
	<u>PO Box 268836</u>
	<u>Oklahoma City, OK 73126</u>
ATTENTION:	<u>Project Manager</u>
PROJECT:	<u>Atlanta Drill Site</u>

ATS #	12-12165
DATE:	07/30/12
ATS TECH.	Russell Harwood
GAGE #:	2
BENCHMARK:	

TEST #	DATE	PROCTOR # / CLASSIFICATION	LABORATORY		FIELD		SPECIFICATIONS			
			% MOIST	DRY DENSITY	% MOISTURE	DRY DENSITY	% COMPACTION	SPEC MOISTURE %	SPEC COMPACTION	PASS
31	07/29/12	#1	9.7	126.5	10.2	120.4	95	+/-2%	95	PASS
32	07/29/12	#1	9.7	126.5	10.1	121.2	96	+/-2%	95	PASS
33	07/29/12	#1	9.7	126.5	8.2	121.7	96	+/-2%	95	PASS
34	07/29/12	#1	9.7	126.5	9.2	121.7	96	+/-2%	95	PASS
35	07/29/12	#1	9.7	126.5	9.9	120.4	95	+/-2%	95	PASS
36	07/29/12	#1	9.7	126.5	9.4	120.8	95	+/-2%	95	PASS
37							#DIV/0!			
38							#DIV/0!			
39							#DIV/0!			
40							#DIV/0!			

TEST #	LOCATION	ELEVATION
31	North 421067.10, East 1179554.40	1920.8
32	North 420928.65, East 1179636.40	1911.25
33	North 420835.80, East 1179608.55	1912.35
34	North 421077.20, East 1179797.50	1922.35
35	North 420932.15, East 1179576.05	1914.35
36	North 420901.40, East 1179652.05	1909.95
37		
38		
39		
40		

NOTES:

RESPECTFULLY SUBMITTED

CC

AMERICAN TECHNICAL SERVICES, INC.

AMERICAN
TECHNICAL
SERVICES. INC.

ENGINEERING • ENVIRONMENTAL • DRILLING • MATERIALS
8105 Black Hawk Rd. • PO Box 558
Black Hawk SD 57718-0558

REPORT OF SOIL DENSITY TESTING - NUCLEAR METHOD

ASTM D6938

CLIENT	CONTINENTAL RESOURCES, INC. PO Box 268836 Oklahoma City, OK 73126	ATS #	12-12165
ATTENTION:	Project Manager	DATE	08/01/12
PROJECT	Atlanta Drill Site	ATS TECH	Russell Harwood
		GAGE #	2
		BENCHMARK	

TEST #	DATE	PROCTOR # / CLASSIFICATION	LABORATORY		FIELD		SPECIFICATIONS			PASS
			% MOIST	DRY DENSITY	% MOISTURE	DRY DENSITY	% COMPACTION	SPEC MOISTURE %	SPEC COMPACTION	
37	07/30/12	#3	15.3	114.2	14.2	108.7	95	+/-2%	95	PASS
38	07/30/12	#3	15.3	114.2	13.7	109.1	96	+/-2%	95	PASS
39	07/30/12	#3	15.3	114.2	13.6	110.4	97	+/-2%	95	PASS
40	07/30/12	#3	15.3	114.2	14.1	109.2	96	+/-2%	95	PASS
41	07/30/12	#3	15.3	114.2	13.8	110.0	96	+/-2%	95	PASS
42	07/30/12	#3	15.3	114.2	14.0	112.6	99	+/-2%	95	PASS
43							#DIV/0!			
44							#DIV/0!			
45							#DIV/0!			
46							#DIV/0!			

TEST #	LOCATION	ELEVATION
37	North 420807.75 East 1179702.80	1909.05
38	North 420783.10 East 1179629.25	1916.6
39	North 421008.30 East 1179597.45	1916.65
40	North 420912.45 East 1179672.00	1910.05
41	North 420800.0 East 1179606.85	1922.55
42	North 420784.65 East 1179714.00	1911.75
43		
44		
45		
46		

NOTES:

RESPECTFULLY SUBMITTED

CC:


AMERICAN TECHNICAL SERVICES, INC.

**AMERICAN
TECHNICAL
SERVICES, INC.**

ENGINEERING • ENVIRONMENTAL • DRILLING • MATERIALS
8105 Black Hawk Rd. • P.O. Box 558
Black Hawk, SD 57718-0558

REPORT OF SOIL DENSITY TESTING - NUCLEAR METHOD

ASTM D6938

CLIENT: **CONTINENTAL RESOURCES, INC.**
PO Box 268836
Oklahoma City, OK 73126

ATTENTION: Project Manager
PROJECT: Atlanta Drill Site

ATS #: 12-12165
DATE: 08/01/12
ATS TECH: Russell Harwood
GAGE #: 2
BENCHMARK:

TEST #	DATE	PROCTOR # / CLASSIFICATION	LABORATORY		FIELD		SPECIFICATIONS			
			% MOIST	DRY DENSITY	% MOISTURE	DRY DENSITY	% COMPACTION	SPEC MOISTURE %	SPEC COMPACTION	PASS
43	07/31/12	#3	15.3	114.2	13.4	108.9	95	+/-2%	95	PASS
44	07/31/12	#3	15.3	114.2	14.1	113.3	99	+/-2%	95	PASS
45	07/31/12	#3	15.3	114.2	13.3	109.5	96	+/-2%	95	PASS
46	07/31/12	#3	15.3	114.2	13.5	115.0	101	+/-2%	95	PASS
47	07/31/12	#1	9.7	126.5	8.9	124.7	99	+/-2%	95	PASS
48							#DIV/0!			
49							#DIV/0!			
50							#DIV/0!			
51							#DIV/0!			
52							#DIV/0!			

TEST #	LOCATION	ELEVATION
43	North 421075.80, East 1179492.75	1925.45
44	North 420939.60, East 1179667.90	1915.7
45	North 421024.15, East 1179494.95	1926.15
46	North 420978.15, East 1179573.50	1923.35
47	North 420958.05, East 1179629.60	1919.6
48		
49		
50		
51		
52		

NOTES: _____

CC: _____

RESPECTFULLY SUBMITTED



AMERICAN TECHNICAL SERVICES, INC.

**A
MERICAN
T
ECHNICAL
S
ERVICES, INC.**

ENGINEERING • ENVIRONMENTAL • DRILLING • MATERIALS
8105 Black Hawk Rd. • PO Box 558
Black Hawk, SD 57718-0558

REPORT OF SOIL DENSITY TESTING - NUCLEAR METHOD

ASTM D6938


CLIENT	CONTINENTAL RESOURCES, INC. PO Box 268836 Oklahoma City, OK 73126	ATS #	12-12165
ATTENTION:	Project Manager	DATE	08/03/12
PROJECT:	Atlanta Drill Site	ATS TECH	Russell Harwood
		GAGE #	2
		BENCHMARK	

TEST #	DATE	PROCTOR # / CLASSIFICATION	LABORATORY		FIELD		SPECIFICATIONS			PASS
			% MOIST	DRY DENSITY	% MOISTURE	DRY DENSITY	% COMPACTION	SPEC MOISTURE %	SPEC COMPACTION	
48	08/01/12	#3	15.3	114.2	13.7	113.9	100	+/-2%	95	PASS
49	08/01/12	#3	15.3	114.2	13.4	112.6	99	+/-2%	95	PASS
50	08/01/12	#3	15.3	114.2	13.5	108.9	95	+/-2%	95	PASS
51	08/01/12	#3	15.3	114.2	14.2	110.0	96	+/-2%	95	PASS
52	08/01/12	#3	15.3	114.2	13.3	113.5	99	+/-2%	95	PASS
53							#DIV/0!			
54							#DIV/0!			
55							#DIV/0!			
56							#DIV/0!			
57							#DIV/0!			

TEST #	LOCATION	ELEVATION
48	78' North of South End of West Valley- Middle	
49	25' North of South End of West Valley-Middle	
50	225' North of South End of West Valley-Middle	
51	North 42 1100.20 East 1179617.10	1924.9
52	North 420962.20 East 1179574.20	1928.75
53		
54		
55		
56		
57		

NOTES: Not Able to Get GPS Readings System Down

RESPECTFULLY SUBMITTED



AMERICAN TECHNICAL SERVICES, INC.

CC:

AMERICAN
TECHNICAL
SERVICES, INC.

ENGINEERING • ENVIRONMENTAL • DRILLING • MATERIALS
8105 Black Hawk Rd. • PO Box 558
Black Hawk, SD 57718-0558

REPORT OF SOIL DENSITY TESTING - NUCLEAR METHOD

ASTM D6938

CLIENT: CONTINENTAL RESOURCES, INC.
PO Box 268836
Oklahoma City, OK 73126
ATTENTION: Project Manager
PROJECT: Atlanta Drill Site

ATS #: 12-12165
DATE: 08/03/12
ATS TECH: Russell Harwood
GAGE #: 2
BENCHMARK:

TEST #	DATE	PROCTOR # / CLASSIFICATION	LABORATORY		FIELD		SPECIFICATIONS			
			% MOIST	DRY DENSITY	% MOISTURE	DRY DENSITY	% COMPACTION	SPEC MOISTURE %	SPEC COMPACTION	PASS
53	08/02/12	#3	15.3	114.2	13.5	114.9	101	+/-2%	95	PASS
54	08/02/12	#3	15.3	114.2	13.7	112.9	99	+/-2%	95	PASS
55	08/02/12	#3	15.3	114.2	13.5	110.2	96	+/-2%	95	PASS
56	08/02/12	#3	15.3	114.2	13.6	114.0	100	+/-2%	95	PASS
57	08/02/12	#3	15.3	114.2	13.6	113.9	100	+/-2%	95	PASS
58	08/02/12	#3	15.3	114.2	13.8	115.5	101	+/-2%	95	PASS
59	08/02/12	#3	15.3	114.2	13.4	109.7	96	+/-2%	95	PASS
60							#DIV/0!			
61							#DIV/0!			
62							#DIV/0!			

TEST #	LOCATION	ELEVATION
53	North 420981.65 East 1179560.25	1930.75
54	North 420989.70 East 1179597.65	1928.25
55	North 420091.15 East 1179511.90	1933.95
56	North 421074.40 East 1179515.05	1933.45
57	North 421145.45 East 1179458.95	1932.75
58	North 421084.85 East 1179531.55	1934.45
59	North 421196.80 East 1179508.90	1934.35
60		
61		
62		

NOTES:

RESPECTFULLY SUBMITTED

AMERICAN TECHNICAL SERVICES, INC.

CC:

**AMERICAN
TECHNICAL
SERVICES, INC.**

ENGINEERS • ENVIRONMENTAL • DRILLING • MATERIALS
8105 Black Hawk Rd. • PO Box 558
Black Hawk, SD 57718-0558

REPORT OF SOIL DENSITY TESTING - NUCLEAR METHOD

ASTM D6938

CLIENT: CONTINENTAL RESOURCES, INC.
P.O. Box 268836
Oklahoma City, OK 73126
ATTENTION: Project Manager
PROJECT: Atlanta Drill Site

ATS #: 12-12165
DATE: 08/07/12
ATS TECH: Russell Harwood
GAGE #: 2
BENCHMARK:

TEST #	DATE	PROCTOR # / CLASSIFICATION	LABORATORY		FIELD		SPECIFICATIONS			
			% MOIST	DRY DENSITY	% MOISTURE	DRY DENSITY	% COMPACTION	SPEC MOISTURE %	SPEC COMPACTION	PASS
60	08/04/12	#3	15.3	114.2	13.9	112.2	98	+/-2%	95	PASS
61	08/04/12	#1	9.7	126.5	8.9	120.6	95	+/-2%	95	PASS
62	08/04/12	#3	15.3	114.2	14.1	113.9	100	+/-2%	95	PASS
63	08/04/12	#3	15.3	114.2	13.4	113.3	99	+/-2%	95	PASS
64							#DIV/0!			
65							#DIV/0!			
66							#DIV/0!			
67							#DIV/0!			
68							#DIV/0!			
69							#DIV/0!			

TEST #	LOCATION	ELEVATION
60	300' North of South Slope, East 1/3 of West Valley	4 to 5' Below
61	100' North of South Slope, East 1/3 of West Valley	4 to 5' Below
62	North 421154.15, East 1179488.85	1930.7
63	North 421086.15, East 1179544.25	1937.05
64		
65		
66		
67		
68		
69		

NOTES: No GPS for Location

RESPECTFULLY SUBMITTED

AMERICAN TECHNICAL SERVICES, INC.

**AMERICAN
TECHNICAL
SERVICES, INC.**

ENGINEERING • ENVIRONMENTAL • DRILLING • MATERIALS
9105 Black Hawk Rd. • PO Box 558
Black Hawk, SD 57718-0558

REPORT OF SOIL DENSITY TESTING - NUCLEAR METHOD

ASTM D6938

CLIENT: **CONTINENTAL RESOURCES, INC.**
PO Box 268836
Oklahoma City, OK 73126
ATTENTION: Project Manager
PROJECT: Atlanta Drill Site

ATS #: 12-12165
DATE: 08/07/12
ATS TECH: Russell Harwood
GAGE #: 2
BENCHMARK:

TEST #	DATE	PROCTOR # / CLASSIFICATION	LABORATORY		FIELD		SPECIFICATIONS			PASS
			% MOIST	DRY DENSITY	% MOISTURE	DRY DENSITY	% COMPACTION	SPEC MOISTURE %	SPEC COMPACTION	
64	08/05/12	#1	9.7	126.5	10.1	124.9	99	+/-2%	95	PASS
65	08/05/12	#3	15.3	114.2	13.4	112.2	98	+/-2%	95	PASS
66	08/05/12	#1	9.7	126.5	8.3	128.5	102	+/-2%	95	PASS
67	08/05/12	#1	9.7	126.5	9.1	121.8	96	+/-2%	95	PASS
68							#DIV/0!			
69							#DIV/0!			
70							#DIV/0!			
71							#DIV/0!			
72							#DIV/0!			
73							#DIV/0!			

TEST #	LOCATION	ELEVATION
64	North 421047 10 East 1179483.90	1939
65	North 421236 15 East 1179463.75	1938.55
66	North 421344 40 East 1179447.75	1940.25
67	North 421219 15 East 1179501.00	1940.4
68		
69		
70		
71		
72		
73		

NOTES

RESPECTFULLY SUBMITTED

AMERICAN TECHNICAL SERVICES, INC.

CC:

**AMERICAN
TECHNICAL
SERVICES, INC.**

ENGINEERING • ENVIRONMENTAL • DRILLING • MATERIALS
9105 Black Hawk Rd • PO Box 558
Black Hawk, SD 57718-0558

REPORT OF SOIL DENSITY TESTING - NUCLEAR METHOD

ASTM D6938

CLIENT: CONTINENTAL RESOURCES, INC.
PO Box 268836
Oklahoma City, OK 73126

ATTENTION: Project Manager
PROJECT: Atlanta Drill Site

ATS #: 12-12165
DATE: 08/09/12
ATS TECH: Russell Harwood
GAGE #: 2
BENCHMARK:

TEST #	DATE	PROCTOR # / CLASSIFICATION	LABORATORY		FIELD		SPECIFICATIONS			
			% MOIST	DRY DENSITY	% MOISTURE	DRY DENSITY	% COMPACTION	SPEC MOISTURE %	SPEC COMPACTION	PASS
68	08/07/12	#1	9.7	126.5	7.8	122.6	97	+/-2%	95	PASS
69	08/07/12	#2	8.3	123.2	7.5	118.7	96	+/-2%	95	PASS
70	08/07/12	#1	9.7	126.5	8.7	126.3	100	+/-2%	95	PASS
71	08/07/12	#1	9.7	126.5	7.8	123.8	98	+/-2%	95	PASS
72							#DIV/0!			
73							#DIV/0!			
74							#DIV/0!			
75							#DIV/0!			
76							#DIV/0!			
77							#DIV/0!			

TEST #	LOCATION	ELEVATION
68	North 420982.95 East 1179952.45	1895.45
69	North 421008.10 East 1179936.05	1896.5
70	North 421099.00 East 1179911.80	1898.75
71	North 421191.80 East 1179859.30	1904.05
72		
73		
74		
75		
76		
77		

NOTES

RESPECTFULLY SUBMITTED

CC:

AMERICAN TECHNICAL SERVICES, INC.

**AMERICAN
TECHNICAL
SERVICES, INC.**

ENGINEERING • ENVIRONMENTAL • DRILLING • MATERIALS
8105 Black Hawk Rd • PO Box 556
Black Hawk, SD 57718-0556

REPORT OF SOIL DENSITY TESTING - NUCLEAR METHOD

ASTM D6938

CLIENT: **CONTINENTAL RESOURCES, INC.**
PO Box 268836
Oklahoma City, OK 73126

ATTENTION: Project Manager
PROJECT: Atlanta Drill Site

ATS #: 12-12165
DATE: 08/09/12
ATS TECH: Russell Harwood
GAGE #: 2
BENCHMARK:

TEST #	DATE	PROCTOR # / CLASSIFICATION	LABORATORY		FIELD		SPECIFICATIONS			
			% MOIST	DRY DENSITY	% MOISTURE	DRY DENSITY	% COMPACTION	SPEC MOISTURE %	SPEC COMPACTION	PASS
72	08/08/12	#1	9.7	126.5	8.6	124.9	99	+/-2%	95	PASS
73	08/08/12	#1	9.7	123.2	7.7	128.6	104	+/-2%	95	PASS
74	08/08/12	#2	8.3	123.2	8.4	117.5	95	+/-2%	95	PASS
75	08/08/12	#1	9.7	126.5	7.9	128.5	102	+/-2%	95	PASS
76							#DIV/0!			
77							#DIV/0!			
78							#DIV/0!			
79							#DIV/0!			
80							#DIV/0!			
81							#DIV/0!			

TEST #	LOCATION	ELEVATION
72	North 421032.80 East 1179904.95	1907.4
73	North 421121.00 East 1179879.00	1909.35
74	North 421046.25 East 1179873.80	1911.65
75	North 421154.10 East 1179910.70	1913.7
76		
77		
78		
79		
80		
81		

NOTES: _____ RESPECTFULLY SUBMITTED

CC:


AMERICAN TECHNICAL SERVICES, INC.

**AMERICAN
TECHNICAL
SERVICES, INC.**

ENGINEERING • ENVIRONMENTAL • DRILLING • MATERIALS
8105 Black Hawk Rd. • PO Box 558
Black Hawk, SD 57718-0558

REPORT OF SOIL DENSITY TESTING - NUCLEAR METHOD

ASTM D6938

CLIENT CONTINENTAL RESOURCES, INC.
PO Box 268836
Oklahoma City, OK 73126

ATTENTION: Project Manager
PROJECT: Atlanta Drill Site

ATS #: 12-12165
DATE: 08/15/12
ATS TECH: Russell Harwood
GAGE #: 2
BENCHMARK:

TEST #	DATE	PROCTOR # / CLASSIFICATION	LABORATORY		FIELD		SPECIFICATIONS			PASS
			% MOIST	DRY DENSITY	% MOISTURE	DRY DENSITY	% COMPACTION	SPEC MOISTURE %	% SPEC COMPACTATION	
76	08/09/12	#1	9.7	126.5	8.0	120.4	95	+/-2%	95	PASS
77	08/09/12	#2	8.3	123.2	8.1	120.3	98	+/-2%	95	PASS
78							#DIV/0!			
79							#DIV/0!			
80							#DIV/0!			
81							#DIV/0!			
82							#DIV/0!			
83							#DIV/0!			
84							#DIV/0!			
85							#DIV/0!			

TEST #	LOCATION	ELEVATION
76	North 421078.95 East 1179862.60	1914.45
77	North 421199.70 East 1179870.90	1915.05
78		
79		
80		
81		
82		
83		
84		
85		

NOTES: _____

RESPECTFULLY SUBMITTED

CC:

AMERICAN TECHNICAL SERVICES, INC.



**A
MERICAN
T
ECHNICAL
S
ERVICES, INC.**

ENGINEERING • ENVIRONMENTAL • DRILLING • MATERIALS
5105 Black Hawk Rd • PO Box 558
Black Hawk, SD 57718-0558

REPORT OF SOIL DENSITY TESTING - NUCLEAR METHOD

ASTM D6938

CLIENT: **CONTINENTAL RESOURCES, INC.**
 PO Box 268836
 Oklahoma City, OK 73126

ATTENTION: Project Manager
 PROJECT: Atlanta Drill Site

ATS #: **12-12165**
 DATE: **08/15/12**
 ATS TECH: **Russell Harwood**
 GAGE #: **2**
 BENCHMARK:

TEST #	DATE	PROCTOR # / CLASSIFICATION	LABORATORY		FIELD		SPECIFICATIONS			
			% MOIST	DRY DENSITY	% MOISTURE	DRY DENSITY	% COMPACTION	SPEC MOISTURE %	SPEC COMPACTION	PASS
82	08/12/12	#1	9.7	126.5	10.0	124.2	98	+/-2%	95	PASS
83	08/12/12	#1	9.7	126.5	10.3	120.7	95	+/-2%	95	PASS
84	08/12/12	#1	9.7	126.5	10.1	122.8	97	+/-2%	95	PASS
85	08/12/12	#3	15.3	114.2	13.4	115.5	101	+/-2%	95	PASS
86	08/12/12	#3	15.3	114.2	14.0	116.6	102	+/-2%	95	PASS
87	08/12/12	#3	15.3	114.2	13.9	114.9	101	+/-2%	95	PASS
88						#DIV/0!				
89						#DIV/0!				
90						#DIV/0!				
91						#DIV/0!				

TEST #	LOCATION	ELEVATION
82	North 421169.15 East 1179661.00	1934.25
83	North 421281.75 East 1179530.30	1935.9
84	North 421187.85 East 1179466.20	1935.2
85	North 421265.35 East 1179372.75	1936.3
86	North 421179.15 East 1179257.80	1935.9
87	North 421253.65 East 1179177.25	1937.1
88		
89		
90		
91		

NOTES: All Test in Overex on West 1/2 Subgrade Before Liner Installation

RESPECTFULLY SUBMITTED

CC:


AMERICAN TECHNICAL SERVICES, INC.

AMERICAN
TECHNICAL
SERVICES, INC.

ENGINEERING • ENVIRONMENTAL • DRILLING • MATERIALS
6105 Black Hawk Rd. • PO Box 558
Black Hawk, SD 57718-0558

REPORT OF SOIL DENSITY TESTING - NUCLEAR METHOD

ASTM D6938

CLIENT: **CONTINENTAL RESOURCES, INC.**
PO Box 268836
Oklahoma City, OK 73126

ATTENTION: Project Manager
PROJECT: Atlanta Drill Site

ATS #: 12-12165
DATE: 08/15/12
ATS TECH: Russell Harwood
GAGE #: 2
BENCHMARK:

TEST #	DATE	PROCTOR # / CLASSIFICATION	LABORATORY		FIELD		SPECIFICATIONS			PASS
			% MOIST	DRY DENSITY	% MOISTURE	DRY DENSITY	% COMPACTION	SPEC MOISTURE %	SPEC COMPACTION	
78	08/12/12	#3	15.3	114.2	13.5	113.9	100	+/-2%	95	PASS
79	08/12/12	#3	15.3	114.2	13.7	115.1	101	+/-2%	95	PASS
80	08/12/12	#3	15.3	114.2	13.4	114.9	101	+/-2%	95	PASS
81	08/12/12	#3	15.3	114.2	13.3	113.3	99	+/-2%	95	PASS
82							#DIV/0!			
83							#DIV/0!			
84							#DIV/0!			
85							#DIV/0!			
86							#DIV/0!			
87							#DIV/0!			

TEST #	LOCATION	ELEVATION
78	North 421150.90 East 1179896.40	1917
79	North 421240.60 East 1179845.60	1917.8
80	North 421006.70 East 1179882.55	1922.3
81	North 420992.55 East 1179992.15	1919.75
82		
83		
84		
85		
86		
87		

NOTES: _____
RESPECTFULLY SUBMITTED

CC:


AMERICAN TECHNICAL SERVICES, INC.

AMERICAN
TECHNICAL
SERVICES, INC.

ENGINEERING • ENVIRONMENTAL • DRILLING • MATERIALS
8105 Back Hawk Rd. • PO Box 558
Black Hawk, SD 57718-0558

REPORT OF SOIL DENSITY TESTING - NUCLEAR METHOD
ASTM D6938

CLIENT: CONTINENTAL RESOURCES INC
PO Box 268836
Oklahoma City, OK 73126

ATTENTION: Project Manager
PROJECT: Atlanta Drill Site

ATS #: 12-12165
DATE: 08/15/12
ATS TECH: Russell Harwood
GAGE #: 2
BENCHMARK:

TEST #	DATE	PROCTOR # / CLASSIFICATION	LABORATORY		FIELD		SPECIFICATIONS			PASS
			% MOIST	DRY DENSITY	% MOISTURE	DRY DENSITY	% COMPACTION	SPEC MOISTURE %	SPEC COMPACTION	
88	08/13/12	#3	15.3	114.2	13.6	113.7	100	+/-2%	95	PASS
89	08/13/12	#3	15.3	114.2	13.8	113.3	99	+/-2%	95	PASS
90	08/13/12	#3	15.3	114.2	13.4	115.5	101	+/-2%	95	PASS
91	08/13/12	#2	8.3	123.2	8.8	118.9	97	+/-2%	95	PASS
92	08/13/12	#1	9.7	126.5	8.9	126.1	100	+/-2%	95	PASS
93							#DIV/0!			
94							#DIV/0!			
95							#DIV/0!			
96							#DIV/0!			
97							#DIV/0!			

TEST #	LOCATION	ELEVATION
88	North 421063.70 East 1179944.20	1918.35
89	North 421008.35 East 1179861.05	1927.7
90	North 421038.50 East 1179985.85	1920.7
91	North 421044.50 East 1179840.40	1927.5
92	North 421017.25 East 1179950.30	1925.65
93		
94		
95		
96		
97		

NOTES:

RESPECTFULLY SUBMITTED

CC:

AMERICAN TECHNICAL SERVICES, INC.

**A
MERICAN
T
ECHNICAL
S
ERVICES, INC.**

ENGINEERING • ENVIRONMENTAL • DRILLING • MATERIALS
8105 Black Hawk Rd. • PO Box 558
Black Hawk, SD 57713-0558

REPORT OF SOIL DENSITY TESTING - NUCLEAR METHOD
ASTM D6938

CLIENT: **CONTINENTAL RESOURCES, INC.**
PO Box 268836
Oklahoma City, OK 73126
ATTENTION: Project Manager
PROJECT: Atlanta Drill Site

ATS #: 12-12165
DATE: 08/15/12
ATS TECH: Russell Harwood
GAGE #: 2
BENCHMARK:

TEST #	DATE	PROCTOR # / CLASSIFICATION	LABORATORY		FIELD		SPECIFICATIONS			
			% MOIST	DRY DENSITY	% MOISTURE	DRY DENSITY	% COMPACTION	SPEC MOISTURE %	SPEC COMPACTION	PASS
98	08/14/12	#1	9.7	126.5	10.2	120.9	96	+/-2%	95	PASS
99	08/14/12	#1	9.7	126.5	10.3	121.3	96	+/-2%	95	PASS
100	08/14/12	#1	9.7	126.5	10.1	121.9	96	+/-2%	95	PASS
101	08/14/12	#3	15.3	114.2	13.3	114.5	100	+/-2%	95	PASS
102	08/14/12	#1	9.7	126.5	10.1	123.5	98	+/-2%	95	PASS
103	08/14/12	#1	9.7	126.5	10.2	121.2	96	+/-2%	95	PASS
104	08/14/12	#3	15.3	114.2	13.4	115.6	101	+/-2%	95	PASS
105							#DIV/0!			
106							#DIV/0!			
107							#DIV/0!			

TEST #	LOCATION	ELEVATION
98	North 421249.95 East 1179384.30	1937.55
99	North 421288.40 East 1179300.25	1938.65
100	North 421171.30 East 1179237.30	1937.9
101	North 421272.15 East 1179362.50	1938.75
102	North 421267.10 East 1179238.35	1939.7
103	North 421229.90 East 1179254.90	1939.2
104	North 421203.80 East 1179320.25	1938.65
105		
106		
107		

NOTES: Drill Pad Area on Liner Fill

RESPECTFULLY SUBMITTED

CC:

AMERICAN TECHNICAL SERVICES, INC.

**AMERICAN
TECHNICAL
SERVICES, INC.**

ENGINEERING • ENVIRONMENTAL • DRILLING • MATERIALS
3105 Black Hawk Rd. • PO Box 558
Black Hawk, SD 57718-0558

REPORT OF SOIL DENSITY TESTING - NUCLEAR METHOD
ASTM D6938

CLIENT: CONTINENTAL RESOURCES, INC.
PO Box 268836
Oklahoma City, OK 73126
ATTENTION: Project Manager
PROJECT: Atlanta Drill Site

ATS #: 12-12165
DATE: 08/15/12
ATS TECH: Russell Harwood
GAGE #: 2
BENCHMARK:

TEST #	DATE	PROCTOR # / CLASSIFICATION	LABORATORY		FIELD		SPECIFICATIONS			
			% MOIST	DRY DENSITY	% MOISTURE	DRY DENSITY	% COMPACTION	SPEC MOISTURE %	SPEC COMPACTION	PASS
93	08/14/12	#3	15.3	114.2	13.6	114.5	100	+/-2%	95	PASS
94	08/14/12	#3	15.3	114.2	13.7	114.7	100	+/-2%	95	PASS
95	08/14/12	#1	9.7	126.5	10.4	122.5	97	+/-2%	95	PASS
96	08/14/12	#1	9.7	126.5	8.7	124.0	98	+/-2%	95	PASS
97	08/14/12	#1	9.7	126.5	9.3	121.3	96	+/-2%	95	PASS
98						#DIV/0!				
99						#DIV/0!				
100						#DIV/0!				
101						#DIV/0!				
102						#DIV/0!				

TEST #	LOCATION	ELEVATION
93	North 421035.45 East 1179873.40	1927.55
94	North 421012.25 East 1179971.80	1925.7
95	North 421091.95 East 1179838.70	1927.15
96	North 421038.25 East 1179899.75	1928.35
97	North 420986.05 East 1170007.50	1925.5
98		
99		
100		
101		
102		

NOTES:

RESPECTFULLY SUBMITTED

CC:

AMERICAN TECHNICAL SERVICES, INC.

**AMERICAN
TECHNICAL
SERVICES, INC.**

ENGINEERING • ENVIRONMENTAL • DRILLING • MATERIALS
8105 Black Hawk Rd. • PO Box 558
Black Hawk, SD 57718-0558

REPORT OF SOIL DENSITY TESTING - NUCLEAR METHOD
ASTM D6938

CLIENT: CONTINENTAL RESOURCES, INC.
PO Box 268836
Oklahoma City, OK 73126

ATTENTION: Project Manager
PROJECT: Atlanta Drill Site

ATS #: 12-12165
DATE: 08/17/12
ATS TECH: Russell Harwood
GAGE #: 2
BENCHMARK:

TEST #	DATE	PROCTOR # / CLASSIFICATION	LABORATORY		FIELD		SPECIFICATIONS			
			% MOIST	DRY DENSITY	% MOISTURE	DRY DENSITY	% COMPACTION	SPEC MOISTURE %	SPEC COMPACTION	PASS
111	08/15/12	#1	9.7	126.5	10.4	120.1	95	+/-2%	95	PASS
112	08/15/12	#3	15.3	114.2	13.7	113.9	100	+/-2%	95	PASS
113							#DIV/0!			
114							#DIV/0!			
115							#DIV/0!			
116							#DIV/0!			
117							#DIV/0!			
118							#DIV/0!			
119							#DIV/0!			
120							#DIV/0!			

TEST #	LOCATION	ELEVATION
111	North 421056 40 East 1179836.10	1931.4
112	North 421052.05 East 1179918.50	1927.8
113		
114		
115		
116		
117		
118		
119		
120		

NOTES:

RESPECTFULLY SUBMITTED

CC:

AMERICAN TECHNICAL SERVICES, INC.

**AMERICAN
TECHNICAL
SERVICES, INC.**

ENGINEERING • ENVIRONMENTAL • DRILLING • MATERIALS
8105 Black Hawk Rd • PO Box 558
Black Hawk, SD 57718-0558

REPORT OF SOIL DENSITY TESTING - NUCLEAR METHOD

ASTM D6938

CLIENT: **CONTINENTAL RESOURCES, INC.**
PO Box 268836
Oklahoma City, OK 73126

ATTENTION: Project Manager
PROJECT: Atlanta Drill Site

ATS #: 12-12165
DATE: 08/17/12
ATS TECH: Russell Harwood
GAGE #: 2
BENCHMARK:

			LABORATORY		FIELD		SPECIFICATIONS			
TEST #	DATE	PROCTOR # / CLASSIFICATION	% MOIST	DRY DENSITY	% MOISTURE	DRY DENSITY	% COMPACTION	SPEC MOISTURE %	% SPEC COMPACTION	PASS
105	08/15/12	#3	15.3	114.2	13.6	118.0	103	+/-2%	95	PASS
106	08/15/12	#2	8.3	123.2	8.9	119.5	97	+/-2%	95	PASS
107	08/15/12	#3	15.3	114.2	13.7	115.6	101	+/-2%	95	PASS
108	08/15/12	#1	9.7	126.5	10.6	123.6	98	+/-2%	95	PASS
109	08/15/12	#3	15.3	114.2	13.4	116.1	102	+/-2%	95	PASS
110	08/15/12	#3	15.3	114.2	13.7	114.7	100	+/-2%	95	PASS
111							#DIV/0!			
112							#DIV/0!			
113							#DIV/0!			
114							#DIV/0!			

TEST #	LOCATION	ELEVATION
105	North 421228.10 East 1179216.50	1941.2
106	North 421250.80 East 1179341.55	1940.4
107	North 421159.45 East 1179335.60	1939.75
108	North 421292.70 East 1179491.85	1939.45
109	North 421261.20 East 1179545.20	1938.45
110	North 421175.25 East 1179545.40	1937.05
111		
112		
113		
114		

NOTES: Drill Pad Back Fill

RESPECTFULLY SUBMITTED

AMERICAN TECHNICAL SERVICES, INC.

**AMERICAN
TECHNICAL
SERVICES, INC.**

ENGINEERING • ENVIRONMENTAL • DRILLING • MATERIALS
8105 Black Hawk Rd. • PO Box 558
Black Hawk, SD 57718-0558

REPORT OF SOIL DENSITY TESTING - NUCLEAR METHOD

ASTM D6938

CLIENT: CONTINENTAL RESOURCES, INC.
PO Box 268836
Oklahoma City, OK 73126

ATTENTION: Project Manager
PROJECT: Atlanta Drill Site

ATS #: 12-12165
DATE: 08/17/12
ATS TECH: Russell Harwood
GAGE #: 2
BENCHMARK: _____

TEST #	DATE	PROCTOR # / CLASSIFICATION	LABORATORY		FIELD		SPECIFICATIONS			
			% MOIST	DRY DENSITY	% MOISTURE	DRY DENSITY	% COMPACTION	SPEC MOISTURE %	SPEC COMPACTION	PASS
119	08/16/12	#1	15.3	114.2	13.7	110.0	96	+/-2%	95	PASS
120	08/16/12	#1	15.3	114.2	13.9	112.0	98	+/-2%	95	PASS
121	08/16/12	#1	15.3	114.2	13.6	112.4	98	+/-2%	95	PASS
122	08/16/12	#1	15.3	114.2	13.4	112.6	99	+/-2%	95	PASS
123	08/16/12	#1	15.3	114.2	13.6	114.0	100	+/-2%	95	PASS
124	08/16/12	#1	15.3	114.2	13.9	115.2	101	+/-2%	95	PASS
125							#DIV/0!			
126							#DIV/0!			
127							#DIV/0!			
128							#DIV/0!			

TEST #	LOCATION	ELEVATION
119	120' East of West Outlet	6' Above Top of Pipe
120	110' East of West Outlet	8' Above Top of Pipe
121	100' East of West Outlet	10' Above Top of Pipe
122	STA 2 + 80	6' Above Top of Pipe
123	STA 2 + 70	8' Above Top of Pipe
124	STA 2 + 60	10' Above Top of Pipe
125		
126		
127		
128		

NOTES: Northwest Storm Sewer Trench Back Fill

RESPECTFULLY SUBMITTED

CC:


AMERICAN TECHNICAL SERVICES, INC.

**AMERICAN
TECHNICAL
SERVICES, INC.**

ENGINEERING • ENVIRONMENTAL • DRILLING • MATERIALS
8105 Black Hawk Rd • PO Box 558
Black Hawk, SD 57718-0558

REPORT OF SOIL DENSITY TESTING - NUCLEAR METHOD

ASTM D6938

CLIENT: CONTINENTAL RESOURCES, INC.
PO Box 268836
Oklahoma City, OK 73126

ATTENTION: Project Manager
PROJECT: Atlanta Drill Site

ATS #: 12-12165
DATE: 08/17/12
ATS TECH: Russell Harwood
GAGE #: 2
BENCHMARK:

TEST #	DATE	PROCTOR # / CLASSIFICATION	LABORATORY		FIELD		SPECIFICATIONS			PASS
			% MOIST	DRY DENSITY	% MOISTURE	DRY DENSITY	% COMPACTION	SPEC MOISTURE %	SPEC COMPACTION	
116	08/16/12	#3	15.3	114.2	13.6	115.5	101	+/-2%	95	PASS
117	08/16/12	#3	15.3	114.2	13.3	111.5	98	+/-2%	95	PASS
118	08/16/12	#3	15.3	114.2	13.8	111.3	97	+/-2%	95	PASS
119							#DIV/0!			
120							#DIV/0!			
121							#DIV/0!			
122							#DIV/0!			
123							#DIV/0!			
124							#DIV/0!			
125							#DIV/0!			

TEST #	LOCATION	ELEVATION
116	North 421295.55 East 1179462.65	1941.3
117	North 421250.20 East 1179528.35	1939.95
118	North 421191.60 East 1179541.70	1939.5
119		
120		
121		
122		
123		
124		
125		

NOTES: Drill Pad Area

RESPECTFULLY SUBMITTED



AMERICAN TECHNICAL SERVICES, INC.

CC:

**AMERICAN
TECHNICAL
SERVICES, INC.**

ENGINEERING • ENVIRONMENTAL • DRILLING • MATERIALS
8105 Black Hawk Rd • P.O. Box 558
Black Hawk, SD 57718-0558

REPORT OF SOIL DENSITY TESTING - NUCLEAR METHOD
ASTM D6938

CLIENT CONTINENTAL RESOURCES, INC.
PO Box 268836
Oklahoma City, OK 73126
ATTENTION: Project Manager
PROJECT Atlanta Drill Site

ATS # 12-12165
DATE: 08/17/12
ATS TECH: Russell Harwood
GAGE # 2
BENCHMARK

TEST #	DATE	PROCTOR # / CLASSIFICATION	LABORATORY		FIELD		SPECIFICATIONS			
			% MOIST.	DRY DENSITY	% MOISTURE	DRY DENSITY	% COMPACTION	SPEC MOISTURE %	SPEC COMPACTION	PASS
113	08/16/12	#3	15.3	114.2	14.5	116.3	102	+/-2%	95	PASS
114	08/16/12	#2	8.3	123.2	9.4	119.5	97	+/-2%	95	PASS
115	08/16/12	#3	15.3	114.2	13.4	114.0	100	+/-2%	95	PASS
116							#DIV/0!			
117							#DIV/0!			
118							#DIV/0!			
119							#DIV/0!			
120							#DIV/0!			
121							#DIV/0!			
122							#DIV/0!			

TEST #	LOCATION	ELEVATION
113	North 421004.30 East 1180053.35	1925.95
114	North 421047.15 East 1179917.95	1929.8
115	North 421131.15 East 1179860.70	1923.2
116		
117		
118		
119		
120		
121		
122		

NOTES: East Valley Fill

RESPECTFULLY SUBMITTED

AMERICAN TECHNICAL SERVICES, INC.

**AMERICAN
TECHNICAL
SERVICES, INC.**

ENGINEERING • ENVIRONMENTAL • DRILLING • MATERIALS
8105 Black Hawk Rd. • PO Box 558
Black Hawk, SD 57718-0558

REPORT OF SOIL DENSITY TESTING - NUCLEAR METHOD

ASTM D6938

CLIENT: CONTINENTAL RESOURCES, INC.
PO Box 268836
Oklahoma City, OK 73126
ATTENTION: Project Manager
PROJECT: Atlanta Drill Site

ATS #: 12-12165
DATE: 08/20/12
ATS TECH: Russell Harwood
GAGE #: 2
BENCHMARK: _____

TEST #	DATE	PROCTOR#/CLASSIFICATION	LABORATORY		FIELD		SPECIFICATIONS			PASS
			% MOIST	DRY DENSITY	% MOISTURE	DRY DENSITY	% COMPACTION	SPEC MOISTURE	% SPEC COMPACTION	
125	08/17/12	#3	15.3	114.2	13.3	110.1	96	+/-2%	95	PASS
126	08/17/12	#1	9.7	126.5	10.4	122.2	97	+/-2%	95	PASS
127	08/17/12	#3	15.3	114.2	13.4	116.7	102	+/-2%	95	PASS
128							#DIV/0!			
129							#DIV/0!			
130							#DIV/0!			
131							#DIV/0!			
132							#DIV/0!			
133							#DIV/0!			
134							#DIV/0!			

TEST #	LOCATION		ELEVATION
125	421406.45	1178944.55	1951.4
126	421405.80	1179870.85	1952.55
127	421474.75	1179005.90	1952.45
128			
129			
130			
131			
132			
133			
134			

NOTES: Road Rebuild Going North & South Along West Side

RESPECTFULLY SUBMITTED

CC:

AMERICAN TECHNICAL SERVICES, INC.



**AMERICAN
TECHNICAL
SERVICES, INC.**

ENGINEERING • ENVIRONMENTAL • DRILLING • MATERIALS
8105 Black Hawk Rd • PO Box 558
Black Hawk, SD 57718-0558

REPORT OF SOIL DENSITY TESTING - NUCLEAR METHOD

ASTM D6938

CLIENT: CONTINENTAL RESOURCES, INC.
PO Box 268836
Oklahoma City, OK 73126
ATTENTION: Project Manager
PROJECT: Atlanta Drill Site

ATS #: 12-12165
DATE: 08/20/12
ATS TECH: Russell Harwood
GAGE #: 2
BENCHMARK:

TEST #	DATE	PROCTOR # / CLASSIFICATION	LABORATORY		FIELD		SPECIFICATIONS		
			% MOIST	DRY DENSITY	% MOISTURE	DRY DENSITY	% COMPACTION	SPEC MOISTURE %	SPEC COMPACTION
128	08/17/12	#1	9.7	126.5	10.3	126.5	100	+/-2%	95
129	08/17/12	#1	9.7	126.5	9.3	124.1	98	+/-2%	95
130	08/17/12	#1	9.7	126.5	10.2	124.2	98	+/-2%	95
131							#DIV/0!		
132							#DIV/0!		
133							#DIV/0!		
134							#DIV/0!		
135							#DIV/0!		
136							#DIV/0!		
137							#DIV/0!		

TEST #	LOCATION	ELEVATION
128	N 421184.10 E 117937.90	1943.55
129	N 421234.95 E 1179377.35	1943.6
130	N 421205.50 E 1179455.95	1943.55
131		
132		
133		
134		
135		
136		
137		

NOTES: Drill Pad Area

RESPECTFULLY SUBMITTED

CC:

AMERICAN TECHNICAL SERVICES, INC.

**AMERICAN
TECHNICAL
SERVICES, INC.**

ENGINEERING • ENVIRONMENTAL • DRILLING • MATERIALS
8105 Black Hawk Rd. • PO Box 558
Black Hawk, SD 57718-0558

REPORT OF SOIL DENSITY TESTING - NUCLEAR METHOD

ASTM D6938

CLIENT: CONTINENTAL RESOURCES, INC.
PO Box 268836
Oklahoma City, OK 73126

ATTENTION: Project Manager
PROJECT: Atlanta Drill Site

ATS #: 12-12165
DATE: 08/20/12
ATS TECH: Russell Harwood
GAGE #: 2
BENCHMARK:

TEST #	DATE	PROCTOR # / CLASSIFICATION	LABORATORY		FIELD		SPECIFICATIONS			
			% MOIST	DRY DENSITY	% MOISTURE	DRY DENSITY	% COMPACTION	SPEC MOISTURE	% SPEC COMPACTION	PASS
131	08/18/12	#2	8.3	123.2	9.0	118.4	96	+/-2%	95	PASS
132	08/18/12	#3	15.3	114.2	13.8	113.9	100	+/-2%	95	PASS
133	08/18/12	#3	15.3	114.2	13.6	113.3	99	+/-2%	95	PASS
134	08/18/12	#3	15.3	114.2	13.4	116.1	102	+/-2%	95	PASS
135	08/18/12	#2	8.3	123.2	9.1	118.5	96	+/-2%	95	PASS
136	08/18/12	#2	8.3	123.2	9.2	117.5	95	+/-2%	95	PASS
137							#DIV/0!			
138							#DIV/0!			
139							#DIV/0!			
140							#DIV/0!			

TEST #	LOCATION	ELEVATION
131	N 421121.60 E 1179889.35	1925.65
132	N 421052.95 E 1179930.80	1929.35
133	N 421037.40 E 1179997.15	1929.1
134	N 421186.90 E 1179885.25	1919.9
135	N 421258.50 E 1179843.35	1920
136	N 421339.55 E 1179823.35	1921.65
137		
138		
139		
140		

NOTES: All Test in East Valley.

RESPECTFULLY SUBMITTED

CC:

AMERICAN TECHNICAL SERVICES, INC.

**AMERICAN
TECHNICAL
SERVICES, INC.**

ENGINEERING • ENVIRONMENTAL • DRILLING • MATERIALS
8105 Black Hawk Rd. • PO Box 558
Black Hawk, SD 57718-0558

REPORT OF SOIL DENSITY TESTING - NUCLEAR METHOD

ASTM D6938

CLIENT: CONTINENTAL RESOURCES, INC.
PO Box 268836
Oklahoma City, OK 73126
ATTENTION: Project Manager
PROJECT: Atlanta Drill Site

ATS #: 12-12165
DATE: 08/20/12
ATS TECH: Russell Harwood
GAGE #: 2
BENCHMARK:

TEST #	DATE	PROCTOR # / CLASSIFICATION	LABORATORY		FIELD		SPECIFICATIONS			
			% MOIST	DRY DENSITY	% MOISTURE	DRY DENSITY	% COMPACTION	SPEC MOISTURE %	SPEC COMPACTION	PASS
137	08/19/12	#3	15.3	114.2	13.3	114.1	100	+/-2%	95	PASS
138	08/19/12	#3	15.3	114.2	14.2	113.5	99	+/-2%	95	PASS
139	08/19/12	#3	15.3	114.2	13.7	110.3	97	+/-2%	95	PASS
140	08/19/12	#3	15.3	114.2	13.5	115.5	101	+/-2%	95	PASS
141							#DIV/0!			
142							#DIV/0!			
143							#DIV/0!			
144							#DIV/0!			
145							#DIV/0!			
146							#DIV/0!			

TEST #	LOCATION	ELEVATION
137	N 421079.05 E 1180014.40	1927.3
138	N 421111.75 E 1179924.40	1928.6
139	N 421192.30 E 1179886.40	1920.7
140	N 421263.65 E 1179839.65	1922.1
141		
142		
143		
144		
145		
146		

NOTES: East Valley

RESPECTFULLY SUBMITTED

CC:

AMERICAN TECHNICAL SERVICES, INC.



**AMERICAN
TECHNICAL
SERVICES, INC.**

ENGINEERING • ENVIRONMENTAL • DRILLING • MATERIALS
8105 Black Hawk Rd. • PO Box 558
Black Hawk, SD 57718-0558

REPORT OF SOIL DENSITY TESTING - NUCLEAR METHOD

ASTM D6938

CLIENT: CONTINENTAL RESOURCES, INC.
PO Box 268836
Oklahoma City, OK 73126

ATTENTION: Project Manager
PROJECT: Atlanta Drill Site

ATS #: 12-12165
DATE: 08/20/12
ATS TECH: Russell Harwood
GAGE #: 2
BENCHMARK:

TEST #	DATE	PROCTOR # / CLASSIFICATION	LABORATORY		FIELD		SPECIFICATIONS			
			% MOIST	DRY DENSITY	% MOISTURE	DRY DENSITY	% COMPACTION	SPEC MOISTURE	% SPEC COMPACTION	PASS
141	08/19/12	#2	8.3	123.2	8.8	121.8	99	+/-2%	95	PASS
142	08/19/12	#2	8.3	123.2	7.2	122.1	99	+/-2%	95	PASS
143	08/19/12	#2	8.3	123.2	7.1	120.4	98	+/-2%	95	PASS
144	08/19/12	#1	9.7	126.5	9.6	123.8	98	+/-2%	95	PASS
145							#DIV/0!			
146							#DIV/0!			
147							#DIV/0!			
148							#DIV/0!			
149							#DIV/0!			
150							#DIV/0!			

TEST #	LOCATION	ELEVATION
141	N 421638.85 E 1178871.85	1963.85
142	N 421644.55 E 1178852.40	1964
143	N 421637.05 E 1178851.85	1967.65
144	N 421669.20 E 1178823.50	1969.9
145		
146		
147		
148		
149		
150		

NOTES: Over Culvert North Road

CC:

RESPECTFULLY SUBMITTED

AMERICAN TECHNICAL SERVICES, INC.



**AMERICAN
TECHNICAL
SERVICES, INC.**

ENGINEERING • ENVIRONMENTAL • DRILLING • MATERIALS
8105 Black Hawk Rd • PO Box 558
Black Hawk, SD 57718-0558

REPORT OF SOIL DENSITY TESTING - NUCLEAR METHOD

ASTM D6938

CLIENT:	CONTINENTAL RESOURCES, INC. PO Box 268836 Oklahoma City, OK 73126	ATS #:	12-12165
ATTENTION:	Project Manager	DATE	08/23/12
PROJECT:	Atlanta Drill Site	ATS TECH:	Russell Harwood
		GAGE #:	2
		BENCHMARK:	

TEST #	DATE	PROCTOR # / CLASSIFICATION	LABORATORY		FIELD		SPECIFICATIONS			
			% MOIST	DRY DENSITY	% MOISTURE	DRY DENSITY	% COMPACTION	SPEC MOISTURE %	SPEC COMPACTION	PASS
145	08/20/12	#3	15.3	114.2	13.4	115.6	101	+/-2%	95	PASS
146	08/20/12	#2	8.3	123.2	7.2	121.5	99	+/-2%	95	PASS
147	08/20/12	#3	15.3	114.2	13.8	115.9	101	+/-2%	95	PASS
148	08/20/12	#3	15.3	114.2	14.2	111.6	98	+/-2%	95	PASS
149							#DIV/0!			
150							#DIV/0!			
151							#DIV/0!			
152							#DIV/0!			
153							#DIV/0!			
154							#DIV/0!			

TEST #	LOCATION	ELEVATION
145	N 421166.85 E 1179865.40	1922.8
146	N 421256.90 E 1179836.55	1923.95
147	N 420996.10 E 1180218.95	1928.9
148	N 421096.00 E 1180016.65	1927.85
149		
150		
151		
152		
153		
154		

NOTES: East Valley Fill

RESPECTFULLY SUBMITTED

CC

AMERICAN TECHNICAL SERVICES, INC.

**AMERICAN
TECHNICAL
SERVICES, INC.**

ENGINEERING • ENVIRONMENTAL • DRILLING • MATERIALS
8105 Black Hawk Rd. • PO Box 558
Black Hawk, SD 57718-0558

REPORT OF SOIL DENSITY TESTING - NUCLEAR METHOD

ASTM D6938

CLIENT: CONTINENTAL RESOURCES, INC.
PO Box 268836
Oklahoma City, OK 73126

ATTENTION: Project Manager
PROJECT: Atlanta Drill Site

ATS #: 12-12165
DATE: 08/23/12
ATS TECH: Russell Harwood
GAGE #: 2
BENCHMARK:

TEST #	DATE	PROCTOR#/ CLASSIFICATION	LABORATORY		FIELD		SPECIFICATIONS			PASS
			% MOIST	DRY DENSITY	% MOISTURE	DRY DENSITY	% COMPACTION	SPEC MOISTURE %	SPEC COMPACTION	
149	08/21/12	#3	15.3	114.2	15.2	111.7	98	+/-2%	95	PASS
150	08/21/12	#3	15.3	114.2	15.1	113.9	100	+/-2%	95	PASS
151	08/21/12	#3	15.3	114.2	15.8	109.2	96	+/-2%	95	PASS
152	08/21/12	#3	15.3	114.2	13.4	112.2	98	+/-2%	95	PASS
153	08/21/12	#1	9.7	126.5	9.8	122.0	96	+/-2%	95	PASS
154							#DIV/0!			
155							#DIV/0!			
156							#DIV/0!			
157							#DIV/0!			
158							#DIV/0!			

TEST #	LOCATION	ELEVATION
149	N 421037.20 E 1180130.55	1932.6
150	N 421061.85 E 1179979.85	1933.1
151	N 421067.40 E 1180184.00	1936.15
152	N 421064.45 E 1180152.60	1937.45
153	N 421025.40 E 1180078.60	1935.85
154		
155		
156		
157		
158		

NOTES: East Valley Fill

RESPECTFULLY SUBMITTED

CC:

AMERICAN TECHNICAL SERVICES, INC.



**AMERICAN
TECHNICAL
SERVICES, INC.**

Engineering • Environmental • Drilling • Materials
3105 Black Hawk Rd. • PO Box 558
Black Hawk, SD 57713-0558

REPORT OF SOIL DENSITY TESTING - NUCLEAR METHOD

ASTM D6938

CLIENT: CONTINENTAL RESOURCES, INC.
PO Box 268836
Oklahoma City, OK 73126
ATTENTION: Project Manager
PROJECT: Atlanta Drill Site

ATS #: 12-12165
DATE: 08/23/12
ATS TECH: Russell Harwood
GAGE #: 2
BENCHMARK:

TEST #	DATE	PROCTOR # / CLASSIFICATION	LABORATORY		FIELD			SPECIFICATIONS		
			% MOIST	DRY DENSITY	% MOISTURE	DRY DENSITY	% COMPACTION	SPEC MOISTURE %	SPEC COMPACTION	PASS
154	08/22/12	#3	15.3	114.2	14.7	108.8	95	+/-2%	95	PASS
155	08/22/12	#3	15.3	114.2	14.3	110.2	96	+/-2%	95	PASS
156	08/22/12	#3	15.3	114.2	14.4	109.7	96	+/-2%	95	PASS
157	08/22/12	#3	15.3	114.2	13.8	110.5	97	+/-2%	95	PASS
158	08/22/12	#3	15.3	114.2	13.5	113.9	100	+/-2%	95	PASS
159	08/22/12	#3	15.3	114.2	13.3	110.0	96	+/-2%	95	PASS
160							#DIV/0!			
161							#DIV/0!			
162							#DIV/0!			
163							#DIV/0!			

TEST #	LOCATION	ELEVATION
154	N 421280.95 E 1178919.20	1926.3
155	N 421212.65 E 1179814.85	1925.7
156	N 421284.60 E 1179834.35	1926.75
157	N 421178.25 E 1179842.25	1929.45
158	N 421253.35 E 1179825.80	1928.9
159	N 421234.00 E 1179906.10	1928.15
160		
161		
162		
163		

NOTES: _____

CC: _____

RESPECTFULLY SUBMITTED

AMERICAN TECHNICAL SERVICES, INC.



**AMERICAN
TECHNICAL
SERVICES, INC.**

ENGINEERING • ENVIRONMENTAL • DRILLING • MATERIALS
8105 Black Hawk Rd • PO Box 558
Black Hawk, SD 57718-0558

REPORT OF SOIL DENSITY TESTING - NUCLEAR METHOD

ASTM D6938

CLIENT	CONTINENTAL RESOURCES, INC. PO Box 268836 Oklahoma City, OK 73126	ATS #	12-12165
ATTENTION:	Project Manager	DATE	08/28/12
PROJECT:	Atlanta Drill Site	ATS TECH	Russell Harwood
		GAGE #	2
		BENCHMARK	

TEST #	DATE	PROCTOR # / CLASSIFICATION	LABORATORY		FIELD		SPECIFICATIONS			
			% MOIST	DRY DENSITY	% MOISTURE	DRY DENSITY	% COMPACTION	SPEC MOISTURE	% SPEC COMPACTION	PASS
160	08/23/12	#3	15.3	114.2	13.3	111.8	98	+/-2%	95	PASS
161	08/23/12	#2	8.3	123.2	9.3	118.7	96	+/-2%	95	PASS
162	08/23/12	#3	15.3	114.2	13.7	115.4	101	+/-2%	95	PASS
163	08/23/12	#3	15.3	114.2	13.4	109.7	96	+/-2%	95	PASS
164	08/23/12	#3	15.3	114.2	13.6	109.3	96	+/-2%	95	PASS
165	08/23/12	#3	15.3	114.2	13.4	115.6	101	+/-2%	95	PASS
166	08/23/12	#3	15.3	114.2	13.5	113.9	100	+/-2%	95	PASS
167							#DIV/0!			
168							#DIV/0!			
169							#DIV/0!			

TEST #	LOCATION	ELEVATION
160	N 421096.35 E 1179858.25	1934.6
161	N 421213.05 E 1179810.50	1932.55
162	N 421263.40 E 1179882.15	1930.9
163	N 421144.40 E 1179949.80	1931.65
164	N 421153.10 E 1179905.35	1933.6
165	N 421225.20 E 1179886.80	1933.15
166	N 421206.55 E 1179945.15	1932.5
167		
168		
169		

NOTES: _____

RESPECTFULLY SUBMITTED

AMERICAN TECHNICAL SERVICES, INC.

CC:

**AMERICAN
TECHNICAL
SERVICES, INC.**

ENGINEERING • ENVIRONMENTAL • DRILLING • MATERIALS
8105 Black Hawk Rd. • PO Box 558
Black Hawk, SD 57718-0558

REPORT OF SOIL DENSITY TESTING - NUCLEAR METHOD

ASTM D6938

CLIENT:	CONTINENTAL RESOURCES, INC
	PO Box 268836
	Oklahoma City, OK 73126
ATTENTION:	Project Manager
PROJECT:	Atlanta Drill Site

ATS #:	12-12165
DATE:	08/28/12
ATS TECH:	Russell Harwood
GAGE #:	2
BENCHMARK:	

TEST #	DATE	PROCTOR #/CLASSIFICATION	LABORATORY		FIELD		SPECIFICATIONS			
			% MOIST	DRY DENSITY	% MOISTURE	DRY DENSITY	% COMPACTION	SPEC MOISTURE %	SPEC COMPACTION	PASS
167	08/24/12	#3	15.3	114.2	14.3	112.8	99	+/-2%	95	PASS
168	08/24/12	#2	8.3	123.2	9.2	119.9	97	+/-2%	95	PASS
169	08/24/12	#2	8.3	123.2	9.4	118.5	96	+/-2%	95	PASS
170							#DIV/0!			
171							#DIV/0!			
172							#DIV/0!			
173							#DIV/0!			
174							#DIV/0!			
175							#DIV/0!			
176							#DIV/0!			

TEST #	LOCATION	ELEVATION
167	N 421222.70 E 1179902.60	1934.85
168	N 421303.55 E 1179866.40	1934.45
169	N 421401.35 E 1179821.85	1933.25
170		
171		
172		
173		
174		
175		
176		

NOTES: _____

RESPECTFULLY SUBMITTED

~~AMERICAN TECHNICAL SERVICES, INC.~~

**AMERICAN
TECHNICAL
SERVICES, INC.**

ENGINEERING • ENVIRONMENTAL • DRILLING • MATERIALS
8105 Black Hawk Rd • PO Box 558
Black Hawk, SD 57718-0558

REPORT OF SOIL DENSITY TESTING - NUCLEAR METHOD

ASTM D6938

CLIENT: **CONTINENTAL RESOURCES, INC.**
PO Box 268836
Oklahoma City, OK 73126

ATTENTION: Project Manager
PROJECT: Atlanta Drill Site

ATS #: 12-12165
DATE: 08/28/12
ATS TECH: Evan Schultze
GAGE #: 2
BENCHMARK: East Valley Fill

TEST #	DATE	PROCTOR # / CLASSIFICATION	LABORATORY		FIELD		SPECIFICATIONS			PASS
			% MOIST	DRY DENSITY	% MOISTURE	DRY DENSITY	% COMPACTION	SPEC MOISTURE	% SPEC COMPACTION	
170	08/24/12	#3	15.3	114.2	14.6	113.5	99	+/-2%	95	PASS
171	08/24/12	#3	15.3	114.2	14.4	111.8	98	+/-2%	95	PASS
172	08/24/12	#3	15.3	114.2	14.9	112.3	98	+/-2%	95	PASS
173							#DIV/0!			
174							#DIV/0!			
175							#DIV/0!			
176							#DIV/0!			
177							#DIV/0!			
178							#DIV/0!			
179							#DIV/0!			

TEST #	LOCATION	ELEVATION
170	N 421153.30 E 1179861.65	1936.7
171	N 421252.75 E 1179826.85	1936.5
172	N 421346.00 E 1179790.95	1936.6
173		
174		
175		
176		
177		
178		
179		

NOTES:

RESPECTFULLY SUBMITTED

AMERICAN TECHNICAL SERVICES, INC.

CC:

**AMERICAN
TECHNICAL
SERVICES, INC.**

ENGINEERING • ENVIRONMENTAL • DRILLING • MATERIALS
8105 Black Hawk Rd • PO Box 558
Black Hawk, SD 57719-0558

REPORT OF SOIL DENSITY TESTING - NUCLEAR METHOD

ASTM D6938

CLIENT: CONTINENTAL RESOURCES, INC.
PO Box 268836
Oklahoma City, OK 73126

ATTENTION: Project Manager
PROJECT: Atlanta Drill Site

ATS #: 12-12165
DATE: 08/28/12
ATS TECH: Evan Schultze
GAGE #: 2
BENCHMARK: South Road Culvert Back Fill

TEST #	DATE	PROCTOR # / CLASSIFICATION	LABORATORY		FIELD			SPECIFICATIONS		
			% MOIST	DRY DENSITY	% MOISTURE	DRY DENSITY	% COMPACTION	SPEC MOISTURE %	SPEC COMPACTION	PASS
191	08/25/12	#3	15.3	114.2	14.0	110.5	97	+/-2%	95	PASS
192							#DIV/0!			
193							#DIV/0!			
194							#DIV/0!			
195							#DIV/0!			
196							#DIV/0!			
197							#DIV/0!			
198							#DIV/0!			
199							#DIV/0!			
200							#DIV/0!			

TEST #	LOCATION	ELEVATION
191	3' East of Center of Pipe-77' South of Type 2 Inlet at STA 545 + 70	5' Above Pipe
192		
193		
194		
195		
196		
197		
198		
199		
200		

NOTES: _____

RESPECTFULLY SUBMITTED

AMERICAN TECHNICAL SERVICES, INC.

CC:

**AMERICAN
TECHNICAL
SERVICES, INC.**

ENGINEERING • ENVIRONMENTAL • DRILLING • MATERIALS
8105 Black Hawk Rd • PO Box 558
Black Hawk, SD 57718-0558

REPORT OF SOIL DENSITY TESTING - NUCLEAR METHOD
ASTM D6938

CLIENT: **CONTINENTAL RESOURCES, INC.**
PO Box 268836
Oklahoma City, OK 73126

ATTENTION: Project Manager
PROJECT: Atlanta Drill Site

ATS #: 12-12165
DATE: 08/28/12
ATS TECH: Evan Schultze
GAGE #: 2
BENCHMARK: East Valley Fill

TEST #	DATE	PROCTOR # / CLASSIFICATION	LABORATORY		FIELD		SPECIFICATIONS			
			% MOIST	DRY DENSITY	% MOISTURE	DRY DENSITY	% COMPACTION	SPEC MOISTURE %	SPEC COMPACTION	PASS
173	08/25/12	#1	9.7	126.5	10.1	121.4	96	+/-2%	95	PASS
174	08/25/12	#1	9.7	126.5	9.4	121.7	96	+/-2%	95	PASS
175	08/25/12	#2	8.3	123.2	7.8	119.7	97	+/-2%	95	PASS
176							#DIV/0!			
177							#DIV/0!			
178							#DIV/0!			
179							#DIV/0!			
180							#DIV/0!			
181							#DIV/0!			
182							#DIV/0!			

TEST #	LOCATION	ELEVATION
173	N 421098.70 E 1179890.60	1936.15
174	N 421274.30 E 1179841.15	1936.7
175	N 421152.42 E 1179836.80	1937.7
176		
177		
178		
179		
180		
181		
182		

NOTES: _____

CC: _____

RESPECTFULLY SUBMITTED


AMERICAN TECHNICAL SERVICES, INC.

**AMERICAN
TECHNICAL
SERVICES, INC.**

ENGINEERING • ENVIRONMENTAL • DRILLING • MATERIALS
8105 Black Hawk Rd • PO Box 558
Black Hawk, SD 57718-0558

REPORT OF SOIL DENSITY TESTING - NUCLEAR METHOD

ASTM D6938

CLIENT: CONTINENTAL RESOURCES, INC.
PO Box 268836
Oklahoma City, OK 73126
ATTENTION: Project Manager
PROJECT: Atlanta Drill Site

ATS #: 12-12165
DATE: 08/28/12
ATS TECH: Evan Schultze
GAGE #: 2
BENCHMARK: East Valley Fill

TEST #	DATE	PROCTOR # / CLASSIFICATION	LABORATORY		FIELD		SPECIFICATIONS			
			% MOIST	DRY DENSITY	% MOISTURE	DRY DENSITY	% COMPACTION	SPEC MOISTURE %	SPEC COMPACTION	PASS
176	08/26/12	#1	9.7	126.5	9.5	123.2	97	+/-2%	95	PASS
177	08/26/12	#3	15.3	114.2	14.8	114.0	100	+/-2%	95	PASS
178	08/26/12	#2	8.3	123.2	8.6	121.6	99	+/-2%	95	PASS
179	08/26/12	#2	8.3	123.2	8.4	119.5	97	+/-2%	95	PASS
180	08/26/12	#1	9.7	126.5	8.9	126.3	100	+/-2%	95	PASS
181							#DIV/0!			
182							#DIV/0!			
183							#DIV/0!			
184							#DIV/0!			
185							#DIV/0!			

TEST #	LOCATION	ELEVATION
176	N 421289.45 E 1179811.95	1937.6
177	N 421261.50 E 1179823.70	1936.9
178	N 421129.50 E 1179936.90	1938.3
179	N 421407.25 E 1179820.20	1937.4
180	N 421405.25 E 1179828.90	1937.25
181		
182		
183		
184		
185		

NOTES:

RESPECTFULLY SUBMITTED

AMERICAN TECHNICAL SERVICES, INC.

CC:

**AMERICAN
TECHNICAL
SERVICES, INC.**

BURNDLEY • ENVIRONMENTAL • DRILLING • MATERIALS
8105 Black Hawk Rd • PO Box 558
Black Hawk, SD 57713-0558

REPORT OF SOIL DENSITY TESTING - NUCLEAR METHOD

ASTM D6938

CLIENT: CONTINENTAL RESOURCES, INC.
PO Box 268836
Oklahoma City, OK 73126

ATTENTION: Project Manager
PROJECT: Atlanta Drill Site

ATS #: 12-12165
DATE: 08/28/12
ATS TECH: Evan Schultze
GAGE #: 2
BENCHMARK: South Road Culvert Back Fill

TEST #	DATE	PROCTOR # / CLASSIFICATION	LABORATORY		FIELD		SPECIFICATIONS		PASS
			% MOIST	DRY DENSITY	% MOISTURE	DRY DENSITY	% COMPACTION	SPEC MOISTURE %	
192	08/26/12	#3	15.3	114.2	15.7	112.8	99	+/-2%	95
193	08/26/12	#3	15.3	114.2	14.2	114.1	100	+/-2%	95
194	08/26/12	#3	15.3	114.2	13.9	113.7	100	+/-2%	95
195	08/26/12	#3	15.3	114.2	15.1	113.9	100	+/-2%	95
196							#DIV/0!		
197							#DIV/0!		
198							#DIV/0!		
199							#DIV/0!		
200							#DIV/0!		
201							#DIV/0!		

TEST #	LOCATION	ELEVATION
192	3' West of Center Pipe-60' South of Type 2 Inlet at STA 545 + 71	4' Above Pipe
193	Center of Pipe-65' South of Type 2 Inlet at STA 545 + 72	7' Above Pipe
194	2' East of Center of Pipe-55' South of Type 2 Inlet at STA 545 + 73	10' Above Pipe
195	2' West of Center of Pipe-50' South of type 2 Inlet at STA 545 + 74	12' Above Pipe
196		
197		
198		
199		
200		
201		

NOTES: _____

CC: _____

RESPECTFULLY SUBMITTED

AMERICAN TECHNICAL SERVICES, INC.

AMERICAN
TECHNICAL
SERVICES, INC.

Engineering • Environmental • Drilling • Mapping
8105 Black Hawk Rd • PO Box 558
Black Hawk, SD 57718-0558

REPORT OF SOIL DENSITY TESTING - NUCLEAR METHOD

ASTM D6938

CLIENT: CONTINENTAL RESOURCES, INC.
PO Box 268836
Oklahoma City, OK 73126

ATTENTION: Project Manager
PROJECT: Atlanta Drill Site

ATS #: 12-12165
DATE: 08/28/12
ATS TECH: Evan Schultze
GAGE #: 2
BENCHMARK: East Valley Fill


TEST #	DATE	PROCTOR # / CLASSIFICATION	LABORATORY		FIELD			SPECIFICATIONS	
			% MOIST	DRY DENSITY	% MOISTURE	DRY DENSITY	% COMPACTION	SPEC MOISTURE %	SPEC COMPACTION
181	08/27/12	#1	9.7	126.5	9.9	120.5	95	+/-2%	95
182	08/27/12	#3	15.3	114.2	13.9	111.8	98	+/-2%	95
183	08/27/12	#2	8.3	123.2	8.1	120.1	97	+/-2%	95
184	08/27/12	#3	15.3	114.2	15.0	113.8	100	+/-2%	95
185	08/27/12	#3	15.3	114.2	14.8	111.3	97	+/-2%	95
186	08/27/12	#3	15.3	114.2	14.2	112.7	99	+/-2%	95
187	08/27/12	#3	15.3	114.2	14.9	112.7	99	+/-2%	95
188	08/27/12	#3	15.3	114.2	13.9	112.8	99	+/-2%	95
189	08/27/12	#1	9.7	126.5	10.1	122.0	96	+/-2%	95
190	08/27/12	#3	15.3	114.2	14.0	111.8	98	+/-2%	95

TEST #	LOCATION	ELEVATION
181	N 421380.15 E 1179686.15	1939.3
182	N 421450.10 E 1179722.45	1940.2
183	N 421439.30 E 1179760.00	1941.5
184	N 421399.40 E 1179722.30	1941.95
185	N 421415.95 E 1179832.95	1942.2
186	N 421485.05 E 1179852.75	1942.95
187	N 421491.20 E 1179749.45	1943.1
188	N 421264.40 E 1179734.90	1938.2
189	N 421224.35 E 1179924.85	1937.5
190	N 421295.60 E 1180039.95	1937.35


NOTES: _____

CC: _____

RESPECTFULLY SUBMITTED



AMERICAN TECHNICAL SERVICES, INC.



REPORT OF SOIL DENSITY TESTING - NUCLEAR METHOD

ASTM D6938

Engineering • Environmental • Drilling • Materials
8105 Black Hawk Rd. • PO Box 558
Black Hawk, CO 80426-0558

CLIENT:	CONTINENTAL RESOURCES, INC. PO Box 268836 Oklahoma City, OK 73126
ATTENTION:	Project Manager
PROJECT:	Atlanta Drill Site

ATS #: 12-12165
DATE: 08/28/12
ATS TECH: Evan Schultze
GAGE #: 2
BENCHMARK: South Road Culvert Back Fill

TEST #	DATE	PROCTOR # / CLASSIFICATION	LABORATORY		FIELD			SPECIFICATIONS		
			% MOIST	DRY DENSITY	% MOISTURE	DRY DENSITY	% COMPACTION	SPEC MOISTURE %	SPEC COMPACTION	PASS
196	08/27/12	#3	15.3	114.2	14.8	112.8	99	+/-2%	95	PASS
197							#DIV/0!			
198							#DIV/0!			
199							#DIV/0!			
200							#DIV/0!			
201							#DIV/0!			
202							#DIV/0!			
203							#DIV/0!			
204							#DIV/0!			
205							#DIV/0!			

TEST #	LOCATION	ELEVATION
196	1' East of Center of Pipe-12' South of type 2 Inlet at STA 545 + 75	5' Above Pipe
197		
198		
199		
200		
201		
202		
203		
204		
205		

NOTES: _____

RESPECTFULLY SUBMITTED


AMERICAN TECHNICAL

AMERICAN TECHNICAL SERVICES, INC.

REPORT OF SOIL DENSITY TESTING - NUCLEAR METHOD
ASTM D6938

CLIENT: **CONTINENTAL RESOURCES, INC.**
 PO Box 268836
 Oklahoma City, OK 73126

ATTENTION: Project Manager
 PROJECT: Atlanta Drill Site

ATS #: 12-12165
 DATE: 08/31/12
 ATS TECH: Evan Schultze
 GAGE #: 2
 BENCHMARK: East Valley Fill

TEST #	DATE	PROCTOR # / CLASSIFICATION	LABORATORY		FIELD			SPECIFICATIONS		
			% MOIST	DRY DENSITY	% MOISTURE	DRY DENSITY	% COMPACTION	SPEC MOISTURE	% SPEC COMPACT	PASS
197	08/28/12	#1	9.7	126.5	8.2	121.3	96	+/-2%	95	PASS
198	08/28/12	#1	9.7	126.5	9.6	123.2	97	+/-2%	95	PASS
199	08/28/12	#1	9.7	126.5	9.8	124.5	98	+/-2%	95	PASS
200	08/28/12	#1	9.7	126.5	9.3	123.6	98	+/-2%	95	PASS
201							#DIV/0!			
202							#DIV/0!			
203							#DIV/0!			
204							#DIV/0!			
205							#DIV/0!			
206							#DIV/0!			

TEST #	LOCATION	ELEVATION
197	421186.95 1180094.55	1939.05
198	421133.25 1179974.25	1938.15
199	421273.45 1179880.10	1937.65
200	421117.15 1179767.85	1938.8
201		
202		
203		
204		
205		
206		

NOTES: _____

RESPECTFULLY SUBMITTED

CC:

AMERICAN TECHNICAL SERVICES, INC.

**AMERICAN
TECHNICAL
SERVICES, INC.**

ENGINEERING • ENVIRONMENTAL • DRILLING • MATERIALS
8105 Black Hawk Rd • PO Box 558
Black Hawk, SD 57718-0558

REPORT OF SOIL DENSITY TESTING - NUCLEAR METHOD
ASTM D6938

CLIENT: **CONTINENTAL RESOURCES, INC.**
PO Box 268836
Oklahoma City, OK 73126

ATTENTION: Project Manager
PROJECT: Atlanta Drill Site

ATS #: 12-12165
DATE: 08/31/12
ATS TECH: Evan Schultze
GAGE #: 2
BENCHMARK:

TEST #	DATE	PROCTOR # / CLASSIFICATION	LABORATORY		FIELD		SPECIFICATIONS			
			% MOIST	DRY DENSITY	% MOISTURE	DRY DENSITY	% COMPACTION	SPEC MOISTURE %	SPEC COMPACTION	PASS
201	08/29/12	#3	15.3	114.2	15.0	112.1	98	+/-2%	95	PASS
202							#DIV/0!			
203							#DIV/0!			
204							#DIV/0!			
205							#DIV/0!			
206							#DIV/0!			
207							#DIV/0!			
208							#DIV/0!			
209							#DIV/0!			
210							#DIV/0!			

TEST #	LOCATION	ELEVATION
201	60' North of Type 2 Inlet at STA 545 + 70	4' Above Pipe
202		
203		
204		
205		
206		
207		
208		
209		
210		

NOTES:

RESPECTFULLY SUBMITTED

AMERICAN TECHNICAL SERVICES, INC.



CC:

**AMERICAN
TECHNICAL
SERVICES, INC.**

Engineering • Environmental • Drilling • Materials
8105 Black Hawk Rd. • PO Box 558
Black Hawk, SD 57718-0558

REPORT OF SOIL DENSITY TESTING - NUCLEAR METHOD

ASTM D6938

CLIENT: **CONTINENTAL RESOURCES, INC.**
PO Box 268836
Oklahoma City, OK 73126
ATTENTION: Project Manager
PROJECT: Atlanta Drill Site

ATS #: 12-12165
DATE: 09/04/12
ATS TECH: Russell Harwood
GAGE #: 2
BENCHMARK:

TEST #	DATE	PROCTOR # / CLASSIFICATION	LABORATORY		FIELD			SPECIFICATIONS	
			% MOIST	DRY DENSITY	% MOISTURE	DRY DENSITY	% COMPACTION	SPEC MOISTURE %	SPEC COMPACTION
202	08/30/12	#2	8.3	123.2	9.7	122.5	99	+/-2%	95
203	08/30/12	#3	15.3	114.2	13.4	115.7	101	+/-2%	95
204	08/30/12	#3	15.3	114.2	13.6	113.0	99	+/-2%	95
205	08/30/12	#3	15.3	114.2	13.5	113.4	99	+/-2%	95
206							#DIV/0!		
207							#DIV/0!		
208							#DIV/0!		
209							#DIV/0!		
210							#DIV/0!		
211							#DIV/0!		

TEST #	LOCATION	ELEVATION
202	200' North of South Manhole	3' Below Grade
203	120' North of South Manhole	2' Below Grade
204	250' North of South Manhole	1' Below Grade
205	80' North of South Manhole	1' Below Grade
206		
207		
208		
209		
210		
211		

NOTES: Storm Sewer in Drill Pad Area

CC:

RESPECTFULLY SUBMITTED

AMERICAN TECHNICAL SERVICES, INC.



**AMERICAN
TECHNICAL
SERVICES, INC.**

ENGINEERING • ENVIRONMENTAL • DRILLING • MATERIALS
8105 Black Hawk Rd. • PO Box 558
Black Hawk, SD 57718-0558

REPORT OF SOIL DENSITY TESTING - NUCLEAR METHOD

ASTM D6938

CLIENT CONTINENTAL RESOURCES, INC.
PO Box 268836
Oklahoma City, OK 73126

ATTENTION Project Manager

PROJECT Atlanta Drill Site

ATS # 12-12165
DATE 09/04/12
ATS TECH Russell Harwood
GAGE # 2
BENCHMARK

TEST #	DATE	PROCTOR # / CLASSIFICATION	LABORATORY		FIELD		SPECIFICATIONS			
			% MOIST	DRY DENSITY	% MOISTURE	DRY DENSITY	% COMPACTION	SPEC MOISTURE %	SPEC COMPACTION	PASS
206	09/01/12	#1	9.7	126.5	9.2	123.4	98	+/-2%	95	PASS
207	09/01/12	#2	8.3	123.2	8.7	121.5	99	+/-2%	95	PASS
208	09/01/12	#2	8.3	123.2	9.3	117.5	95	+/-2%	95	PASS
209	09/01/12	#1	9.7	126.5	10.5	120.4	95	+/-2%	95	PASS
210	09/01/12	#1	9.7	126.5	8.9	122.6	97	+/-2%	95	PASS
211	09/01/12	#1	9.7	126.5	9.0	120.5	95	+/-2%	95	PASS
212	09/01/12	#3	15.3	114.2	13.3	114.1	100	+/-2%	95	PASS
213							#DIV/0!			
214							#DIV/0!			
215							#DIV/0!			

TEST #	LOCATION	ELEVATION
206	N 421148.50 E 1179772.65	1939
207	N 421278.05 E 1179873.65	1936.95
208	N 421243.90 E 1179995.40	1937
209	N 421256.85 E 1180111.45	1937
210	N 421246.20 E 1180276.70	1936.7
211	N 421165.45 E 1180219.90	1937
212	N 421131.65 E 1180128.40	1937
213		
214		
215		

NOTES: Drill Pad Subgrade Pre-Liner

RESPECTFULLY SUBMITTED

CC:

AMERICAN TECHNICAL SERVICES, INC.



**AMERICAN
TECHNICAL
SERVICES, INC.**

ENGINEERING • ENVIRONMENTAL • DRILLING • MATERIALS
8105 Black Hawk Rd • PO Box 558
Black Hawk, SD 57718-0558

REPORT OF SOIL DENSITY TESTING - NUCLEAR METHOD

ASTM D6938

CLIENT: CONTINENTAL RESOURCES, INC.
PO Box 268836
Oklahoma City, OK 73126

ATTENTION: Project Manager
PROJECT: Atlanta Drill Site

ATS #: 12-12165
DATE: 09/04/12
ATS TECH: Russell Harwood
GAGE #: 2
BENCHMARK:

TEST #	DATE	PROCTOR # / CLASSIFICATION	LABORATORY		FIELD			SPECIFICATIONS		
			% MOIST	DRY DENSITY	% MOISTURE	DRY DENSITY	% COMPACTION	SPEC MOISTURE %	SPEC COMPACTION	PASS
213	09/02/12	#3	15.3	114.2	13.4	112.5	99	+/-2%	95	PASS
214	09/02/12	#2	8.3	123.2	8.5	119.2	97	+/-2%	95	PASS
215	09/02/12	#2	8.3	123.2	7.6	119.4	97	+/-2%	95	PASS
216	09/02/12	#3	15.3	114.2	13.6	114.1	100	+/-2%	95	PASS
217	09/02/12	#3	15.3	114.2	13.5	114.1	100	+/-2%	95	PASS
218	09/02/12	#1	9.7	126.5	9.2	121.9	96	+/-2%	95	PASS
219	09/02/12	#1	9.7	126.5	8.5	121.7	96	+/-2%	95	PASS
220							#DIV/0!			
221							#DIV/0!			
222							#DIV/0!			

TEST #	LOCATION	ELEVATION
213	N 421177.85 E 1179944.00	1939.2
214	N 421197.20 E 1179980.55	1938.5
215	N 421155.10 E 1180018.00	1938.65
216	N 421161.40 E 1179809.10	1940.8
217	N 421166.65 E 1179943.15	1940.55
218	N 421198.80 E 1179984.45	1939.55
219	N 421207.30 E 1179940.30	1939.9
220		
221		
222		

NOTES: Drill Pad Area Over Liner Fill

RESPECTFULLY SUBMITTED

CC:

AMERICAN TECHNICAL SERVICES, INC.





Engineering • Environmental • Drilling • Materials
8105 Black Hawk Rd. • PO Box 556
Black Hawk, SD 57718-0556

REPORT OF SOIL DENSITY TESTING - NUCLEAR METHOD
ASTM D6938

CLIENT: CONTINENTAL RESOURCES, INC.
PO Box 268836
Oklahoma City, OK 73126
ATTENTION: Project Manager
PROJECT: Atlanta Drill Site

ATS #: 12-12165
DATE: 09/04/12
ATS TECH: Russell Harwood
GAGE #: 2
BENCHMARK:

TEST #	DATE	PROCTOR # / CLASSIFICATION	LABORATORY		FIELD			SPECIFICATIONS	
			% MOIST	DRY DENSITY	% MOISTURE	DRY DENSITY	% COMPACTION	SPEC MOISTURE %	SPEC COMPACTION
220	09/03/12	#3	15.3	114.2	13.7	114.9	101	+/-2%	95
221	09/03/12	#3	15.3	114.2	13.4	114.1	100	+/-2%	95
222	09/03/12	#3	15.3	114.2	13.8	114.8	101	+/-2%	95
223							#DIV/0!		
224							#DIV/0!		
225							#DIV/0!		
226							#DIV/0!		
227							#DIV/0!		
228							#DIV/0!		
229							#DIV/0!		

TEST #	LOCATION	ELEVATION
220	N 421261.45 E 1179919.60	1940.9
221	N 421234.80 E 1179980.75	1940.75
222	N 421166.65 E 1179999.30	1940.65
223		
224		
225		
226		
227		
228		
229		

NOTES: Drill Pad Area Over Liner Fill

CC:

RESPECTFULLY SUBMITTED

AMERICAN TECHNICAL SERVICES, INC.

**AMERICAN
TECHNICAL
SERVICES, INC.**

ENGINEERING • ENVIRONMENTAL • DRILLING • MATERIALS
8105 Black Hawk Rd. • PO Box 658
Black Hawk, CO 80428-0658

REPORT OF SOIL DENSITY TESTING - NUCLEAR METHOD
ASTM D6938

CLIENT: CONTINENTAL RESOURCES, INC.
PO Box 268836
Oklahoma City, OK 73126
ATTENTION: Project Manager
PROJECT: Atlanta Drill Site

ATS #: 12-12165
DATE: 09/07/12
ATS TECH: Russell Harwood
GAGE #: 2
BENCHMARK: _____

TEST #	DATE	PROCTOR # / CLASSIFICATION	LABORATORY		FIELD			SPECIFICATIONS	
			% MOIST	DRY DENSITY	% MOISTURE	DRY DENSITY	% COMPACTION	SPEC MOISTURE	% SPEC COMPACTION
223	09/04/12	#3	15.3	114.2	13.6	110.4	97	+/-2%	95
224	09/04/12	#3	15.3	114.2	13.4	110.8	97	+/-2%	95
225	09/04/12	#3	15.3	114.2	13.7	111.2	97	+/-2%	95
226	09/04/12	#3	15.3	114.2	13.3	115.9	101	+/-2%	95
227	09/04/12	#1	9.7	126.5	10.2	121.0	96	+/-2%	95
228	09/04/12	#1	9.7	126.5	10.1	121.1	96	+/-2%	95
229	09/04/12	#1	9.7	126.5	9.3	120.6	95	+/-2%	95
230	09/04/12	#3	15.3	114.2	13.8	115.6	101	+/-2%	95
231	09/04/12	#3	15.3	114.2	14.4	111.7	98	+/-2%	95
232							#DIV/0!		

TEST #	LOCATION	ELEVATION
223	N 421253.00 E 1180307.60	1938
224	N 421215.25 E 1180269.15	1938.7
225	N 421166.55 E 1180234.35	1938.1
226	N 421208.40 E 1180056.70	1941.35
227	N 421254.80 E 1179946.55	1941.45
228	N 421191.80 E 1179850.65	1941.75
229	N 421178.45 E 1179723.60	1943.35
230	N 421233.40 E 1180248.00	1939.75
231	N 421180.50 E 1180248.70	1940.4
232		

NOTES: Drill Pad Area

CC:

RESPECTFULLY SUBMITTED

AMERICAN TECHNICAL SERVICES, INC.

**AMERICAN
TECHNICAL
SERVICES, INC.**

Engineering • Environmental • Drilling • Materials
8105 Black Hawk Rd • PO Box 558
Black Hawk, SD 57712-0558

REPORT OF SOIL DENSITY TESTING - NUCLEAR METHOD

ASTM D6938

CLIENT: CONTINENTAL RESOURCES, INC.
PO Box 268836
Oklahoma City, OK 73126

ATTENTION: Project Manager

PROJECT: Atlanta Drill Site

ATS #: 12-12165

DATE: 09/07/12

ATS TECH: Russell Harwood

GAGE #: 2

BENCHMARK:

TEST #	DATE	PROCTOR # / CLASSIFICATION	LABORATORY		FIELD		SPECIFICATIONS			
			% MOIST	DRY DENSITY	% MOISTURE	DRY DENSITY	% COMPACTION	SPEC MOISTURE %	SPEC COMPACTION	PASS
232	09/05/12	#3	15.3	114.2	13.3	114.1	100	+/-2%	95	PASS
233	09/05/12	#3	15.3	114.2	13.6	114.0	100	+/-2%	95	PASS
234	09/05/12	#2	8.3	123.2	9.5	120.3	98	+/-2%	95	PASS
235	09/05/12	#3	15.3	114.2	13.4	114.2	100	+/-2%	95	PASS
236	09/05/12	#3	15.3	114.2	13.7	114.4	100	+/-2%	95	PASS
237							#DIV/0!			
238							#DIV/0!			
239							#DIV/0!			
240							#DIV/0!			
241							#DIV/0!			

TEST #	LOCATION	ELEVATION
232	N 421154.40 E 1180235.30	1941.3
233	N 421194.20 E 1180115.05	1941.25
234	N 421154.70 E 1179961.25	1941.2
235	N 421215.40 E 1179812.25	1943.3
236	N 421164.80 E 1179750.50	1943.2
237		
238		
239		
240		
241		

NOTES: Drill Pad Final Subgrade

RESPECTFULLY SUBMITTED

AMERICAN TECHNICAL SERVICES, INC.

CC:

**AMERICAN
TECHNICAL
SERVICES, INC.**

Engineering • Environmental • Drilling • Materials
510S Black Hawk Rd • PO Box 558
Black Hawk, SD 57718-0558

REPORT OF SOIL DENSITY TESTING - NUCLEAR METHOD

ASTM D6938

CLIENT: **CONTINENTAL RESOURCES, INC.**
PO Box 258836
Oklahoma City, OK 73126

ATTENTION: Project Manager
PROJECT: Atlanta Drill Site

ATS #: 12-12165
DATE: 09/11/12
ATS TECH: Russell Harwood
GAGE #: 2
BENCHMARK:

TEST #	DATE	PROCTOR # / CLASSIFICATION	LABORATORY		FIELD			SPECIFICATIONS		
			% MOIST	DRY DENSITY	% MOISTURE	DRY DENSITY	% COMPACTION	SPEC MOISTURE %	SPEC COMPACTION	PASS
237	09/07/12	#2	8.3	123.2	7.9	122.1	99	+/-2%	95	PASS
238	09/07/12	#3	15.3	114.2	14.5	108.7	95	+/-2%	95	PASS
239	09/07/12	#2	8.3	123.2	8.1	118.5	96	+/-2%	95	PASS
240	09/07/12	#3	15.3	114.2	14.0	110.0	96	+/-2%	95	PASS
241	09/07/12	#3	15.3	114.2	13.4	114.1	100	+/-2%	95	PASS
242	09/07/12	#3	15.3	114.2	13.7	111.0	97	+/-2%	95	PASS
243	09/07/12	#2	8.3	123.2	8.1	117.4	95	+/-2%	95	PASS
244	09/07/12	#3	15.3	114.2	14.1	109.9	96	+/-2%	95	PASS
245							#DIV/0!			
246							#DIV/0!			

TEST #	LOCATION	ELEVATION
237	N 421519.00 E 1180368.00	1963.9
238	N 421460.00 E 1180390.40	1956.8
239	N 421424.20 E 1180438.15	1961.7
240	N 421414.40 E 1180424.20	1954.1
241	N 421365.45 E 1180416.00	1960.75
242	N 421362.70 E 1180451.00	1954.5
243	N 421279.10 E 1180484.90	1961.7
244	N 421283.65 E 1180471.85	1952.45
245		
246		

NOTES: East Berm

CC:

RESPECTFULLY SUBMITTED

AMERICAN TECHNICAL SERVICES, INC.

REPORT OF SOIL DENSITY TESTING - NUCLEAR METHOD
ASTM D6938

CLIENT: **CONTINENTAL RESOURCES, INC.**
PO Box 268836
Oklahoma City, OK 73126
ATTENTION: Project Manager
PROJECT: Atlanta Drill Site

ATS #: 12-12165
DATE: 09/18/12
ATS TECH: Russell Harwood
GAGE #: 2
BENCHMARK:

TEST #	DATE	PROCTOR # / CLASSIFICATION	LABORATORY		FIELD			SPECIFICATIONS		
			% MOIST	DRY DENSITY	% MOISTURE	DRY DENSITY	% COMPACTION	SPEC MOISTURE	% SPEC COMPACTION	PASS
245	09/14/12	#4	7.2	131.4	5.3	127.4	97	+/-2%	95	PASS
246	09/14/12	#4	7.2	131.4	5.7	131.0	100	+/-2%	95	PASS
247	09/14/12	#4	7.2	131.4	5.4	131.1	100	+/-2%	95	PASS
248	09/14/12	#4	7.2	131.4	5.6	127.9	97	+/-2%	95	PASS
249	09/14/12	#4	7.2	131.4	5.5	131.5	100	+/-2%	95	PASS
250	09/14/12	#4	7.2	131.4	5.3	130.5	99	+/-2%	95	PASS
251	09/14/12	#4	7.2	131.4	5.4	131.3	100	+/-2%	95	PASS
252							#DIV/0!			
253							#DIV/0!			
254							#DIV/0!			

TEST #	LOCATION	ELEVATION
245	N 421250.10 E 1180221.35	1941.9
246	N 421172.20 E 1180121.95	1941.9
247	N 421231.95 E 1180017.80	1941.95
248	N 421271.80 E 1179924.75	1941.9
249	N 421228.85 E 1179835.15	1943.9
250	N 421180.60 E 1179720.90	1943.9
251	N 421236.80 E 1179604.75	1943.9
252		
253		
254		

NOTES: Drill Pad Gravel

RESPECTFULLY SUBMITTED

CC:

AMERICAN TECHNICAL SERVICES, INC.



SHORING • ENVIRONMENTAL • DRILLING • MATERIALS
9105 Black Hawk Rd • PO Box 558
Black Hawk, SD 57715-0558

REPORT OF SOIL DENSITY TESTING - NUCLEAR METHOD
ASTM D6938

CLIENT: CONTINENTAL RESOURCES, INC.
PO Box 268836
Oklahoma City, OK 73126

ATTENTION: Project Manager

PROJECT: Atlanta Drill Site

ATS #: 12-12165
DATE: 09/18/12
ATS TECH: Russell Harwood
GAGE #: 2
BENCHMARK:

TEST #	DATE	PROCTOR # / CLASSIFICATION	LABORATORY		FIELD			SPECIFICATIONS		
			% MOIST	DRY DENSITY	% MOISTURE	DRY DENSITY	% COMPACTION	SPEC MOISTURE %	SPEC COMPACTION	PASS
252	09/17/12	#3	15.3	114.2	13.3	109.3	96	+/-2%	96	PASS
253	09/17/12	#3	15.3	114.2	13.4	108.9	95	+/-2%	95	PASS
254	09/17/12	#1	9.7	126.5	8.9	122.4	97	+/-2%	95	PASS
255	09/17/12	#3	15.3	114.2	13.8	110.3	97	+/-2%	95	PASS
256	09/17/12	#2	8.3	123.2	8.1	118.4	96	+/-2%	95	PASS
257							#DIV/0!			
258							#DIV/0!			
259							#DIV/0!			
260							#DIV/0!			
261							#DIV/0!			

TEST #	LOCATION	ELEVATION
252	N 420632.90 E 1180063.05	1880.8
253	N 420613.15 E 1179979.55	1870.1
254	N 420646.00 E 1179961.30	1864.95
255	N 420670.10 E 1179894.80	1872.05
256	N 420613.40 E 1179840.10	1873.45
257		
258		
259		
260		
261		

NOTES: South Pond Pre-Liner (Finish Subgrade)

CC:

RESPECTFULLY SUBMITTED

AMERICAN TECHNICAL SERVICES, INC.

**AMERICAN
TECHNICAL
SERVICES, INC.**

Engineering • Environmental • Drilling • Materials
8105 Bent Hwy Rd • PO Box 558
Clark Ferry, SD 57712-0558

REPORT OF SOIL DENSITY TESTING - NUCLEAR METHOD

ASTM D6938

CLIENT: **CONTINENTAL RESOURCES, INC.**
PO Box 268836
Oklahoma City, OK 73126

ATTENTION: Project Manager
PROJECT: Atlanta Drill Site

ATS #: 12-12165
DATE: 09/25/12
ATS TECH: Russell Harwood
GAGE #: 2
BENCHMARK:

TEST #	DATE	PROCTOR # / CLASSIFICATION	LABORATORY		FIELD			SPECIFICATIONS		
			% MOIST	DRY DENSITY	% MOISTURE	DRY DENSITY	% COMPACTION	SPEC MOISTURE %	SPEC COMPACTION	PASS
257	09/22/12	#3	15.3	114.2	14.1	109.2	96	+/-2%	95	PASS
258	09/22/12	#2	8.3	123.2	7.2	118.5	96	+/-2%	95	PASS
259	09/22/12	#2	8.3	123.2	8.0	118.7	96	+/-2%	95	PASS
260	09/22/12	#2	8.3	123.2	7.1	120.7	98	+/-2%	95	PASS
261	09/22/12	#3	15.3	114.2	13.8	110.0	96	+/-2%	95	PASS
262	09/22/12	#2	8.3	123.2	7.9	119.6	97	+/-2%	95	PASS
263	09/22/12	#3	15.3	114.2	13.4	109.4	96	+/-2%	95	PASS
264							#DIV/0!			
265							#DIV/0!			
266							#DIV/0!			

TEST #	LOCATION	ELEVATION
257	N 420679.75 E 1180078.75	1870.1
258	N 420720.90 E 1180029.20	1878.2
259	N 420680.85 E 1179984.50	1870.7
260	N 420614.75 E 1179949.80	1869.95
261	N 420614.40 E 1179901.55	1868.85
262	N 420594.10 E 1179848.15	1877.55
263	N 420592.00 E 1179984.65	1884.6
264		
265		
266		

NOTES: Pond Subgrade After Liner & Finish Grade

CC:

RESPECTFULLY SUBMITTED

AMERICAN TECHNICAL SERVICES, INC.



**AMERICAN
TECHNICAL
SERVICES, INC.**

ENGINEERING • ENVIRONMENTAL • DRILLING • MATERIALS
8105 Black Hawk Rd. • PO Box 558
Black Hawk, SD 57718-0558

REPORT OF SOIL DENSITY TESTING - NUCLEAR METHOD
ASTM D6938

CLIENT	CONTINENTAL RESOURCES, INC. PO Box 268836 Oklahoma City, OK 73126	ATS #	12-12165
ATTENTION:	Project Manager	DATE	10/15/12
PROJECT:	Atlanta Drill Site	ATS TECH	Evan Schultze
		GAGE #	26
		BENCHMARK	Atlanta Pad Road


TEST #	DATE	PROCTOR # / CLASSIFICATION	LABORATORY		FIELD		SPECIFICATIONS			
			% MOIST	DRY DENSITY	% MOISTURE	DRY DENSITY	% COMPACTION	SPEC MOISTURE	% SPEC COMPACTION	PASS
264	10/10/12	#1	9.7	126.5	9.3	120.3	95	+/-2%	95	PASS
265	10/10/12	#1	9.7	126.5	9.5	120.9	96	+/-2%	95	PASS
266	10/10/12	#1	9.7	126.5	9.8	122.1	97	+/-2%	95	PASS
267							#VALUE!			
268							#VALUE!			
269							#VALUE!			
270							#VALUE!			
271							#DIV/0!			
272							#DIV/0!			
273							#DIV/0!			

TEST #	LOCATION	ELEVATION
264	N 48D07.125' W 103D44.108'	1.5' Below Top of Subgrade
265	N 48D07.071' W 103D44.106'	1' Below Top of Subgrade
266	N 48D07.053' W 103D44.018'	5' Below Top of Subgrade
267		
268		
269		
270		
271		
272		
273		

NOTES: _____

 CC: _____

RESPECTFULLY SUBMITTED



AMERICAN TECHNICAL SERVICES, INC.

AMERICAN
TECHNICAL
SERVICES, INC.

ENGINEERING • ENVIRONMENTAL • DRILLING • MATERIALS
8105 Black Hawk Rd • PO Box 558
Black Hawk, SD 57718-0558

REPORT OF SOIL DENSITY TESTING - NUCLEAR METHOD

ASTM D6938

CLIENT: CONTINENTAL RESOURCES, INC.
PO Box 268836
Oklahoma City, OK 73126
ATTENTION: Project Manager
PROJECT: Atlanta Drill Site

ATS #: 12-12165
DATE: 10/15/12
ATS TECH: Evan Schultze
GAGE #: 26
BENCHMARK: Atlanta Pad Road


TEST #	DATE	PROCTOR # / CLASSIFICATION	LABORATORY		FIELD		SPECIFICATIONS			PASS
			% MOIST	DRY DENSITY	% MOISTURE	DRY DENSITY	% COMPACTION	SPEC MOISTURE %	SPEC COMPACTION	
267	10/11/12	#1	9.7	126.5	8.9	123.4	98	+/-2%	95	PASS
268	10/11/12	#1	9.7	126.5	9.2	122.8	97	+/-2%	95	PASS
269	10/11/12	#1	9.7	126.5	8.8	124.3	98	+/-2%	95	PASS
270	10/11/12	#1	9.7	126.5	9.1	123.7	98	+/-2%	95	PASS
271							#VALUE!			
272							#VALUE!			
273							#VALUE!			
274							#DIV/0!			
275							#DIV/0!			
276							#DIV/0!			

TEST #	LOCATION		ELEVATION
267	N 48D06.762'	W 103D44.019'	5' Below Top of Subgrade
268	N 48D07.078'	W 103D44.106'	5' Below Top of Subgrade
269	N 48D07.101'	W 103D44.020'	1' Below Top of Subgrade
270	N 48D07.164'	W 103D44.019'	2' Below Top of Subgrade
271			
272			
273			
274			
275			
276			

NOTES: _____

CC: _____

RESPECTFULLY SUBMITTED



AMERICAN TECHNICAL SERVICES, INC.

**AMERICAN
TECHNICAL
SERVICES, INC.**

ENGINEERING • ENVIRONMENTAL • DRILLING • MATERIALS
8105 Black Hawk Rd. • PO Box 558
Black Hawk, SD 57718-0558

REPORT OF SOIL DENSITY TESTING - NUCLEAR METHOD
ASTM D6938

CLIENT: CONTINENTAL RESOURCES, INC.
PO Box 268836
Oklahoma City, OK 73126
ATTENTION: Project Manager
PROJECT: Atlanta Drill Site

ATS #: 12-12165
DATE: 10/15/12
ATS TECH: Evan Schultze
GAGE #: 26
BENCHMARK: Atlanta Pad Road

TEST #	DATE	PROCTOR # / CLASSIFICATION	LABORATORY		FIELD		SPECIFICATIONS			
			% MOIST	DRY DENSITY	% MOISTURE	DRY DENSITY	% COMPACTION	SPEC MOISTURE %	SPEC COMPACTION	PASS
271	10/12/12	#1	9.7	126.5	9.4	124.8	99	+/-2%	95	PASS
272							#VALUE!			
273							#VALUE!			
274							#VALUE!			
275							#VALUE!			
276							#VALUE!			
277							#VALUE!			
278							#DIV/0!			
279							#DIV/0!			
280							#DIV/0!			


TEST #	LOCATION		ELEVATION
271	N 48D06.807'	W 103D44.019'	1' Below Top of Subgrade
272			
273			
274			
275			
276			
277			
278			
279			
280			

NOTES: _____

CC: _____

RESPECTFULLY SUBMITTED

AMERICAN TECHNICAL SERVICES, INC.



AMERICAN
TECHNICAL
SERVICES, INC.

ENGINEERING • ENVIRONMENTAL • DRILLING • MATERIALS
8105 Black Hawk Rd. • PO Box 558
Black Hawk, SD 57718-0558

REPORT OF SOIL DENSITY TESTING - NUCLEAR METHOD

ASTM D6938

CLIENT: **CONTINENTAL RESOURCES, INC.**
PO Box 268836
Oklahoma City, OK 73126
ATTENTION: Project Manager
PROJECT: Atlanta Drill Site

ATS #: 12-12165
DATE: 10/17/12
ATS TECH: Evan Schultze
GAGE #: 26
BENCHMARK: Atlanta Pad Road- Cement Stabilized Soil

TEST #	DATE	PROCTOR # / CLASSIFICATION	LABORATORY		FIELD		SPECIFICATIONS			
			% MOIST	DRY DENSITY	% MOISTURE	DRY DENSITY	% COMPACTION	SPEC MOISTURE %	SPEC COMPACTION	PASS
283	10/16/12	#1	9.7	126.5	9.7	123.0	97	+/-2%	95	PASS
284	10/16/12	#1	9.7	126.5	9.5	124.2	98	+/-2%	95	PASS
285	10/16/12	#1	9.7	126.5	9.9	122.3	97	+/-2%	95	PASS
286	10/16/12	#1	9.7	126.5	9.8	123.4	98	+/-2%	95	PASS
287	10/16/12	#1	9.7	126.5	10.3	124.1	98	+/-2%	95	PASS
288	10/16/12	#1	9.7	126.5	10.5	121.9	96	+/-2%	95	PASS
289							#VALUE!			
290							#DIV/0!			
291							#DIV/0!			
292							#DIV/0!			

TEST #	LOCATION			ELEVATION
283	North 48d07 167'	West 103d44 014		1.5' Below Top of Subgrade
284	North 48d07 187'	West 103d44 021		2' Below Top of Subgrade
285	North 48d07 175'	West 103d44 017		1' Below Top of Subgrade
286	North 48d06 217'	West 103d44 015		1' Below Top of Subgrade
287	North 48d07 235'	West 103d44 013		.5' Below Top of Subgrade
288	North 48d07 197'	West 103d44 014		5' Below Top of Subgrade
289				
290				
291				
292				

NOTES: _____

CC: _____

RESPECTFULLY SUBMITTED


AMERICAN TECHNICAL SERVICES, INC.



Oil and Gas Division

Lynn D. Helms - Director

Bruce E. Hicks - Assistant Director

Department of Mineral Resources

Lynn D. Helms - Director

North Dakota Industrial Commission

www.dmr.nd.gov/oilgas

23359
TH

RECKY BARNES
CONTINENTAL RESOURCES, INC.
PO BOX 1032
ENID, OK 73702-1032 USA

Date: 7/23/2012

RE: CORES AND SAMPLES

Well Name: ATLANTA 14-6H Well File No.: 23359
Location: NENW 6-153-101 County: WILLIAMS
Permit Type: Development - HORIZONTAL
Field: BAKER Target Horizon: THREE FORKS

Dear BECKY BARNES:

North Dakota Century Code (NDCC) Section 38-08-04 provides for the preservation of cores and samples and their shipment to the State Geologist when requested. The following is required on the above referenced well:

- 1) All cores, core chips and samples must be submitted to the State Geologist as provided for the NDCC Section 38-08-04 and North Dakota Administrative Code 43-02-03-38.1.
- 2) Samples shall include all cuttings from:

Base of the Last Charles Salt

Samples of cuttings shall be taken at 30' maximum intervals through all vertical, build and horizontal sections. Samples must be washed, dried, packed in sample envelopes in correct order with labels showing operator, well name, location and depth, and forwarded in standard boxes to the State Geologist within 30 days of the completion of drilling operations.

- 3) Cores: ALL CORES cut shall be preserved in correct order, properly boxed, and forwarded to the State Geologist within 90 days of completion of drilling operations. Any extension of time must have written approval from the State Geologist.
- 4) All cores, core chips, and samples must be shipped, prepaid, to the State Geologist at the following address:

ND Geological Survey Core Library
Campus Road and Cornell
Grand Forks, ND 58202

- 5) NDCC Section 38-08-16 allows for a civil penalty for any violation of Chapter 38 08 not to exceed \$12,500 for each offense, and each day's violation is a separate offense.

Sincerely

Richard A. Suggs
Geologist



SUNDY NOTICES AND REPORTS ON WELLS - FORM 4

INDUSTRIAL COMMISSION OF NORTH DAKOTA
OIL AND GAS DIVISION
600 EAST BOULEVARD DEPT 405
BISMARCK, ND 58505-0840
SFN 5740 (09-2006)

Well File No.

23359



PLEASE READ INSTRUCTIONS BEFORE FILLING OUT FORM.
PLEASE SUBMIT THE ORIGINAL AND ONE COPY.

<input type="checkbox"/> Notice of Intent	Approximate Start Date	<input type="checkbox"/> Drilling Prognosis	Spill Report
<input type="checkbox"/> Report of Work Done	Date Work Completed	<input type="checkbox"/> Redrilling or Repair	<input type="checkbox"/> Shooting
<input type="checkbox"/> Notice of Intent to Begin a Workover Project that may Qualify for a Tax Exemption Pursuant to NDCC Section 57-51.1-03.		<input type="checkbox"/> Casing or Liner	<input type="checkbox"/> Acidizing
Approximate Start Date		<input type="checkbox"/> Plug Well	<input type="checkbox"/> Fracture Treatment
		<input type="checkbox"/> Supplemental History	<input type="checkbox"/> Change Production Method
		<input type="checkbox"/> Temporarily Abandon	<input type="checkbox"/> Reclamation
		<input checked="" type="checkbox"/> Other	<u>Open Hole Log Waiver</u>

Well Name and Number

Atlanta 14-6H

Footages	Qtr-Qtr	Section	Township	Range
495 F N L	1485 F W L	NENW	6	153 N 101 W
Field	Pool Bakken		County	Williams

24-HOUR PRODUCTION RATE

Before		After	
Oil	Bbls	Oil	Bbls
Water	Bbls	Water	Bbls
Gas	MCF	Gas	MCF

Name of Contractor(s)

Address

City

State

Zip Code

DETAILS OF WORK

Requested variance to not run openhole logs. GR/CBL/CCL will be run from deepest point obtainable to base of surface casing.

Offset logs used will be the Brigham Oil and Gas, LP, Lippert 1-12, Sec 1-153N-102W, Williams County, ND.

The Gamma Ray Log will be run all the way to surface and all mud logs will be submitted as one digital tiff formatted file and one digital LAS formatted file.

Company Continental Resources, Inc.	Telephone Number 580-233-8955	
Address P.O. Box 1032		
City Enid	State OK	Zip Code 73702
Signature <i>Terry L. Olson</i>	Printed Name Terry L. Olson	
Title Regulatory Compliance Specialist	Date May 8, 2012	
Email Address Terry.Olson@clr.com		

FOR STATE USE ONLY

<input type="checkbox"/> Received	<input checked="" type="checkbox"/> Approved
Date 7-20-2012	
By <i>R.A. Suggs</i>	
Title Richard A. Suggs	
Geologist	



Approved
David Tabor
7-20-2012

Engineering Technician

July 20, 2012


Industrial Commission of North Dakota
Oil & Gas Division
600 East Boulevard, Dept 405
Bismarck, North Dakota 58505

Continental Resources, Inc. (CRI) respectfully requests a waiver to the requirement to delay commencement of operations until three business days following approval of the drilling permit for the Atlanta 1-14-6H.

Township 153N, Range 101W of the 5th P.M.
Section 6, N/2 NW/4 Williams County, North Dakota.


In the event that another owner seeks revocation of the drilling permit, CRI should retain the permit for the following reasons:

- 1) CRI has the necessary technical ability to drill and complete the well(s).
- 2) CRI has drilled and completed more than 130 horizontal Bakken wells in North Dakota.
- 3) CRI operates more than 500 wells in North Dakota and more than 100 in McKenzie County.
- 4) CRI has a contract with Cyclone Drilling that may require standby payments in the event a location is not ready to move onto. There are no near term lease expirations associated with the subject well.
- 5) CRI controls a working interest of 55.54% and is the majority working interest owner within the subject spacing unit consisting of 2560 acres of sections 5, 6, 7, 8, 153N – 101W of the 5th P.M.


Chad Newby, Operations Land Coordinator
Continental Resources, Inc.

STATE OF OKLAHOMA)
)
COUNTY OF GARFIELD)

On the 20th day of July 2012, before me, a Notary Public in and for said County and State, personally appeared Chad Newby, known to me to be the Operations Land Coordinator of Continental Resources, Inc., the Corporation that executed the within instrument, and acknowledged to me that such Corporation executed the same.


Notary Public


Garfield County, Oklahoma

My Commission Expires: 7/5/2015

Commission No.: 11006023

P.O. Box 1032 • 302 N. Independence • Enid, OK 73702
Voice (580) 233-8955 • Fax (580) 242-4703





Oil and Gas Division

Lynn D. Helms - Director

Bruce E. Hicks - Assistant Director

Department of Mineral Resources

Lynn D. Helms - Director

North Dakota Industrial Commission

www.oilgas.nd.gov

July 20, 2012

Terry L. Olson
Regulatory Compliance Specialist
CONTINENTAL RESOURCES, INC.
P.O. Box 1032
Enid, OK 73702

**RE: HORIZONTAL WELL
ATLANTA 14-6H
NENW Section 6-153N-101W
Williams County
Well File # 23359**

Dear Terry :

Pursuant to Commission Order No. 19840, approval to drill the above captioned well is hereby given. The approval is granted on the condition that all portions of the well bore not isolated by cement, be no closer than the **500' setback** from the north or west boundaries and **200' setback** from the east or south boundaries within the 2560 acre spacing unit consisting of Sections 5, 6, 7, & 8 T153N R101W. . **Tool error is not required pursuant to order.**

PERMIT STIPULATIONS: A sufficient number of horizontal wells shall be drilled and completed in the 2560-acre spacing unit described as Sections 5, 6, 7, and 8, Township 153 North, Range 101 West, McKenzie and Williams Counties, North Dakota, which reasonably develop all portions of the 2560-acre spacing unit within two years after the first horizontal well is completed. If this condition is not met, the Commission shall schedule the matter for a consideration to reduce the size of the spacing unit **THIS WELL IS LOCATED IN A SURFACE WATER PROTECTION AREA: ONSITE INSPECTION REQUIRED (CONTACT NDIC FIELD INSPECTOR FOR SITE SPECIFIC STIPULATIONS). TO INCLUDE BUT NOT LIMITED TO: CLOSED MUD SYSTEM, NO DRILLING PIT, AND IMPERMEABLE LINER IS REQUIRED ON THE ENTIRE LOCATION AND A STRING OF CASING MUST BE PLACED IN THE RAT AND MOUSE HOLE AND CEMENTED TO GROUND LEVEL. FURTHERMORE CONTINENTAL MUST COMPLY WITH ALL AFFIDAVIT'S. LASTLY, AN IMPERMEABLE PERIMETER DIKE MUST BE PLACED AROUND THE ENTIRE LOCATION. CONTINENTAL RESOURCES must contact NDIC Field Inspector John Axtman at 701-770-2564 prior to location construction.**

Drilling pit

NDAC 43-02-03-19.4 states that "a pit may be utilized to bury drill cuttings and solids generated during well drilling and completion operations, providing the pit can be constructed, used and reclaimed in a manner that will prevent pollution of the land surface and freshwaters. Reserve and circulation of mud system through earthen pits are prohibited. All pits shall be inspected by an authorized representative of the director prior to lining and use. Drill cuttings and solids must be stabilized in a manner approved by the director prior to placement in a cuttings pit."

Form 1 Changes & Hard Lines

Any changes, shortening of casing point or lengthening at Total Depth must have prior approval by the NDIC. The proposed directional plan is at a legal location. The minimum legal coordinate from the well head at casing point is: 5S. Also, based on the azimuth of the proposed lateral the maximum legal coordinate from the well head is: 5S & 8827E.

Location Construction Commencement (Three Day Waiting Period)

Operators shall not commence operations on a drill site until the 3rd business day following publication of the approved drilling permit on the NDIC - OGD Daily Activity Report. If circumstances require operations to commence before the 3rd business day following publication on the Daily Activity Report, the waiting period may be waived by the Director. Application for a waiver must be by sworn affidavit providing the information necessary to evaluate the extenuating circumstances, the factors of NDAC 43-02-03-16.2 (1), (a)-(f), and any other information that would allow the Director to conclude that in the event another owner seeks revocation of the drilling permit, the applicant should retain the permit.

Permit Fee & Notification

Payment was received in the amount of \$100 via credit card. It is requested that notification be given immediately upon the spudding of the well. This information should be relayed to the Oil & Gas Division, Bismarck, via telephone. The following information must be included: Well name, legal location, permit number, drilling contractor, company representative, date and time of spudding. Office hours are 8:00 a.m. to 12:00 p.m. and 1:00 p.m. to 5:00 p.m. Central Time. Our telephone number is (701) 328-8020, leave a message if after hours or on the weekend.

Survey Requirements for Horizontal, Horizontal Re-entry, and Directional Wells

NDAC Section 43-02-03-25 (Deviation Tests and Directional Surveys) states in part (that) the survey contractor shall file a certified copy of all surveys with the director free of charge within thirty days of completion. Surveys must be submitted as one electronic copy, or in a form approved by the director. However, the director may require the directional survey to be filed immediately after completion if the survey is needed to conduct the operation of the director's office in a timely manner. Certified surveys must be submitted via email in one adobe document, with a certification cover page to certsurvey@nd.gov. Survey points shall be of such frequency to accurately determine the entire location of the well bore. Specifically, the Horizontal and Directional well survey frequency is 100 feet in the vertical, 30 feet in the curve (or when sliding) and 90 feet in the lateral.

Confidential status

Your request for confidential status of all information furnished to the Director, or his representatives, is hereby granted. Such information, except production runs, shall remain confidential for six months commencing on the date the well is spud.

Confidential status notwithstanding, the Director and his representatives shall have access to all well records wherever located. Your company personnel, or any person performing work for your company shall permit the Director and his representatives to come upon any lease, property, well, or drilling rig operated or controlled by them, complying with all safety rules, and to inspect the records and operation of such wells and to have access at all times to any and all records of

Logs

NDAC Section 43-02-03-31 requires the running of (1) a suite of open hole logs from which formation tops and porosity zones can be determined, (2) a Gamma Ray Log run from total depth to ground level elevation of the well bore, and (3) a log from which the presence and quality of cement can be determined (Standard CBL or Ultrasonic cement evaluation log) in every well in which production or intermediate casing has been set, this log must be run prior to completing the well. All logs run must be submitted free of charge, as one digital TIFF (tagged image file format) copy and one digital LAS (log ASCII) formatted copy. Digital logs may be submitted on a standard CD, DVD, or attached to an email sent to digitallogs@nd.gov. Thank you for your cooperation.

Sincerely,

Todd L. Holweger
Mineral Resources Permit Manager



APPLICATION FOR PERMIT TO DRILL HORIZONTAL WELL - FORM 1H

INDUSTRIAL COMMISSION OF NORTH DAKOTA
OIL AND GAS DIVISION
600 EAST BOULEVARD DEPT 405
BISMARCK, ND 58505-0840
SFN 54269 (08-2005)

PLEASE READ INSTRUCTIONS BEFORE FILLING OUT FORM.

PLEASE SUBMIT THE ORIGINAL AND ONE COPY.

Type of Work New Location	Type of Well Oil & Gas	Approximate Date Work Will Start 6 / 1 / 2012	Confidential Status Yes
Operator CONTINENTAL RESOURCES, INC.		Telephone Number 580-233-8955	
Address P.O. Box 1032		City Enid	State OK Zip Code 73702

Notice has been provided to the owner of any permanently occupied dwelling within 1,320 feet.

This well is not located within five hundred feet of an occupied dwelling.

WELL INFORMATION (If more than one lateral proposed, enter data for additional laterals on page 2)

Well Name ATLANTA			Well Number 14-6H				
Surface Footages 495 F N L 1485 F W L		Qtr-Qtr NENW	Section 6	Township 153 N	Range 101 W	County Williams	
Longstring Casing Point Footages 506 F N L 2056 F W L		Qtr-Qtr NENW	Section 5	Township 153 N	Range 101 W	County Williams	
Longstring Casing Point Coordinates From Well Head 11 S From WH 571 E From WH		Azimuth 91 °	Longstring Total Depth 10910 Feet MD 10584 Feet TVD				
Bottom Hole Footages From Nearest Section Line 660 F N L 200 F E L		Qtr-Qtr NENE	Section 5	Township 153 N	Range 101 W	County McKenzie	
Bottom Hole Coordinates From Well Head 165 S From WH 8827 E From WH		KOP Lateral 1 10011 Feet MD	Azimuth Lateral 1 91 °	Estimated Total Depth Lateral 1 19167 Feet MD 10606 Feet TVD			
Latitude of Well Head 48 ° 06 ' 33.65 "	Longitude of Well Head -103 ° 43 ' 39.06 "	NAD Reference NAD83		Description of Spacing Unit: Sec 5, 6, 7, & 8 T153N R101W (Subject to NDIC Approval)			
Ground Elevation 1948 Feet Above S.L.	Acres in Spacing/Drilling Unit 2560	Spacing/Drilling Unit Setback Requirement Feet N/S Feet E/W			Industrial Commission Order 19840		
North Line of Spacing/Drilling Unit 10516 Feet	South Line of Spacing/Drilling Unit 10510 Feet	East Line of Spacing/Drilling Unit 10422 Feet			West Line of Spacing/Drilling Unit 10367 Feet		
Objective Horizons Three Forks						Pierre Shale Top 1867	
Proposed Surface Casing	Size 9 - 5/8 "	Weight 36 Lb./Ft.	Depth 1970 Feet	Cement Volume 743 Sacks	NOTE: Surface hole must be drilled with fresh water and surface casing must be cemented back to surface.		
Proposed Longstring Casing	Size 7 - "	Weight(s) 26-32 Lb./Ft.	Longstring Total Depth 10910 Feet MD 10584 Feet TVD		Cement Volume 839 Sacks	Cement Top 0 Feet	Top Dakota Sand 4925 Feet
Base Last Charles Salt (If Applicable) 9011 Feet		NOTE: Intermediate or longstring casing string must be cemented above the top Dakota Group Sand.					
Proposed Logs CBL/GR from deepest depth obtainable to ground surface/mud							
Drilling Mud Type (Vertical Hole - Below Surface Casing) Invert				Drilling Mud Type (Lateral) Brine			
Survey Type in Vertical Portion of Well MWD Every 100 Feet		Survey Frequency: Build Section 30 Feet		Survey Frequency: Lateral 90 Feet		Survey Contractor Baker Hughes	

NOTE: A Gamma Ray log must be run to ground surface and a CBL must be run on intermediate or longstring casing string if set.

Surveys are required at least every 30 feet in the build section and every 90 feet in the lateral section of a horizontal well. Measurement inaccuracies are not considered when determining compliance with the spacing/drilling unit boundary setback requirement except in the following scenarios: 1) When the angle between the well bore and the respective boundary is 10 degrees or less; or 2) If Industry standard methods and equipment are not utilized. Consult the applicable field order for exceptions.

If measurement inaccuracies are required to be considered, a 2° MWD measurement inaccuracy will be applied to the horizontal portion of the well bore. This measurement inaccuracy is applied to the well bore from KOP to TD.

REQUIRED ATTACHMENTS: Certified surveyor's plat, horizontal section plat, estimated geological tops, proposed mud/cementing plan, directional plot/plan, \$100 fee.

See Page 2 for Comments section and signature block.

COMMENTS, ADDITIONAL INFORMATION, AND/OR LIST OF ATTACHMENTS**Proposed FW casing: 13 3/8, 48#, 0-500', 189 sks cmt. Setbacks: 500' N&W 200' S&E**

Lateral 2

KOP Lateral 2 Feet MD	Azimuth Lateral 2 °	Estimated Total Depth Lateral 2 Feet MD Feet TVD			KOP Coordinates From Well Head From WH From WH		
Formation Entry Point Coordinates From Well Head From WH From WH		Bottom Hole Coordinates From Well Head From WH From WH					
KOP Footages From Nearest Section Line F L F L		Qtr-Qtr	Section	Township N	Range W	County	
Bottom Hole Footages From Nearest Section Line F L F L		Qtr-Qtr	Section	Township N	Range W	County	

Lateral 3

KOP Lateral 3 Feet MD	Azimuth Lateral 3 °	Estimated Total Depth Lateral 3 Feet MD Feet TVD			KOP Coordinates From Well Head From WH From WH		
Formation Entry Point Coordinates From Well Head From WH From WH		Bottom Hole Coordinates From Well Head From WH From WH					
KOP Footages From Nearest Section Line F L F L		Qtr-Qtr	Section	Township N	Range W	County	
Bottom Hole Footages From Nearest Section Line F L F L		Qtr-Qtr	Section	Township N	Range W	County	

Lateral 4

KOP Lateral 4 Feet MD	Azimuth Lateral 4 °	Estimated Total Depth Lateral 4 Feet MD Feet TVD			KOP Coordinates From Well Head From WH From WH		
Formation Entry Point Coordinates From Well Head From WH From WH		Bottom Hole Coordinates From Well Head From WH From WH					
KOP Footages From Nearest Section Line F L F L		Qtr-Qtr	Section	Township N	Range W	County	
Bottom Hole Footages From Nearest Section Line F L F L		Qtr-Qtr	Section	Township N	Range W	County	

Lateral 5

KOP Lateral 5 Feet MD	Azimuth Lateral 5 °	Estimated Total Depth Lateral 5 Feet MD Feet TVD			KOP Coordinates From Well Head From WH From WH		
Formation Entry Point Coordinates From Well Head From WH From WH		Bottom Hole Coordinates From Well Head From WH From WH					
KOP Footages From Nearest Section Line F L F L		Qtr-Qtr	Section	Township N	Range W	County	
Bottom Hole Footages From Nearest Section Line F L F L		Qtr-Qtr	Section	Township N	Range W	County	

I hereby swear or affirm the information provided is true, complete and correct as determined from all available records.

Date

5 / 8 / 2012

ePermitPrinted Name
Terry L. Olson

Title

Regulatory Compliance Specialist**FOR STATE USE ONLY**


Permit and File Number 23359	API Number 33 - 105 - 02719
Field BAKER	
Pool BAKKEN	Permit Type DEVELOPMENT

FOR STATE USE ONLY

Date Approved 7 / 20 / 2012
By Todd L. Holweger
Title Mineral Resources Permit Manager

WELL LOCATION PLAT
CONTINENTAL RESOURCES INC.
ATLANTA 14-6H
SECTION 6, T153N, R101W
WILLIAMS COUNTY, NORTH DAKOTA
495' FNL & 1485' FWL

REVISED: 4-23-2012

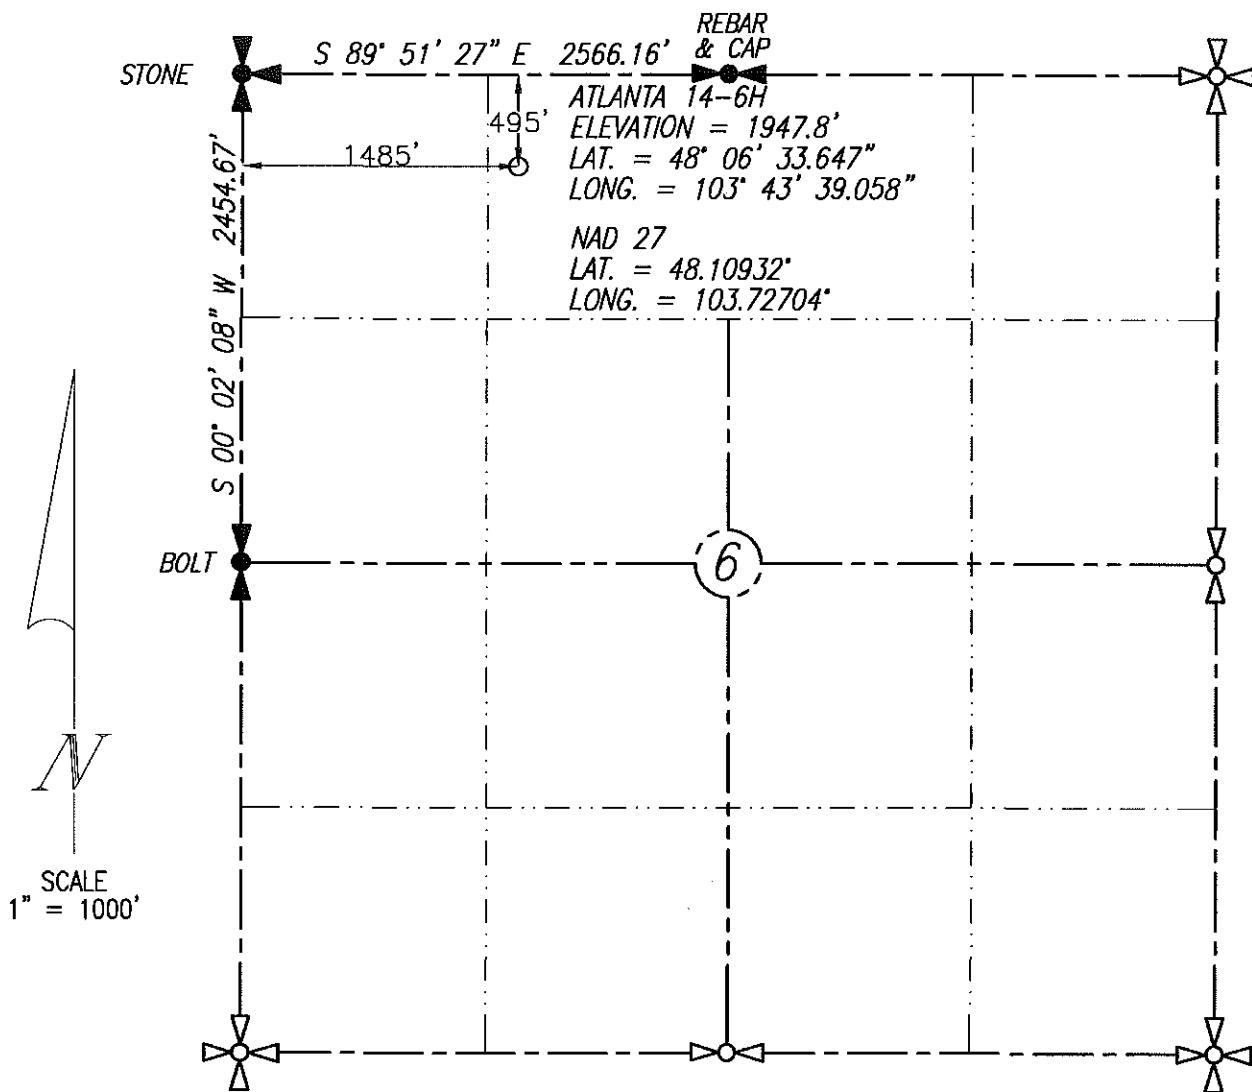

I CERTIFY THAT THIS PLAT CORRECTLY REPRESENTS
WORK PERFORMED BY ME OR UNDER MY RESPONSIBLE
CHARGE, AND IS TRUE AND CORRECT TO THE BEST OF
MY KNOWLEDGE AND BELIEF

JOHN PAULSON PLS. #3366
REGISTERED PLAT. LAND
SURVEYOR
L.S. 3366

DATE STAKED: 2-9-2012
BASIS OF VERTICAL DATUM:
NAVD 1988 GEODETIC 09

PERSON AUTHORIZING SURVEY;
CHAD NEWBY

EXPLANATION AREA: NAD83(CORS96)

BASIS OF BEARING: TRUE NORTH

BROSZ ENGINEERING INC.

BOX 357
BOWMAN, N.D. 58623
PHONE: 701-523-3340
FAX: 701-523-5243
PROJECT NO. 12-10

Continental Resources, Inc. (CRI) respectfully submits the following information concerning the drilling of the Atlanta 1, 2, 3, 4, 5, 6, 7, 8, 9, 10, 11, 12, 13, 14 -- 6H, N/2 NW/4 Sec. 6, T153N, R101W, Williams County, North Dakota.

The Atlanta well(s) are located in a Well Head Protection Area. CRI would like to propose the following safeguards and precautions to be taken to prevent any contamination to freshwater sources during the drilling and completion of the well.

- 1) During construction of the location, the entire location will be constructed per NDIC permit stipulations, and to ensure any spills or runoff which occur on location do not penetrate the fresh ground water and are contained on surface of the location.
- 2) Drainage will be re-routed to avoid the location and fiber rolls will be employed around the site to reduce sediment contamination to freshwater runoff due to weather events.
- 3) The earthen berm constructed to keep any freshwater runoff off the location will also eliminate any spills from leaving the location
- 4) No reserve pit or dry cuttings pit will be utilized on location.
- 5) The conductor will be drilled to a depth of 80' and 20" pipe will be run to depth and cemented to surface.
- 6) During drilling operations, a freshwater protection string of 13-3/8" 48# H40 casing will be set to a depth of 500' and cemented to surface to protect the shallow freshwater zones. Standard 9-5/8" 36# J-55 surface casing will be set 100' into the Pierre Shale to a depth of 1970' and cemented to surface.
- 7) A frac string will be used to protect the intermediate casing during hydraulic fracturing of the well.
- 8) CRI is submitting a comprehensive; site specific Spill Contingency Plan to prepare for any event which may occur during drilling and completion operations.
- 9) CRI believes a Flood Prevention plan is not necessary for this site due to the Army Corps of Engineers documentation that the high water level for Lake Sakakawea will not affect any elevation 1855' above sea level or higher. The finished rig grade elevation for Atlanta location is 1959.6' above sea level.
- 10) The Atlanta wells will be drilled continuously. They will be batch drilled. The order of drilling for all wells on the pad will be:
 - a. 1, 2, 3, 4,
 - b. 11, 12, 13, 14,
 - c. 9, 10,
 - d. 5, 6, 7, 8.

CRI believes adequate planning and precautions are being taken to prevent any contamination to ground water, shallow aquifers, and fresh water reservoirs.


Chad Newby, Operations Land Coordinator
Continental Resources, Inc.

STATE OF OKLAHOMA)
)ss:
COUNTY OF GARFIELD)

On the 8th day of June 2012, before me, a Notary Public in and for said County and State, personally appeared Chad Newby, known to me to be the Operations Land Coordinator of Continental Resources, Inc., the Corporation that executed the within instrument, and acknowledged to me that such Corporation executed the same.


Notary Public

Garfield County, Oklahoma

My Commission Expires: 7/5/2015

Commission No.: 11006023



Continental Resources Atlanta Site Contact List

Drilling & Completions / Production

		phone	mobile
Construction / Reclaim & ROW	Title		
Terry Chapman	Construction foreman		970.673.2411
Chad Newby	Operations Land Coordinator - Office		405.574.2172
Drilling			
Company man Cyclone 2 Rig Phone		701.570.8834	
Jared Miller	Lead Company Man Cyclone 2		701.290.0443
Brandon Simkins	Relief Company Man Cyclone 2		307.231.6420
Don Radke	Drilling Superintendent - Field		701.570.6326
Kyle Davis	Drilling Engineer - Office	580.249.4750	
Bryan George	Drilling Superintendent - Office	580.249.4757	
Alan McNally	Drilling Manager - Office	580.249.4792	
Completions			
Jason Walters	Production Superintendent		406.489.1456
Gene Dowhaniuk	Production Superintendent		701.770.8358
Chris Nichols	Area Completions Manager - Office	580.249.4711	580.278.9003
Production			
Howard Hill	Operator		406.489.2832
Brent Bowlds	Production Foreman	406.433.3006	406.489.3029
Donald Kennedy	Senior Production Engineer - Office	580.249.4788	
Russ Atkins	Area Production Manager		406.433.3006
Brad Aman	VP Production Northern Region	580.548.5283	

Health Safety Environmental

Dusty Grosulak	Safety Supervisor		701.260.1138
Zach Laird	Safety Manager		405.742.2696
Mike White	Northern Region Senior Environment Specialist		406.941.2521
Stacy Aguirre	Northern Region Environmental Supervisor		406.478.4450
Andy Truhan	Director of Environmental Compliance		405.535.8967

Public Relations & Media Contact Information

Kristin Miskovsky	VP Public Relations	405.234.9480	
-------------------	---------------------	--------------	--

Burns, David J.

From: Shawn Svob <ShawnSvob@contres.com>
Sent: Tuesday, March 13, 2012 3:23 PM
To: Burns, David J.
Cc: Holweger, Todd L.; Becky Barnes; Nicole Caddell; Terry Olson
Subject: Clarification of Drilling and Mud program

Continental Resources respectfully submits this memo as clarification on previously submitted permits.

In the Drilling Program, sub-section Mud Program, Surface Holes will be drilled with Fresh Water. Current Drilling Programs state "Native" as the current mud system. Future permits will reflect Fresh Water as the mud system.

Please contact me if you have further questions or require more clarification.

Respectfully,

Shawn Svob
580-747-6678

Shawn

NOTICE: This message contains confidential information and is intended for the individual named. If you are not the named addressee, you should not disseminate, distribute or copy this e-mail. Please notify the sender immediately by reply e-mail if you have received this e-mail by mistake and delete this e-mail from your system. E-mail transmission cannot be guaranteed to be secure or error-free as information could be intercepted, corrupted, lost, destroyed, arrive late or incomplete, or contain viruses. The sender therefore does not accept liability for any errors or omissions in the contents of this message which arise as a result of e-mail transmission.

PRELIMINARY DRILLING PROGRAM

5/7/2012

Lease and Well No.

Atlanta 14-6H

MUD PROGRAM

Depth	Type	Weight	Remarks
0' - 1970'	Native Freshwater	8.4-8.8	Add Soap Sticks for Mud Rings
1970' - 6500'	Invert	9.3-9.5	35-50 sec, 10-30 cc's
6500' - 10910'	Invert	9.6-10.0	40-55 sec, 10-15 cc's O/W 70/30 to 80/20
10910' - TD	Brine	8.7-10.0	Cuttings Pit

TUBULAR PROGRAM

String Type	Hole Size	Depth	Feet	Casing Diameter	Weight, Grade, Connection	ERW/Seamless	Critical Inspection
FW	17 1/2 "	500 '	500 '	13-3/8 "	13-3/8", 48 #, H-40, STC	ERW	BCI & Drift
		Float shoe,	shoe joint & float collar.	Centralize bottom 3 jts and every 4th jt to surface.			
Surf	12 1/4 "	1970 '	1970 '	9 5/8 "	9-5/8", 36 #, J-55, STC	ERW	BCI & Drift
		Float shoe,	shoe joint & float collar.	Centralize bottom joint then 5 more every other, 1 at conductor			
Int	8 3/4 "	80 '	80 '	7 "	7", 32#, P-110 IC, LTC	ERW	BCI & Drift
		4000 '	3920 '	7 "	7", 26#, P-110 IC, LTC	ERW	BCI & Drift
		8100 '	4100 '	7 "	7", 29#, P-110 IC, LTC	ERW	BCI & Drift
		9210 '	1110 '	7 "	7", 32#, P-110 IC, LTC	Seamless	BCI & Drift
		10910 '	1700 '	7 "	7", 29#, P-110 IC, LTC	ERW	BCI & Drift
		Float shoe,	shoe joint & float collar.	Centralize bottom 3 joints. Centralize thru curve and across all salts.			
Liner	6 "	18990 '	9020 '	4 1/2 "	4-1/2", 11.6 #, P-110, BTC		
Tubing		10010 '	10010 '	2 7/8 "	2-7/8", 6.5 #, L-80, EUE		

Notes: Pipe to end up in hole from top to bottom as shown.

CEMENT PROGRAM

String Type	SHOE/DV Depth	Stage Lead/Tail	Cement Bottom	Cement Top	No Sacks	Cement System	Cement Yield	Cement Weight
		Lead	350 '	0 '	111	35/65 Poz/Class "C", 3% CaCl, 12% gel	2.39	12
FW	500	Tail	500 '	350 '	77.8	Class "C", 2% CaCl	1.46	14.3
(Basis: Guage hole + 55% excess, tail 30% of length, lead to surface.)								
		Lead	1380 '	0 '	437	35/65 Poz/Class "C", 3% CaCl, 12% gel	2.39	12
Surf	1970	Tail	1970 '	1380 '	306	Class "C", 2% CaCl	1.46	14.3
(Basis: Guage hole + 55% excess, tail 30% of length, lead to surface.)								
Int	10910	Lead	7800 '	0 '	457	35/65 Poz/Class "C", 3% KCl, 5 #/sk Silica	3.21	11.3
		Tail	10910 '	7800 '	382	Class "G", 3% KCl, 35% Silica	1.59	15.6
(Basis: Gauge hole + 30% excess, Tail to 500 ft above top of Charles Salt, Lead to Surface)								

GEOLOGIC PROGNOSIS

Well Name: Atlanta 14-6H
Rig: Cyclone 02
Prospect: Williston
Target: Three Forks
Spacing: 2560

SHL: 495' FNL & 1485' FWL
 Sec. 6 - 153N - 101W
 Williams , ND

BHL: 660' FNL & 200' FEL
 Sec. 5 - 153N - 101W
 Williams , ND

Pre-Staked
 Staked

Rig Grade Elevation: 1945'
 KB: 22'
 RKB: 1967'

FORMATION	SUBSEA	TVD
Pierre Shale	100	1,867
Greenhorn	-2,582	4,549
Dakota Group (fka Mowry)	-2,958	4,925
Basal Dakota Sand	-3,657	5,624
Dunham Salt Top	NA	
Dunham Salt Base	NA	
Pine Salt Top	-5,189	7,156
Pine Salt Base	-5,216	7,183
Minnekahta	-5,235	7,202
Opeche Salt Top	NA	
Opeche Salt Base	NA	
Minnelusa Group	-5,464	7,431
Tyler	-5,650	7,617
Kibby	-6,186	8,153
Top Charles	-6,333	8,300
Base Last Charles Salt	-7,044	9,011
Mission Canyon	-7,267	9,234
Lodgepole	-7,820	9,787
Upper Bakken Shale	-8,529	10,496
Middle Bakken Member	-8,543	10,510
Lower Bakken Shale	-8,574	10,541
Three Forks/Base of Shale	-8,602	10,569
Three Forks Target	-8,617	10,584
End of Lateral	-8,639	10,606



To: Todd Holweger, NDIC
From: Shawn Svob
Date: 4/5/2012
Re: Continental Resources standard CCL, CBL, 4-1/2" liner running and testing procedures

Continental Resources' standard practice for running the cement bond log and casing caliper log is to run both logs immediately after coming out of the hole after TD, prior to running the 4-1/2" liner, to the deepest depth obtainable; however, if there are well control concerns that require us to run the liner sooner, only the CBL will be run and the CCL will be run after setting the liner.

Based on the CCL results, we determine the actual API minimum burst allowance for the 7" casing. If the downgraded API burst pressure is below our minimum required frac pressures, we will run a 4-1/2" frac string; if severe wear or holes are found in the casing, we will run a 5" cemented, to surface, tie back string.

The CBL log is run in order to determine the top of cement, as required by the NDIC. Our current 4-1/2" liner program for a 1280 unit is 30, evenly spaced, stages with 29 swellable packers. The liner shoe is set approximately 180 feet off bottom. The shoe stage below the last packer has 2 joints, a double valved float, one joint, and a ported guide shoe – appx 130 ft. The liner is run using a running tool on the end of 4" DP. The 7" packer/hanger is set about 40 ft above KOP between two casing collars but conditions occasionally occur that require setting higher, either through unexpected failure or in order to isolate casing wear close to KOP. Recently we have tried 40 stage liners and the trend to explore the optimum stage count will continue.. Once the liner is at depth, a ball is dropped through the DP, the ball is pressured up against the setting tool to approximately 2500 psi, and the 7" packer/hanger is set.

A push pull test is done to confirm the hanger has set. Then, a 4500 psi pressure test is completed on the back side of the 4" DP to confirm the packer has set. The setting tool is then backed off and the 4" DP/running tool is laid down.

Immediately after the rotary rig has been moved off the well location, the 7" csg and liner packer/ hanger are tested to the frac pressure. The testers will rig up and test the tubing head to 5000 psi. Next a test plug will be run and set, using wire line, in the top of the 7" packer/hanger. Testers will pressure up to our frac pressure, typically 8500 psi, to confirm the 7" is ready for completion.

Shawn Svob
Drilling Operations Coordinator

CONTINENTAL RESOURCES

Location: NORTH DAKOTA Slot: SLOT#14 ATLANTA 14-6H(495'FNL & 1485'FWL,SEC.06)
 Field: WILLIAMS COUNTY Well: ATLANTA 14-6H
 Facility: SEC.06-T153N-R101W Wellbore: ATLANTA 14-6H PWB

Plot reference wellpath is ATLANTA 14-6H (REV-D.0) PWP

True vertical depths are referenced to CYCLONE 2 (RK8)	Grid System: NAD83 / Lambert North Dakota SP, Northern Zone (30B), U.S. feet.
Measured depths are referenced to CYCLONE 2 (RK8)	North Reference: True north
CYCLONE 2 (RK8) is Mean Sea Level: 1087 feet	Scale: True distance
Mean Sea Level to Mud line (At Slot: SLOT#14 ATLANTA 14-6H(495'FNL & 1485'FWL,SEC.06)) 0 feet	Depths are in feet
Coordinates are in feet referenced to Slot	Created by: parmer on 5/7/2012

Location Information


Facility Name		Grid East (US ft)	Grid North (US ft)	Latitude	Longitude
SEC.06-T153N-R101W		1173034.108	421169.028	48°09'33.379"N	103°43'56.580"W
Slot	Local N (ft)	Local E (ft)	Grid East (US ft)	Grid North (US ft)	Latitude
SLOT#14 ATLANTA 14-6H(495'FNL & 1485'FWL,SEC.06)	27.20	1214.83	1160249.110	421175.270	48°09'33.847"N 103°43'58.028"W
CYCLONE 2 (RK8) to Mud line (At Slot: SLOT#14 ATLANTA 14-6H(495'FNL & 1485'FWL,SEC.06))					10957 ft
Mean Sea Level to Mud line (At Slot: SLOT#14 ATLANTA 14-6H(495'FNL & 1485'FWL,SEC.06))					0 ft
CYCLONE 2 (RK8) to Mean Sea Level					10957 ft

Targets


Name	MD (ft)	TVD (ft)	Local N (ft)	Local E (ft)	Grid East (US ft)	Grid North (US ft)	Latitude	Longitude
ATLANTA 14-6H SECTION 05	0.00	0.00	0.00	1160249.12	421175.28	48°09'33.647"N	103°43'59.034"W	
ATLANTA 14-6H SECTION 06	0.00	0.00	0.00	1160249.12	421175.28	48°09'33.847"N	103°43'59.055"W	
ATLANTA 14-6H SECTION 05	0.00	0.00	0.00	1160249.12	421175.28	48°09'33.647"N	103°43'59.055"W	
ATLANTA 14-6H SECTION LINES	0.00	0.00	0.00	1160249.12	421175.28	48°09'33.647"N	103°43'59.055"W	
ATLANTA 14-6H BHL REV-1(660'FNL & 200'FEL,SEC.05)	10692.00	-184.71	8573.00	119380.17	420651.40	48°09'32.002"N	103°43'59.709"W	
ATLANTA 14-6H BHL REV-2(660'FNL & 200'FEL,SEC.05)	10592.00	-165.04	8475.00	119380.82	420638.01	48°09'31.999"N	103°43'59.280"W	
ATLANTA 14-6H HARDLINE(200'FWL & 200'FEL)	10628.00	0.00	8522.00	119328.12	421115.29	48°09'33.647"N	103°43'59.059"W	
ATLANTA 14-6H BHL REV-3(660'FNL & 200'FEL,SEC.05)	10596.00	-165.00	8519.00	1193644.79	420664.12	48°09'31.998"N	103°43'59.280"W	
ATLANTA 14-6H BHL REV-4(660'FNL & 200'FEL,SEC.05)	19160.65	106.00	871.00	1195050.87	420640.95	48°09'31.997"N	103°43'59.274"W	

Well Profile Data

Design Comment	MD (ft)	Inc (°)	Az (°)	TVD (ft)	Local N (ft)	Local E (ft)	DLS (*100ft)	VS (ft)
Tie On	22.00	0.000	91.071	22.00	0.00	0.00	0.00	0.00
End of Tangent	10011.04	0.000	91.071	10011.04	0.00	0.00	0.00	0.00
End of Build	10909.51	89.847	91.071	10584.00	-10.68	571.33	10.00	571.43
End of Tangent	19166.65	89.847	91.071	10606.00	-165.00	8827.00	0.00	8828.54

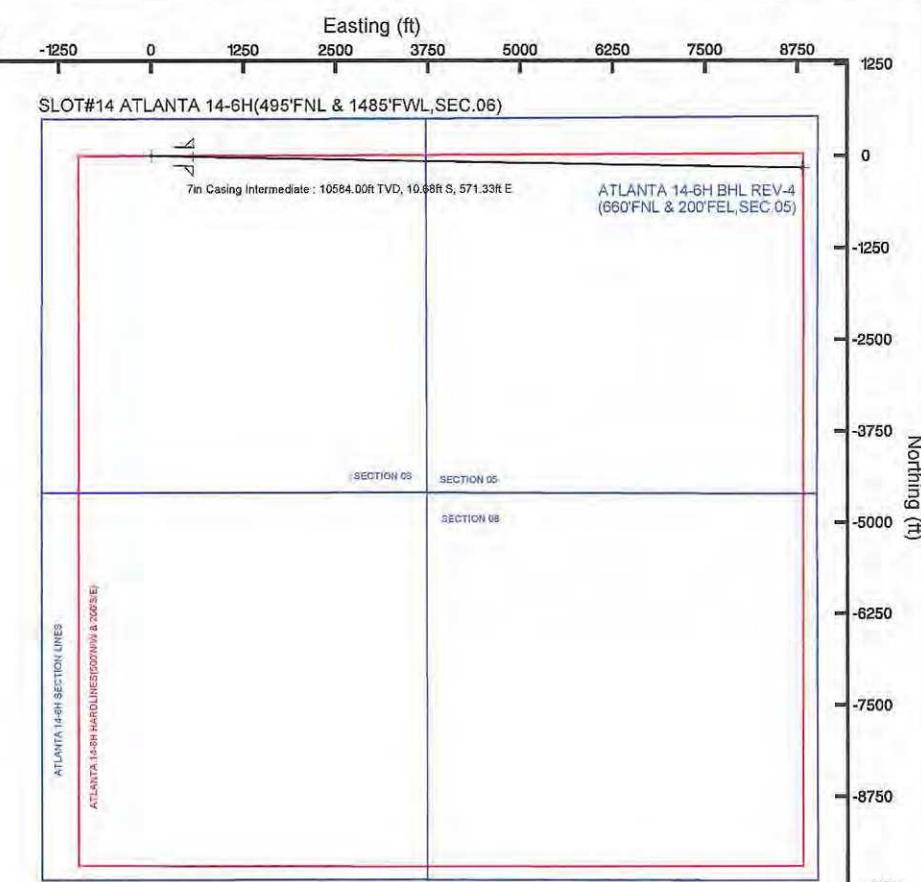


True Vertical Depth (ft)



BGGM (1945.0 to 2013.0) Dip: 73.08° Field: 56635.5 nT

To correct azimuth from Magnetic to True add 8.76 degrees
 For example: if the Magnetic North Azimuth = 90 degrees, then the True North Azimuth = 90 + 8.76 = 98.76





Planned Wellpath Report

ATLANTA 14-6H (REV-D.0) PWP

Page 1 of 10



REFERENCE WELLPATH IDENTIFICATION

Operator	CONTINENTAL RESOURCES	Slot	SLOT#14 ATLANTA 14-6H(495'FNL & 1485'FWL,SEC.06)
Area	NORTH DAKOTA	Well	ATLANTA 14-6H
Field	WILLIAMS COUNTY	Wellbore	ATLANTA 14-6H PWB
Facility	SEC.06-T153N-R101W		

REPORT SETUP INFORMATION

Projection System	NAD83 / Lambert North Dakota SP, Northern Zone (3301), US feet	Software System	WellArchitect® 3.0.2
North Reference	True	User	Painsetr
Scale	0.999936	Report Generated	5/7/2012 at 1:21:13 PM
Convergence at slot	2.40° West	Database/Source file	WA_Denver/ATLANTA_14-6H_PWB.xml

WELLPATH LOCATION

	Local coordinates		Grid coordinates		Geographic coordinates	
	North[ft]	East[ft]	Easting[US ft]	Northing[US ft]	Latitude	Longitude
Slot Location	27.20	1214.93	1180249.12	421175.28	48°06'33.647"N	103°43'39.058"W
Facility Reference Pt			1179034.20	421199.10	48°06'33.379"N	103°43'56.960"W
Field Reference Pt			1379474.78	594749.03	48°36'17.680"N	102°56'05.560"W

WELLPATH DATUM

Calculation method	Minimum curvature	CYCLONE 2 (RKB) to Facility Vertical Datum	1967.00ft
Horizontal Reference Pt	Slot	CYCLONE 2 (RKB) to Mean Sea Level	1967.00ft
Vertical Reference Pt	CYCLONE 2 (RKB)	CYCLONE 2 (RKB) to Mud Line at Slot (SLOT#14 ATLANTA 14-6H(495'FNL & 1485'FWL,SEC.06))	1967.00ft
MD Reference Pt	CYCLONE 2 (RKB)	Section Origin	N 0.00, E 0.00 ft
Field Vertical Reference	Mean Sea Level	Section Azimuth	91.07°



Planned Wellpath Report

ATLANTA 14-6H (REV-D.0) PWP

Page 2 of 10



REFERENCE WELLPATH IDENTIFICATION

Operator	CONTINENTAL RESOURCES	Slot	SLOT#14 ATLANTA 14-6H(495'FNL & 1485'FWL,SEC.06)
Area	NORTH DAKOTA	Well	ATLANTA 14-6H
Field	WILLIAMS COUNTY	Wellbore	ATLANTA 14-6H PWB
Facility	SEC.06-T153N-R101W		

WELLPATH DATA (196 stations) † = interpolated/extrapolated station

MD [ft]	Inclination [°]	Azimuth [°]	TVD [ft]	Vert Sect [ft]	North [ft]	East [ft]	DLS [°/100ft]	Comments
0.00†	0.000	91.071	0.00	0.00	0.00	0.00	0.00	
22.00	0.000	91.071	22.00	0.00	0.00	0.00	0.00	Tie On
122.00†	0.000	91.071	122.00	0.00	0.00	0.00	0.00	
222.00†	0.000	91.071	222.00	0.00	0.00	0.00	0.00	
322.00†	0.000	91.071	322.00	0.00	0.00	0.00	0.00	
422.00†	0.000	91.071	422.00	0.00	0.00	0.00	0.00	
522.00†	0.000	91.071	522.00	0.00	0.00	0.00	0.00	
622.00†	0.000	91.071	622.00	0.00	0.00	0.00	0.00	
722.00†	0.000	91.071	722.00	0.00	0.00	0.00	0.00	
822.00†	0.000	91.071	822.00	0.00	0.00	0.00	0.00	
922.00†	0.000	91.071	922.00	0.00	0.00	0.00	0.00	
1022.00†	0.000	91.071	1022.00	0.00	0.00	0.00	0.00	
1122.00†	0.000	91.071	1122.00	0.00	0.00	0.00	0.00	
1222.00†	0.000	91.071	1222.00	0.00	0.00	0.00	0.00	
1322.00†	0.000	91.071	1322.00	0.00	0.00	0.00	0.00	
1422.00†	0.000	91.071	1422.00	0.00	0.00	0.00	0.00	
1522.00†	0.000	91.071	1522.00	0.00	0.00	0.00	0.00	
1622.00†	0.000	91.071	1622.00	0.00	0.00	0.00	0.00	
1722.00†	0.000	91.071	1722.00	0.00	0.00	0.00	0.00	
1822.00†	0.000	91.071	1822.00	0.00	0.00	0.00	0.00	
1922.00†	0.000	91.071	1922.00	0.00	0.00	0.00	0.00	
2022.00†	0.000	91.071	2022.00	0.00	0.00	0.00	0.00	
2122.00†	0.000	91.071	2122.00	0.00	0.00	0.00	0.00	
2222.00†	0.000	91.071	2222.00	0.00	0.00	0.00	0.00	
2322.00†	0.000	91.071	2322.00	0.00	0.00	0.00	0.00	
2422.00†	0.000	91.071	2422.00	0.00	0.00	0.00	0.00	
2522.00†	0.000	91.071	2522.00	0.00	0.00	0.00	0.00	
2622.00†	0.000	91.071	2622.00	0.00	0.00	0.00	0.00	
2722.00†	0.000	91.071	2722.00	0.00	0.00	0.00	0.00	
2822.00†	0.000	91.071	2822.00	0.00	0.00	0.00	0.00	



Planned Wellpath Report

ATLANTA 14-6H (REV-D.0) PWP
Page 3 of 10



REFERENCE WELLPATH IDENTIFICATION								
Operator	CONTINENTAL RESOURCES			Slot	SLOT#14 ATLANTA 14-6H(495'FNL & 1485'FWL,SEC.06)			
Area	NORTH DAKOTA			Well	ATLANTA 14-6H			
Field	WILLIAMS COUNTY			Wellbore	ATLANTA 14-6H PWB			
Facility	SEC.06-T153N-R101W							

WELLPATH DATA (196 stations) † = interpolated/extrapolated station								
MD [ft]	Inclination [°]	Azimuth [°]	TVD [ft]	Vert Sect [ft]	North [ft]	East [ft]	DLS [°/100ft]	Comments
2922.00†	0.000	91.071	2922.00	0.00	0.00	0.00	0.00	
3022.00†	0.000	91.071	3022.00	0.00	0.00	0.00	0.00	
3122.00†	0.000	91.071	3122.00	0.00	0.00	0.00	0.00	
3222.00†	0.000	91.071	3222.00	0.00	0.00	0.00	0.00	
3322.00†	0.000	91.071	3322.00	0.00	0.00	0.00	0.00	
3422.00†	0.000	91.071	3422.00	0.00	0.00	0.00	0.00	
3522.00†	0.000	91.071	3522.00	0.00	0.00	0.00	0.00	
3622.00†	0.000	91.071	3622.00	0.00	0.00	0.00	0.00	
3722.00†	0.000	91.071	3722.00	0.00	0.00	0.00	0.00	
3822.00†	0.000	91.071	3822.00	0.00	0.00	0.00	0.00	
3922.00†	0.000	91.071	3922.00	0.00	0.00	0.00	0.00	
4022.00†	0.000	91.071	4022.00	0.00	0.00	0.00	0.00	
4122.00†	0.000	91.071	4122.00	0.00	0.00	0.00	0.00	
4222.00†	0.000	91.071	4222.00	0.00	0.00	0.00	0.00	
4322.00†	0.000	91.071	4322.00	0.00	0.00	0.00	0.00	
4422.00†	0.000	91.071	4422.00	0.00	0.00	0.00	0.00	
4522.00†	0.000	91.071	4522.00	0.00	0.00	0.00	0.00	
4622.00†	0.000	91.071	4622.00	0.00	0.00	0.00	0.00	
4722.00†	0.000	91.071	4722.00	0.00	0.00	0.00	0.00	
4822.00†	0.000	91.071	4822.00	0.00	0.00	0.00	0.00	
4922.00†	0.000	91.071	4922.00	0.00	0.00	0.00	0.00	
5022.00†	0.000	91.071	5022.00	0.00	0.00	0.00	0.00	
5122.00†	0.000	91.071	5122.00	0.00	0.00	0.00	0.00	
5222.00†	0.000	91.071	5222.00	0.00	0.00	0.00	0.00	
5322.00†	0.000	91.071	5322.00	0.00	0.00	0.00	0.00	
5422.00†	0.000	91.071	5422.00	0.00	0.00	0.00	0.00	
5522.00†	0.000	91.071	5522.00	0.00	0.00	0.00	0.00	
5622.00†	0.000	91.071	5622.00	0.00	0.00	0.00	0.00	
5722.00†	0.000	91.071	5722.00	0.00	0.00	0.00	0.00	
5822.00†	0.000	91.071	5822.00	0.00	0.00	0.00	0.00	



Planned Wellpath Report

ATLANTA 14-6H (REV-D.0) PWP

Page 4 of 10



REFERENCE WELLPATH IDENTIFICATION

Operator	CONTINENTAL RESOURCES	Slot	SLOT#14 ATLANTA 14-6H(495'FNL & 1485'FWL,SEC.06)
Area	NORTH DAKOTA	Well	ATLANTA 14-6H
Field	WILLIAMS COUNTY	Wellbore	ATLANTA 14-6H PWB
Facility	SEC.06-T153N-R101W		

WELLPATH DATA (196 stations) † = interpolated/extrapolated station

MD [ft]	Inclination [°]	Azimuth [°]	TVD [ft]	Vert Sect [ft]	North [ft]	East [ft]	DLS [°/100ft]	Comments
5922.00†	0.000	91.071	5922.00	0.00	0.00	0.00	0.00	
6022.00†	0.000	91.071	6022.00	0.00	0.00	0.00	0.00	
6122.00†	0.000	91.071	6122.00	0.00	0.00	0.00	0.00	
6222.00†	0.000	91.071	6222.00	0.00	0.00	0.00	0.00	
6322.00†	0.000	91.071	6322.00	0.00	0.00	0.00	0.00	
6422.00†	0.000	91.071	6422.00	0.00	0.00	0.00	0.00	
6522.00†	0.000	91.071	6522.00	0.00	0.00	0.00	0.00	
6622.00†	0.000	91.071	6622.00	0.00	0.00	0.00	0.00	
6722.00†	0.000	91.071	6722.00	0.00	0.00	0.00	0.00	
6822.00†	0.000	91.071	6822.00	0.00	0.00	0.00	0.00	
6922.00†	0.000	91.071	6922.00	0.00	0.00	0.00	0.00	
7022.00†	0.000	91.071	7022.00	0.00	0.00	0.00	0.00	
7122.00†	0.000	91.071	7122.00	0.00	0.00	0.00	0.00	
7222.00†	0.000	91.071	7222.00	0.00	0.00	0.00	0.00	
7322.00†	0.000	91.071	7322.00	0.00	0.00	0.00	0.00	
7422.00†	0.000	91.071	7422.00	0.00	0.00	0.00	0.00	
7522.00†	0.000	91.071	7522.00	0.00	0.00	0.00	0.00	
7622.00†	0.000	91.071	7622.00	0.00	0.00	0.00	0.00	
7722.00†	0.000	91.071	7722.00	0.00	0.00	0.00	0.00	
7822.00†	0.000	91.071	7822.00	0.00	0.00	0.00	0.00	
7922.00†	0.000	91.071	7922.00	0.00	0.00	0.00	0.00	
8022.00†	0.000	91.071	8022.00	0.00	0.00	0.00	0.00	
8122.00†	0.000	91.071	8122.00	0.00	0.00	0.00	0.00	
8222.00†	0.000	91.071	8222.00	0.00	0.00	0.00	0.00	
8322.00†	0.000	91.071	8322.00	0.00	0.00	0.00	0.00	
8422.00†	0.000	91.071	8422.00	0.00	0.00	0.00	0.00	
8522.00†	0.000	91.071	8522.00	0.00	0.00	0.00	0.00	
8622.00†	0.000	91.071	8622.00	0.00	0.00	0.00	0.00	
8722.00†	0.000	91.071	8722.00	0.00	0.00	0.00	0.00	
8822.00†	0.000	91.071	8822.00	0.00	0.00	0.00	0.00	



Planned Wellpath Report

ATLANTA 14-6H (REV-D.0) PWP
Page 5 of 10



REFERENCE WELLPATH IDENTIFICATION

Operator	CONTINENTAL RESOURCES	Slot	SLOT#14 ATLANTA 14-6H(495'FNL & 1485'FWL,SEC.06)
Area	NORTH DAKOTA	Well	ATLANTA 14-6H
Field	WILLIAMS COUNTY	Wellbore	ATLANTA 14-6H PWB
Facility	SEC.06-T153N-R101W		

WELLPATH DATA (196 stations) † = interpolated/extrapolated station

MD [ft]	Inclination [°]	Azimuth [°]	TVD [ft]	Vert Sect [ft]	North [ft]	East [ft]	DLS [°/100ft]	Comments
8922.00†	0.000	91.071	8922.00	0.00	0.00	0.00	0.00	
9022.00†	0.000	91.071	9022.00	0.00	0.00	0.00	0.00	
9122.00†	0.000	91.071	9122.00	0.00	0.00	0.00	0.00	
9222.00†	0.000	91.071	9222.00	0.00	0.00	0.00	0.00	
9322.00†	0.000	91.071	9322.00	0.00	0.00	0.00	0.00	
9422.00†	0.000	91.071	9422.00	0.00	0.00	0.00	0.00	
9522.00†	0.000	91.071	9522.00	0.00	0.00	0.00	0.00	
9622.00†	0.000	91.071	9622.00	0.00	0.00	0.00	0.00	
9722.00†	0.000	91.071	9722.00	0.00	0.00	0.00	0.00	
9822.00†	0.000	91.071	9822.00	0.00	0.00	0.00	0.00	
9922.00†	0.000	91.071	9922.00	0.00	0.00	0.00	0.00	
10011.04	0.000	91.071	10011.04	0.00	0.00	0.00	0.00	End of Tangent
10022.00†	1.096	91.071	10022.00	0.10	0.00	0.10	10.00	
10122.00†	11.096	91.071	10121.31	10.71	-0.20	10.71	10.00	
10222.00†	21.096	91.071	10217.27	38.40	-0.72	38.39	10.00	
10322.00†	31.096	91.071	10306.96	82.33	-1.54	82.32	10.00	
10422.00†	41.096	91.071	10387.66	141.17	-2.64	141.15	10.00	
10522.00†	51.096	91.071	10456.92	213.13	-3.98	213.09	10.00	
10622.00†	61.096	91.071	10512.62	296.02	-5.53	295.97	10.00	
10722.00†	71.096	91.071	10553.09	387.33	-7.24	387.26	10.00	
10822.00†	81.096	91.071	10577.09	484.28	-9.05	484.19	10.00	
10909.51	89.847	91.071	10584.00	571.43	-10.68	571.33	10.00	End of Build
10922.00†	89.847	91.071	10584.03	583.92	-10.91	583.82	0.00	
11022.00†	89.847	91.071	10584.30	683.92	-12.78	683.80	0.00	
11122.00†	89.847	91.071	10584.56	783.92	-14.65	783.78	0.00	
11222.00†	89.847	91.071	10584.83	883.92	-16.52	883.76	0.00	
11322.00†	89.847	91.071	10585.09	983.92	-18.39	983.74	0.00	
11422.00†	89.847	91.071	10585.36	1083.92	-20.26	1083.73	0.00	
11522.00†	89.847	91.071	10585.63	1183.92	-22.13	1183.71	0.00	
11622.00†	89.847	91.071	10585.89	1283.92	-24.00	1283.69	0.00	



Planned Wellpath Report

ATLANTA 14-6H (REV-D.0) PWP

Page 6 of 10



REFERENCE WELLPATH IDENTIFICATION

Operator	CONTINENTAL RESOURCES	Slot	SLOT#14 ATLANTA 14-6H(495'FNL & 1485'FWL,SEC.06)
Area	NORTH DAKOTA	Well	ATLANTA 14-6H
Field	WILLIAMS COUNTY	Wellbore	ATLANTA 14-6H PWB
Facility	SEC.06-T153N-R101W		

WELLPATH DATA (196 stations) † = interpolated/extrapolated station

MD [ft]	Inclination [°]	Azimuth [°]	TVD [ft]	Vert Sect [ft]	North [ft]	East [ft]	DLS [°/100ft]	Comments
11722.00†	89.847	91.071	10586.16	1383.91	-25.86	1383.67	0.00	
11822.00†	89.847	91.071	10586.43	1483.91	-27.73	1483.66	0.00	
11922.00†	89.847	91.071	10586.69	1583.91	-29.60	1583.64	0.00	
12022.00†	89.847	91.071	10586.96	1683.91	-31.47	1683.62	0.00	
12122.00†	89.847	91.071	10587.23	1783.91	-33.34	1783.60	0.00	
12222.00†	89.847	91.071	10587.49	1883.91	-35.21	1883.58	0.00	
12322.00†	89.847	91.071	10587.76	1983.91	-37.08	1983.57	0.00	
12422.00†	89.847	91.071	10588.03	2083.91	-38.95	2083.55	0.00	
12522.00†	89.847	91.071	10588.29	2183.91	-40.82	2183.53	0.00	
12622.00†	89.847	91.071	10588.56	2283.91	-42.68	2283.51	0.00	
12722.00†	89.847	91.071	10588.83	2383.91	-44.55	2383.49	0.00	
12822.00†	89.847	91.071	10589.09	2483.91	-46.42	2483.48	0.00	
12922.00†	89.847	91.071	10589.36	2583.91	-48.29	2583.46	0.00	
13022.00†	89.847	91.071	10589.63	2683.91	-50.16	2683.44	0.00	
13122.00†	89.847	91.071	10589.89	2783.91	-52.03	2783.42	0.00	
13222.00†	89.847	91.071	10590.16	2883.91	-53.90	2883.41	0.00	
13322.00†	89.847	91.071	10590.42	2983.91	-55.77	2983.39	0.00	
13422.00†	89.847	91.071	10590.69	3083.91	-57.64	3083.37	0.00	
13522.00†	89.847	91.071	10590.96	3183.91	-59.51	3183.35	0.00	
13622.00†	89.847	91.071	10591.22	3283.91	-61.37	3283.33	0.00	
13722.00†	89.847	91.071	10591.49	3383.91	-63.24	3383.32	0.00	
13822.00†	89.847	91.071	10591.76	3483.91	-65.11	3483.30	0.00	
13922.00†	89.847	91.071	10592.02	3583.91	-66.98	3583.28	0.00	
14022.00†	89.847	91.071	10592.29	3683.91	-68.85	3683.26	0.00	
14122.00†	89.847	91.071	10592.56	3783.91	-70.72	3783.25	0.00	
14222.00†	89.847	91.071	10592.82	3883.91	-72.59	3883.23	0.00	
14322.00†	89.847	91.071	10593.09	3983.91	-74.46	3983.21	0.00	
14422.00†	89.847	91.071	10593.36	4083.91	-76.33	4083.19	0.00	
14522.00†	89.847	91.071	10593.62	4183.90	-78.19	4183.17	0.00	
14622.00†	89.847	91.071	10593.89	4283.90	-80.06	4283.16	0.00	



Planned Wellpath Report

ATLANTA 14-6H (REV-D.0) PWP

Page 7 of 10



**BAKER
HUGHES**

REFERENCE WELLPATH IDENTIFICATION

Operator	CONTINENTAL RESOURCES	Slot	SLOT#14 ATLANTA 14-6H(495'FNL & 1485'FWL,SEC.06)
Area	NORTH DAKOTA	Well	ATLANTA 14-6H
Field	WILLIAMS COUNTY	Wellbore	ATLANTA 14-6H PWB
Facility	SEC.06-T153N-R101W		

WELLPATH DATA (196 stations) † = interpolated/extrapolated station

MD [ft]	Inclination [°]	Azimuth [°]	TVD [ft]	Vert Sect [ft]	North [ft]	East [ft]	DLS [°/100ft]	Comments
14722.00†	89.847	91.071	10594.16	4383.90	-81.93	4383.14	0.00	
14822.00†	89.847	91.071	10594.42	4483.90	-83.80	4483.12	0.00	
14922.00†	89.847	91.071	10594.69	4583.90	-85.67	4583.10	0.00	
15022.00†	89.847	91.071	10594.96	4683.90	-87.54	4683.09	0.00	
15122.00†	89.847	91.071	10595.22	4783.90	-89.41	4783.07	0.00	
15222.00†	89.847	91.071	10595.49	4883.90	-91.28	4883.05	0.00	
15322.00†	89.847	91.071	10595.75	4983.90	-93.15	4983.03	0.00	
15422.00†	89.847	91.071	10596.02	5083.90	-95.01	5083.01	0.00	
15522.00†	89.847	91.071	10596.29	5183.90	-96.88	5183.00	0.00	
15622.00†	89.847	91.071	10596.55	5283.90	-98.75	5282.98	0.00	
15722.00†	89.847	91.071	10596.82	5383.90	-100.62	5382.96	0.00	
15822.00†	89.847	91.071	10597.09	5483.90	-102.49	5482.94	0.00	
15922.00†	89.847	91.071	10597.35	5583.90	-104.36	5582.92	0.00	
16022.00†	89.847	91.071	10597.62	5683.90	-106.23	5682.91	0.00	
16122.00†	89.847	91.071	10597.89	5783.90	-108.10	5782.89	0.00	
16222.00†	89.847	91.071	10598.15	5883.90	-109.97	5882.87	0.00	
16322.00†	89.847	91.071	10598.42	5983.90	-111.84	5982.85	0.00	
16422.00†	89.847	91.071	10598.69	6083.90	-113.70	6082.84	0.00	
16522.00†	89.847	91.071	10598.95	6183.90	-115.57	6182.82	0.00	
16622.00†	89.847	91.071	10599.22	6283.90	-117.44	6282.80	0.00	
16722.00†	89.847	91.071	10599.49	6383.90	-119.31	6382.78	0.00	
16822.00†	89.847	91.071	10599.75	6483.90	-121.18	6482.76	0.00	
16922.00†	89.847	91.071	10600.02	6583.90	-123.05	6582.75	0.00	
17022.00†	89.847	91.071	10600.28	6683.90	-124.92	6682.73	0.00	
17122.00†	89.847	91.071	10600.55	6783.90	-126.79	6782.71	0.00	
17222.00†	89.847	91.071	10600.82	6883.90	-128.66	6882.69	0.00	
17322.00†	89.847	91.071	10601.08	6983.90	-130.52	6982.68	0.00	
17422.00†	89.847	91.071	10601.35	7083.89	-132.39	7082.66	0.00	
17522.00†	89.847	91.071	10601.62	7183.89	-134.26	7182.64	0.00	
17622.00†	89.847	91.071	10601.88	7283.89	-136.13	7282.62	0.00	



Planned Wellpath Report

ATLANTA 14-6H (REV-D.0) PWP

Page 8 of 10



REFERENCE WELLPATH IDENTIFICATION

Operator	CONTINENTAL RESOURCES	Slot	SLOT#14 ATLANTA 14-6H(495'FNL & 1485'FWL,SEC.06)
Area	NORTH DAKOTA	Well	ATLANTA 14-6H
Field	WILLIAMS COUNTY	Wellbore	ATLANTA 14-6H PWB
Facility	SEC.06-T153N-R101W		

WELLPATH DATA (196 stations) † = interpolated/extrapolated station

MD [ft]	Inclination [°]	Azimuth [°]	TVD [ft]	Vert Sect [ft]	North [ft]	East [ft]	DLS [°/100ft]	Comments
17722.00†	89.847	91.071	10602.15	7383.89	-138.00	7382.60	0.00	
17822.00†	89.847	91.071	10602.42	7483.89	-139.87	7482.59	0.00	
17922.00†	89.847	91.071	10602.68	7583.89	-141.74	7582.57	0.00	
18022.00†	89.847	91.071	10602.95	7683.89	-143.61	7682.55	0.00	
18122.00†	89.847	91.071	10603.22	7783.89	-145.48	7782.53	0.00	
18222.00†	89.847	91.071	10603.48	7883.89	-147.35	7882.51	0.00	
18322.00†	89.847	91.071	10603.75	7983.89	-149.21	7982.50	0.00	
18422.00†	89.847	91.071	10604.02	8083.89	-151.08	8082.48	0.00	
18522.00†	89.847	91.071	10604.28	8183.89	-152.95	8182.46	0.00	
18622.00†	89.847	91.071	10604.55	8283.89	-154.82	8282.44	0.00	
18722.00†	89.847	91.071	10604.82	8383.89	-156.69	8382.43	0.00	
18822.00†	89.847	91.071	10605.08	8483.89	-158.56	8482.41	0.00	
18922.00†	89.847	91.071	10605.35	8583.89	-160.43	8582.39	0.00	
19022.00†	89.847	91.071	10605.61	8683.89	-162.30	8682.37	0.00	
19122.00†	89.847	91.071	10605.88	8783.89	-164.17	8782.35	0.00	
19166.65	89.847	91.071	10606.00 ¹	8828.54	-165.00	8827.00	0.00	End of Tangent

HOLE & CASING SECTIONS - Ref Wellbore: ATLANTA 14-6H PWB Ref Wellpath: ATLANTA 14-6H (REV-D.0) PWP

String/Diameter	Start MD [ft]	End MD [ft]	Interval [ft]	Start TVD [ft]	End TVD [ft]	Start N/S [ft]	Start E/W [ft]	End N/S [ft]	End E/W [ft]
7in Casing Intermediate	22.00	10909.51	10887.51	22.00	10584.00	0.00	0.00	-10.68	571.33



Planned Wellpath Report

ATLANTA 14-6H (REV-D.0) PWP
Page 9 of 10



REFERENCE WELLPATH IDENTIFICATION								
Operator	CONTINENTAL RESOURCES			Slot	SLOT#14 ATLANTA 14-6H(495'FNL & 1485'FWL,SEC.06)			
Area	NORTH DAKOTA			Well	ATLANTA 14-6H			
Field	WILLIAMS COUNTY			Wellbore	ATLANTA 14-6H PWB			
Facility	SEC.06-T153N-R101W							

TARGETS									
Name	MD [ft]	TVD [ft]	North [ft]	East [ft]	Grid East [US ft]	Grid North [US ft]	Latitude	Longitude	Shape
ATLANTA 14-6H SECTION 05		0.00	0.00	0.00	1180249.12	421175.28	48°06'33.647"N	103°43'39.058"W	polygon
ATLANTA 14-6H SECTION 06		0.00	0.00	0.00	1180249.12	421175.28	48°06'33.647"N	103°43'39.058"W	polygon
ATLANTA 14-6H SECTION 08		0.00	0.00	0.00	1180249.12	421175.28	48°06'33.647"N	103°43'39.058"W	polygon
ATLANTA 14-6H SECTION LINES		0.00	0.00	0.00	1180249.12	421175.28	48°06'33.647"N	103°43'39.058"W	polygon
ATLANTA 14-6H BHL ON PLAT REV-1 (660'FNL & 500'FEL,SEC.05)	10592.00	-164.71	8575.05	1188809.17	420651.40	48°06'32.002"N	103°41'32.706"W	point	
ATLANTA 14-6H BHL REV-2(660'FNL & 200'FEL,SEC.05)	10592.00	-165.04	8875.00	1189108.82	420638.51	48°06'31.998"N	103°41'28.286"W	point	
ATLANTA 14-6H HARDLINES(500'N/W & 200'S/E)	10606.00	0.00	0.00	1180249.12	421175.28	48°06'33.647"N	103°43'39.058"W	polygon	
ATLANTA 14-6H BHL REV-3(660'FNL & 200'FEL,SEC.05)	10606.00	-165.00	8810.90	1189044.78	420641.24	48°06'31.998"N	103°41'29.230"W	point	
1) ATLANTA 14-6H BHL REV-4(660'FNL & 200'FEL,SEC.05)	19166.65	10606.00	-165.00	8827.00	1189060.87	420640.56	48°06'31.998"N	103°41'28.993"W	point

SURVEY PROGRAM - Ref Wellbore: ATLANTA 14-6H PWB			Ref Wellpath: ATLANTA 14-6H (REV-D.0) PWP		
Start MD [ft]	End MD [ft]	Positional Uncertainty Model		Log Name/Comment	Wellbore
22.00	21000.00	NaviTrak (Standard)			ATLANTA 14-6H PWB



Planned Wellpath Report

ATLANTA 14-6H (REV-D.0) PWP

Page 10 of 10



REFERENCE WELLPATH IDENTIFICATION


Operator	CONTINENTAL RESOURCES	Slot	SLOT#14 ATLANTA 14-6H(495'FNL & 1485'FWL,SEC.06)
Area	NORTH DAKOTA	Well	ATLANTA 14-6H
Field	WILLIAMS COUNTY	Wellbore	ATLANTA 14-6H PWB
Facility	SEC.06-T153N-R101W		

DESIGN COMMENTS

MD [ft]	Inclination [°]	Azimuth [°]	TVD [ft]	Comment
22.00	0.000	91.071	22.00	Tie On
10011.04	0.000	91.071	10011.04	End of Tangent
10909.51	89.847	91.071	10584.00	End of Build
19166.65	89.847	91.071	10606.00	End of Tangent

HORIZONTAL SECTION PLAT
CONTINENTAL RESOURCES INC.

ATLANTA 14-6H
SECTION 5, T153N, R101W
WILLIAMS COUNTY, NORTH DAKOTA
MCKENZIE COUNTY, NORTH DAKOTA

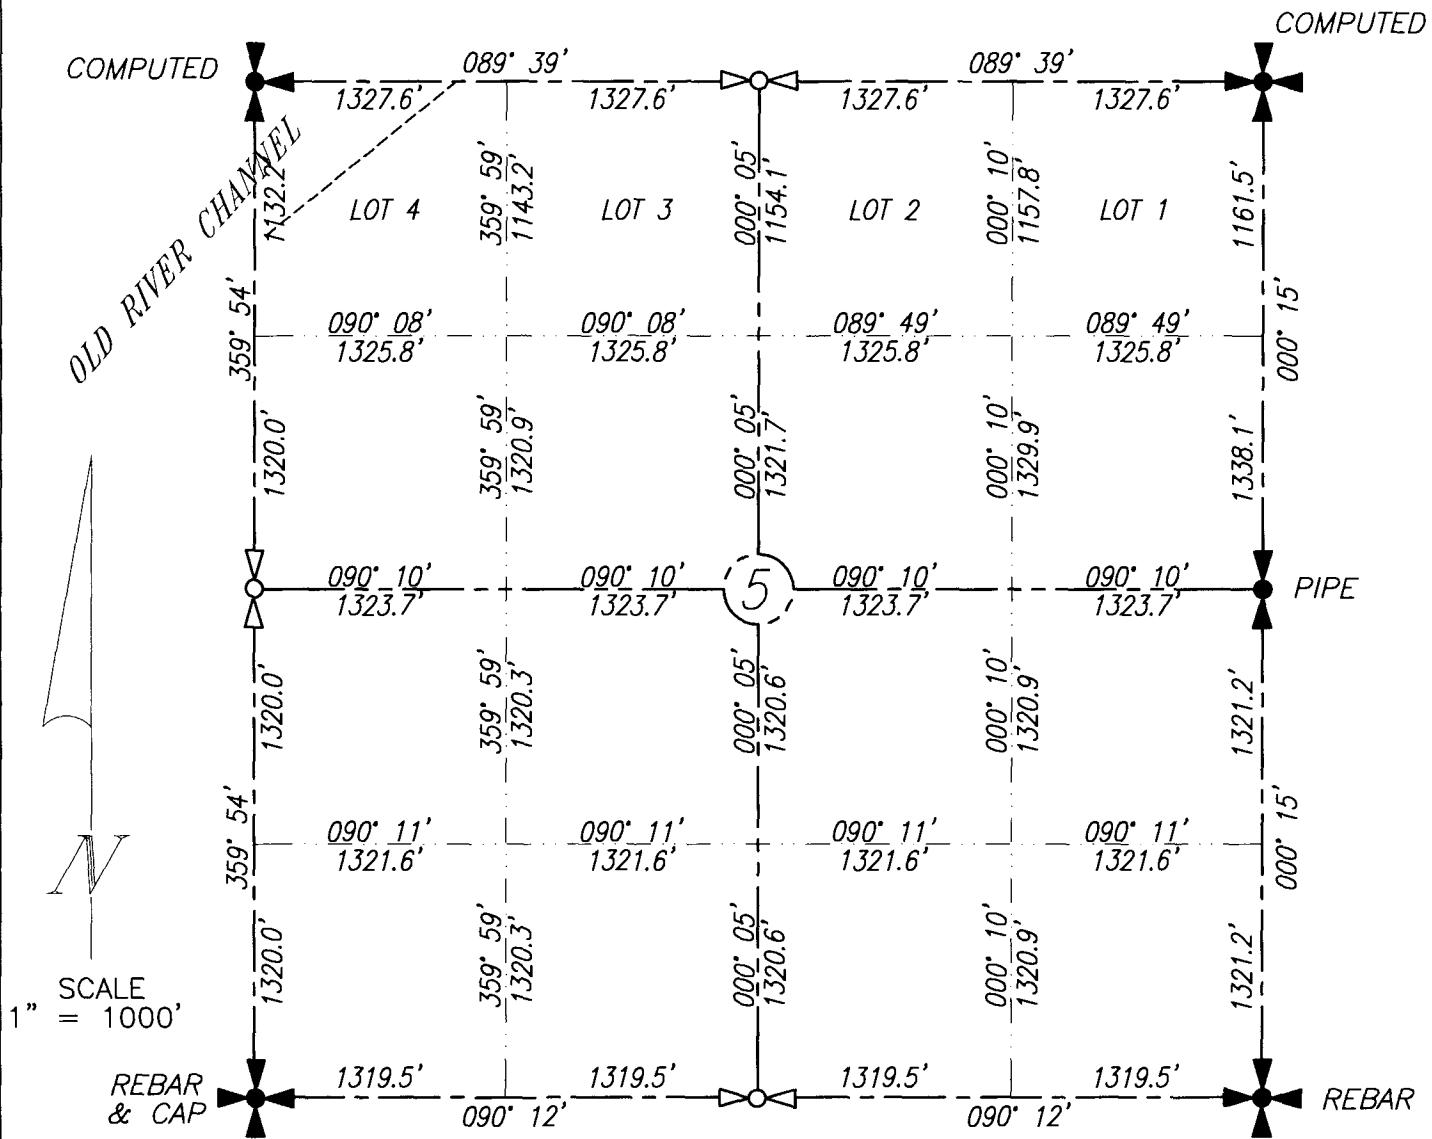

ALL CORNERS SHOWN ON THIS PLAT WERE FOUND IN THE FIELD
DISTANCES TO ALL OTHERS ARE CALCULATED.
ALL BEARINGS SHOWN ARE ASSUMED.


I CERTIFY THAT THIS PLAT CORRECTLY REPRESENTS
WORK PERFORMED BY ME OR UNDER MY RESPONSIBLE
CHARGE AND IS TRUE AND CORRECT TO THE BEST OF
MY KNOWLEDGE AND BELIEF
L.S. 3366

John Paulson P.L.S. 3366

BROSZ ENGINEERING INC.

BOX 357
BOWMAN, N.D. 58623
PHONE: 701-523-3340
FAX: 701-523-5243
PROJECT NO. 12-10

HORIZONTAL SECTION PLAT
CONTINENTAL RESOURCES INC.
ATLANTA 5-6H
SECTION 6, T153N, R101W
WILLIAMS COUNTY, NORTH DAKOTA
MCKENZIE COUNTY, NORTH DAKOTA

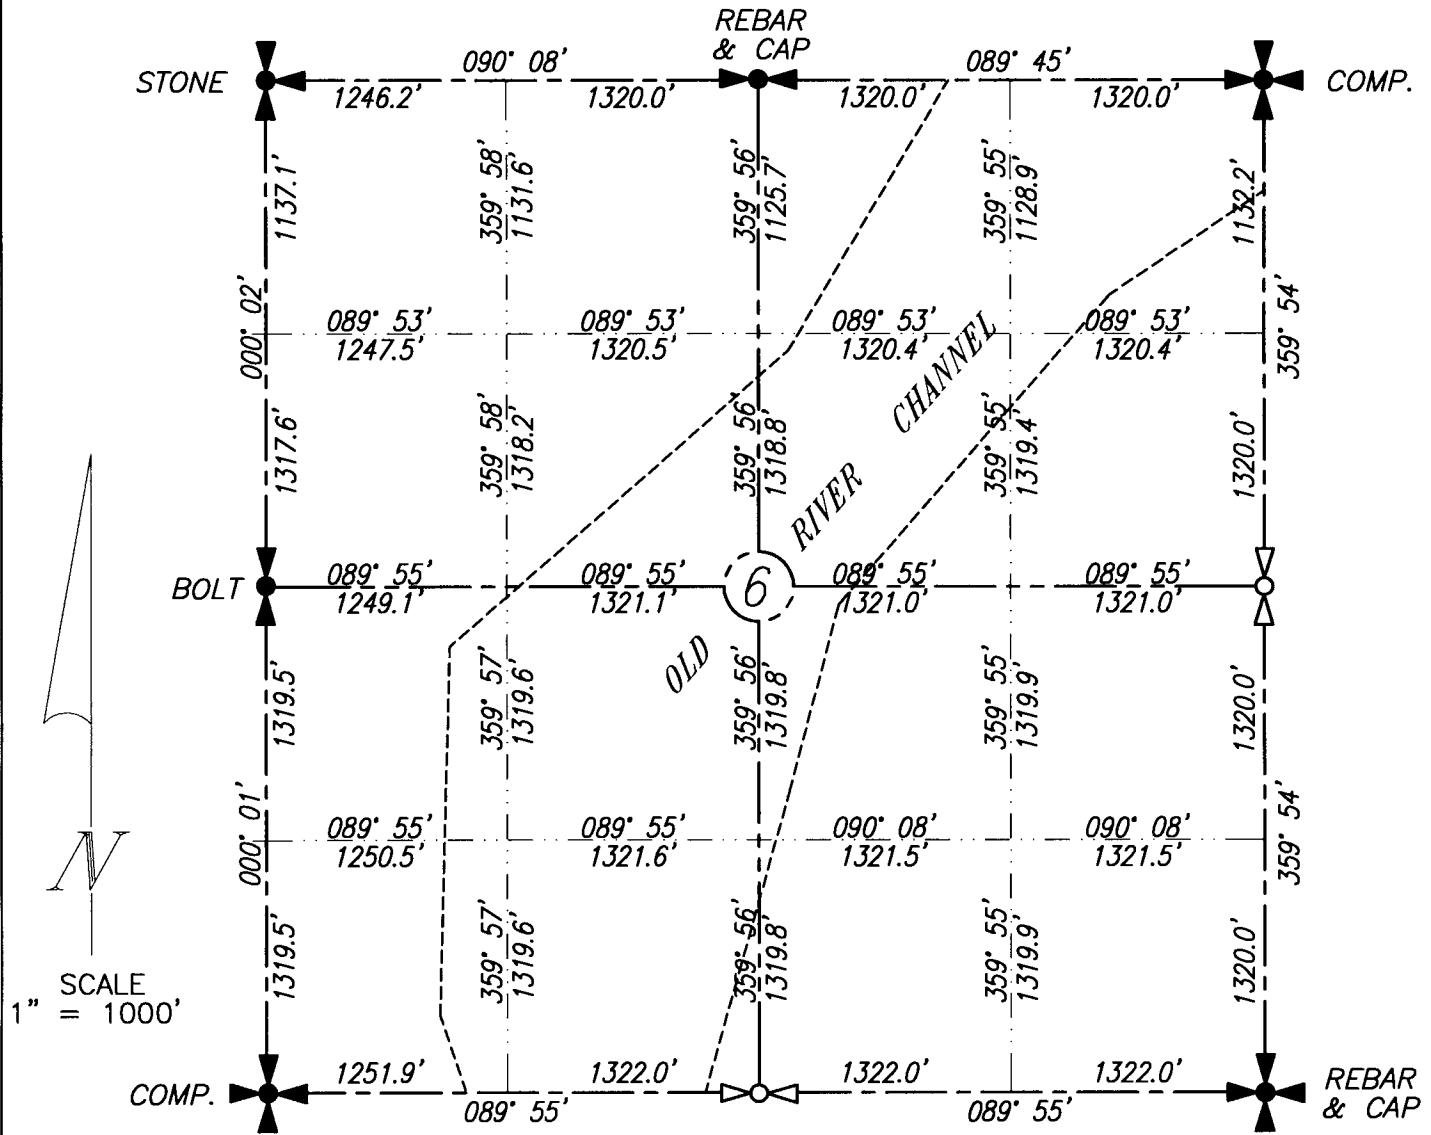

MOST OF THE SECTION IS LOTTED DUE TO THE MISSOURI RIVER.

ALL CORNERS SHOWN ON THIS PLAT WERE FOUND IN THE FIELD
DISTANCES TO ALL OTHERS ARE CALCULATED.

BEARINGS SHOWN ARE ASSUMED.

JOHN PAULSON

I CERTIFY THAT THE DRAWING CORRECTLY REPRESENTS
WORK PERFORMED BY ME OR UNDER MY RESPONSIBLE
CHARGE, AND IS SURVEYED AND CORRECT TO THE BEST OF
MY KNOWLEDGE AND ABILITY.

John Paulson, R.L.S. #3366


BROSZ ENGINEERING INC.

BOX 357
BOWMAN, N.D. 58623
PHONE: 701-523-3340
FAX: 701-523-5243

PROJECT NO. 12-10

HORIZONTAL SECTION PLAT
CONTINENTAL RESOURCES INC.

ATLANTA 4-6H
SECTION 7, T153N, R101W
MCKENZIE COUNTY, NORTH DAKOTA

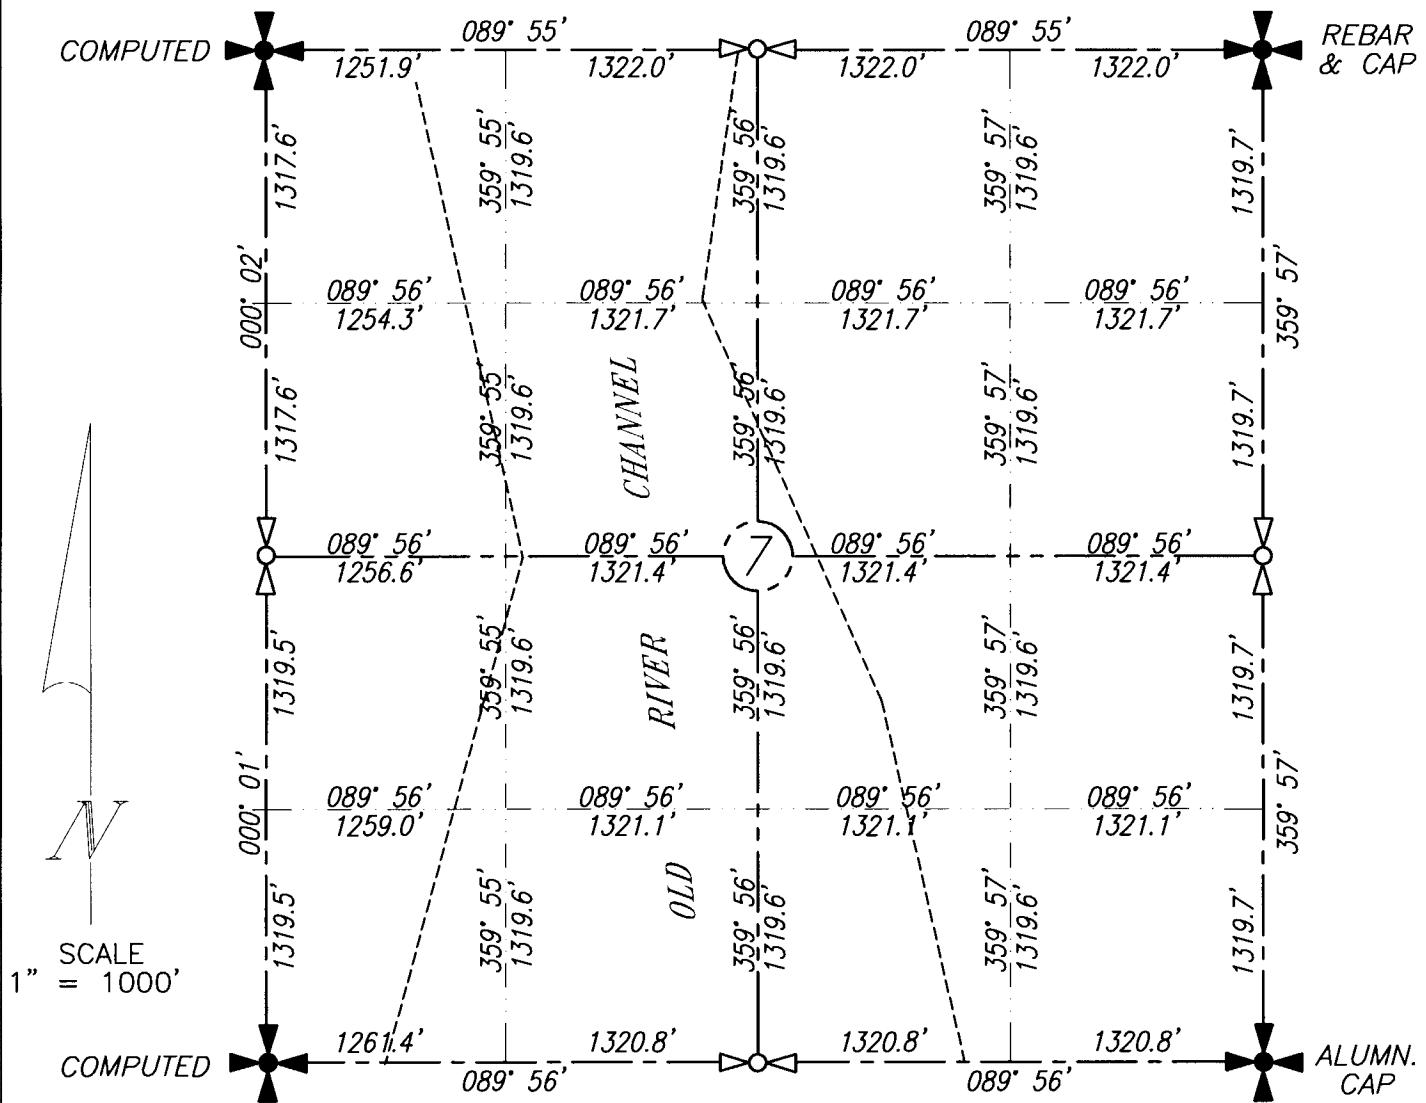

MOST OF THE SECTION IS LOTTED DUE TO THE MISSOURI RIVER.

ALL CORNERS SHOWN ON THIS PLAT WERE FOUND IN THE FIELD
DISTANCES TO ALL OTHERS ARE CALCULATED.
ALL BEARINGS SHOWN ARE ASSUMED.

I CERTIFY THAT THIS PLAT CORRECTLY REPRESENTS
WORK PERFORMED BY ME OR UNDER MY RESPONSIBLE
CHARGE, AND IS TRUE AND CORRECT TO THE BEST OF
MY KNOWLEDGE AND BELIEF
REGISTERED
125.3366

JOHN PAULSON, P.E., S.R.E. #3366


BROSZ ENGINEERING INC.

BOX 357
BOWMAN, N.D. 58623
PHONE: 701-523-3340
FAX: 701-523-5243

PROJECT NO. 12-10

HORIZONTAL SECTION PLAT
CONTINENTAL RESOURCES INC.
ATLANTA 5-6H FEDERAL
SECTION 8, T153N, R101W
MCKENZIE COUNTY, NORTH DAKOTA

REVISED: 5-2-2012

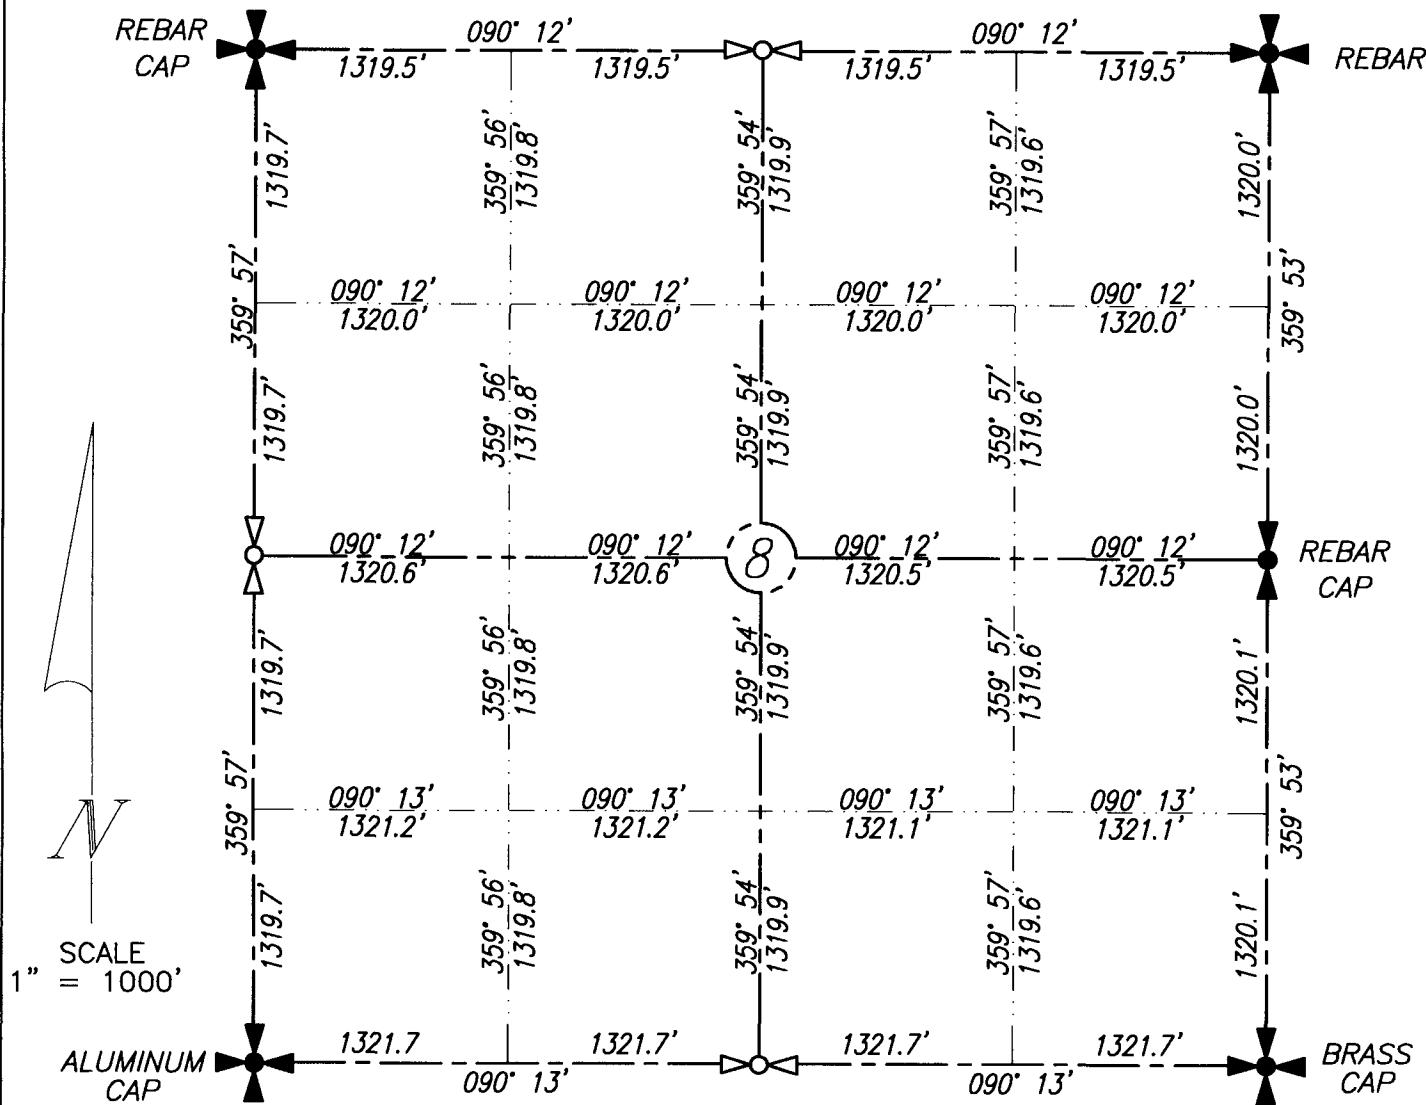

ALL CORNERS SHOWN ON THIS PLAT WERE FOUND IN THE FIELD
DISTANCES TO ALL OTHERS ARE CALCULATED.
ALL BEARINGS SHOWN ARE ASSUMED.


I CERTIFY THAT THIS PLAT CORRECTLY REPRESENTS
WORK PERFORMED BY ME OR UNDER MY RESPONSIBLE
CHARGE, AND IS TRUE AND CORRECT TO THE BEST OF
MY KNOWLEDGE AND BELIEF SURVEYOR
L.S. 3366
John Paulson
JOHN PAULSON R.L.S. 3366 N.D.
5-2-12

BROSZ ENGINEERING INC.


BOX 357
BOWMAN, N.D. 58623
PHONE: 701-523-3340
FAX: 701-523-5243
PROJECT NO. 12-10

BOTTOM HOLE LOCATION PLAT
 CONTINENTAL RESOURCES INC.
 ATLANTA 14-6H
 SECTION 6, T153N, R101W
 WILLIAMS COUNTY, NORTH DAKOTA
 495' FNL & 1485' FWL

REVISED: 5-4-2012

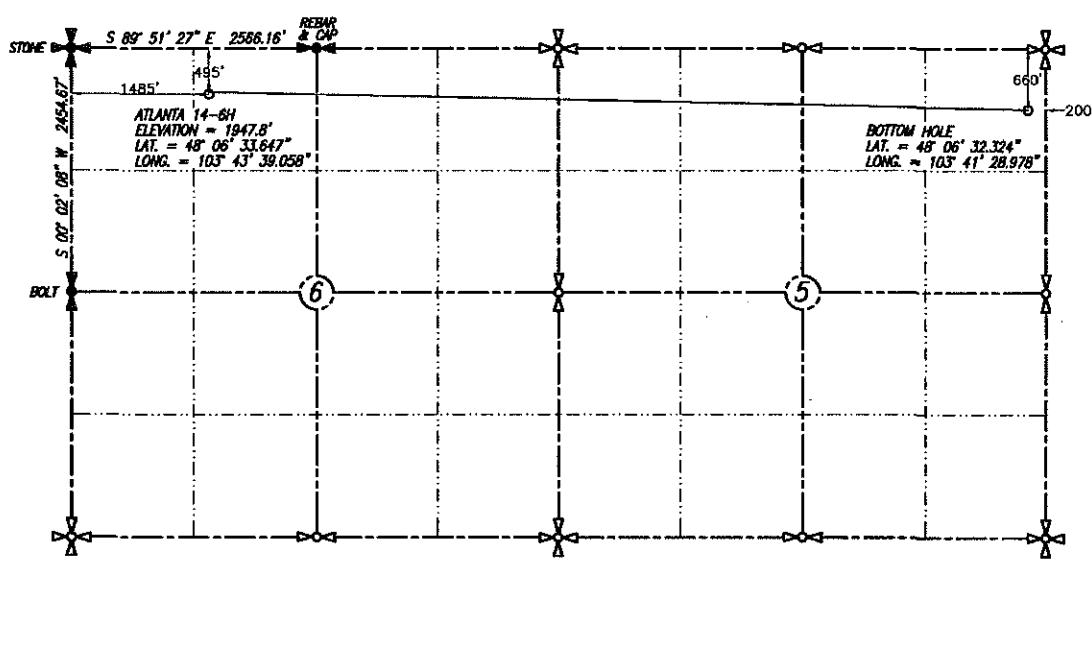

I CERTIFY THAT THIS PLAT CORRECTLY REPRESENTS
 WORK PERFORMED BY ME OR UNDER MY RESPONSIBLE
 CHARGE, AND IS TRUE AND CORRECT TO THE BEST OF
 MY KNOWLEDGE AND BELIEF



5-4-12

DATE STAKED: 2-9-2012

BASIS OF VERTICAL DATUM:
 NAVD 1988 GEODETIC 09


PERSON AUTHORIZING SURVEY;
CHAD NEWBY

EXPLANATION AREA: NAD83(CORS96)

BASIS OF BEARING: TRUE NORTH

BROSZ ENGINEERING INC.

BOX 357
 BOWMAN, N.D. 58623
 PHONE: 701-523-3340
 FAX: 701-523-5243
 PROJECT NO. 12-10

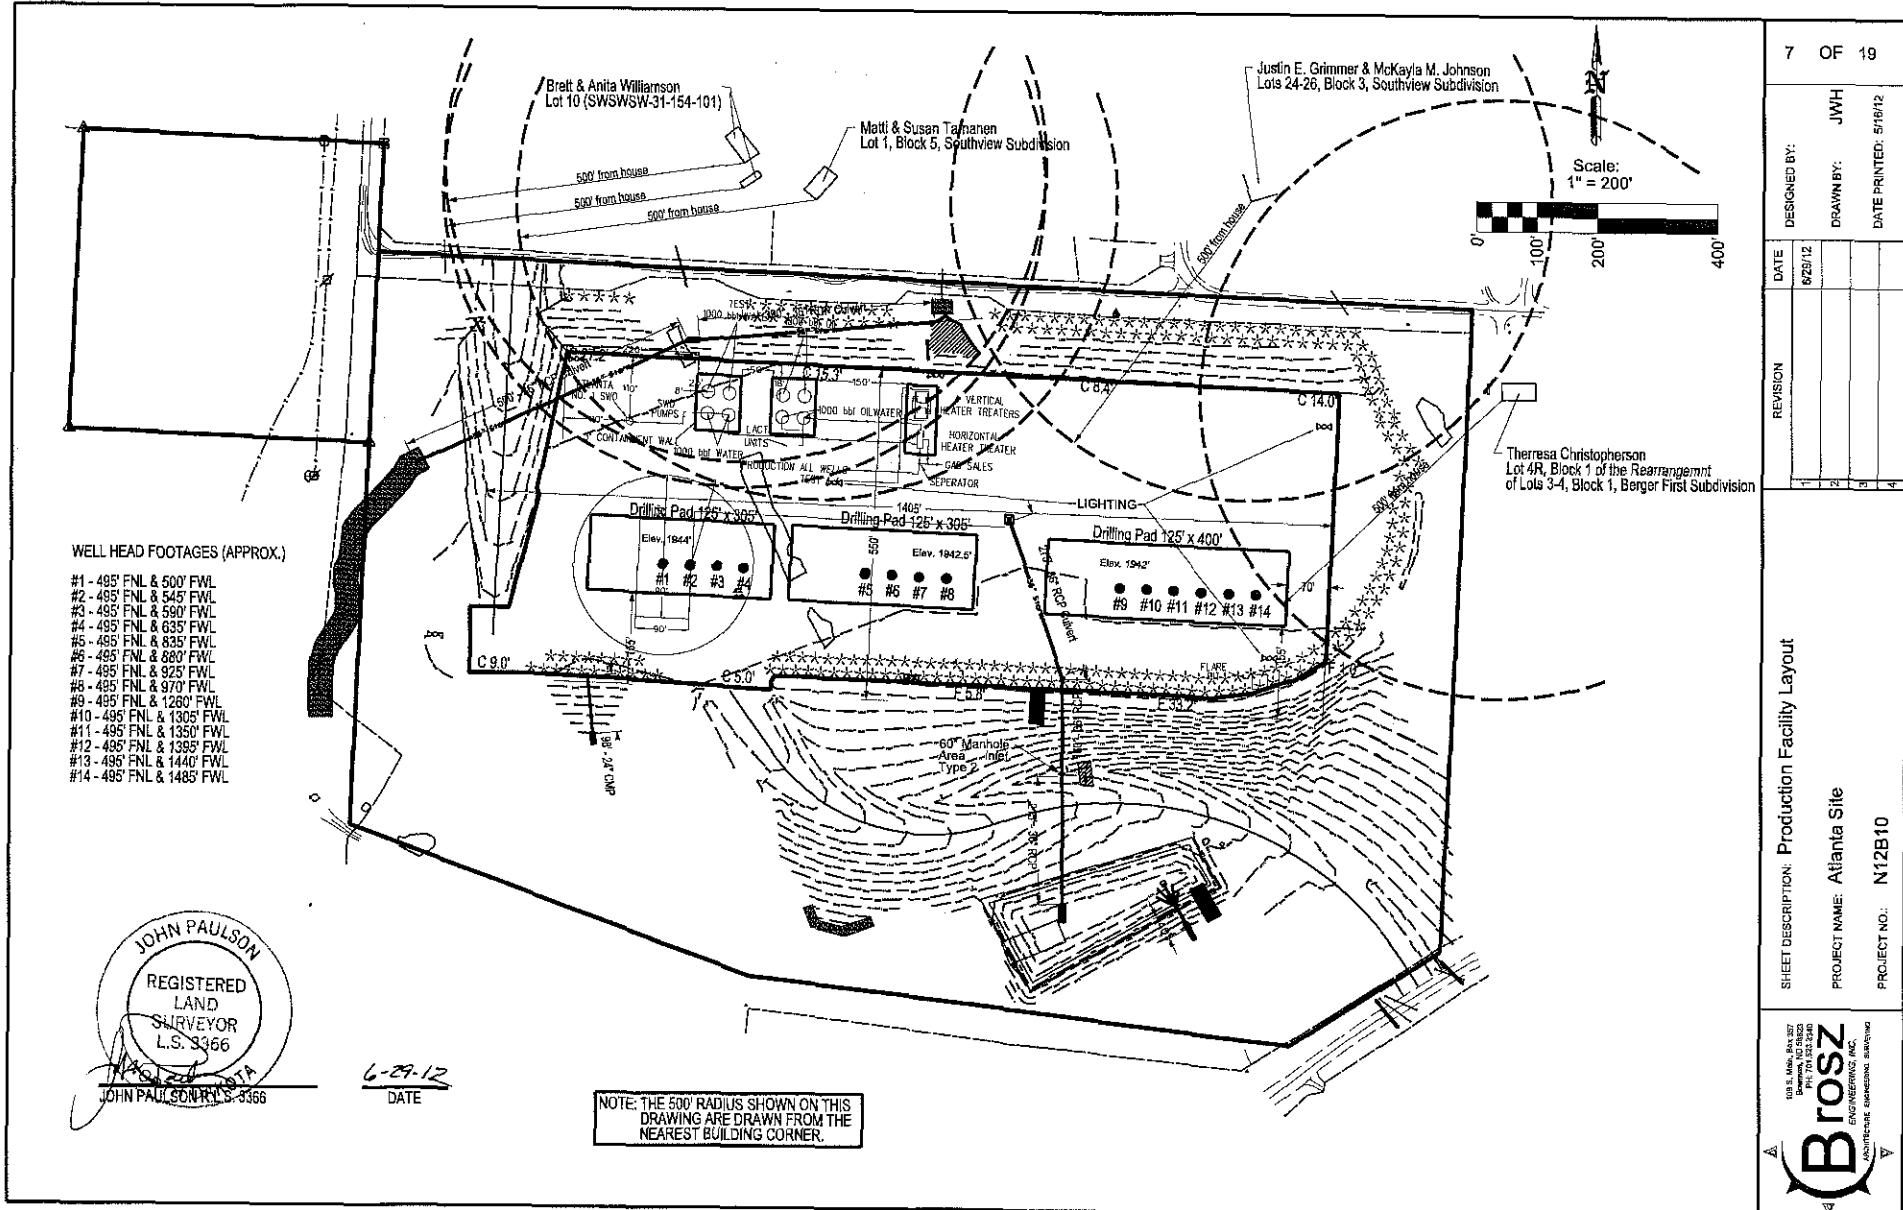

Spill Toolkit Inventory

(To be Checked After Each Use)

Supplies	Quantity	Actual	Supplies	Quantity	Actual
Personal Protection			Miscellaneous		
Trauma/1st Aid Kit	1		EnviroClean (5-gal units of concentrate)	2	
Eye Wash	1		Duct Tape (Case)	3	
Hand Cleaner	2		Flashlights	6	
Nitrile Gloves (L & XL Case)	2		Flood Lights	2	
FRC Rain Coat - Extra Large	3		Extension Cord 50' 12-gauge	5	
FRC Rain Coat - Large	3		55-gal. Drums w/lids	2	
Rubber Safety Toed Boots - Size 10	2		Large Trash Cans	2	
Rubber Safety Toed Boots - Size 11	2		HD Drum Liners - boxes	2	
Rubber Safety Toed Boots - Size 12	2		Hoses - Kit (Blue & Green)	5	
FRC Tyvex Suits - Case XL	1		Plastic Buckets	5	
Neoprene Chest Waders - L	1		Propane Cylinders - 20-lb.	2	
Neoprene Chest Waders - L	1		Propane Weed Burner W/Hose	1	
Containment			Pump - Trash	2	
Absorbent (sphag)	10		Pump - 115V Water Transfer	2	
Absorbent Boom 3" x 10'	2		Gas Powered Generator (3-5K Watt)	1	
Absorbent Boom 5" x 10'	10		Misc. Ratchet Straps	6	
Absorbent Boom 8" x 10'	8		Rope 1/2" x 100'	2	
Containment Boom - Fast Water	3		Rope 1/4" x 50'	4	
Absorbent Pads (Hydrocarbon)	10		Rope 3/8" x 100'	2	
Absorbent Pads (Universal)	5		Shop Towels - box	2	
Absorbent Pillows 18" x 18" box	3		Caulking Gun	2	
Absorbent Pom Pom Cube	7		Silicon Tubes	10	
Absorbent Sweep - 16" x 100' - Bag	5		Metal Stakes/Spikes	8	
Miscellaneous			Metal T-Posts	6	
Antifreeze	2		Bungee Cords	3	
Push Broom	2		Wire - 25' roll - smooth	1	
Shovels	2		Fire Extinguisher	1	
Rake	5		Equipment Hooks	6	
Squeegees	2		Shelving	4	
Scoop	2		Drawers	1	
Spark Resistant Scoop	1		Misc. Building Supplies	1	

Tabor, David

From: Becky Barnes <Becky.Barnes@clr.com>
Sent: Wednesday, June 06, 2012 1:46 PM
To: Tabor, David
Subject: Atlanta Pad Wells

All cuttings for the Atlanta Pad wells will be hauled to the Tioga Prairie disposal.


Prairie Disposal for Cuttings
102C10 52nd St NW
Tioga ND 58852

Let me know if there is anything else that you need.


Thanks.

Bb

Becky Barnes
Regulatory Compliance Specialist
Continental Resources, Inc.
Office 405-234-9161
Fax 580-548-5293




NOTICE: This message contains confidential information and is intended for the individual named. If you are not the named addressee, you should not disseminate, distribute or copy this e-mail. Please notify the sender immediately by reply e-mail if you have received this e-mail by mistake and delete this e-mail from your system. E-mail transmission cannot be guaranteed to be secure or error-free as information could be intercepted, corrupted, lost, destroyed, arrive late or incomplete, or contain viruses. The sender therefore does not accept liability for any errors or omissions in the contents of this message which arise as a result of e-mail transmission.

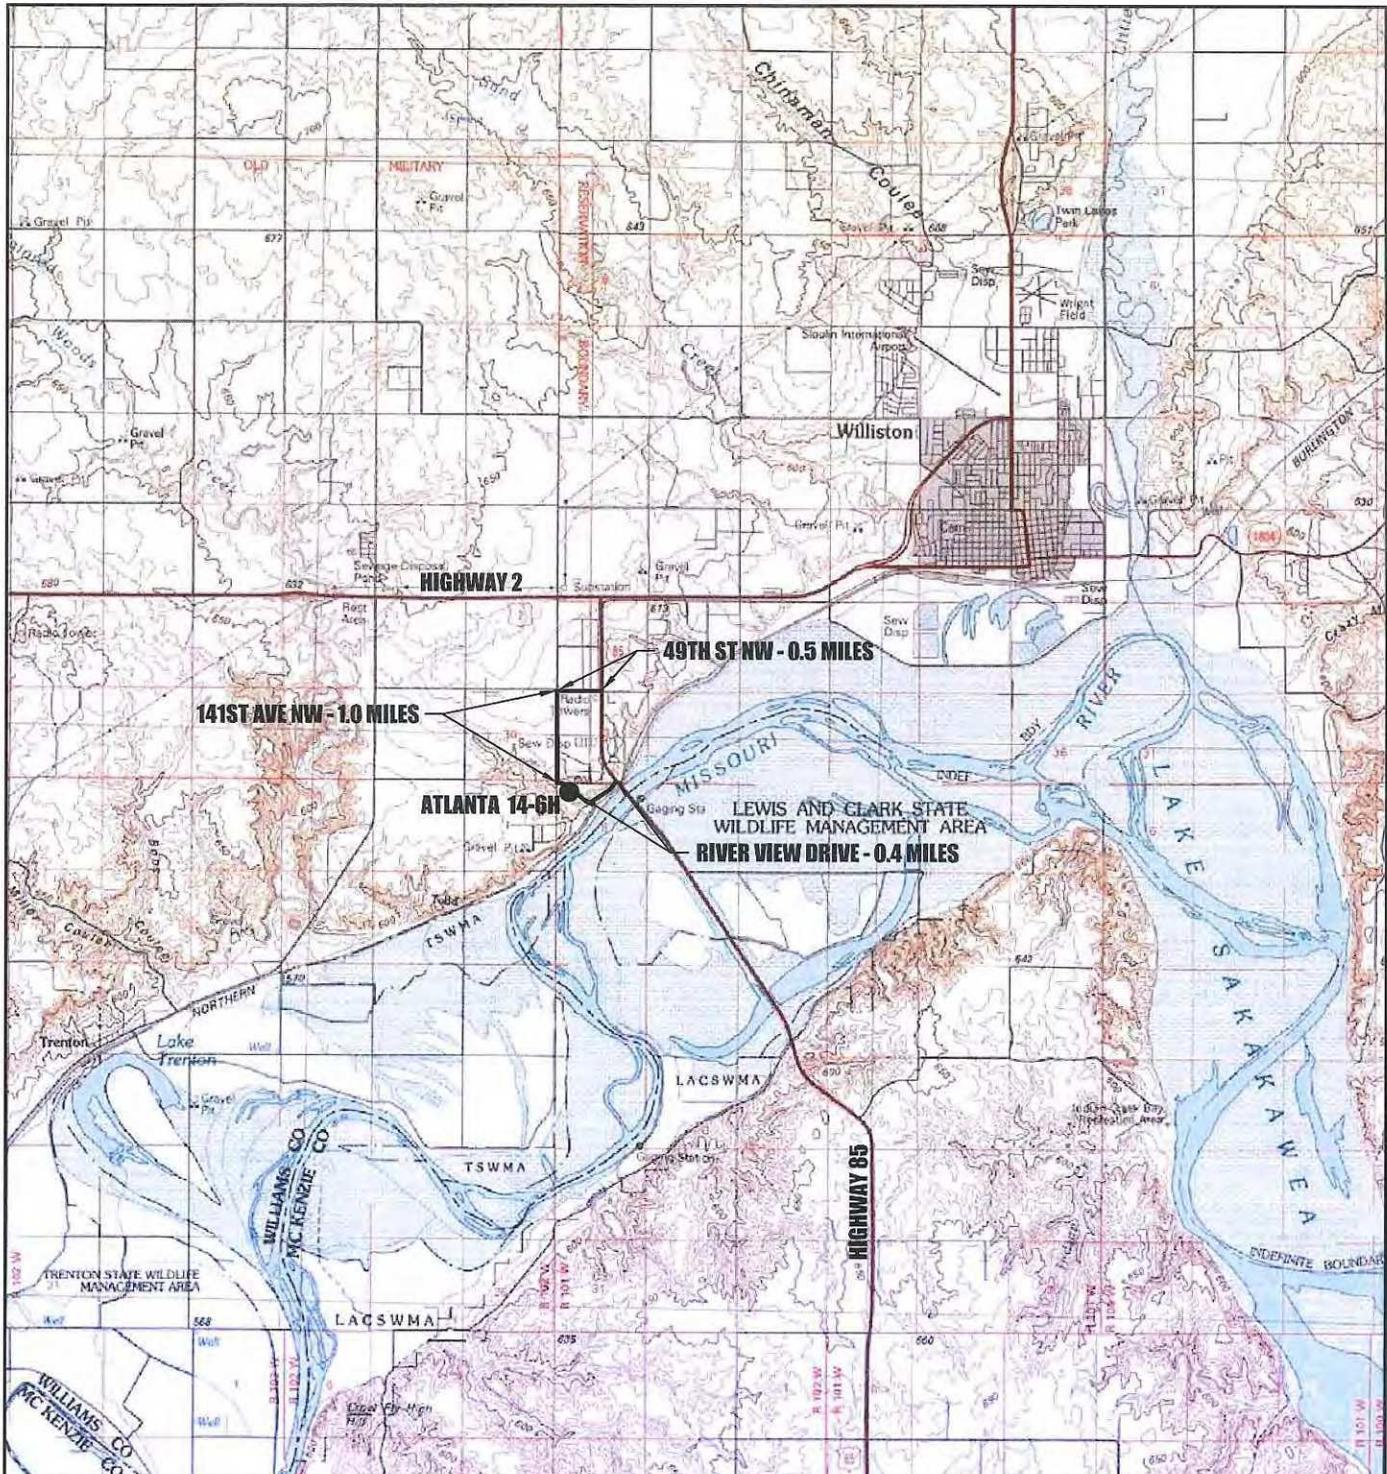


CONTINENTAL RESOURCES INC.

**EXHIBIT 1
VICINITY MAP
PROPOSED ACCESS ROUTE**

**ATLANTA 14-6H
SECTION 6, T153N, R101W
WILLIAMS COUNTY, NORTH DAKOTA**



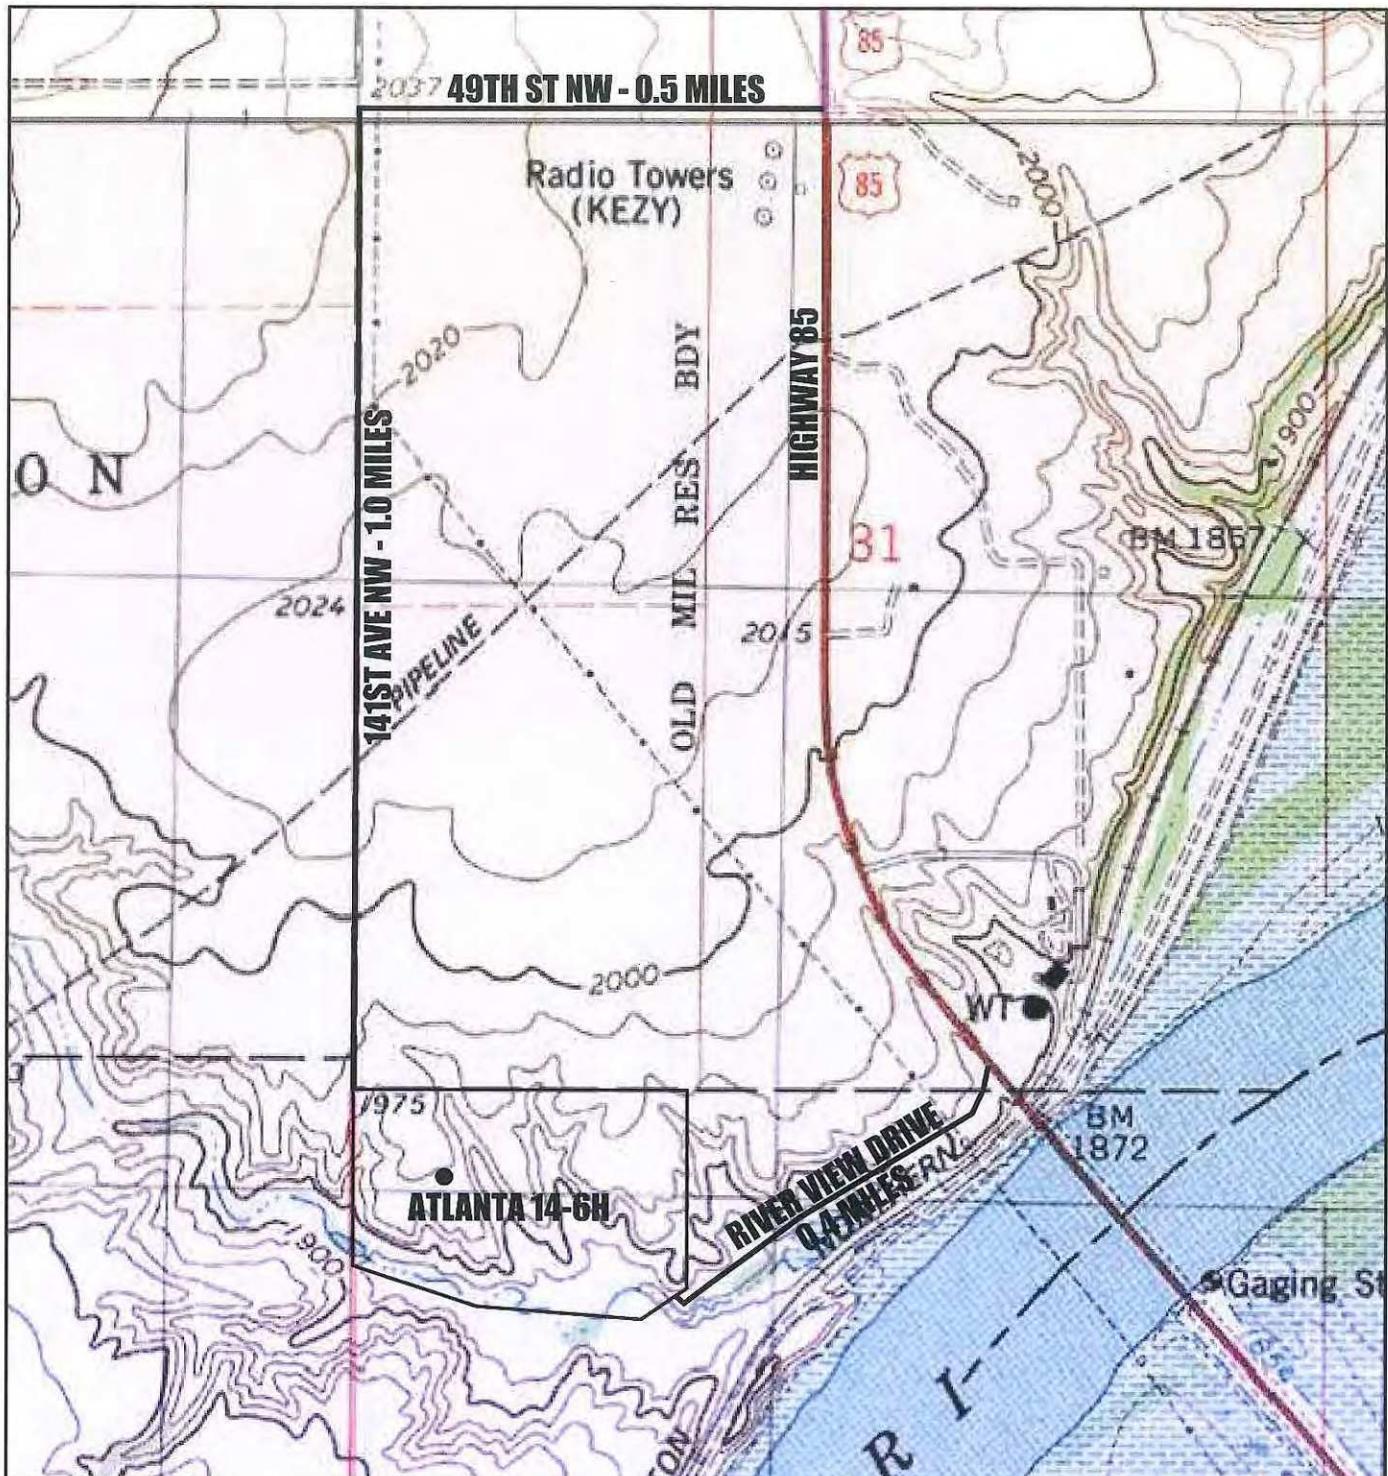

CONTINENTAL RESOURCES INC.

EXHIBIT 2
QUAD ACCESS

ATLANTA 14-6H
SECTION 6, T153N, R101W
WILLIAMS COUNTY, NORTH DAKOTA




Continental Resources, Inc. (CRI) respectfully submits the following information concerning the drilling of the Atlanta 1 through 14-H, NWNW Sec. 6, T153N, R101W, Williams County, North Dakota.

The Atlanta site is located in an area with neighboring occupied dwellings located within 500 feet of the production equipment and is therefore subject to the provisions of:

NORTH DAKOTA ADMINISTRATIVE CODE § 43-02-03-28.

1. To illustrate more clearly the proximity of the occupied dwellings, the Atlanta Site Production Facility Layout, page 7 of 19 revised 6/29/12 of the plan set has been attached with this affidavit.
2. To comply with the provisions of NORTH DAKOTA ADMINISTRATIVE CODE § 43-02-03-28, waivers from the affected homeowners have been executed and are attached with this affidavit and illustrated on the attached.
 - a. Homeowners affected: Brett and Anita Williamson in Lot 10(SWSWSW-31-154-101).
 - b. Homeowners affected: Matti & Susan Tarnanen in Lot 1, Block 5, Southview Subdivision.
3. Shown on the Atlanta Site Production Facility Layout, page 7 of 19 revised 6/29/12, but not subject to the provisions of NORTH DAKOTA ADMINISTRATIVE CODE § 43-02-03-28 are the homes of:
 - a. Justin E. Grimmer & McKayla M. Johnson in Lots 24-26, Block 3, Southview Subdivision.
 - b. Therresa Christopherson in Lot 4R, Block 1 of the Rearrangement of Lots 3-4, Block 1, Berger First Subdivision.
 - i. Waivers from these homeowners have not been executed.

CRI believes adequate planning and precautions are being taken to limit the impact to the affected homeowners through enhanced drilling and completion techniques such as electric line fed drilling and supplying water pipelined to the site instead of trucking along with visual mitigation via landscaping and privacy fencing to be installed as part of the construction of the site. Fire suppression and other safety equipment will be employed on the site to ensure the safety of these homeowners and their property.



Alan McNally, Drilling Manager
Continental Resources, Inc.

STATE OF OKLAHOMA)
)ss:
COUNTY OF GARFIELD)

On the 29th day of June 2012, before me, a Notary Public in and for said County and State, personally appeared Alan McNally, known to me to be the Drilling Manager of Continental Resources, Inc., the Corporation that executed the within instrument, and acknowledged to me that such Corporation executed the same.

Becky Barnes
Notary Public

Garfield County, Oklahoma

My Commission Expires: 7/5/2015

Commission No.: 11006023



**AFFIDAVIT WAIVING PROVISIONS OF
NORTH DAKOTA ADMINISTRATIVE CODE § 43-02-03-28**

STATE OF NORTH DAKOTA)
)ss:
COUNTY OF WILLIAMS)

Brett M. Williamson and Anita J. Williamson, being duly sworn deposes and states as follows:

1. That we are the owners of two houses located on a parcel of land in SW¼SW¼SW¼ (Lot 10) MFD in Document #720523 containing 5.0 acres more or less in TWN 154 RNG 101 SEC 31 of the Williston Township.
2. That we are aware of the proposed location for Continental Resources, Inc.'s Atlanta multi well pad, which is less than 500 feet from the location of our houses which are located on the above parcel of land.
3. That Section 43-02-03-28 of the North Dakota Administrative Code provided in pertinent part "no well shall be drilled nor production equipment installed less than five hundred feet [152.40 meters] from an occupied dwelling unless agreed to in writing by the surface owner or authorized by order of the commission."
4. I hereby agree to the location of the Continental Resources, Inc.'s Atlanta multi well pad which is less than 500 feet from our houses. Further, I waive any rights that I might otherwise have to protest or contest such location.

Dated this 22nd day of June, 2012.

Affiant:

x Brett Williamson
Brett M. Williamson


Affiant:

x Anita Williamson
Anita J. Williamson

STATE OF NORTH DAKOTA)
)ss:
COUNTY OF WILLIAMS)

The foregoing instrument was acknowledged before me this 22nd day of June, 2012, by
Brett M. Williamson and Anita J. Williamson.

Michael J. Kuhn
Notary Public
My Commission Expires: OCT 4th - 2017



**AFFIDAVIT WAIVING PROVISIONS OF
NORTH DAKOTA ADMINISTRATIVE CODE § 43-02-03-28**

STATE OF NORTH DAKOTA)
)ss:
COUNTY OF WILLIAMS)

Matti K. Tarnanen and Susan V. Tarnanen, being duly sworn deposes and states as follows:

1. That we are the owners of the house located on a parcel of land in Lot 1 Block 5 of Southview Subdivision in TWN 154 RNG 101 SEC 31 of the Williston Township.
2. That we are aware of the proposed location for Continental Resources, Inc.'s Atlanta multi well pad, which is less than 500 feet from the location of our house which is located on the above parcel of land.
3. That Section 43-02-03-28 of the North Dakota Administrative Code provided in pertinent part "no well shall be drilled nor production equipment installed less than five hundred feet [152.40 meters] from an occupied dwelling unless agreed to in writing by the surface owner or authorized by order of the commission."
4. I hereby agree to the location of the Continental Resources, Inc.'s Atlanta multi well pad which is less than 500 feet from our house. Further, I waive any rights that I might otherwise have to protest or contest such location.

Dated this 20th day of June, 2012.

Affiant:

X Matti K. Tarnanen
Matti K. Tarnanen

Affiant:

X Susan V. Tarnanen
Susan V. Tarnanen

STATE OF NORTH DAKOTA)
)ss:
COUNTY OF WILLIAMS)

The foregoing instrument was acknowledged before me this 20th day of June, 2012, by
Matti K. Tarnanen and Susan V. Tarnanen.


Notary Public
My Commission Expires: Jan 31, 2016





July 19, 2012

Industrial Commission of North Dakota
Oil & Gas Division
600 East Boulevard, Dept 405
Bismarck, North Dakota 58505

Continental Resources, Inc. (CRI) respectfully submits the following information concerning the drilling of the Atlanta 1, 2, 3, 4, 5, 6, 7, 8, 9, 10, 11, 12, 13, 14 -- 6H,

Township 153N, Range 101W of the 5th P.M.
Section 6, N/2 NW/4 Williams County, North Dakota.

Continental Resources Inc. is currently conducting or planning to conduct the following work in the following manner in accordance with NDIC requirements:

- 1) Testing of water well(s)
 - a. The water well on the Atlanta property will be kept operable and has had baseline testing conducted including, hydrocarbon, salinity etc. These results will be kept on record and the well tested from time to time or as requested.
 - b. Currently, the environmental and operations teams are researching other wells in the area to sample.
- 2) CEMENT STABILIZATION:
 - a. Per NDIC requirement, samples will be taken for stabilized areas at pad grade and will be tested for current levels of: pH / EC / CEC / SAR / Soil Permeability.
 - b. These test results will be submitted before cement stabilization work begins and submitted via the appropriate NDIC Form 4 sundry
- 3) The contractor on the project is OE Construction - 16702 West 56th Drive Golden, CO 80403
 - a. Cement soil stabilization will be conducted in accordance NDIC requirements and project specifications stated on:
Plan Page 3, of the construction plan set, section 4. B. Cement Application and Blending:
Portland cement shall be added to the top 8 inches of the final subgrade at a rate of 5 percent by weight of material or as otherwise indicated in the basis of estimate. The specified manner that allows for uniform distribution of cement over the entire area. The contractor shall supply and use a computer controlled vane feeder to place the cement on the sub-grade prior to mixing. The vane feeder will spread the cement uniformly in the quantity specified. Dumping or blowing cement directly on the ground will not be accepted. The contractor shall apply the cement in a way that minimizes dust and is satisfactory to the Owner.
- 4) RECLAMATION PLAN for the stabilized portion of the drilling pad will be to rip and till the soil adding soil amendments as applicable to reach the original pH, permeability, and other test levels identified above.
- 5) REASON FOR CEMENT STABILIZATION: Cement stabilization will be conducted on this drilling pad to produce the most serviceable and least permeable surface possible so that water that falls on site will sheet directly to the planned site drainage system where it can be disposed of in a controlled fashion.

July 19, 2012

- 6) LINING OF THE SITE: Soil stabilization will be conducted in conjunction with permanently lining with a poly liner, the area around the wellheads, the trenches containing the flow lines from the well heads to the production equipment and the area under the production equipment itself inside the steel containment berms along with the detention pond. Under these systems, a minimum of 1ft. compacted clay liner of native and / or engineered fill material will be placed in 6" lifts maximum and density tested to 95% proctor per specifications provided in the Geotechnical Engineering Analysis for the project dated June 12, 2012 from American Technical Services.
- 7) As the land owner of the property in question, CRI is fully aware and approves of this system. This will also be identified on the sundry form 4 to be provided with the testing data listed above prior to beginning stabilization work.



Chad Newby, Operations Land Coordinator
Continental Resources, Inc.

STATE OF OKLAHOMA)
)ss:
COUNTY OF GARFIELD)

On the 19th day of July 2012, before me, a Notary Public in and for said County and State, personally appeared Chad Newby, known to me to be the Operations Land Coordinator of Continental Resources, Inc., the Corporation that executed the within instrument, and acknowledged to me that such Corporation executed the same.


Notary Public

Garfield County, Oklahoma

My Commission Expires: 7/5/2015

Commission No.: 11006023



Sincerely,

CONTINENTAL RESOURCES, INC.

Becky Barnes
Regulatory Compliance Specialist

**OILFIELD SAFETY INC
A Total Safety Company**

CONTINGENCY PLAN

This Contingency Plan was written
Specifically for:

**Continental Resources Inc.
P.O. Box 1032
Enid, Oklahoma 73702**

SAFETY PROGRAM & EMERGENCY EVACUATION PLAN

**Continental Resources Inc.
Williams County, North Dakota**

**Oilfield Safety Inc.
A Total Safety Company
2523 2nd Street West
Williston, ND 58801**

TABLE OF CONTENTS	PAGE
PURPOSE OF PROGRAM	1
RESPONSIBILITIES AND DUTIES	2
DIRECTIONS TO WELLSITE	4
LOCAL AREA MAP (Figure #1)	5
THE DRILL SITE	6
DRILLING EQUIPMENT LAYOUT (Figure #2)	9
RESIDENCE WITHIN ONE (1) MILE RADIUS	10
MAP OF RESIDENCE LOCATIONS (Figure #3)	11
NAMES AND DUTIES OF PERSONS WITH PRIME RESPONSIBILITIES	12
EMERGENCY NOTIFICATION	13
PHYSICAL AND CHEMICAL PROPERTIES OF HYDROGEN SULFIDE	14
PHYSICAL EFFECTS OF HYDROGEN SULFIDE POISONING	15
H ₂ S TOXICITY TABLE	16
RESUSCITATION CHART	17
TREATMENT FOR HYDROGEN SULFIDE POISONING	18
EFFECTS OF HYDROGEN SULFIDE ON METAL	19
CASING AND DRILL PIPE GRADES FOR H ₂ S SERVICE	20
DRILL STEM TEST	21
H ₂ S EQUIPMENT ON LOCATION	22
IGNITING THE WELL	24
BLOWOUT PREVENTION EQUIPMENT	25
SPECIAL EQUIPMENT	26
MUD ADDITIVES	27
EMERGENCY DRILLS	28

THIS PLAN IS SUBJECT TO UPDATING

PURPOSE OF PROGRAM

It is Continental Resources Inc. practice, to provide for the safety of its employees and contractor's employees at the job site, and to provide for the protection of the environment in accordance with applicable laws and regulations.

The primary purpose of this contingency plan is to guide location personnel in the responses expected of them in the event that hydrogen sulfide (H₂S) is liberated during the drilling program.

Hydrogen Sulfide is extremely hazardous to normal oil field operations due to its capability (1) of destroying life at very low concentrations and (2) of causing instantaneous failure of high strength metals. Drilling and producing operations of hydrocarbons containing toxic gases can, however, be performed safely and without incident when the necessary precautions are taken and the outlined safety procedures are followed. It is imperative that sulfide resistant materials be used, that the proper safety equipment be used, that this equipment be properly maintained, and that all safety regulations be complied with.

The procedures outlined are for your safety and the safety of all others: therefore, it is mandatory that each individual give his one hundred percent cooperation.

RESPONSIBILITIES AND DUTIES

ALL PERSONNEL

1. It is the responsibility of all personnel on location to familiarize themselves with the safety procedures.
2. All personnel will attend to their personal safety first.
3. Help anyone who may be injured or overcome by toxic gases. The Drilling Foreman will assign someone to administer first aid to unconscious person (s).
4. Report to the designated "SAFE BRIEFING AREA" and follow the instructions of the Drilling Foreman.

DRILLING FOREMAN

1. It is the responsibility of the Drilling Foreman to see that these safety and emergency procedures are observed by all personnel on location.
2. The Drilling Foreman will advise Oilfield Safety Inc. whenever the procedures as specified herein are complied with or cannot be followed.
3. The Drilling Foreman will notify the Safety Advisor at least two weeks before the safety equipment specified herein is needed.
4. The Drilling Foreman will keep the number of personnel on location to a minimum during hazardous operations.
5. The Drilling Foreman is responsible for designating the "SAFE BRIEFING AREA". This "SAFE BRIEFING AREA" will change depending upon wind direction and must be redesignated as soon as a wind change occurs.
6. If an unexpected emergency occurs or the H2S alarm sounds, the Drilling Foreman will assess the situation and will advise all personnel what condition exists.
7. When it is necessary to secure the location, the access road to location will be blocked; personnel from the rig crew will be used to guard same.

TEMPORARY SERVICE PERSONNEL

All service personnel such as cementing crews, logging crews, specialists, mechanics, and welders will furnish their own safety equipment as required, to comply with OSHA and the DRILLING FOREMAN for CONTINENTAL RESOURCES INC.

VISITORS

1. VISITORS will be restricted when Hydrogen Sulfide might be unless accompanied by the DRILLING FOREMAN for CONTINENTAL RESOURCES INC.
2. VISITORS and non-essential personnel will be prohibited from remaining in or entering contaminated areas where Hydrogen Sulfide concentration in the atmosphere exceeds 10 ppm.

NOTE: WHEN HYDROGEN SULFIDE MIGHT BE ENCOUNTERED NO PERSONNEL ON LOCATION WILL BE PERMITTED TO SLEEP IN VEHICLES.

DIRECTIONS TO: Atlanta 5-6H Federal

From Williston, ND head West on E Broadway toward 2nd Ave E; turn left onto Main St; Take the first right onto N Dakota 1804 W/2nd St W; continue to follow N Dakota 1804 W for 4.8 miles; Turn left onto US-85 S for 2 miles; Turn right onto 47th Ln NW; Turn right onto 48th St NW ; Continue onto 141st Ave NW and your destination will be ahead.

THE DRILL SITE

The location as shown in Figure 2 is planned in order to obtain the maximum safety benefits consistent with the rig configuration, well depth, and prevailing winds.

1. Through the use of several maps, the area within a One mile radius of the location has been surveyed and contacts with all permanent residents have been made. Except in a dead calm and a tremendous release of high concentration gases, the probability of lethal dosages beyond one mile is extremely unlikely. Note on the rig layout plat, Figure 2, the direction of prevailing winds.
2. The location of houses, schools, roads, and anything where people may be present and who might need to be warned or evacuated in a crisis have been surveyed. This information with names and telephone numbers are keyed and listed on page 11 and Figure 3 for use if evacuation might be necessary should an emergency develop.
3. The drilling rig, see Figure 2, should be situated at such a location that prevailing winds blow across the rig toward the flare pit.
4. Two (2) SAFETY BRIEFING AREAS will be established not less than 200 feet from the wellhead and in locations so that at least one SAFE BRIEFING AREA will be up-wind of the well at all times.
5. Protective equipment will be stored in strategic locations around the wellsite and each of the SAFE BRIEFING AREAS. Such equipment will include Self Contained Breathing Apparatus (SCBA), First Aid Kits, Stretchers, and Hydrogen Sulfide Hand Operated Detectors. In the event of an emergency, personnel should assemble at the up-wind SAFE BRIEFING AREA for instructions from their supervisor.
6. Windsocks or streamers will be utilized to give wind directions at several elevations; i.e., tree top, derrick floor level, and 6 to 8 feet above ground level. PERSONNEL SHOULD DEVELOP THE PRACTICE OF ROUTINE OBSERVATION OF WIND DIRECTION.
7. Windbreakers and rig curtains can be removed from around the derrick floor and monkey board, if hazardous amounts of H₂S encountered.
8. Explosion proof ventilating fans if required will be positioned to ensure adequate circulation at the derrick floor, cellar area and any other location where hydrogen sulfide is accumulating in excess of 10 PPM.
9. A kill line of ample strength and securely staked should be laid to the well head from a safe location to permit pumping into the well in an emergency.
10. When approaching a depth where Hydrogen Sulfide may be encountered, the MUD SHOULD BE MAINTAINED IN AN OVER BALANCED CONDITION TO restrict the Hydrogen Sulfide to be treated to that contained in the formation drilled.
11. When approaching a depth where Hydrogen Sulfide may be encountered, appropriate operational danger or caution sign(s) shall be displayed along all controlled accesses to the site.

12. When available 24-hour radio or telephone communication will be provided at the rig. Emergency telephone numbers will be prominently posted: SHERIFF'S DEPARTMENT, AMBULANCE, HOSPITALS, DOCTORS, AND OPERATORS' SUPERVISORY PERSONNEL.
13. Filter-type gas masks are not suitable for protection from Hydrogen Sulfide on drilling rigs. Pressure demand, SCBA'S will be provided for use in any Hydrogen Sulfide concentration. They are not physically exhausting to use, are rugged and dependable, and require little maintenance.
14. SCBA'S will be stored on racks and protected from the weather. Rig crew equipment will be located at readily accessible location on the rig floor. For hygienic reasons, SCBA'S are to be cleaned and sterilized at regular intervals. A six outlet air supply manifold will be installed on the rig floor for continuous use by crews and supervisory personnel working in a "Mask On" situation. The multi-bottle supply cylinders are to be located approximately 200 feet from the well. A minimum of 3,600 cu. ft. compressed breathing air will be on location at all times.
15. An alarm system which can be heard during operations and which can be activated from several points if gas is detected will be installed. When the alarm is sounded, personnel must assemble at the BRIEFING AREA designated SAFE. However, your company may have steps different from these, so pay heed to the requirements on your rig.
16. There will be No Smoking on rig floor or near wellhead. Designated Smoking Areas will be provided by your Supervisor.
17. Safety meetings and training sessions will be held at frequent intervals by the Safety Advisor, the Drilling Supervisor, or the Rig Supervisor. All persons required to work on location will be thoroughly familiar with the use, care and servicing of the following: Personal protective equipment such as respirators, and gas detection equipment.
18. All electric lighting, wiring and electrical devices within 100 feet of the well will be put in vapor-proof condition to minimize the possibility of explosion.
19. Blowout preventers should meet or exceed the recommendations for hydrogen sulfide service (API RP 53). Choke manifolds will be of similar materials.
20. Inspection of installation, operation, and testing of blowout preventers, choke manifolds, etc., dressed for Hydrogen Sulfide services, will be conducted regularly.
21. Every person involved in the operation will be informed of the characteristics of Hydrogen Sulfide and its dangers, safe procedures to use when it is encountered, and recommended first aid procedures. This will be done through frequent safety talks and training sessions.

NAMES AND DUTIES OF PERSONS WITH PRIME RESPONSIBILITIES

A. Continental Resources Inc.
P.O. Box 1032
Enid, Oklahoma 73702

B. OILFIELD SAFETY INC.
2523 2nd Street West
Williston, ND 58802

Terrie Turbiville
District Manager
Office: 701-774-3014
Cell: 701-580-2912

EMERGENCY NOTIFICATION

LOCAL OFFICIALS AND MEDICAL

WILLISTON, NORTH DAKOTA

AMBULANCE	911
FIRE	911
NON-EMERGENCY	701-627-3903
POLICE	911
THREE AFFILIATED TRIBES	701-627-3244
MOUNTRAIL COUNTY SHERIF.....	701-628-2975
MOUNTRAIL COUNTY SHERIFF DISPATCH	911

WATFORD CITY, NORTH DAKOTA

AMBULANCE	911
FIRE	911
POLICE	911 OR 701-842-2400
McKenzie COUNTY SHERIFF DISPATCH	911

BUREAU OF LAND MANAGEMENT

OFFICE REPRESENTATIVE	DICKINSON, ND 701-225-9148
-----------------------------	-------------------------------

NORTH DAKOTA HIGHWAY EMERGENCY ASSISTANCE 1-800-472-2121

PHYSICAL AND CHEMICAL PROPERTIES

1. Extremely toxic (almost as toxic as Hydrogen Cyanide and 5 to 6 times toxic as Carbon Monoxide).
2. Colorless.
3. Offensive odor, often described as that of rotten eggs.
4. Heavier than air - specific gravity 1.189 (Air = 1.000 @ 60° F.). Vapors may travel considerable distance to a source of ignition and flash back.
5. Forms an explosive mixture with a concentration between 4.3 and 46 percent by volume with auto-ignition occurring at 500° F.
6. Burns with a blue flame and produces Sulfur Dioxide (SO₂), which is less toxic than Hydrogen Sulfide but very irritating to eyes and lungs and causes serious injury.
7. Soluble in both water and liquid hydrocarbons.
8. Produces irritation to eyes, throat and respiratory system.
9. Threshold Limit Valve (TLV) - Maximum of eight hours exposure.
10. Corrosive to all electrochemical series metals.
11. Boiling Point (-79° F).
12. Melting Point (-177° F).

PHYSICAL EFFECTS OF HYDROGEN SULFIDE POISONING

THE PRINCIPAL HAZARD IS DEATH BY INHALATION. When the amount of gas absorbed into the blood stream exceeds that which is readily oxidized, systemic poisoning results, with a general action on the nervous system. Labored respiration occurs shortly, and respiratory paralysis may follow immediately at concentrations of 700 ppm and above. This condition may be reached almost without warning as the originally detected odor of Hydrogen Sulfide may have disappeared due to olfactory paralysis. Death then occurs from asphyxiation unless the exposed person is removed immediately to fresh air and breathing stimulated by artificial respiration. Other levels of exposure may cause the following symptoms individually or in combinations:

- a. Headache
- b. Dizziness
- c. Excitement
- d. Nausea or gastro-intestinal disturbances
- e. Dryness and sensation of pain in nose, throat and chest
- f. Coughing
- g. Drowsiness

All personnel should be alerted to the fact that detection of Hydrogen Sulfide solely by smell is highly dangerous as the sense of smell is rapidly paralyzed by the gas.

H2S TOXICITY TABLE

1 ppm	=	.0001% (1/10,000 of 1%)	Can smell
10 ppm	=	.001% (1/1000 of 1%)	Allowable for 8 hours' exposure. OVER THE ALLOWABLE CONCENTRATION, PROTECTIVE EQUIPMENT WILL BE NECESSARY.
100 ppm	=	.01% (1/100 of 1%)	Kills smell in 3 to 15 minutes. May burn eyes and throat.
200 ppm	=	.02% (2/100 of 1%)	Kills smell rapidly. Burns eyes and throat.
500 ppm	=	.05% (5/100 of 1%)	Loses sense of reasoning and balance. Respiratory disturbances in 2 to 15 minutes. Needs prompt artificial resuscitation.
700 ppm	=	.07% (7/100 of 1%)	Will become unconscious quickly. Breathing will stop and death result if not rescued promptly. Immediate artificial resuscitation.
1,000 ppm	=	.10% (1/10 of 1%)	Unconscious at once. PERMANENT BRAIN DAMAGE MAY RESULT UNLESS RESCUED PROMPTLY.

Ppm= Parts of gas per million parts of air by volume.

1%= 10,000 ppm

RESUSCITATION CHART

DID YOU KNOW?

THERE IS NO TIME TO WASTE
WHEN BREATHING STOPS!

ARTIFICIAL RESUSCITATION MUST BE STARTED IMMEDIATELY!!!

After Breathing is stopped for:

1 Minute
2 Minutes
3 Minutes
4 Minutes
5 Minutes
6 Minutes
7 Minutes
8 Minutes
9 Minutes
10 Minutes
11 Minutes
12 Minutes

The Chances for Life are:
98 out of 100
92 out of 100
72 out of 100
50 out of 100
25 out of 100 *
11 out of 100 *
8 out of 100 *
5 out of 100 *
2 out of 100 *
1 out of 100 *
1 out of 1,000 *
1 out of 10,000 *

* Irreparable brain damage starts at about the fifth minute.

COOL-HEADED ACTION IN RESCUE IS CRITICAL.

TREATMENT FOR HYDROGEN SULFIDE POISONING

INHALATION

As Hydrogen Sulfide in the blood oxidizes rapidly, symptoms of acute poisoning pass off when inhalation of the gas ceases. It is important, therefore, to get the victim of poisoning to fresh air as quickly as possible. He should be kept at rest and chilling should be prevented. If respiration is slow, labored, or impaired, artificial respiration may be necessary. Most persons overcome by Hydrogen Sulfide may be revived if artificial respiration is applied before the heart action ceases. Victims of poisoning should be under the care of a physician as soon as possible. Irritation due to sub-acute poisoning may lead to serious complications such as pneumonia. Under those conditions, treatment by the physician necessarily would be symptomatic. The patient should be kept in fresh air, and hygienic conditions should be watched carefully.

CONTACT WITH EYES

Eye contact with liquid and/or gas containing Hydrogen Sulfide will cause painful irritation (conjunctivitis). Keep patient in a darkened room, apply ice compresses to eyes, put ice on forehead, and send for a physician. Eye irritation caused by exposure to Hydrogen Sulfide requires treatment by a physician, preferably an eye specialist. The progress to recovery in these cases is usually good.

CONTACT WITH SKIN

Skin absorption is very low. Skin discoloration is possible after contact with liquids containing Hydrogen Sulfide. If such skin contact is suspected, the area should be thoroughly washed.

EFFECTS OF HYDROGEN SULFIDE ON METAL

Hydrogen Sulfide dissolves in water to form a weak acid that can cause some pitting, particularly in the presence of oxygen and/or carbon dioxide. However, the most significant action of H₂S is its contribution to a form of hydrogen embrittlement known as sulfide stress cracking. Sulfide stress cracking is a result of metals being subjected to high stress levels in a corrosive environment where H₂S is present. The metal will often fail catastrophically in a brittle manner. Sulfide stress cracking of steel is dependent upon and determined by:

- a. Strength (hardness) of the steel - the higher the strength, the greater the susceptibility to sulfide stress cracking. Steels having yield strengths up to 95,000 psi and hardness up to Rockwell C 22 are generally resistant to sulfide stress cracking. These limitations can be extended slightly higher for properly quenched and tempered materials.
- b. Total member stress (load) - the higher the stress level (load) the greater the susceptibility to sulfide stress cracking.
- c. Corrosive environment - corrosive reactions, acids, bacterial action, thermal degradation, or low PH fluid environment.

Use as protection against sulfide stresses cracking, all casing, BOP and safety equipment should be of H₂S resistant material.

CASING GRADES ACCEPTABLE FOR H2S SERVICE

CASING GRADE	H2S SERVICE	COMMENTS **	
H-40	YES		
K-55	YES		
C-75	YES		
N-80	CONDITIONAL	ABOVE	200° F
L-80	YES		
MN-80	YES		
C-90	YES		
C-95	YES		
S-95	NO	ABOVE	200° F
SOO-95	NO	ABOVE	200° F
S-105	NO	ABOVE	200° F
SOO-90	YES	ABOVE	200° F
P-110	NO	ABOVE	200° F
S-135	NO	ABOVE	200° F
V-150	NO	ABOVE	200° F

* Service conditions for any H2S environment.

** Denotes usable grades above 200° F.

DRILL PIPE GRADES FOR H2S SERVICE

<u>GRADE</u>	<u>H2S SERVICE</u>
D	YES
E	YES
X-95	YES
G-105	NO
S-135	YES
ALUMINUM	YES

DRILL STEM TEST

1. Drill Stem testing shall be done during daylight hours whenever practical. If it is necessary to work under artificial light, levels shall be sufficient to allow employees to conduct the test safely.
2. Ammine Corrosion Inhibitor should be used to coat inside of drill pipe prior to conducting Drill Stem Test in order to prevent Sulfide Stress Cracking.
3. If warranted, the use of Ammonia Hydroxide (26 Degree B'eaume Aqua Ammonia) for neutralizing Hydrogen Sulfide from tubing or drill pipe can be used.

H2S SAFETY EQUIPMENT ON LOCATION

(PROVIDED BY SAFETY CONTRACTOR)

1. One safety trailer with a cascade system of cylinders of compressed GRADE D breathing air, complete with high pressure regulator.
2. Low pressure breathing air line (approximately 1,000 feet depending on the location). Equipped with quick connects.
3. Two low pressure manifold systems.
4. Eight pressure-demand type breathing apparatus (SCBA) 30 minute duration, NIOSH, and MSHA approved.
5. Eight airline breathing apparatus c/w 7 cu. ft. egress cylinders.
6. One four (4) channel fixed electronic monitoring system with sensors and alarms (explosion proof light and siren).
7. One hand operated portable pump type (with low and high range H2S detector tubes).
8. One first aid kit.
9. One stretcher (Ferro folding).
10. Three luminous wind socks with frames and extension poles. Windsocks must be placed so that they are visible by day and by night from all points on location.
11. One Flare Piston with 12 gauge meteor flares for igniting well.
12. One operating condition sign with flags at well entrance.
Condition I - Normal Operating Conditions (green flag);
Condition II - Potential to Moderate Danger to Life (yellow flag);
Condition III - Moderate to Extreme Danger to Life (red flag).
13. One fire blanket.
14. One warning light.
15. One warning siren.

H2S SAFETY EQUIPMENT ON LOCATION

(PROVIDED BY THE SAFETY CONTRACTOR)

16. Two traffic cones.
17. Two compressed breathing air cylinders for briefing area number 2.
18. Briefing area stand
19. Briefing area number 2 sign.

NOTE: ADDITIONAL EQUIPMENT WILL BE ADDED IF WELL CONDITIONS REQUIRE OR UPON REQUEST

NOTE: Equipment for a maximum of sixteen (16) people on location.

Equipment will be rigged up and operational when drilling reaches a depth of 500 ft. above, or three days, whichever is sooner, prior to penetrating the first zone containing or reasonably expected to contain H2S.

IGNITING THE WELL

RESPONSIBILITY

THE DECISION TO IGNITE THE WELL IS THE RESPONSIBILITY OF THE DRILLING FOREMAN. In the event he is incapacitated, it becomes the responsibility of the Rig Tool Pusher. This decision should be made only as a last resort and in a situation where it is clear that:

1. Human life and property are endangered.
2. No hope exists for controlling the blowout under prevailing conditions at the well.

Notify the Oilfield Safety Inc. office, if time permits, but do not delay if human life is in danger. Initiate first phase of evacuation plan.

INSTRUCTIONS FOR IGNITING THE WELL

1. Two people are required for the actual igniting operation. They must wear self-contained breathing units and have a safety rope attached. One man will check the atmosphere for explosive gases with the Explosimeter. The other man is responsible for igniting the well.
2. Primary method to ignite: Meteor-type Flare Gun.
3. Ignite upwind and do not approach any closer than is warranted.
4. Select the ignition site which is best for protection.
5. Select area for hasty retreat.
6. BEFORE FIRING, check regarding combustible gases.
7. Since Hydrogen Sulfide converts to Sulfur Dioxide, the area is not safe after igniting the well.
8. After igniting, continue emergency action and procedure as before.
9. All unassigned personnel will limit their actions to only those directed by the Drilling Foreman.

REMEMBER: AFTER WELL IS IGNITED, BURNING HYDROGEN SULFIDE WILL CONVERT TO SULFUR DIOXIDE, WHICH IS ALSO HIGHLY TOXIC. DO NOT ASSUME THE AREA IS SAFE AFTER THE WELL IS IGNITED.

BLOWOUT PREVENTION EQUIPMENT

1. A kill line of ample strength and length should be laid to a safe point to allow pumping into the well in an emergency situation.
2. The closing unit should be located a safe distance from the wellbore and positioned for maximum utilization based on the prevailing wind direction.
3. BOP equipment will be tested in accordance with standard company practice.
4. All equipment should be H2S trimmed for service in sour gas environments.
5. All drill pipe and casing will be of a grade acceptable for H2S service.

SPECIAL EQUIPMENT

1. If a MUD-GAS SEPARATOR is installed, it will be installed with one or more flare lines.
2. Flare lines should be as long as practical and securely staked.
3. Flare Systems must be equipped with a safe and suitable means of ignition. The ignition system must either be electrically or gas operated. Buckets of diesel fuel and torches are no longer acceptable.
4. An automatic Hydrogen Sulfide monitor will be installed with a combination visual and audible alarm system located where it can be seen and/or heard throughout the drilling location. This system will have the capabilities of being activated from several points, which are the rig floor, cellar, and shale shaker.
5. The automatic monitor should be set to trigger the drilling location visual/audible alarms when the Hydrogen Sulfide concentration in the atmosphere reaches 10 ppm. Explosion proof lights and sirens will be provided at or near the rig floor and such that all personnel will be subject to visual and audible warnings.

MUD ADDITIVES

DRILLING FLUID RECOMMENDATION

MUD TYPE


An overbalanced mud should be used to drill potential pay zone with necessary additives for all stabilization.

In the event of H₂S contamination of the mud system, Hydrogen Sulfide scavengers should be added to the mud.

EMERGENCY DRILLS

Hydrogen Sulfide Alarm Drills


The Safety Advisor will conduct frequent H2S emergency drills for each crew by manually activating the H2S detector. When the lights flash, all personnel on location will assemble at the Upwind Briefing Area. A head count will be taken at this time to determine if rescue operations are indicated. The Safety Advisor must be notified if more personnel are on location than during normal operations. A "Masks On" policy will prevail until the all clear is sounded. These drills will be implemented as frequently as required to familiarize all personnel with the procedures to be followed in the event an actual emergency occurs.

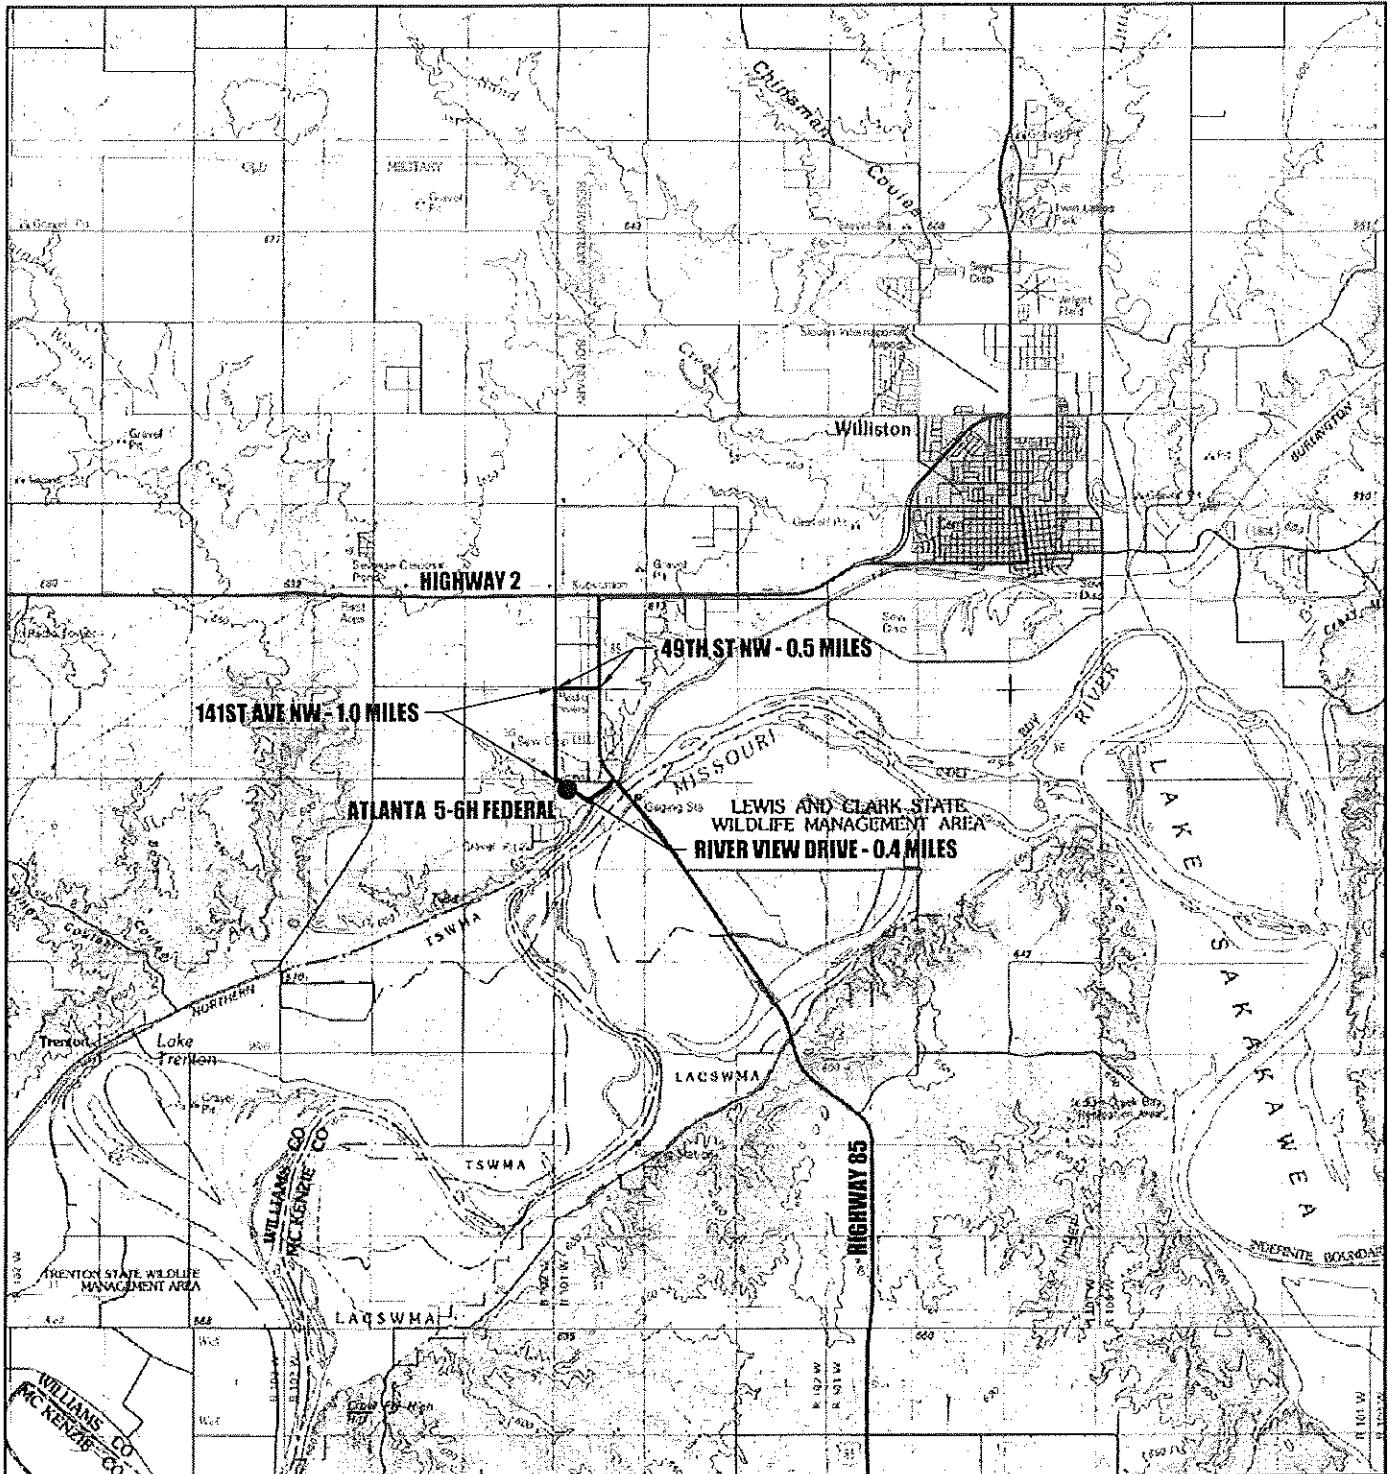

CONTINENTAL RESOURCES INC.

EXHIBIT 1
VICINITY MAP
PROPOSED ACCESS ROUTE

ATLANTA 5-6H FEDERAL
SECTION 6, T153N, R101W
WILLIAMS COUNTY, NORTH DAKOTA

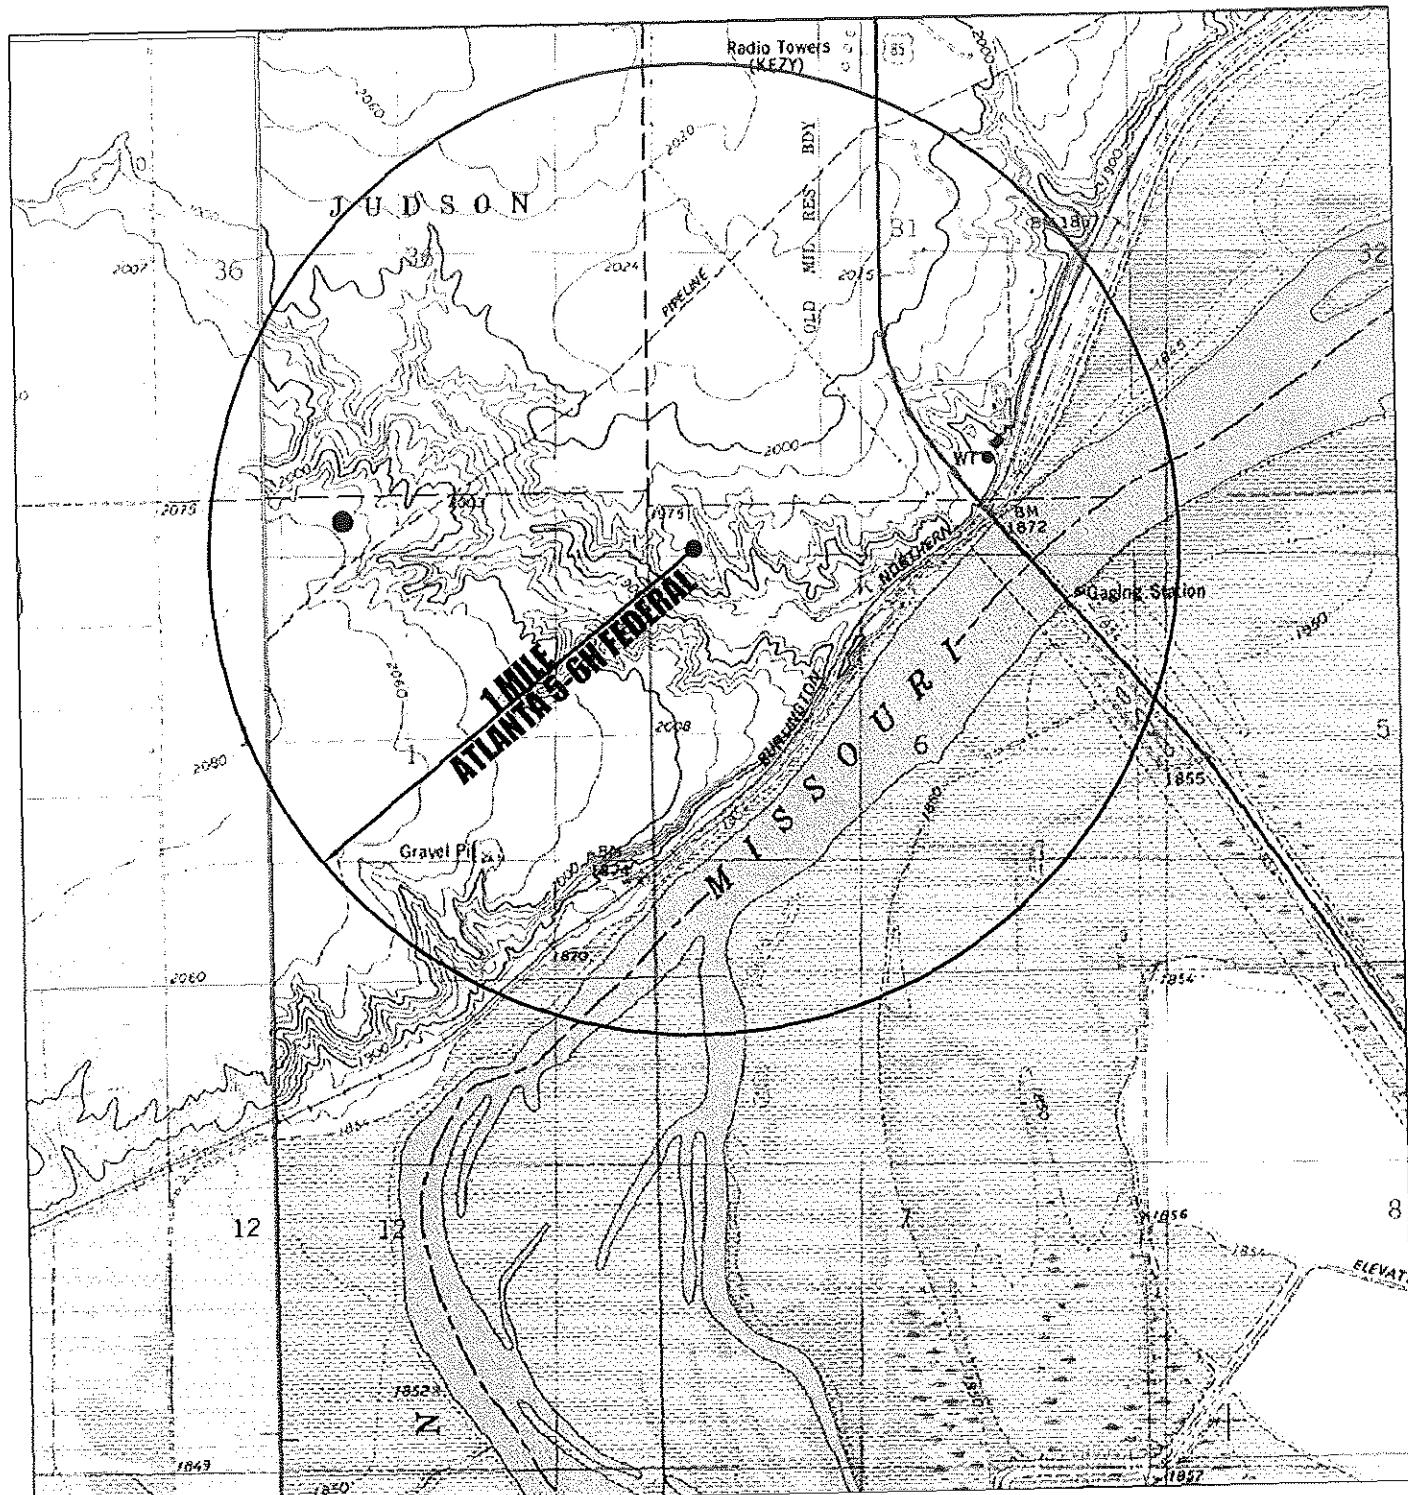

CONTINENTAL RESOURCES INC.

 = OIL WELL





EXHIBIT 3
ONE-MILE RADIUS MAP

ATLANTA 5-6H FEDERAL
SECTION 6, T153N, R101W
WILLIAMS COUNTY, NORTH DAKOTA

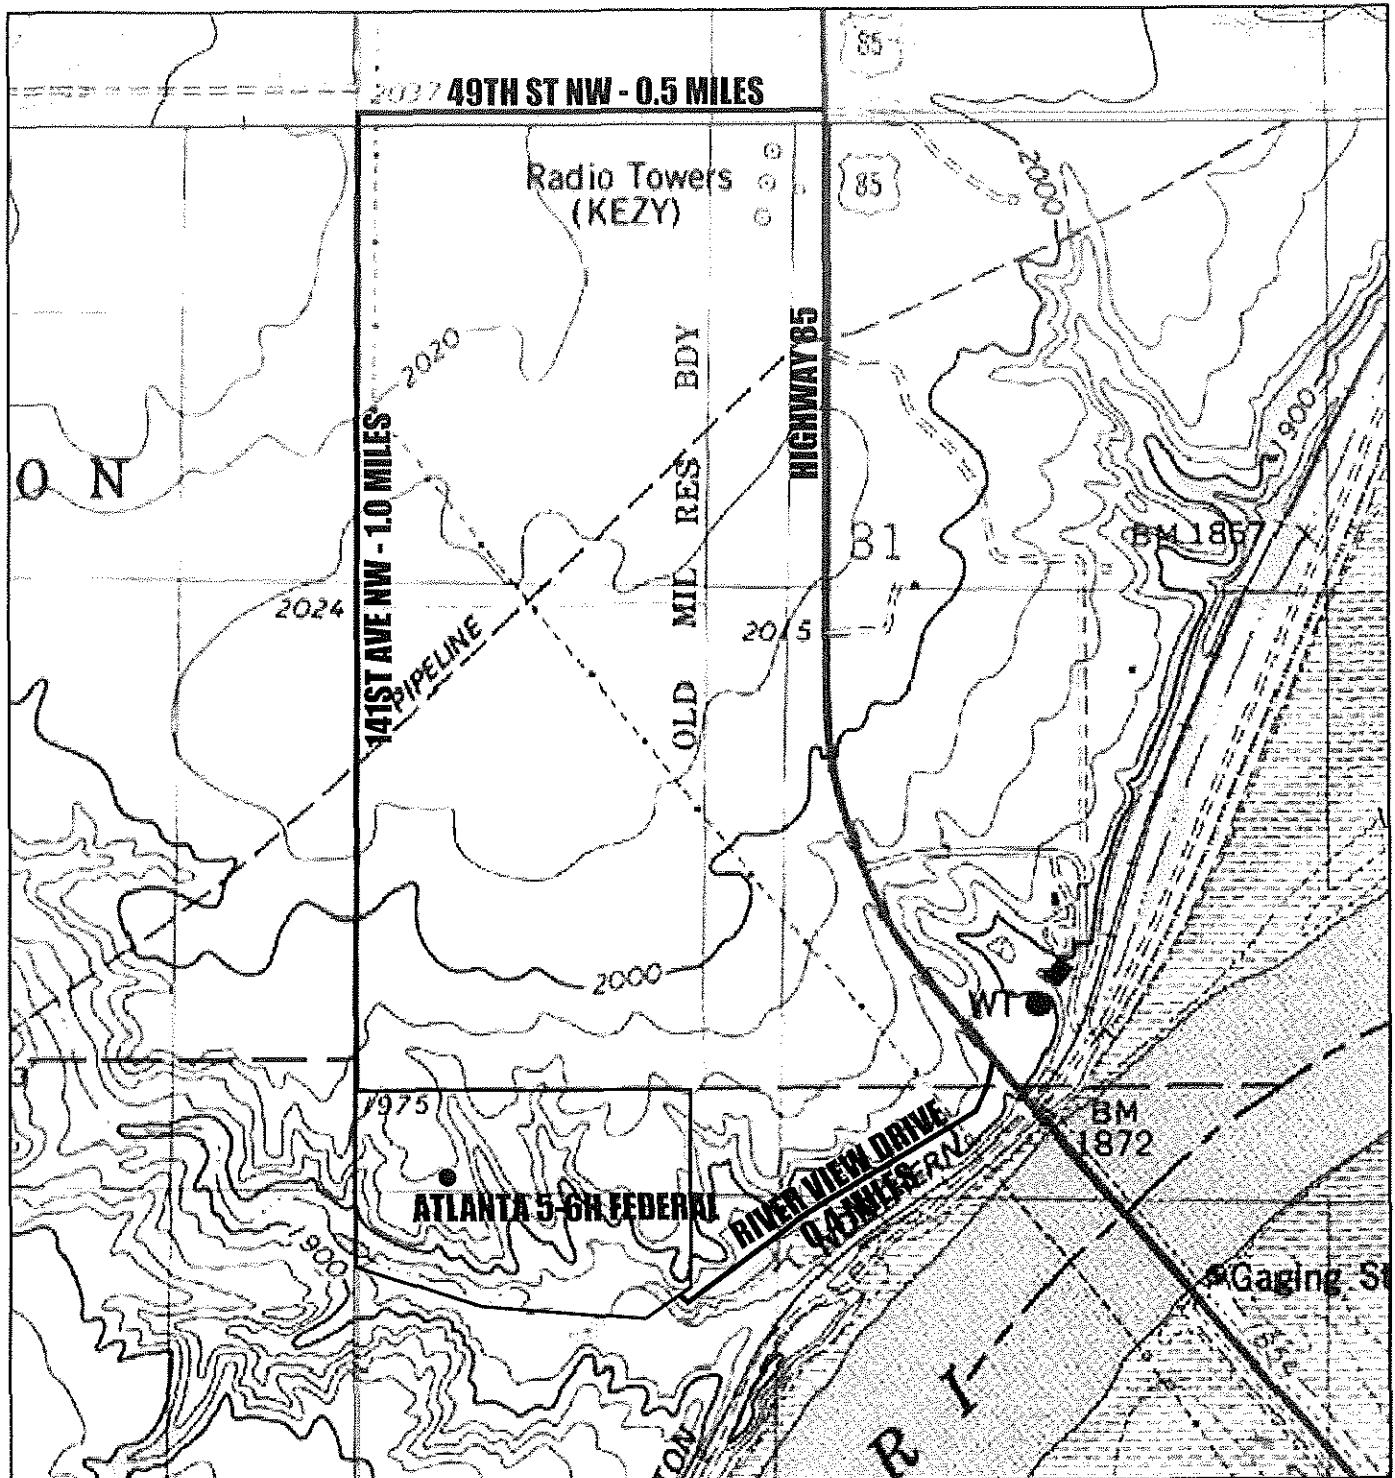


CONTINENTAL RESOURCES INC.

EXHIBIT 2
QUAD ACCESS


ATLANTA 5-6H FEDERAL
SECTION 6, T153N, R101W
WILLIAMS COUNTY, NORTH DAKOTA

REVISED: 4-23-2012

WELL LOCATION PLAT
CONTINENTAL RESOURCES INC.
ATLANTA 5-6H FEDERAL
SECTION 6, T153N, R101W
WILLIAMS COUNTY, NORTH DAKOTA
495' FNL & 835' FWL

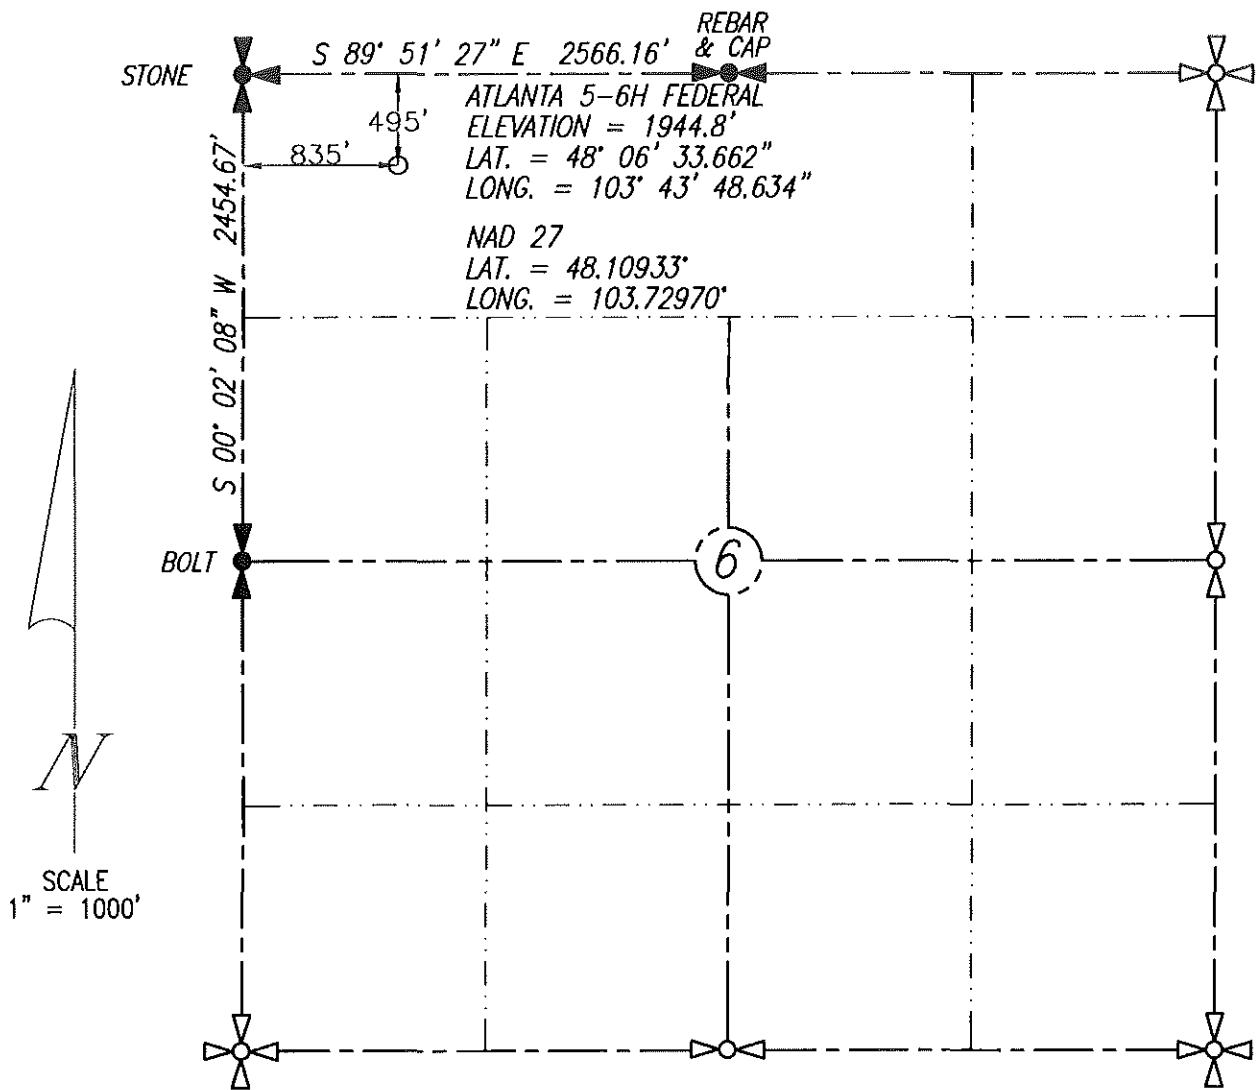

I CERTIFY THAT THIS PLAT CORRECTLY REPRESENTS
WORK PERFORMED BY ME OR UNDER MY RESPONSIBLE
CHARGE, AND IS TRUE AND CORRECT TO THE BEST OF
MY KNOWLEDGE AND BELIEF



4-23-12

DATE STAKED: 2-9-2012

BASIS OF VERTICAL DATUM:
NAVD 1988 GEOID 09

PERSON AUTHORIZING SURVEY;
CHAD NEWBY


EXPLANATION AREA: NAD83(CORS96)

BASIS OF BEARING: TRUE NORTH

BROSZ ENGINEERING INC.

BOX 357
BOWMAN, N.D. 58623
PHONE: 701-523-3340
FAX: 701-523-5243
PROJECT NO. 12-10

HORIZONTAL SECTION PLAT
CONTINENTAL RESOURCES INC.
ATLANTA 5-6H FEDERAL
SECTION 5, T153N, R101W
WILLIAMS COUNTY, NORTH DAKOTA
MCKENZIE COUNTY, NORTH DAKOTA

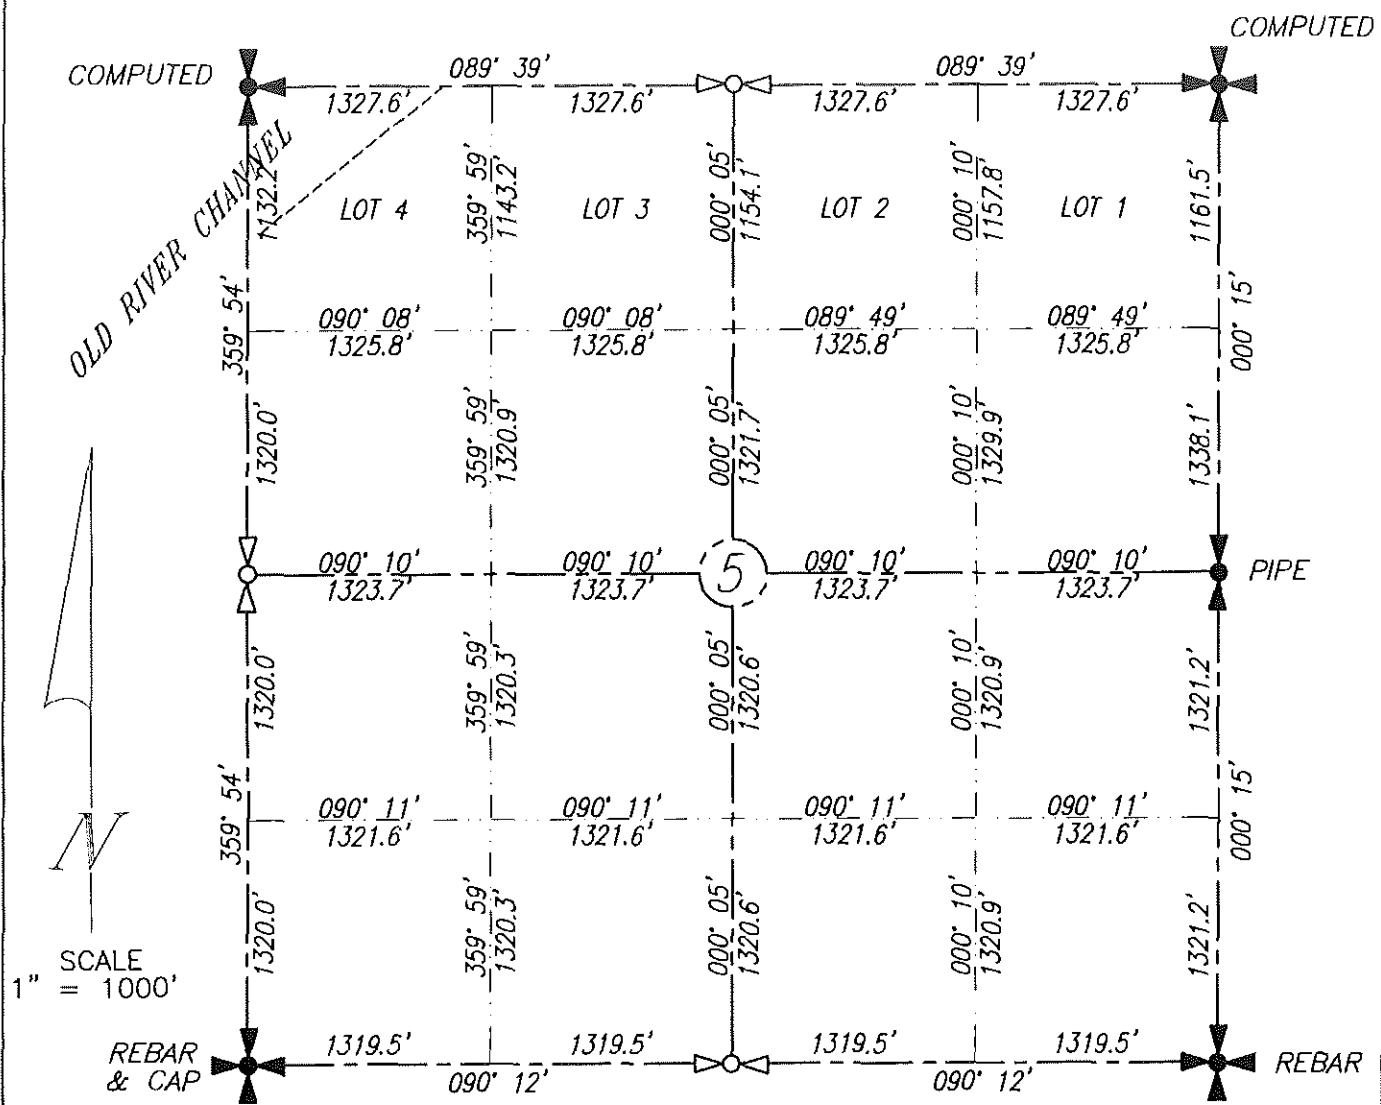

ALL CORNERS SHOWN ON THIS PLAT WERE FOUND IN THE FIELD
DISTANCES TO ALL OTHERS ARE CALCULATED.
ALL BEARINGS SHOWN ARE ASSUMED.


I CERTIFY THAT THIS PLAN CORRECTLY REPRESENTS
WORK PERFORMED BY ME OR UNDER MY RESPONSIBLE
CHARGE, AND IS STRIVED AND CORRECT TO THE BEST OF
MY KNOWLEDGE AND BELIEF
SURVEYOR

John Paulsson R.L.S. SURVEYOR
R.L.S. 3366
JOHN PAULSSON R.L.S. 3366
DATH LAKOTA

4-9-12

BROSZ ENGINEERING INC.
BOX 357
BOWMAN, N.D. 58623
PHONE: 701-523-3340
FAX: 701-523-5243
PROJECT NO. 12-10

HORIZONTAL SECTION PLAT
CONTINENTAL RESOURCES INC.
ATLANTA 5-6H FEDERAL
SECTION 6, T153N, R101W
WILLIAMS COUNTY, NORTH DAKOTA
MCKENZIE COUNTY, NORTH DAKOTA

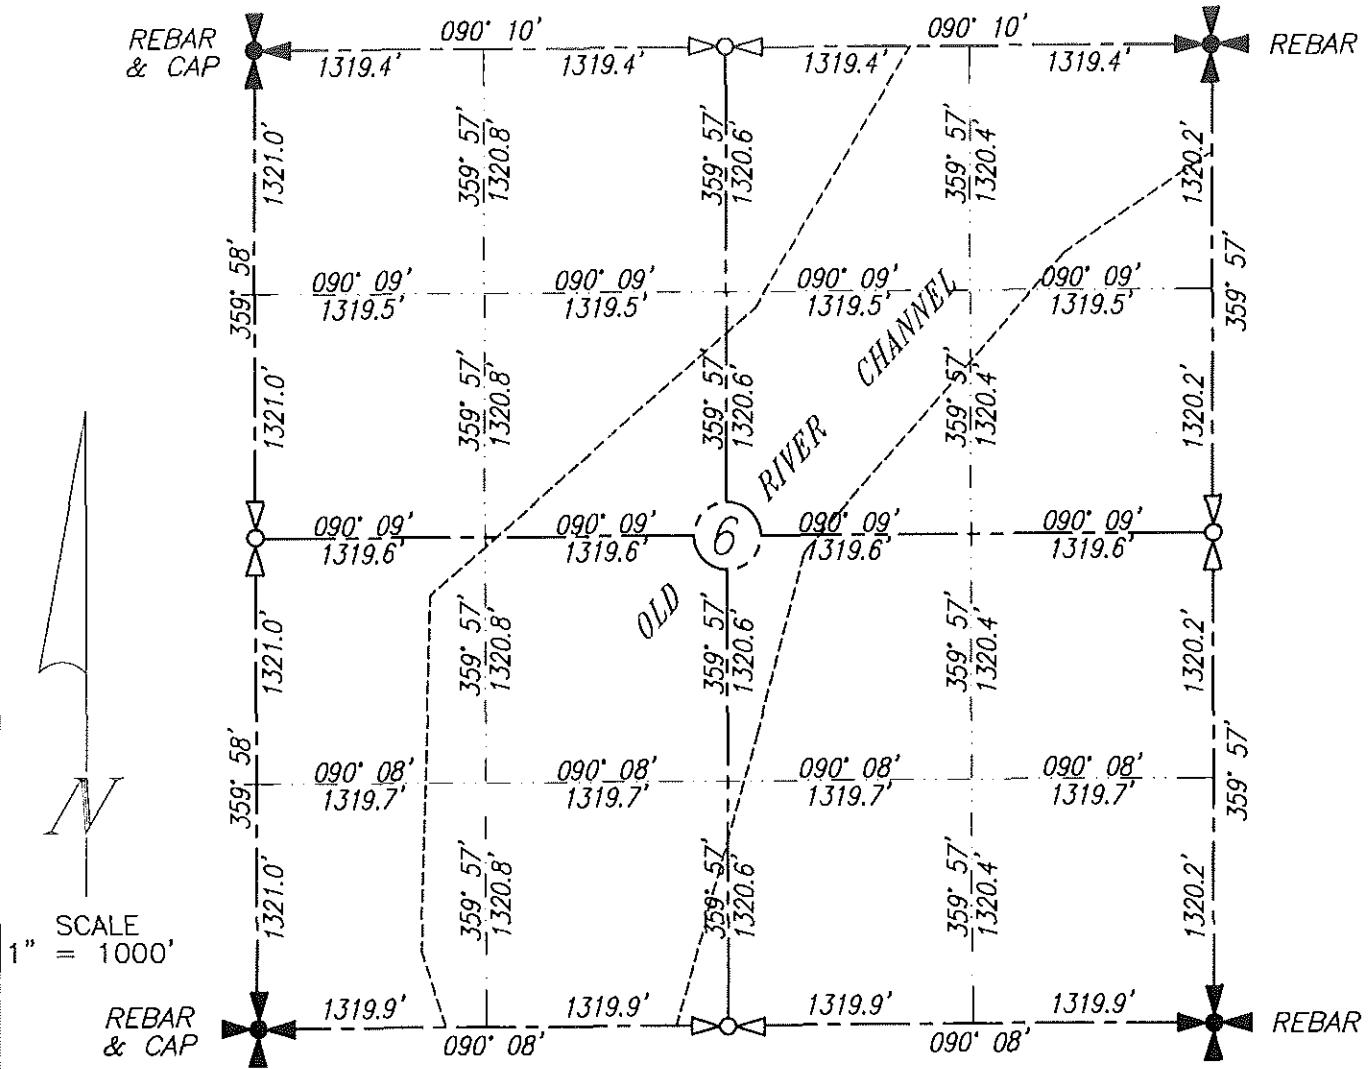

MOST OF THE SECTION IS LOTTED DUE TO THE MISSOURI RIVER.

ALL CORNERS SHOWN ON THIS PLAT WERE FOUND IN THE FIELD
DISTANCES TO ALL OTHERS ARE CALCULATED.

~~DISADVANTAGE OF THE CURRENT LINE~~
~~ALL BEARINGS SHOWN ARE ASSUMED.~~

I CERTIFY THAT THIS PLAT CORRECTLY REPRESENTS
WORK PERFORMED BY ME OR UNDER MY RESPONSIBLE
CHARGE, AND IS TRUE AND CORRECT TO THE BEST OF
MY KNOWLEDGE AND BELIEF

~~JOHN PATRICK DALE~~ 49-12
JOHN PATRICK DALE S. 3366

BROSZ ENGINEERING INC.

BOX 357


BOWMAN, N.D. 58623

PHONE: 701-523-3340

FAX: 701-523-5243

PROJECT NO. 12-10

HORIZONTAL SECTION PLAT
CONTINENTAL RESOURCES INC.
ATLANTA 5-6H FEDERAL
SECTION 7, T153N, R101W
MCKENZIE COUNTY, NORTH DAKOTA

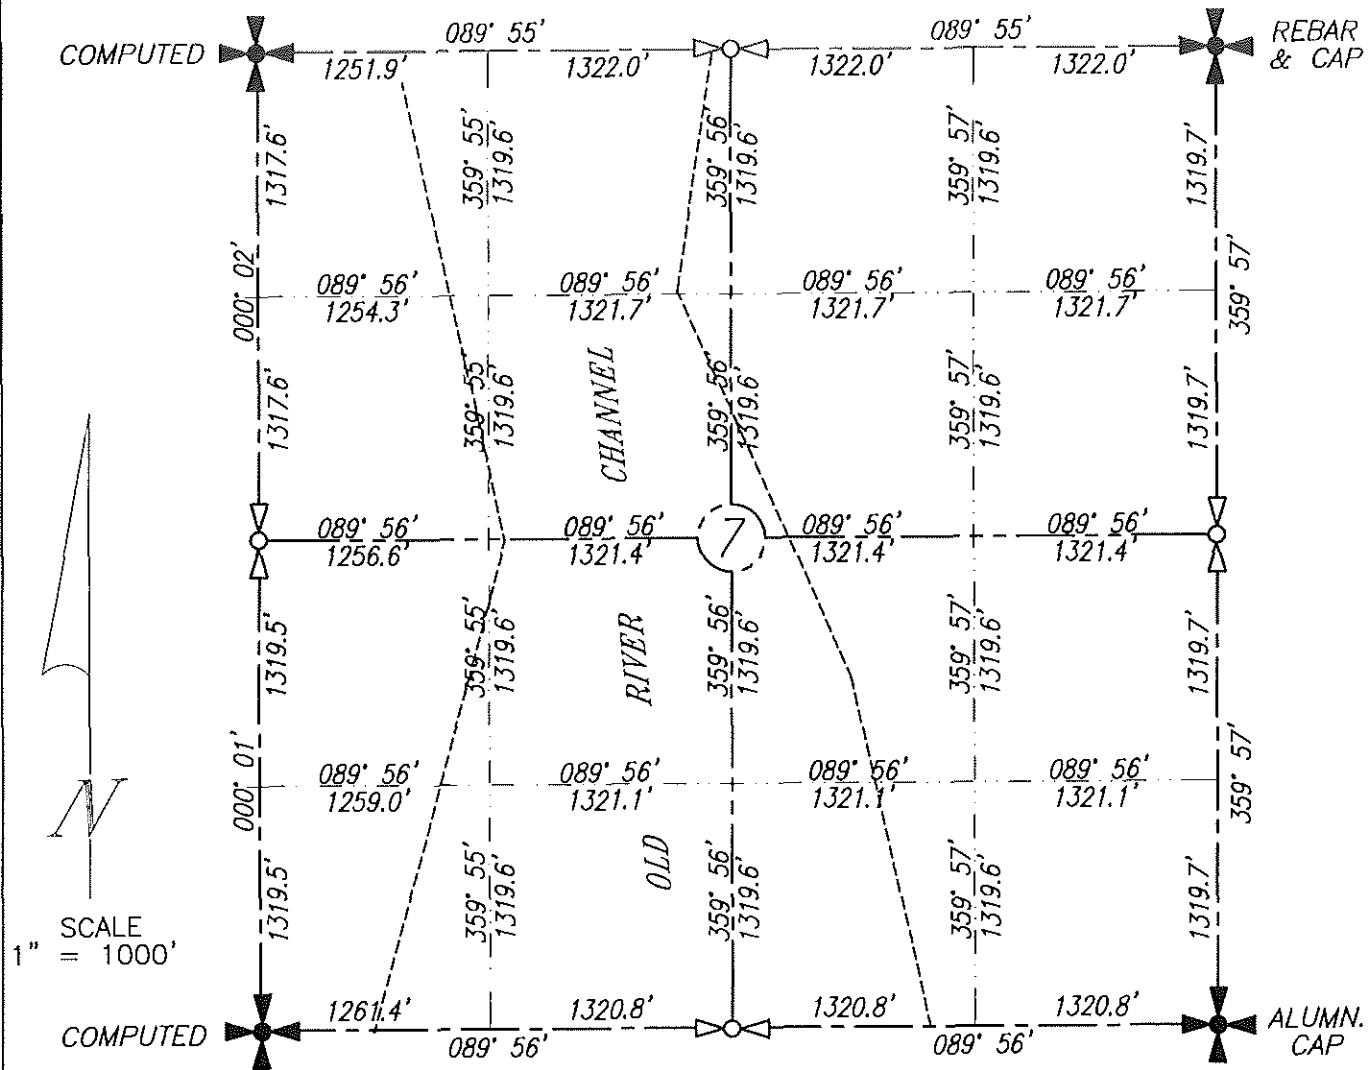

MOST OF THE SECTION IS LOTTED DUE TO THE MISSOURI RIVER.

ALL CORNERS SHOWN ON THIS PLAT WERE FOUND IN THE FIELD

JOHN PAULSON
APC

REGISTERED
I CERTIFY THAT THIS PLAT CORRECTLY REPRESENTS
WORK PERFORMED BY ME OR UNDER MY RESPONSIBLE
CHARGE, AND IS TRUE AND CORRECT TO THE BEST OF
MY KNOWLEDGE AND BELIEF

4-9-12


JOHN PAULSON R.L.S. 3366

BROSZ ENGINEERING INC.

BOX 357
BOWMAN, N.D. 58623
PHONE: 701-523-3340
FAX: 701-523-5243

PROJECT NO. 12-10

HORIZONTAL SECTION PLAT
CONTINENTAL RESOURCES INC.
ATLANTA 5-6H FEDERAL
SECTION 8, T153N, R101W
MCKENZIE COUNTY, NORTH DAKOTA

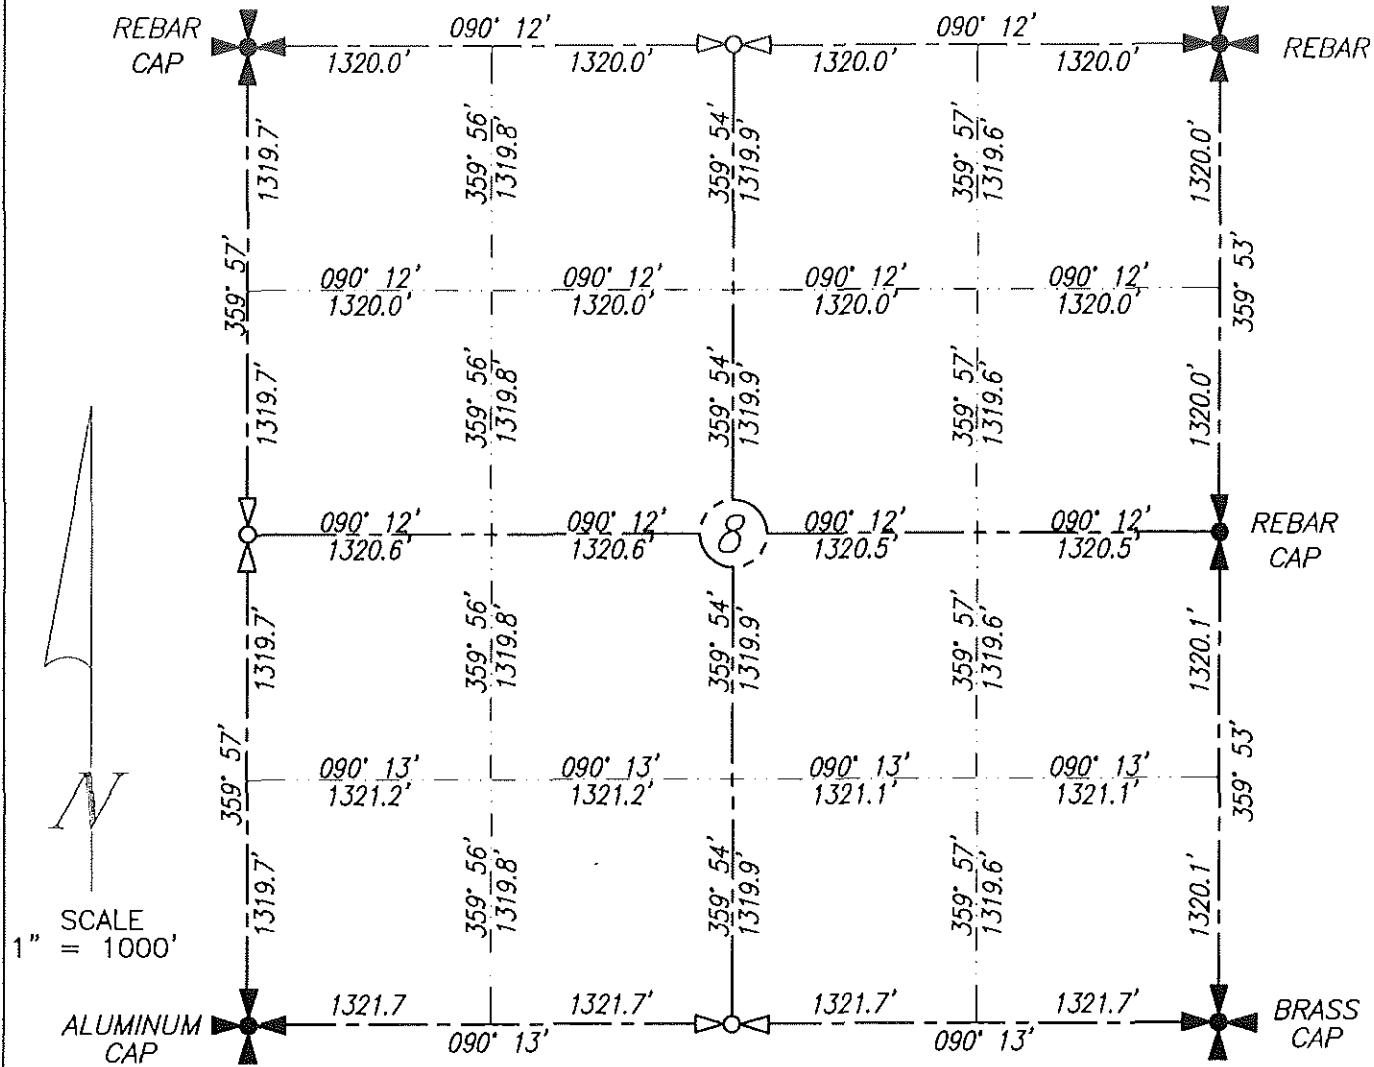


ALL CORNERS SHOWN ON THIS PLAT WERE FOUND IN THE FIELD
DISTANCES TO ALL OTHERS ARE CALCULATED.
ALL BEARINGS SHOWN ARE ASSUMED.

I CERTIFY THAT THIS PLAT CORRECTLY REPRESENTS
WORK PERFORMED THEREON OR UNDER MY RESPONSIBLE
CHARGE, AND IS FAIR AND CORRECT TO THE BEST OF
MY KNOWLEDGE AND JUDGMENT
L.S. 3365

L.S. 3366

BROSZ ENGINEERING INC.
BOX 357
BOWMAN, N.D. 58623
PHONE: 701-523-3340
FAX: 701-523-5243
PROJECT NO. 12-10

BOTTOM HOLE LOCATION PLAT
 CONTINENTAL RESOURCES INC.
 ATLANTA 5-6H FEDERAL
 SECTION 6, T153N, R101W
 WILLIAMS COUNTY, NORTH DAKOTA
 495' FNL & 835' FWL

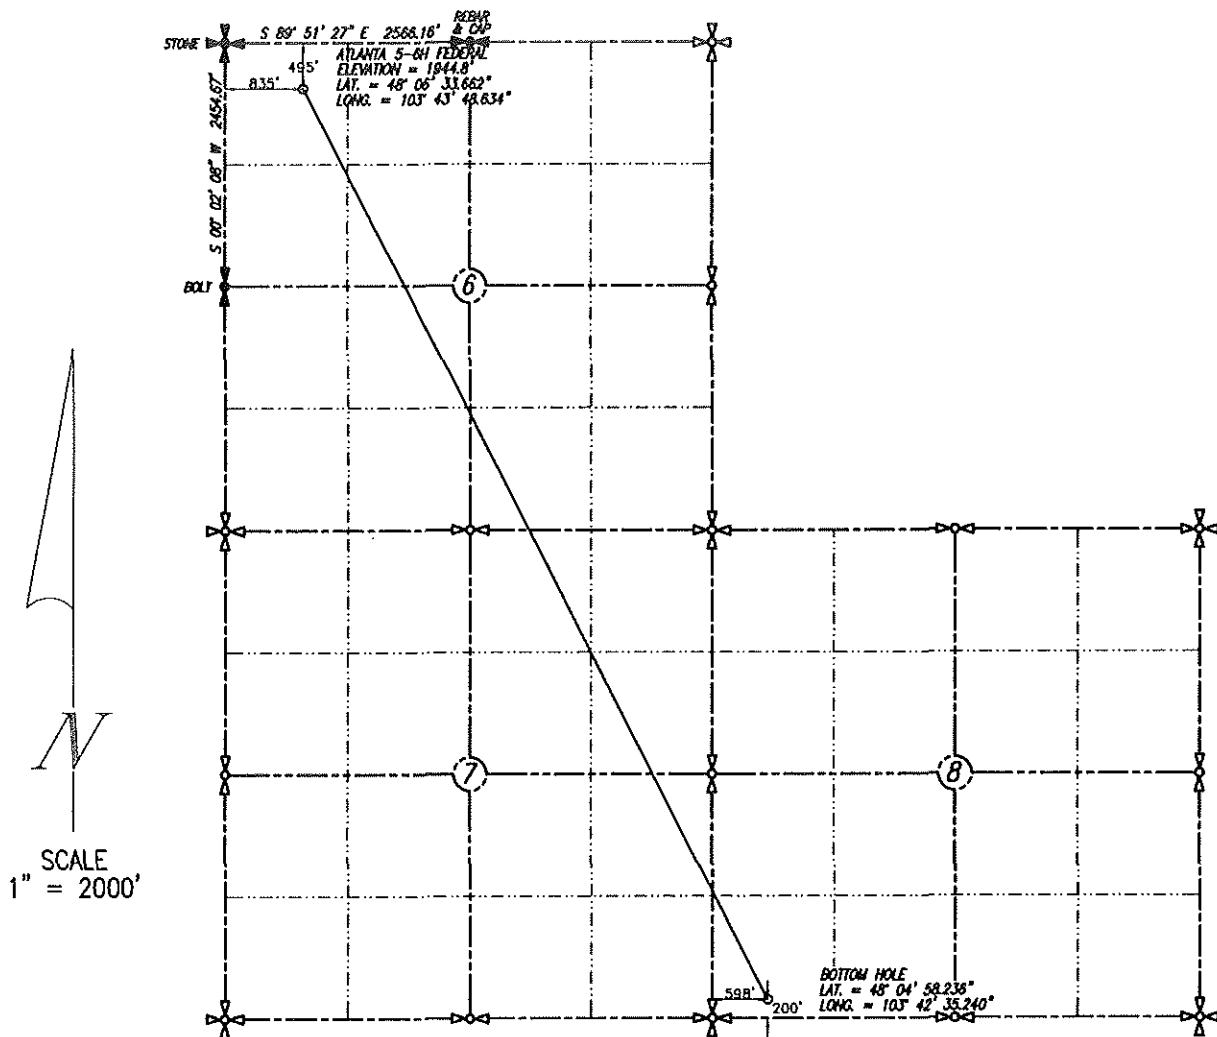

I CERTIFY THAT THIS PLAT CORRECTLY REPRESENTS
 WORK PERFORMED BY ME OR UNDER MY RESPONSIBLE
 CHARGE, AND IS TRUE AND CORRECT TO THE BEST OF
 MY KNOWLEDGE AND BELIEF

John Pagsund -23-12
 JOHN PAGSUND L.S. 3366
 LAND SURVEYOR
 L.S. 3366

NORTH DAKOTA

DATE STAKED: 2-9-2012

BASIS OF VERTICAL DATUM:
 NAVD 1988 GEODETIC


PERSON AUTHORIZING SURVEY;
CHAD NEWBY

EXPLANATION AREA: NAD83(CORS96)

BASIS OF BEARING: TRUE NORTH

BROSZ ENGINEERING INC.

BOX 357
 BOWMAN, N.D. 58623
 PHONE: 701-523-3340
 FAX: 701-523-5243
 PROJECT NO. 12-10

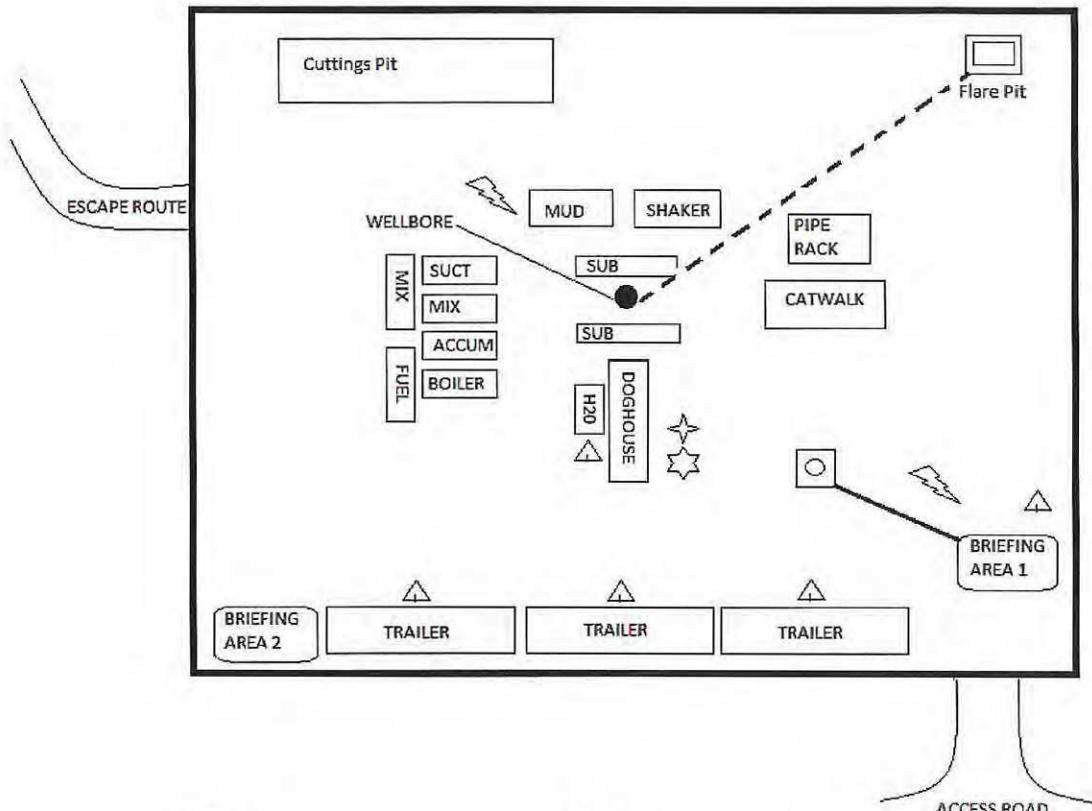

LEGEND

- ⚡ WINDSOCK
- ★ ALARM FLASHING LIGHT
- ☆ ALARM SIREN
- ▲ 30 MIN AIRPACK
- AIRLINE BREATHING APPARATUS W/MANIFOLD
- WELLBORE
- 1/2" LOW PRESSURE HOSE CONNECTED TO BREATHING AIR TRAILER
- SAFETY TRAILER W/ CASCADE AIRSYSTEM

NOTE: Continuous H₂S monitoring heads located:

- A. Return airline while air drilling
- B. Shaker while mud drilling
- C. Floor
- D. Substructure, Bell Nipple

READOUT INSTRUMENT IN DOGHOUSE

Continental Resources, Inc	
Name: Atlanta Federal 5-6H	Site Plan of Safety Equipment
Location: Sec 6-T153N-R101W	
State: ND County: Williams	



July 20, 2012

Industrial Commission of North Dakota
Oil & Gas Division
600 East Boulevard, Dept 405
Bismarck, North Dakota 58505

Continental Resources, Inc. (CRI) respectfully submits the following information concerning the drilling of the Atlanta 1, 2, 3, 4, 5, 6, 7, 8, 9, 10, 11, 12, 13, 14 -- 6H,
Township 153N, Range 101W of the 5th P.M.
Section 6, N/2 NW/4 Williams County, North Dakota.

Continental Resources Inc. would like to propose the following automatic shut down equipment and level sensing monitoring equipment be installed on the site to aid in the prevention of any accidental release or safety issue. One-line schematic diagrams, flowchart model, and general product information are attached for your review and approval with this affidavit.

- 1) Tank Side – i) K-Tek Guided Wave Radar and Z-Bend High Level Switch Level Detectors ii) High level switches for oil and water tanks ii) Battery box with solar backup
- 2) Treater / Separator – i) Buffer Switch ii) U003 Gap Switch iii) 2 - AST 4600 pressure transducers – monitor pressure & liquid content of flare / gas sales lines iv) Battery box with solar backup
- 3) Wellhead – i) TotalFlow Controller ii) Emergency ShutDown Valve package iii) Battery box with solar backup
- 4) System Automation through the proposed equipment will provide an independent control system on all equipment on site which will be able to shut the well(s) in should any of the other equipment be incapacitated or functioning improperly.
- 5) Once the system is operational and linked to the CRI Williston Basin SCADA system, a notification will be sent directly to the (Sidney, MT) field office, and field personnel in charge of the site's operation. This system will also provide the capability for remote shutdown from a computer terminal on the system at another location. In the event that an alert was sent from the site, or a call received, CRI estimates that personnel would be able to respond to an incident through the remote system within minutes and be present at the site within 15 to 30 minutes.


Chad Newby, Operations Land Coordinator
Continental Resources, Inc.

STATE OF OKLAHOMA)
)
COUNTY OF GARFIELD)
)

On the 20th day of July 2012, before me, a Notary Public in and for said County and State, personally appeared Chad Newby, known to me to be the Operations Land Coordinator of Continental Resources, Inc., the Corporation that executed the within instrument, and acknowledged to me that such Corporation executed the same.


Notary Public

Garfield County, Oklahoma

My Commission Expires: 7/5/2015



Commission No.: 11006023




Continental Resources Wellhead Automation



Analog
Radio
RS485 Modbus
Digital I/O

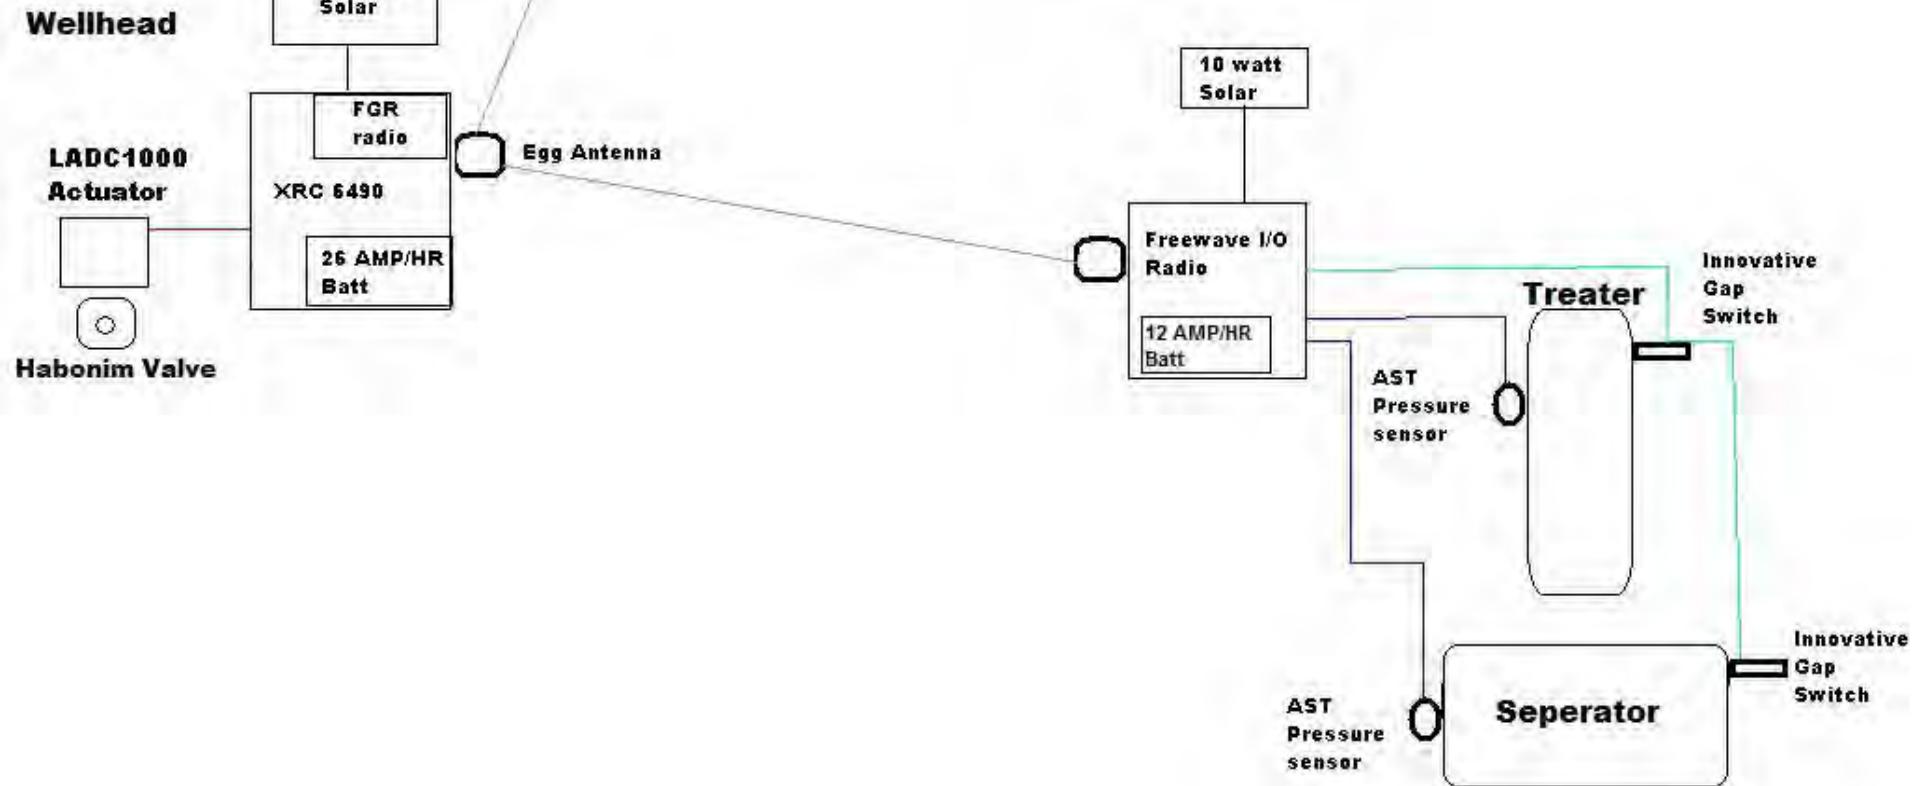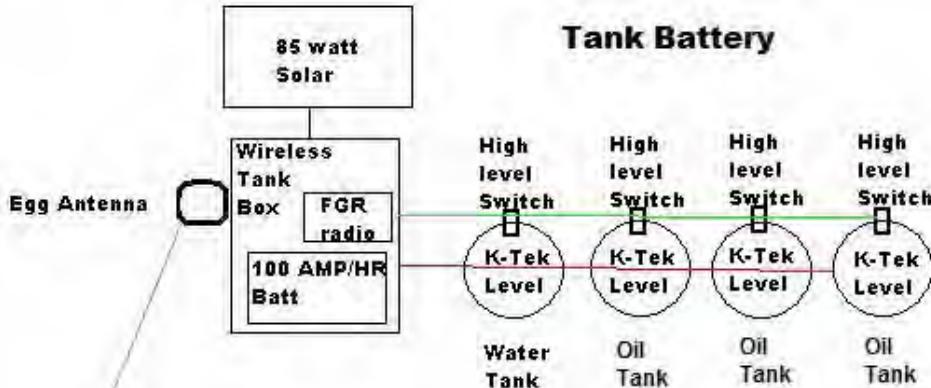

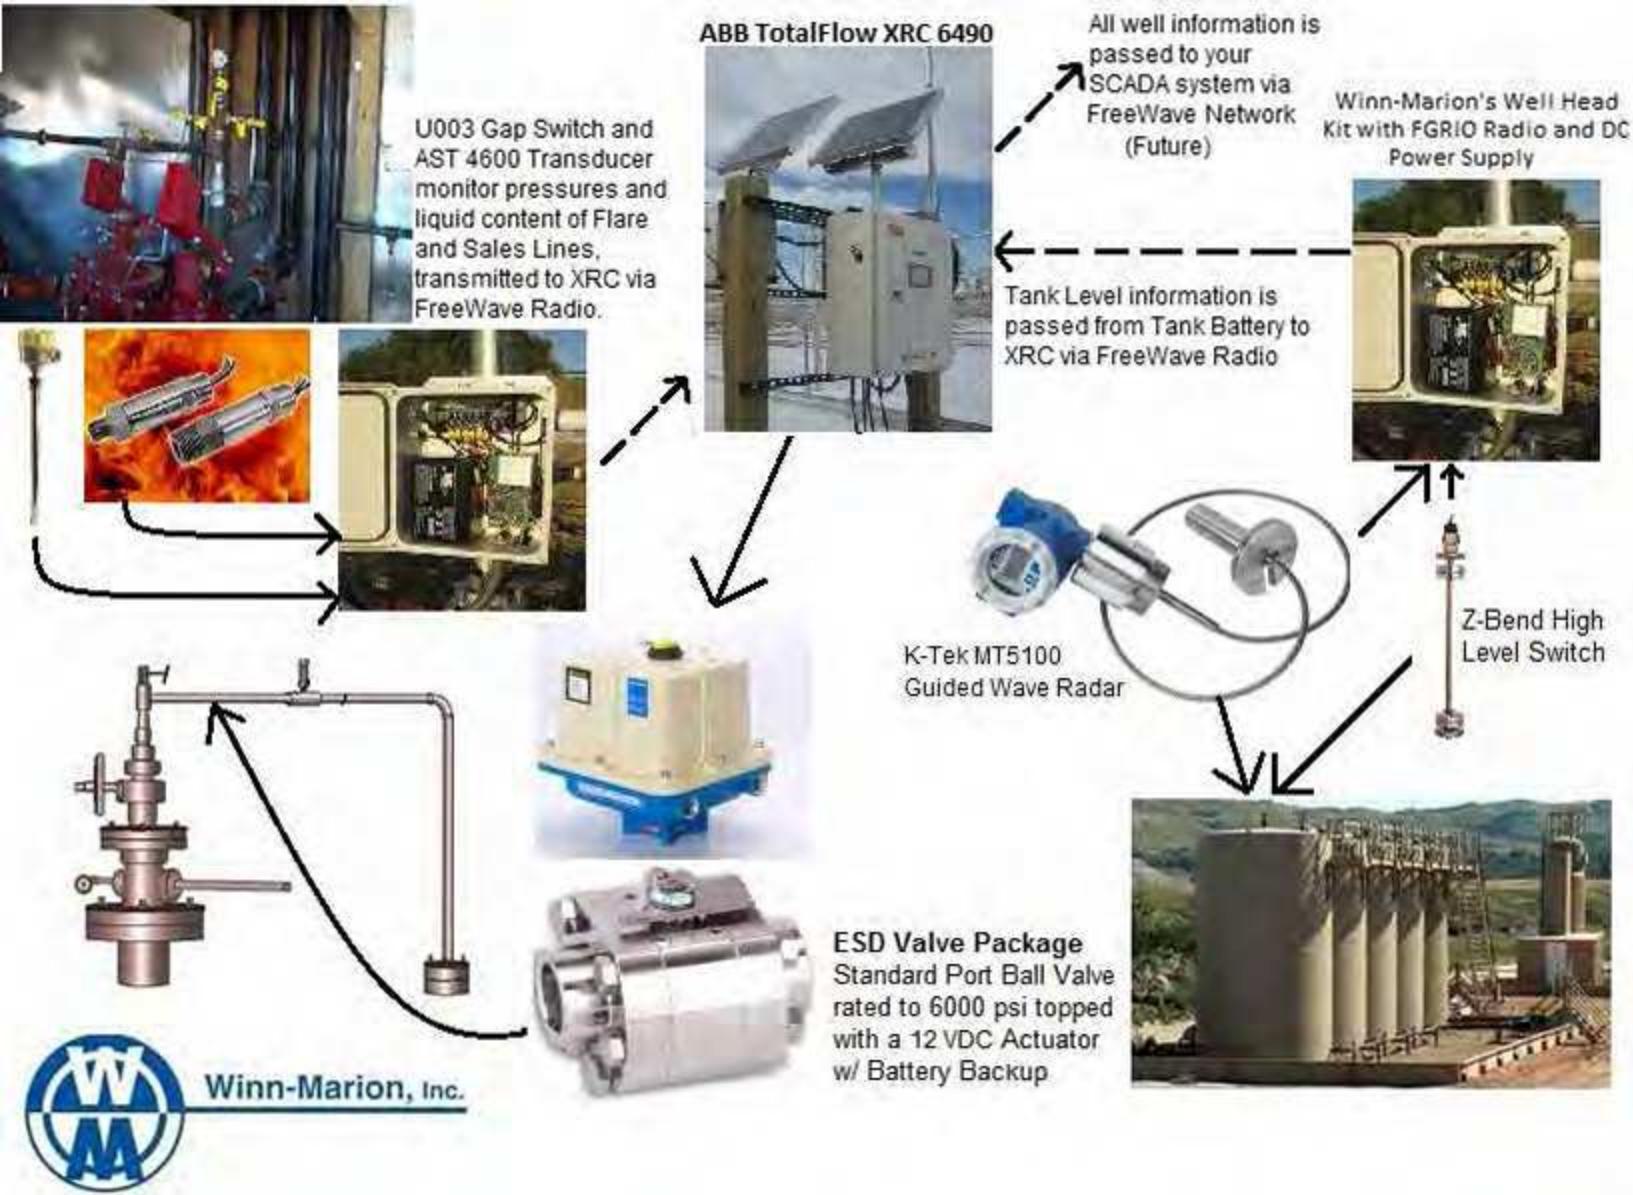

Tank Side


Contains the following Equipment

- 4 K-Tek Guided Wave Radar Level Detectors
- 3 High Level Switches (Oil Tanks)
- 1 Side Level Switch (Water Tank)
- Battery box with 100 AH Battery and 90 W Solar





WM Automation
Service, LLC

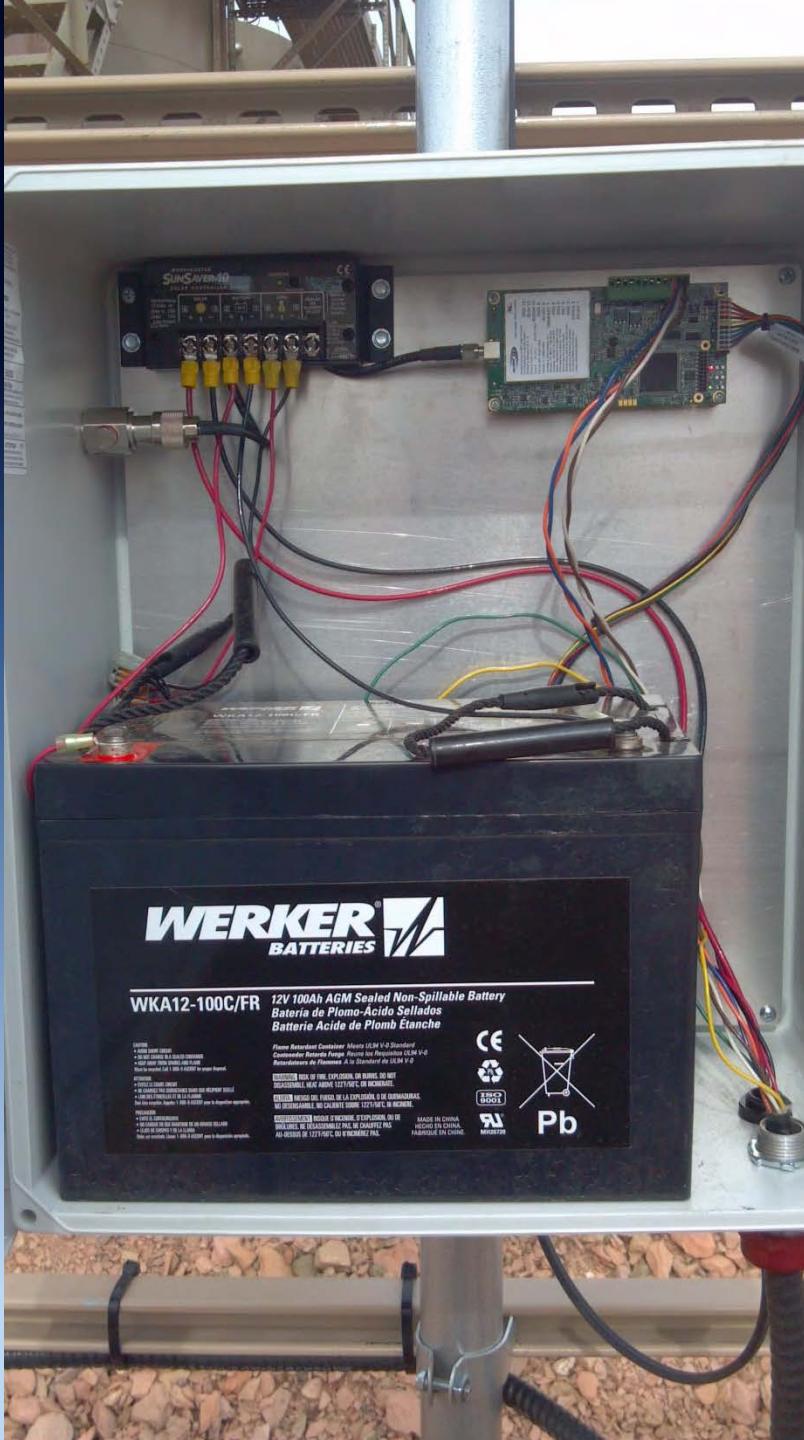

WM Automation
Service, LLC



WM Automation
Service, LLC



WM Automation
Service, LLC



WM Automation
Service, LLC

Treater Shack

Contains the following Equipment

- 1 Buffer Switch (Short Gap Switch)
- 1 Gap Switch
- 2 Pressure Transducers
- Battery box with 35 AH Battery and 10 W Solar





WM Automation
Service, LLC



WM Automation
Service, LLC



WM Automation
Service, LLC





WM Automation
Service, LLC



WM Automation
Service, LLC

Wellhead

Contains the following Equipment

- TotalFlow
- ESD Valve
- Battery box with 100 AH Battery and 50 W Solar






WM Automation
Service, LLC



WM Automation
Service, LLC

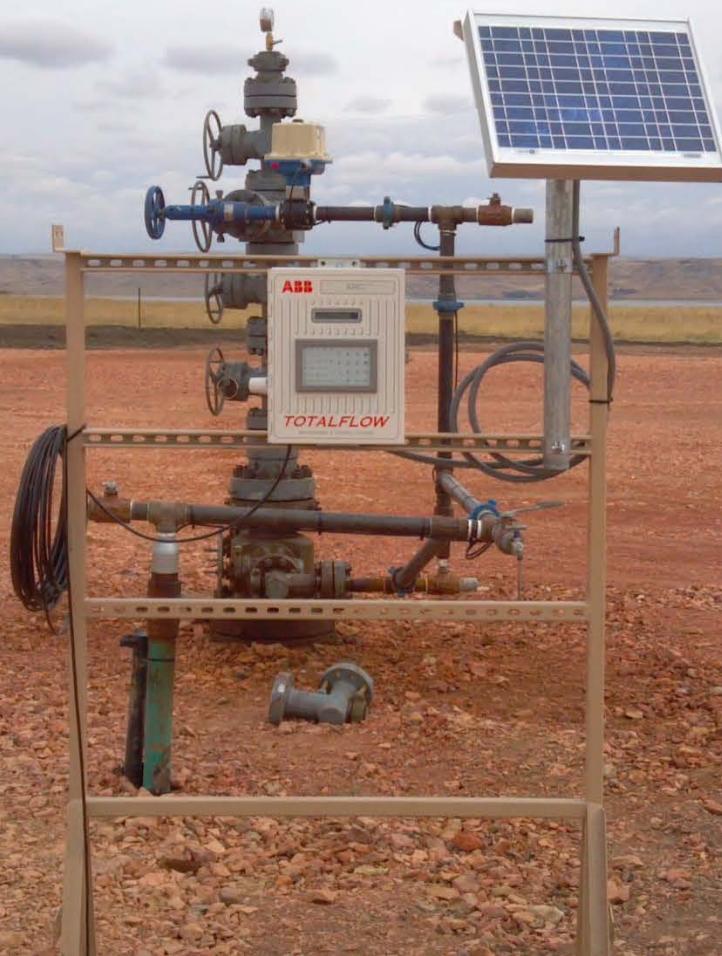

WM Automation
Service, LLC

**Cyclone Drilling Rig No. 20
Contingency Plan
For Drilling Activities Conducted at
Continental Resources, Inc.'s
Atlanta 1-6H
Located in Williams County, ND**



November 2011

**CYCLONE DRILLING, INC. RIG NO. 20
CONTINGENCY PLAN
FOR DRILLING ACTIVITIES CONDUCTED AT THE
CONTINENTAL RESOURCES, INC. ATLANTA 1-6H
6-153N-101W, WILLIAMS COUNTY, NORTH DAKOTA**

TABLE OF CONTENTS

1.	INTRODUCTION	1.
2.	GENERAL INFORMATION	1.
2.1	Equipment Description.....	1.
2.2	Proximity of Rigs to Navigable Waters.....	1.
2.3	Potential Spills and Releases	1.
3.	OIL/FUEL STORAGE	2.
3.1	Oil, Fuel and Used Oil Storage Tanks.....	2.
3.2	Container Storage.....	2.
3.3	Transfer Facilities.....	2.
3.4	Drainage and Containment Facilities	3.
3.5	Bulk Storage Tanks.....	3.
3.6	Truck Loading/Unloading Areas.....	3.
4.	FLOOD CONTINGENCY.....	3.
4.1	Flood Watch	3.
4.2	Flash Flood Watch.....	4.
4.3	Flood Warning	4.
4.4	Flash Flood Warning	4.
4.5	Flood Evacuation Plan.....	4.
5.	PREPAREDNESS AND PREVENTION REQUIREMENTS	4.
5.1	Emergency Equipment.....	4.
5.2	Internal Communication	4.
5.3	External Communication.....	4.
5.4	Inspections	5.
5.5	Training	5.
5.6	Emergency Evacuation Plan.....	5.
6.	EMERGENCY RESPONSE	5.
6.1	Response to a Minor Discharge.....	5.
6.2	Response to a Major Discharge	6.
7.	SPILL NOTIFICATION REPORTING	6.
7.1	Spill Notification and Reporting.....	6.
7.1.1	North Dakota Industrial Commission	6.
7.1.2	National Response Center	7.
8.	PLAN ADMENDMENT	7.
9.	MANAGEMENT APPROVAL	7.

LIST OF FIGURES

FIGURE 1	ONE-MILE RADIUS MAP
FIGURE 2	DRILLING RIG LAYOUT
FIGURE 3	WELL LOCATION MAP

CYCLONE DRILLING, INC. RIG NO. 20
CONTINGENCY PLAN
FOR DRILLING ACTIVITIES CONDUCTED AT THE
CONTINENTAL RESOURCES, INC. ATLANTA 1-6H
6-153N-101W, WILLIAMS COUNTY, NORTH DAKOTA

1. INTRODUCTION

The purpose of this Contingency Plan is to outline the procedures that will be implemented by Cyclone Drilling, Inc.'s Rig No. 20 personnel should a spill or flood occur during drilling activities conducted at the Continental Resources, Inc. Atlanta 1-6H lease located in Section 6, 153N, 101W in Williams County, North Dakota. Such procedures are designed to minimize the effects of spills and potential flooding on Cyclone field personnel, Continental facilities, the surrounding community, and the environment in general.

2. GENERAL INFORMATION

2.1 Equipment Description. Cyclone Drilling, Inc. operates drilling rigs that are moved from site to site therefore, the exact equipment layout will vary slightly. The Atlanta 1-6H location encompasses 3.1-acres and the standard equipment for most drilling jobs is as follows:

- r Mobile Rig (w/integrated fuel/oil storage tanks)
- r Storage Facilities
- r Mud Pumps (diesel-powered pumps w/integrated fuel storage tanks)
- r Generators (w/integrated fuel storage tanks)
- r Water Tanks
- r Pipe Racks


2.2 Proximity of Rigs to Navigable Waters. According to 40 CFR 112.7(e)(6)(i), mobile drilling equipment should be positioned or located so as to prevent spilled oil from reaching navigable waters. Depending on the location, catch basins or diversion structures may be necessary to intercept and contain fuel, crude oil, or oily drilling fluid spills.

The nearest potential receiving water for an oil spill is unnamed intermittent tributary of the Missouri River located approximately 500-ft. south of the Atlanta 1-6 lease. A One-Mile Radius Map indicating the location of Continental's Atlanta 1-6H lease is included herein as *Figure 1*.

Cyclone personnel will locate Rig No. 20 and its associated equipment to best prevent a potential release to waterways and provide drainage and containment, as discussed in *Section 3.4* of this Plan. A Drilling Rig Layout Map is included herein as *Figure 2*.


2.3 Potential Spills and Releases. The spill prevention system includes visual inspections and containment structures to help reduce the potential for releases to the off-site soil or surface waters. Generally, minor spills or leaks within the work site will be contained by drip pans located on skid-mounted equipment and cleaned-up using an absorbent (i.e., granular or pads). A list of activities that represent the greatest potential for a release of oil to the environment is as follows:

- r Loading/unloading fuel, oil, and used oil to/from storage tanks and containers.
- r Temporary storage of oil containers outside of secondary containment.

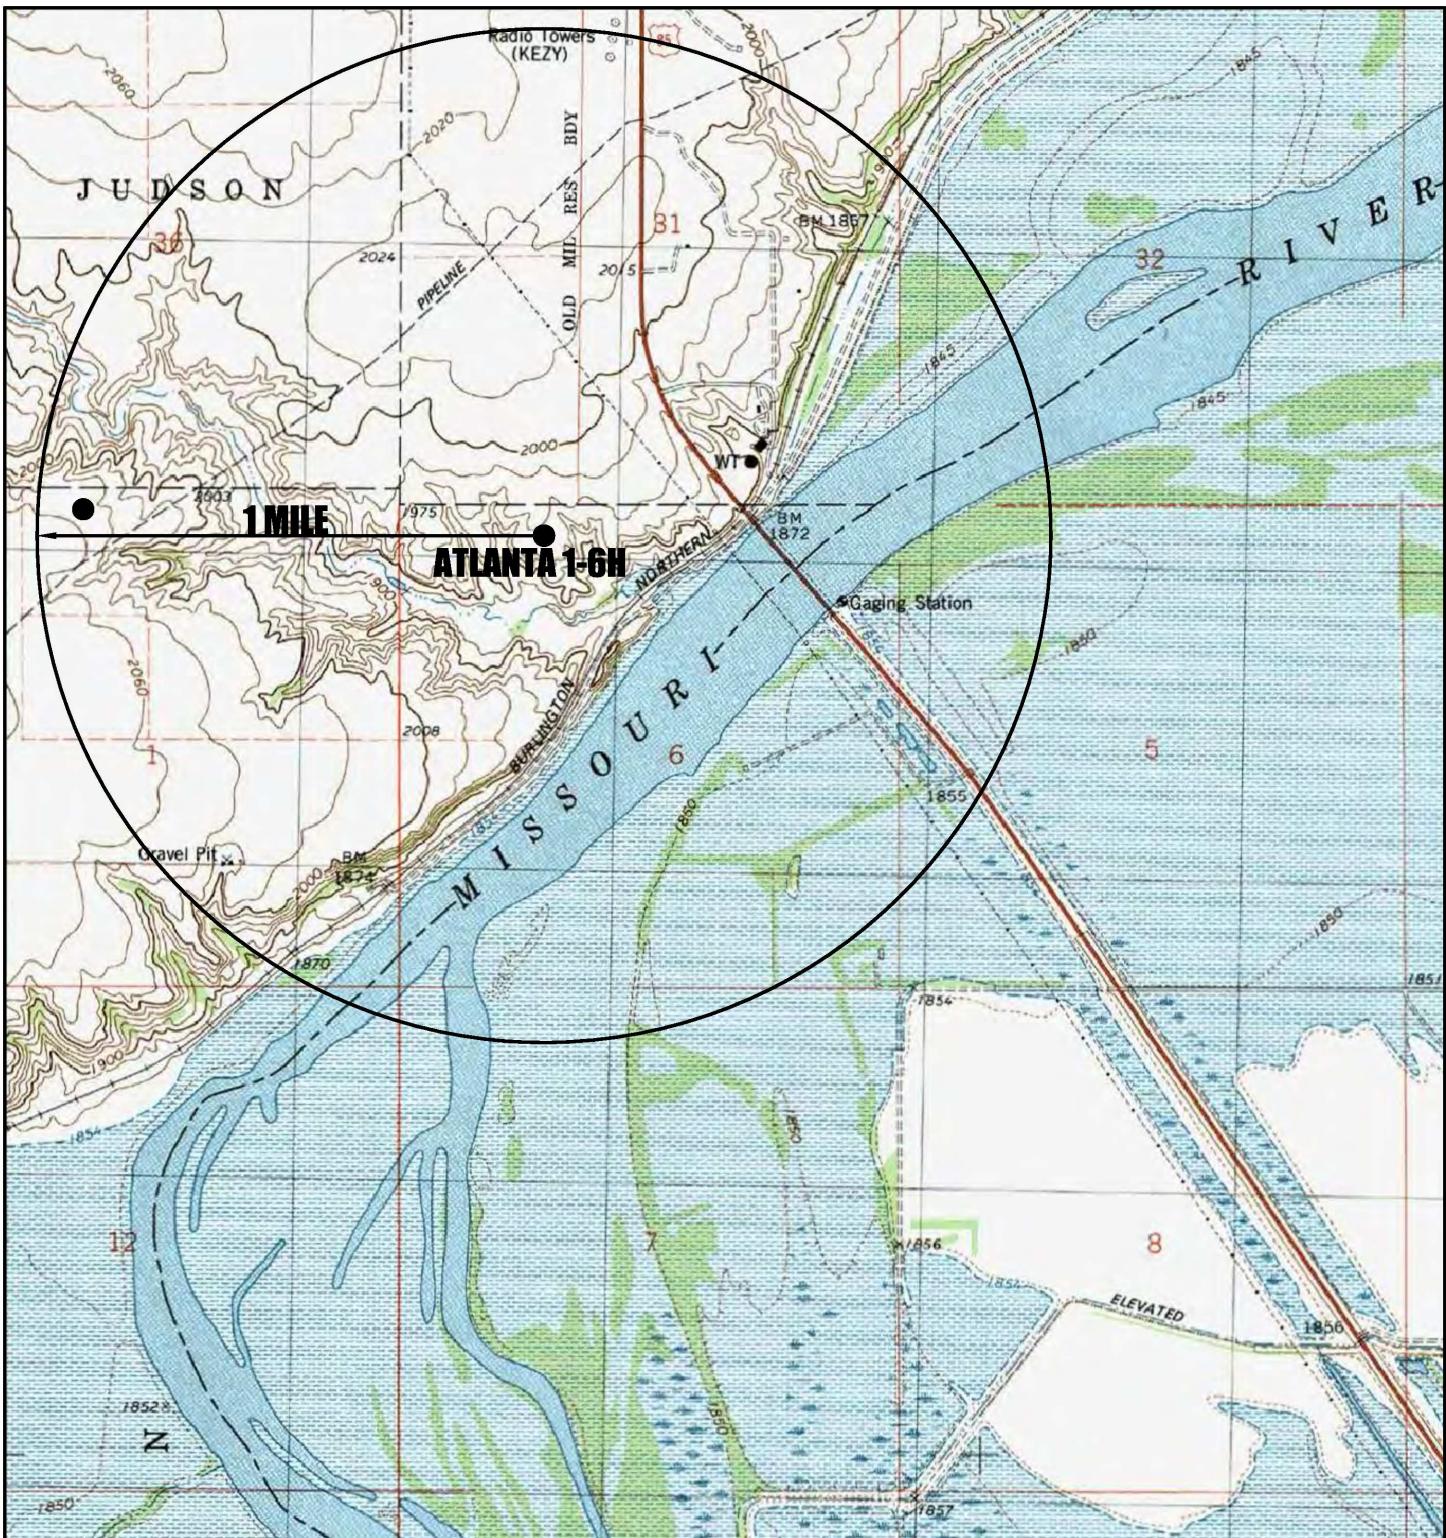


CONTINENTAL RESOURCES INC.
ONE-MILE RADIUS MAP

● = OIL WELL



SCALE 1" = 2000'

ATLANTA 1-6H
SECTION 6, T153N, R101W
WILLIAMS COUNTY, NORTH DAKOTA

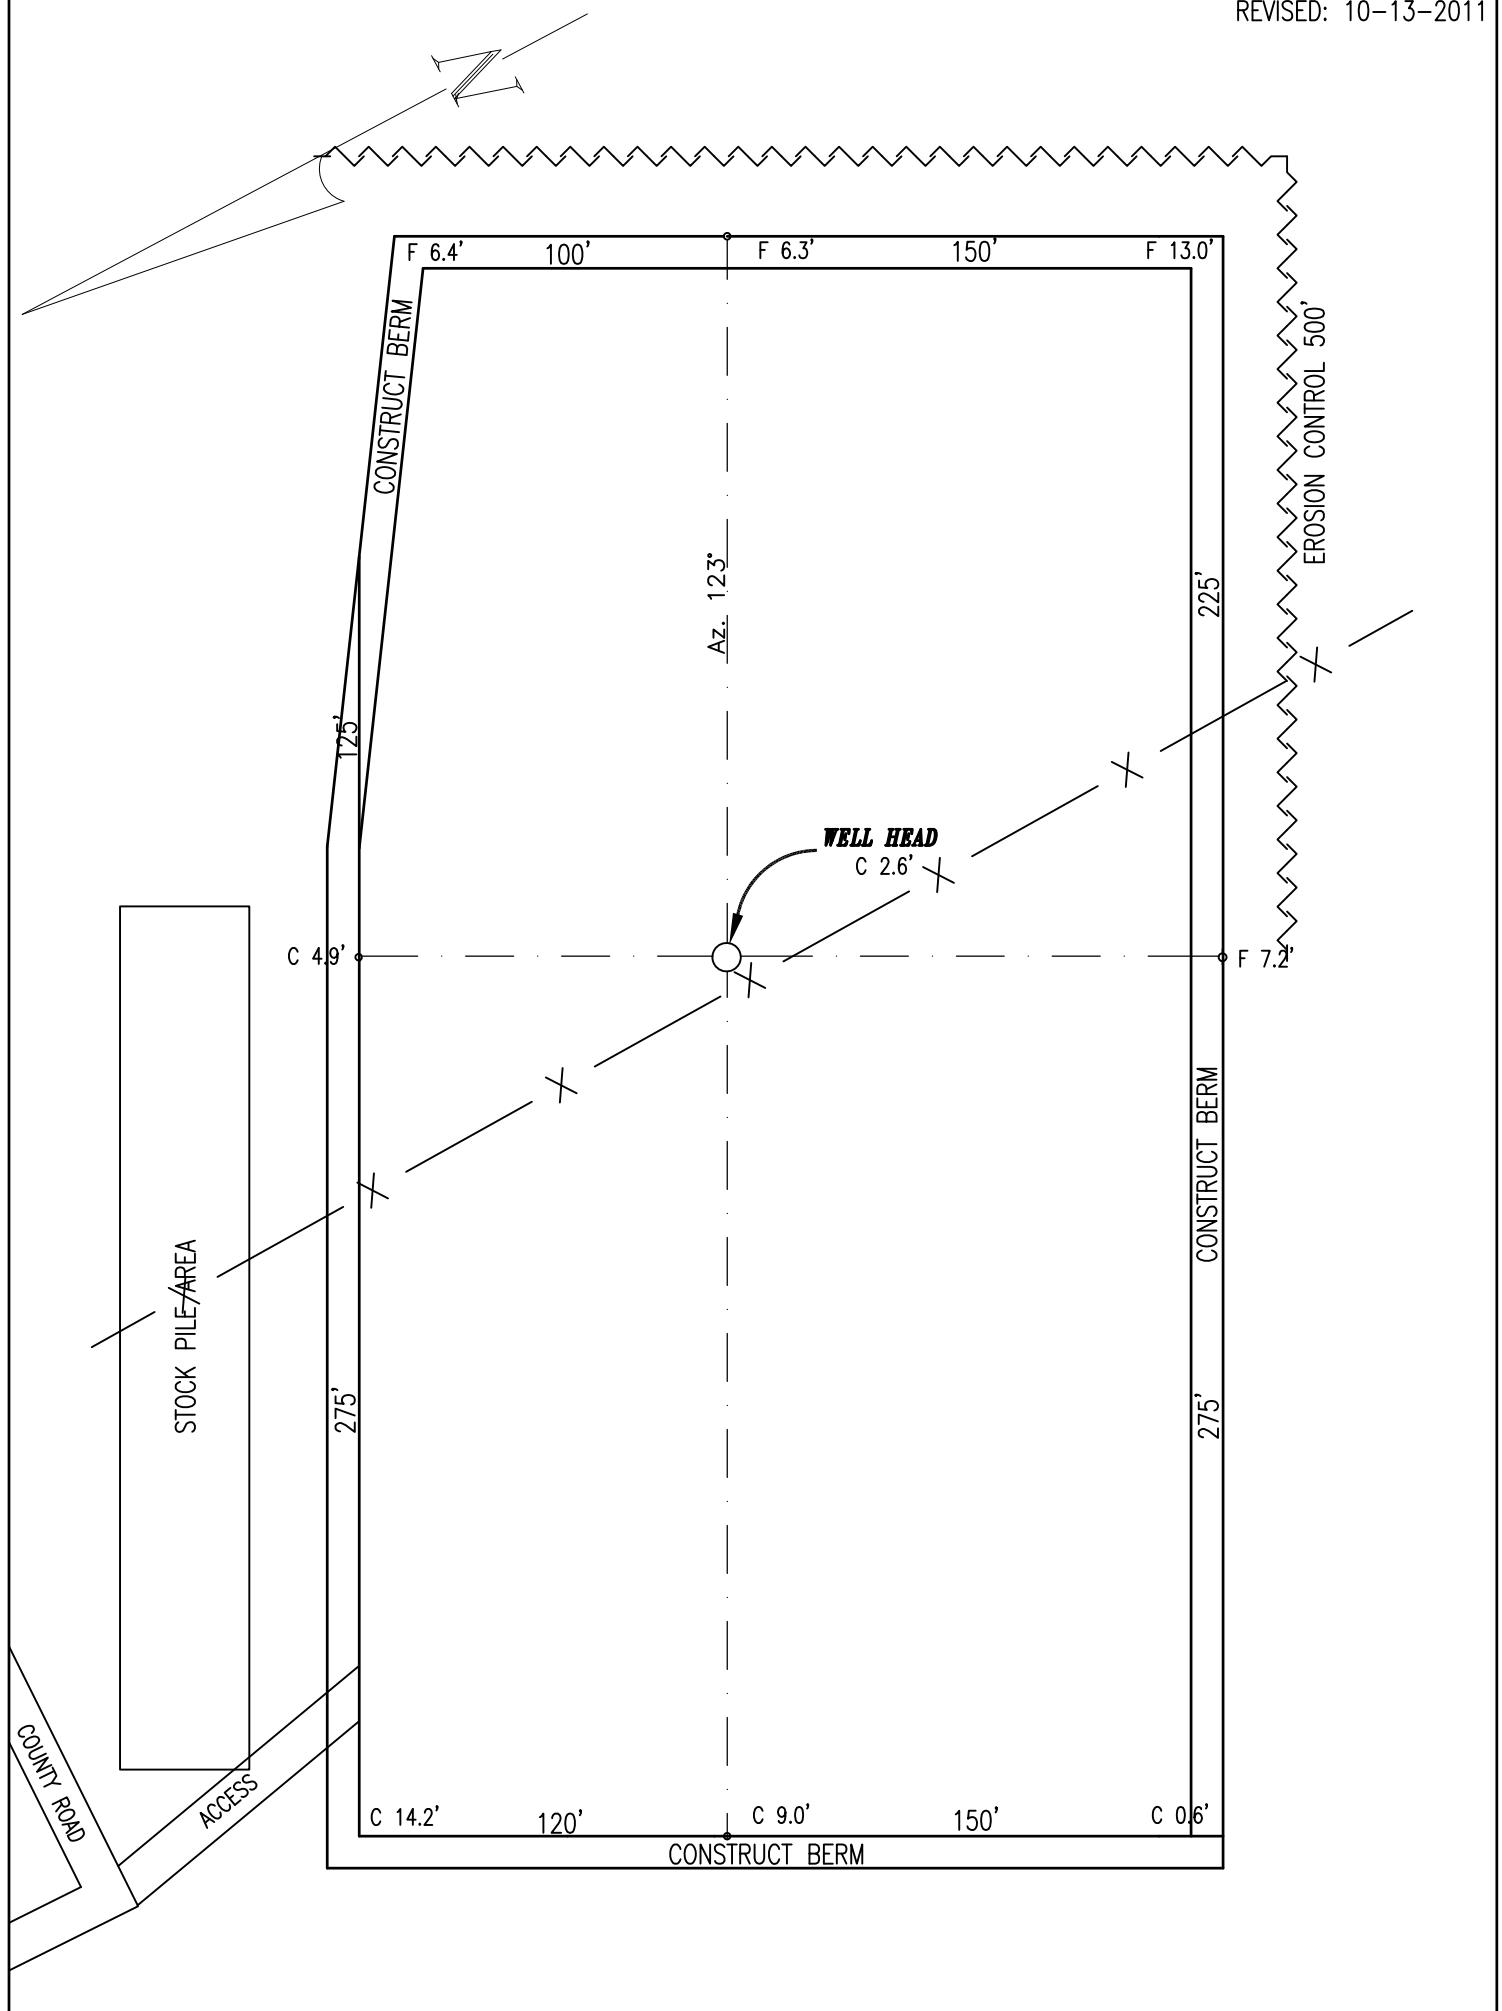

CONTINENTAL RESOURCES INC.
PO BOX 1032
ENID, OKLAHOMA 73702

DRILLING RIG LAYOUT
ATLANTA 1-6H
SECTION 6, T153N, R101W
WILLIAMS COUNTY, NORTH DAKOTA

ESTIMATED EARTH QUANTITIES

TOP-SOIL:	2,500	CUBIC YARDS
SUB-SOIL:	14,531	CUBIC YARDS

TOTAL CUT:	17,031	CUBIC YARDS
------------	--------	-------------

TOTAL FILL:	12,769	CUBIC YARDS
-------------	--------	-------------

Use excess materials in access road fill

ALL INDICATED
CUTS & FILLS
ARE STAKED
GRADE ELEVA-
TIONS.

BACKSLOPES
ASSUMED
AT 1 1/2 : 1 %

Ground Elevation at Well Head: 1955.6 ft. ASL
Finished Rig Grade Elevation: 1953.0 ft. ASL

**CYCLONE DRILLING, INC. RIG NO. 20
CONTINGENCY PLAN
FOR DRILLING ACTIVITIES CONDUCTED AT THE
CONTINENTAL RESOURCES, INC. ATLANTA 1-6H
6-153N-101W, WILLIAMS COUNTY, NORTH DAKOTA**

- r Rigs that are operated without a fresh water or well fluids pit.

3. OIL/FUEL STORAGE

- 3.1 Oil, Fuel, and Used Oil Storage Tanks.** The materials stored on-site are mainly used to operate the drilling rig's generators and pumps and generally included the following:

- r Diesel Fuel
- r Engine Oil
- r Hydraulic Oil
- r Gear Oil
- r Used Oil

- 3.2 Container Storage.** Multi-compartment storage containers are used to store hydraulic, motor and gear oil in approximate 100- to 150-gal. capacities. These container is generally located within the operating area near the accumulator valve skid. In lieu of such a multi-compartment storage container, fresh oil may be stored in 55-gal. drums.

Used oil is stored in 55-gal. drums prior to contractor removal. Because of limited available space within the rig's operating area, these drums are usually stored outside the operating area. In this event, these drums will be placed in a spill containment pan or within an earthen berm.

Containers stored within the trenched operating area would be contained by drainage to the well fluids pit. Containers used at sites that do not use pits are provided with earthen dike containment or other containment (i.e., metal containment pan.) The containment volume for containers located outside of the trenched operating area will be approximately 10% of the total volume of all containers within the containment area.

- 3.3 Transfer Facilities.** Fuel is transferred from bulk tanks into smaller day tanks located on the drilling rig, pump skids, and generator skids. Most bulk fuel tanks are equipped with a fuel pump attached to the skid. The fuel level in the day tanks is usually monitored until the tank is full.

Personnel transfer fresh oil from bulk storage tanks or drums into smaller tanks located on the drilling rig by filling 5-gal. buckets and manually filling the smaller tanks. Personnel transfer used equipment oil into 55-gal. drums using 5-gal. buckets.

Cyclone personnel are present at all times during oil and diesel transfer operations to ensure quick response in the event of a release. In addition, all pumps are securely grounded for static electricity for safety and personnel protection purposes.

- 3.4 Drainage and Containment Facilities.** The drains on containment systems will be closed and sealed except during water drainage. Prior to draining water the following steps will be taken:

**CYCLONE DRILLING, INC. RIG NO. 20
CONTINGENCY PLAN
FOR DRILLING ACTIVITIES CONDUCTED AT THE
CONTINENTAL RESOURCES, INC. ATLANTA 1-6H
6-153N-101W, WILLIAMS COUNTY, NORTH DAKOTA**

- r Visually inspect the diked areas around tanks to ensure that the water does not exhibit an oily sheen and will not result in a harmful discharge.
- r Opening, closing, and locking the bypass valve under responsible supervision following drainage activities.
- r Maintain adequate drainage operation records.

3.5 Bulk Storage Tanks. The bulk storage tanks are located within a trenched area where releases drain into the well fluids pit. The well fluids pit will be sized to provide containment volume to accommodate the largest tank within the containment area as well as sufficient volume for stormwater accumulation and the volume required for well fluid storage. Bulk storage tanks at sites that do not use pits are contained by an earthen containment dike constructed around the tank.

Stormwater that collects within the trenched area flows into the well fluids pit. Stormwater that collects within the earthen dike containment structures is inspected and if no free oil or oil sheen is observed, Continental field personnel or their on-site representatives may pump the water outside of the containment structure. In the event oil is observed in the stormwater within the earthen dike containment structures, it is pumped into a temporary container or storage tank for off-site disposal.

3.6 Truck Loading/Unloading Areas. Cyclone personnel will use spill containment booms to contain a release from a truck during loading/unloading operations or hand shovels and containment booms to direct the release to a containment trench or pit. Collected oil from such a release will be pumped into a temporary container or storage tank for off-site disposal.

4. FLOOD CONTINGENCY

Floods can develop slowly during an extended period of rain, or in a warming trend following a heavy snow. Others, such as flash floods, can occur quickly, even without any visible signs of rain. It's important to be prepared for flooding when working in a low-lying area, near water or downstream from a dam. The Atlanta 1-6H lease is located approximately 500-ft. north of an unnamed intermittent tributary of the Missouri River at an approximate elevation of 1,953-ft. above Mean Sea Level (MSL). A Well Location Map reflecting the topography of the subject site is presented herein as *Figure 3*.

- 4.1 Flood Watch.** A Flood Watch indicates flooding is possible. Tune in to NOAA Weather Radio, commercial radio, or television for information regarding potential timing of flooding. Begin preparing to move portable equipment and storage tanks to higher ground. Anchor equipment and storage tanks that cannot be readily moved.
- 4.2 Flash Flood Watch.** A Flash Flood Watch indicates flooding may occur without warning. Be prepared to move personnel, equipment, and portable storage tanks to higher ground; listen to NOAA Weather Radio, commercial radio, or television for information.



CONTINENTAL RESOURCES
WELL LOCATION



ATLANTA 1-6H
SECTION 6, T153N, R101W
WILLIAMS CO., NORTH DAKOTA

**CYCLONE DRILLING, INC. RIG NO. 20
CONTINGENCY PLAN
FOR DRILLING ACTIVITIES CONDUCTED AT THE
CONTINENTAL RESOURCES, INC. ATLANTA 1-6H
6-153N-101W, WILLIAMS COUNTY, NORTH DAKOTA**

- 4.3 Flood Warning.** A Flood Warning indicates flooding is occurring or will occur soon; if advised to evacuate, do so immediately, if safe to do so move equipment and portable storage tanks to higher ground.
- 4.4 Flash Flood Warning.** A Flash Flood Warning indicates flash flood is occurring; personnel should seek higher ground on foot immediately.
- 4.5 Flood Evacuation Plan.** In the event the Cyclone Drilling Foreman determines that the facility must be evacuated due to flooding, they will notify the personnel concerned by verbally announcing an evacuation or using internal two-way radios. All personnel will be required to meet at the designated evacuation assembly area.

The Cyclone Drilling Foreman will account for all employees at the work site. In the event any employees are missing, an immediate report will be made to the Safety Department. Good judgment must be used in evacuation procedures to avoid placing people in greater danger.

5. PREPAREDNESS AND PREVENTION REQUIREMENTS

Preparedness and prevention is required for all spills and potential flooding. The Cyclone Drilling Foreman will function as Emergency Coordinator and be responsible for establishing and implementing the preparedness and prevention measures discussed in the following sections of this Plan.

- 5.1 Emergency Equipment.** Cyclone Rig No. 20 located at the Atlanta 1-6H will be properly equipped so that Cyclone personnel can immediately respond to an emergency during working hours utilizing emergency equipment. Typical emergency equipment includes but is not limited to fire extinguishers, eyewash stations, first-aid stations, and spill response equipment. Employees will be trained and familiarized with the use and location of all emergency equipment prior to beginning operations at a work site
- 5.2 Internal Communication.** For larger jobs, Cyclone personnel use two-way radios to communicate between the rig personnel and supervisor. For smaller jobs, verbal communication is sufficient. During emergency situations, verbal communication and two-way radios (if available) will be used to provide immediate instructions to emergency response personnel. These systems are maintained, as necessary, to ensure proper operation during an emergency.
- 5.3 External Communication.** Telephones (available on some larger jobs) and cell phones are used to notify Continental's office in the event of an emergency. The office would telephone for assistance from local emergency response personnel, if necessary. The phones are routinely used to ensure proper operation.
- 5.4 Inspections.** Inspections of oil storage units, containment, and emergency equipment are conducted routinely to detect malfunctions and deterioration, operator errors, and/or

**CYCLONE DRILLING, INC. RIG NO. 20
CONTINGENCY PLAN
FOR DRILLING ACTIVITIES CONDUCTED AT THE
CONTINENTAL RESOURCES, INC. ATLANTA 1-6H
6-153N-101W, WILLIAMS COUNTY, NORTH DAKOTA**

discharges that may lead to, or cause a release of, oil from containment units or from the work site.

- 5.5 Training.** Cyclone personnel that are likely to respond to an incident are trained at least annually in solid waste management, spill response procedures, and stormwater management according to the procedures contained in this Plan. These employees are trained to perform in a manner that emphasizes accident and pollution prevention in an effort to safeguard human health and the environment.

The Cyclone Drilling Foreman is responsible for instructing appropriate personnel in the operation and maintenance of spill response equipment as well as all applicable spill control procedures. When employees are assigned to areas where oil spills may occur, it is required that a review of this Contingency Plan be conducted during on-the-job training sessions.

- 5.6 Emergency Evacuation Plan.** In the event the Cyclone Drilling Foreman determines that the facility has experienced a release, fire, or explosion that could threaten human health, they will notify the personnel concerned by verbally announcing an evacuation or using internal two-way radios. All personnel in the immediate vicinity of the emergency will be required to leave the area and report to his/her immediate supervisor at the designated evacuation assembly area. The assembly area will be determined prior to beginning operations at a work site, but may change based on wind direction during an actual emergency. The assembly area should be upwind of the work site.

The Cyclone Drilling Foreman will account for all employees at the work site. In the event any employees are missing, an immediate report will be made to the Safety Department. Good judgment must be used in evacuation procedures to avoid placing people in greater danger.

6. EMERGENCY RESPONSE PROCEDURES

Emergency Response Procedures have been established for Cyclone's work sites in the event of a spill. All spills, major and minor, will be reported to the Cyclone Drilling Foreman and Continental's Environmental Specialist. The emergency response procedures are included in *Appendix A*. The responsibilities of the First Responder, Cyclone Drilling Foreman, and Continental's Environmental Specialist are addressed in the following sections of this Plan.

- 6.1 First Responder.** When a spill occurs, the employee observing the incident will immediately notify the Cyclone Drilling Foreman and proceed to eliminate the spill source, if possible.
- 6.2 Emergency Coordinator Responsibilities.** The Cyclone Drilling Foreman will **(a)** be responsible for determining whether the release could reach navigable waters or threaten human health and/or the environment; **(b)** assess the hazard, make immediate notifications, and implement spill response procedures; **(c)** collect the necessary information for regulatory notifications and reports; and **(d)** provide the reporting information to Continental's Environmental Specialist.

**CYCLONE DRILLING, INC. RIG NO. 20
CONTINGENCY PLAN
FOR DRILLING ACTIVITIES CONDUCTED AT THE
CONTINENTAL RESOURCES, INC. ATLANTA 1-6H
6-153N-101W, WILLIAMS COUNTY, NORTH DAKOTA**

Continental's Environmental Specialist will make immediate verbal notifications and prepare and submit all required written spill reports.

Material Safety Data Sheets (MSDS) for the hazardous materials used at the work site are maintained on-site in the "doghouse" and provide information on the chemical hazards at the work site. Most releases will be minor and require only clean-up and disposal of small quantities of material. However, in the event the assessment indicates that evacuation of local areas may be advisable, they will immediately notify appropriate local authorities, as necessary. Appropriate authorities may include local police and fire departments, hospitals, and state and local emergency response teams, as identified in *Table 1*.

The Cyclone Drilling Foreman will immediately notify Continental's Environmental Specialist who will make initial verbal notifications to regulatory agencies and prepare written follow-up reports, as required. In the event the release has impacted the environment, the Cyclone Drilling Foreman and Continental's Environmental Specialist will determine clean-up requirements. In addition, the Cyclone Drilling Foreman and Environmental Specialist will coordinate the appropriate disposal of waste material generated during the response activities.

7. SPILL NOTIFICATION REPORTING

7.1 Spill Notification and Reporting. Upon receiving spill information, the Emergency Coordinator will notify Continental's Environmental Specialist who will determine if the spill requires notification and/or reporting to regulatory agencies, as outlined below:

7.1.1 North Dakota Industrial Commission (NDIC). According to the North Dakota Industrial Commission's (NDIC) General Rules and Regulations North Dakota Administrative Code (NAC) Chapter 43-02-03 Section C. Drilling:

All persons controlling or operating any well, pipeline, receiving tank, storage tank, or production facility into which oil, gas, or water is produced, received, stored, processed, or through which oil, gas, or water is injected, piped, or transported, shall verbally notify the director within 24-hrs. after discovery of any fire, leak, spill, blowout, or release of fluid. If any such incident occurs or travels offsite of a facility, the persons, as named above, responsible for proper notification shall within a reasonable time also notify the surface owners upon whose land the incident occurred or traveled. Notification requirements prescribed by this section do not apply to any leak, spill or release of fluid that is less than 1-bbl total volume and remains onsite of a facility. The verbal notification must be followed by a written report within 10-days after cleanup of the incident, unless deemed unnecessary by the director.

7.1.2 National Response Center (NRC). Any discharge to water must be reported immediately to the National Response Center. Therefore, the Cyclone Drilling Foreman must immediately inform Continental's Environmental Specialist with details regarding the spill so that official notifications can be made to the National Response Center.

CYCLONE DRILLING, INC. RIG NO. 20
CONTINGENCY PLAN
FOR DRILLING ACTIVITIES CONDUCTED AT THE
CONTINENTAL RESOURCES, INC. ATLANTA 1-6H
6-153N-101W, WILLIAMS COUNTY, NORTH DAKOTA

8. PLAN AMENDMENT

In the event that a reportable spill or flooding occurs, Cyclone personnel will review the event to determine if an amendment to this Plan is necessary. In addition, Cyclone personnel will amend the Plan whenever there is a modification in the facility design, construction, storage capacity, operation, or maintenance that renders the existing Plan inadequate.

9. MANAGEMENT APPROVAL

This Contingency Plan has been prepared for operation of Cyclone Drilling, Inc.'s Rig No. 20 to be reviewed prior to beginning operations at the Continental Resources, Inc. Atlanta 1-6 lease. The Plan will be implemented as herein described.

Ryan M

(Signature)

Ryan Nelson *Drilling Engineer*

(Name and Title - Please Print)



May 8, 2012

Industrial Commission of North Dakota
Oil & Gas Division
600 East Boulevard, Dept 405
Bismarck, North Dakota 58505

Re: Atlanta 14-6H

Continental Resources, Inc., would like to request all filings and information regarding the above captioned well be considered "Tight Hole".

Please charge the Continental Resources, Inc., credit card that is on file with your agency for the application fee of this well.

Thank you for your prompt attention to this matter. If you have any questions, you may contact me at 580-548-5139 or email the following Terry.Olson@clr.com.

Sincerely,

CONTINENTAL RESOURCES, INC.


Terry L. Olson
Regulatory Compliance Specialist
